



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 04/13/2021  
Weather: 64 degrees. Partly Sunny. High 69 degrees today.  
Hours Worked: 13:30hrs – 15:30hrs (2hrs) Site Visit.

**There was an error in my Report yesterday that Todd Demetriou pointed out. My Report said that there were only five (5) men on site from Colonial Webb when actually there were 39 men on site.**

I went by Alexes Lee's Office today and signed March's Pay Application.

I walked the site and observed the work being performed.

**Beuchert Excavation:** Six (6) men on site today. They continue to work on the Eastside of the site reshaping the Retention ponds along County Park Drive. I obtained some grass seed from the County early this morning and seeded the section of ground between the two entrances to the School from County Park Road and Beuchert laid straw matting over the area. Rain is in the forecast for tomorrow.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Twenty-seven (27) men are on site. Crews continue to lay brick on the Westside of Area E. A crew is also grouting and laying block in Vestibule C10, Area C.

**Hazzard Electric:** Thirteen (13) men are on site today. They continue to work in Area A & B & D running conduit. They have starting setting the Panels in the Kitchen Area.

**Colonial Webb:** Thirty-nine (39) men are on site today. A crew is running sanitary pipe in Area B; another crew is working on the Grease Trap that was set on Friday outside of Area D. 6 cubic yards of Concrete arrived at approximately 13:30hrs and was poured around the Grease Trap. They are also running Water Line Pipe in the Kitchen. They are also insulating pipe in Area B.

**Weldon Steel:** Six (6) men are on site today. They continue to set and weld steel in Area C.

**JP Construction:** Thirteen (13) men are on site today. They continue to erect interior walls in Area A, 2<sup>nd</sup> floor, hanging sheet rock on the 1<sup>st</sup> floor of Area A; installing flashing on the Northside of Area A and flashing around the Parapet Wall cap on the High Roof of Area E.

**AAR Roofing:** Four (4) men are on site today. They are working on the High roof of Area A.

**Tailored Foam:** Two (2) men are on site today but I did not observe where they are working.

**FG & M:** Three (3) men are on site. They continue to work on the large Storefront on the eastside of Area A and are setting glass in Storefronts on the 2<sup>nd</sup> floor of Area A.

**United Sprinkler:** One (1) man are on site today running Sprinkler pipe on the 2<sup>nd</sup> floor of Area B.

**S&S Concrete Cutting Company:** I did not observe anyone on site during my visit today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** I did not observe anyone on site during my visit.

**Questions to or from Branch Builds:** I met with Brian Topper and Cooper in the Trailer this morning and we discussed what was happening on site today. Brian said that the roofer are still going to move to the low Roof above the Mechanical Room in Area D once they finish the roof in Area A. I briefed Brian on what Beuchert and I agreed to related to the Seeding along the Rec Park Road.

Brian asked me to reach out to the County to determine what the requirements would be after temporary seeding is done and it comes time for permanent seeding to occur. Beth McDonnel said that generally Permanent Seeding can be applied directly over the Temporary seeding. However, if the soil is compacted it may require for the soil to be aerated.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** Last Inspection was yesterday on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) –**

**Submittals –**

**RFIs –**

**Patrick Byrne –**

**Change Order/PCOs/Pay App –** I signed March Pay Application

**Changes in Procore –**

**Weekly Submittal Status Report –**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**



Photo 1 - Work continues on the Storefront located on the Eastside of Area A





Photo 2 - Concrete being poured around Grease Trap





Photo 3 - Steel being welded in Area C



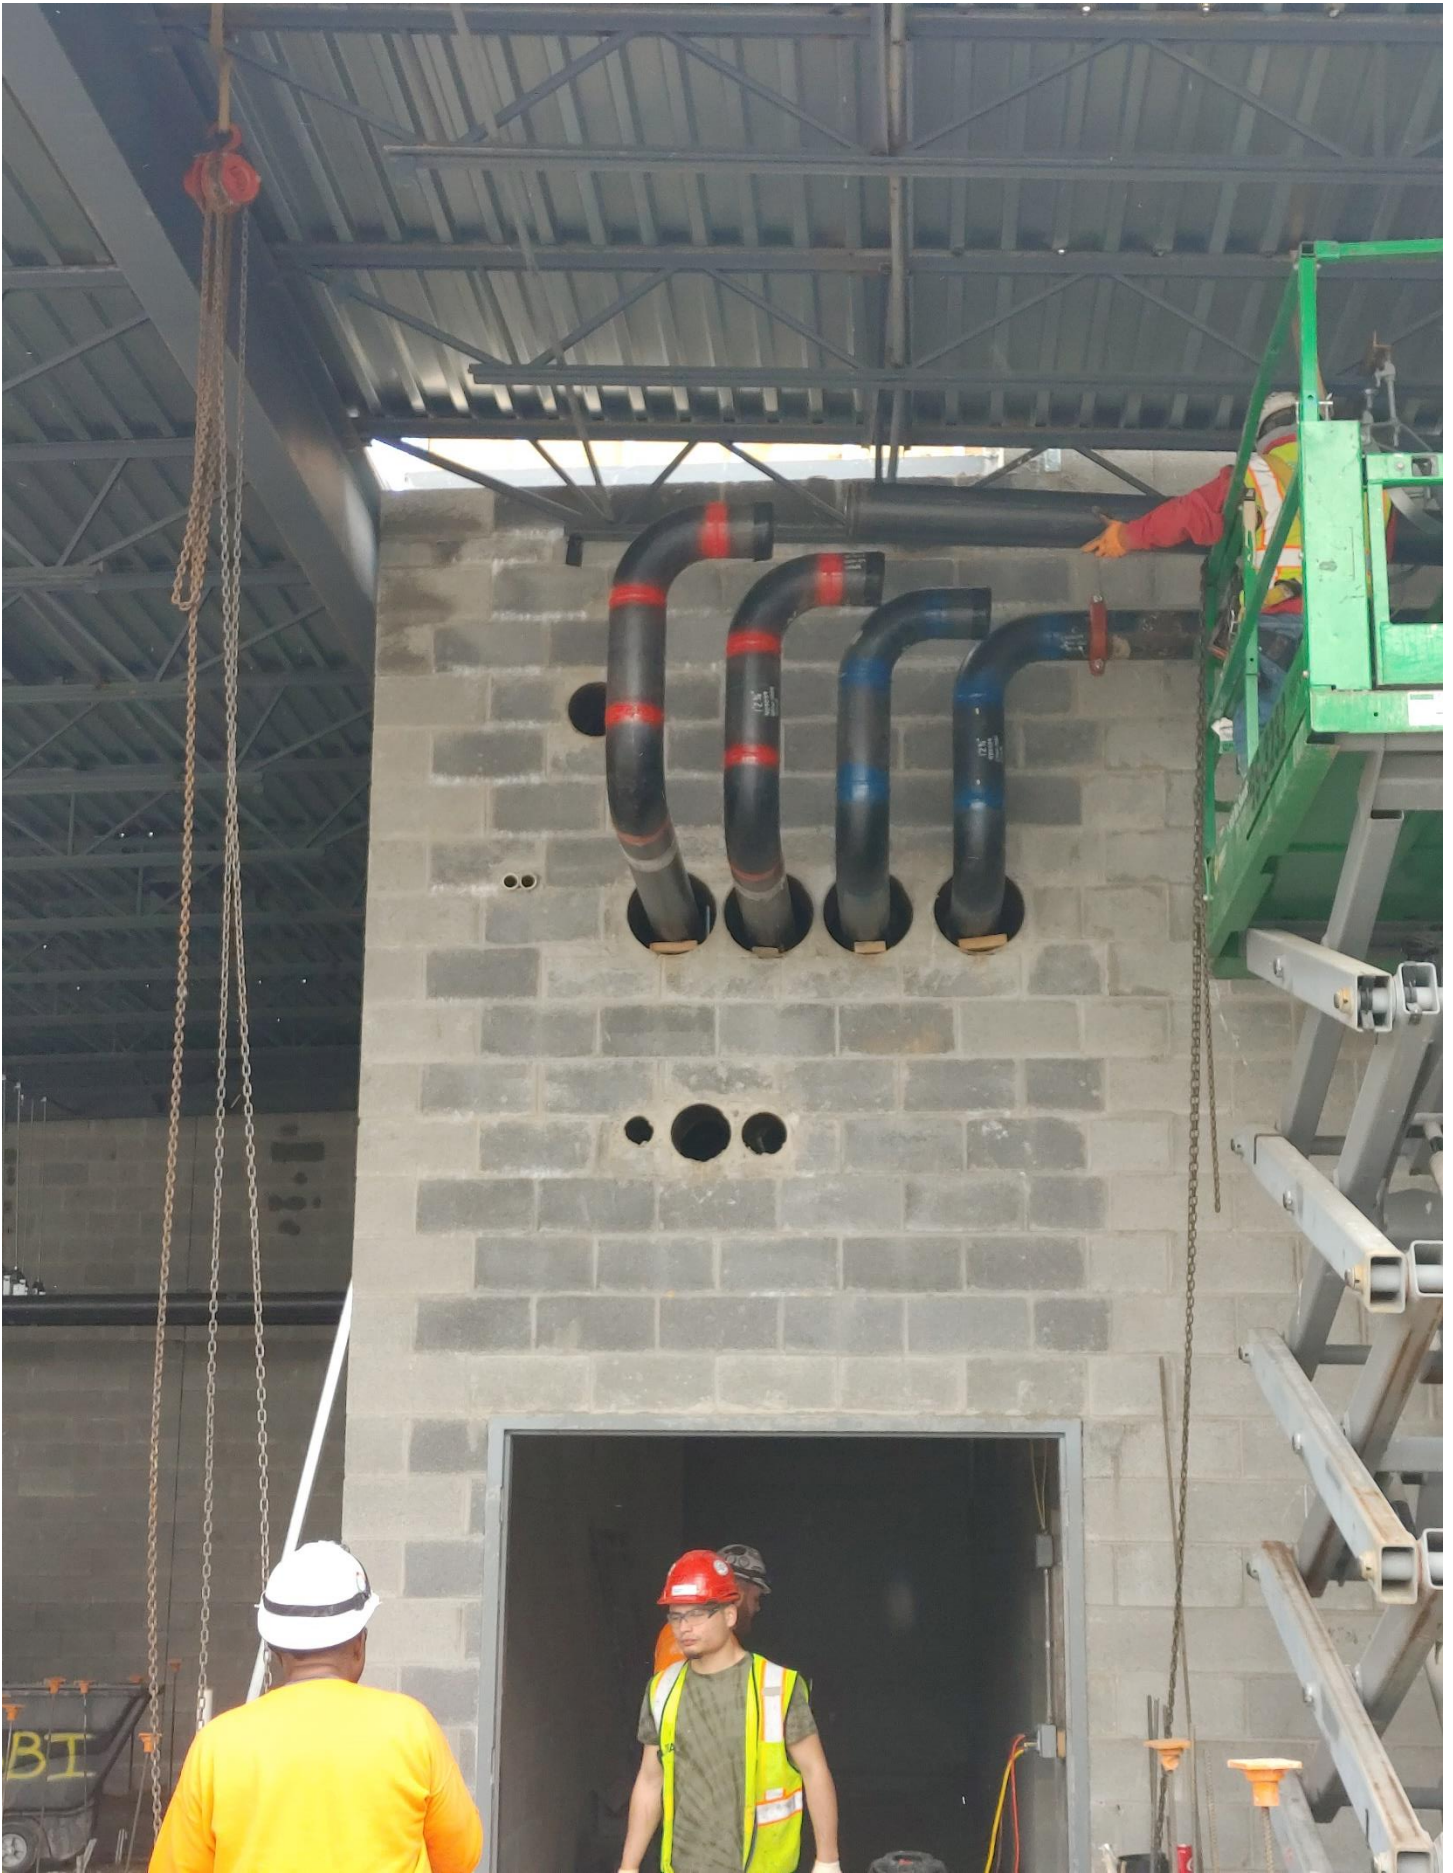


Photo 4 - Pipe being ran by Colonial Webb in Area C





Photo 5 - Hazzard Electric setting Panel Boxes in the Kitchen Area





Photo 6 - Block being laid and Grouted in Vestibule C10





Photo 7 - Masons laying Brick on the Westside of Area E





Photo 8 - High Roof Parapet Roof Cap being flashed and caulked Area E





Photo 9 – Fredericksburg Glass & Mirror setting Glass on the 2<sup>nd</sup> floor of Area A





Photo 10 - Pipe being insulated in Area B





Photo 11 - Roofers working on the high roof of Area A





Photo 12 - Weldon Steel setting steel I-Beam in Area C





Photo 13 - Brick Flashing continues to be installed on the Northside of Area A





Photo 14 - Completed Brick Flashing on the Northside of Area A
