



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/14/2021
Weather: 49 degrees at 07:30hrs. Sunny. High degrees today.
Hours Worked: 7:30hrs – 10:00hrs (2.5hrs) Site Visit.

I walked the site and observed the work being performed.

Beuchert Excavation: Six (6) men on site today. They continue to work on the Eastside of the site reshaping the Retention ponds along County Park Drive and now are also begun to work on the Westside of the site. They are also pumping Retention Pond #1 so that they can start work in that area.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Twenty-seven (27) men are on site. Crews continue to lay brick on the Westside of Area E. A crew is laying Brick on the Eastside of Area E

Hazzard Electric: Thirteen (13) men are on site today. They continue to work in Area A & B & D running conduit.

Colonial Webb: Forty (40) men are on site today. A crew to run sanitary pipe in Area B; another crew is working in the area between Area A & D running Sanitary pipe. They are also running Water Lines in Area A. They are also insulating pipe in Area B and running HVAC Duct.

Weldon Steel: Six (6) men are on site today. They continue to set and weld steel in Area C.

JP Construction: Sixteen (16) men are on site today. They continue to erect interior walls in Area A, 2nd floor, hanging sheet rock on the 1st floor of Area A; installing flashing on the Northside of Area B above windows and flashing around the Parapet Wall cap on the High Roof of Area E. They are also installing metal framing on the Southside of Area E.

AAR Roofing: Four (4) men are on site today. I am told they have a few items remaining to wrap up in Area B and then they are going to begin working on the low roof of Area D.

Tailored Foam: Two (2) men are on site today and are working on the Air Barrier in Area D.

FG & M: Four (4) men are on site. They are setting glass on the Northside of Area A.

United Sprinkler: One (1) man are on site today running Sprinkler pipe on the 2nd floor of Area B.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: Met with Brian in the Trailer and he said he is working on two mock-ups. One of a "Learning Studio" front A105 and a Stairwell tread for the stairwells. I asked Brian when he thought that his Steel guys would be finished because I noted that they don't have very much steel left to set. Brian said he is pushing them, but they still have to install the decking in Area C and wrap up a lot of little things. So it will be a while yet before they finish.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was yesterday on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report - 04/13/2021

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –



Photo 1 - JP installing metal framing on the Southside of Area E

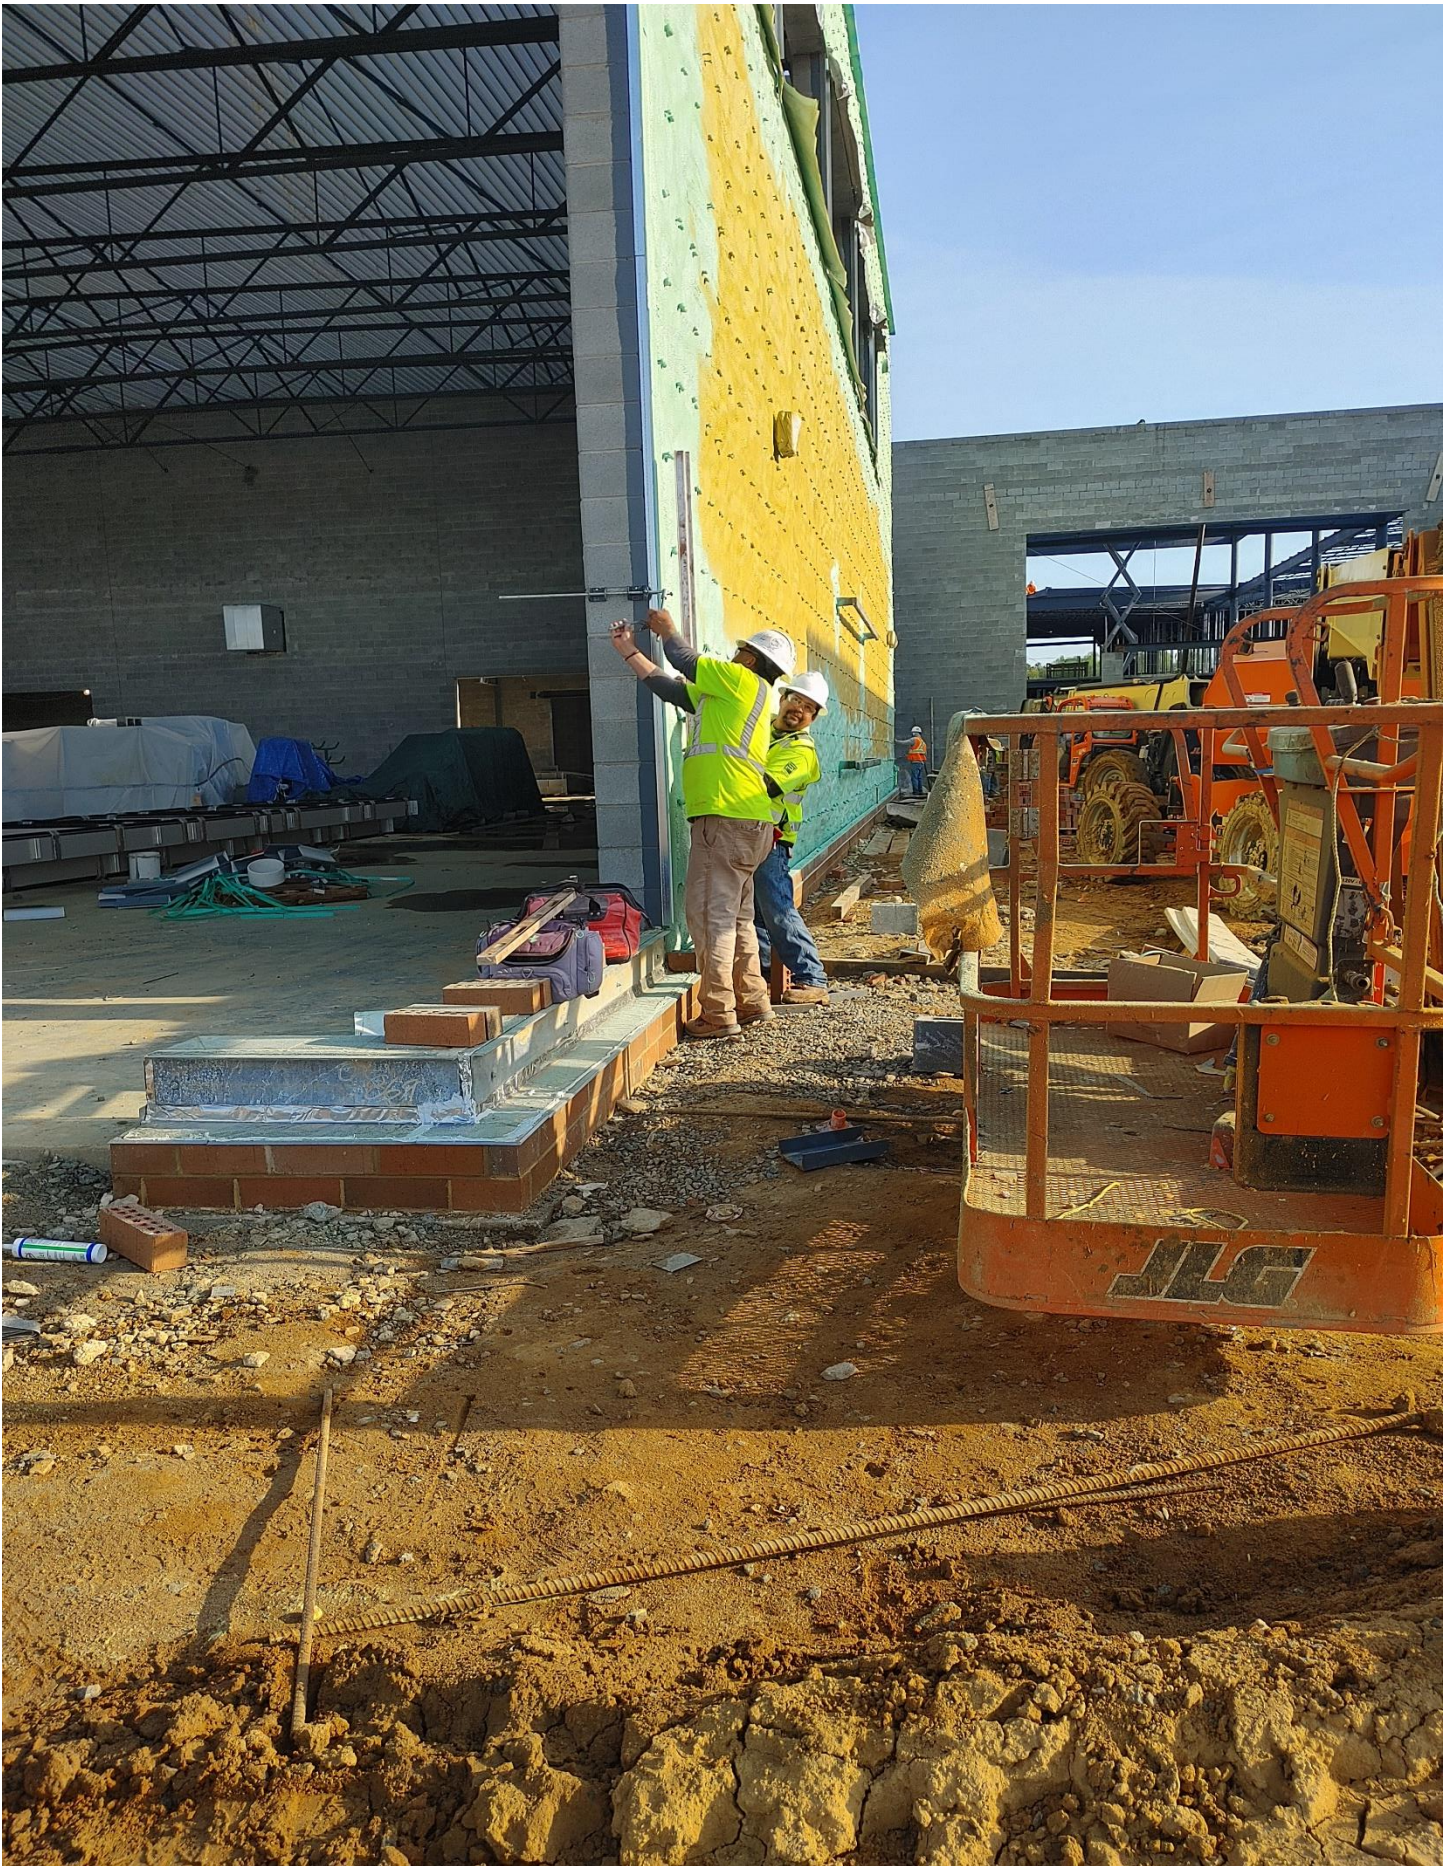


Photo 2 - JP Long setting up and preparing to lay brick on the Eastside of Area E



Photo 3 - Weldon Steel setting steel in Area C



Photo 4 - Masons laying brick on the Westside of Area E



Photo 5 - Windows are being flashed on the Northside of Area B

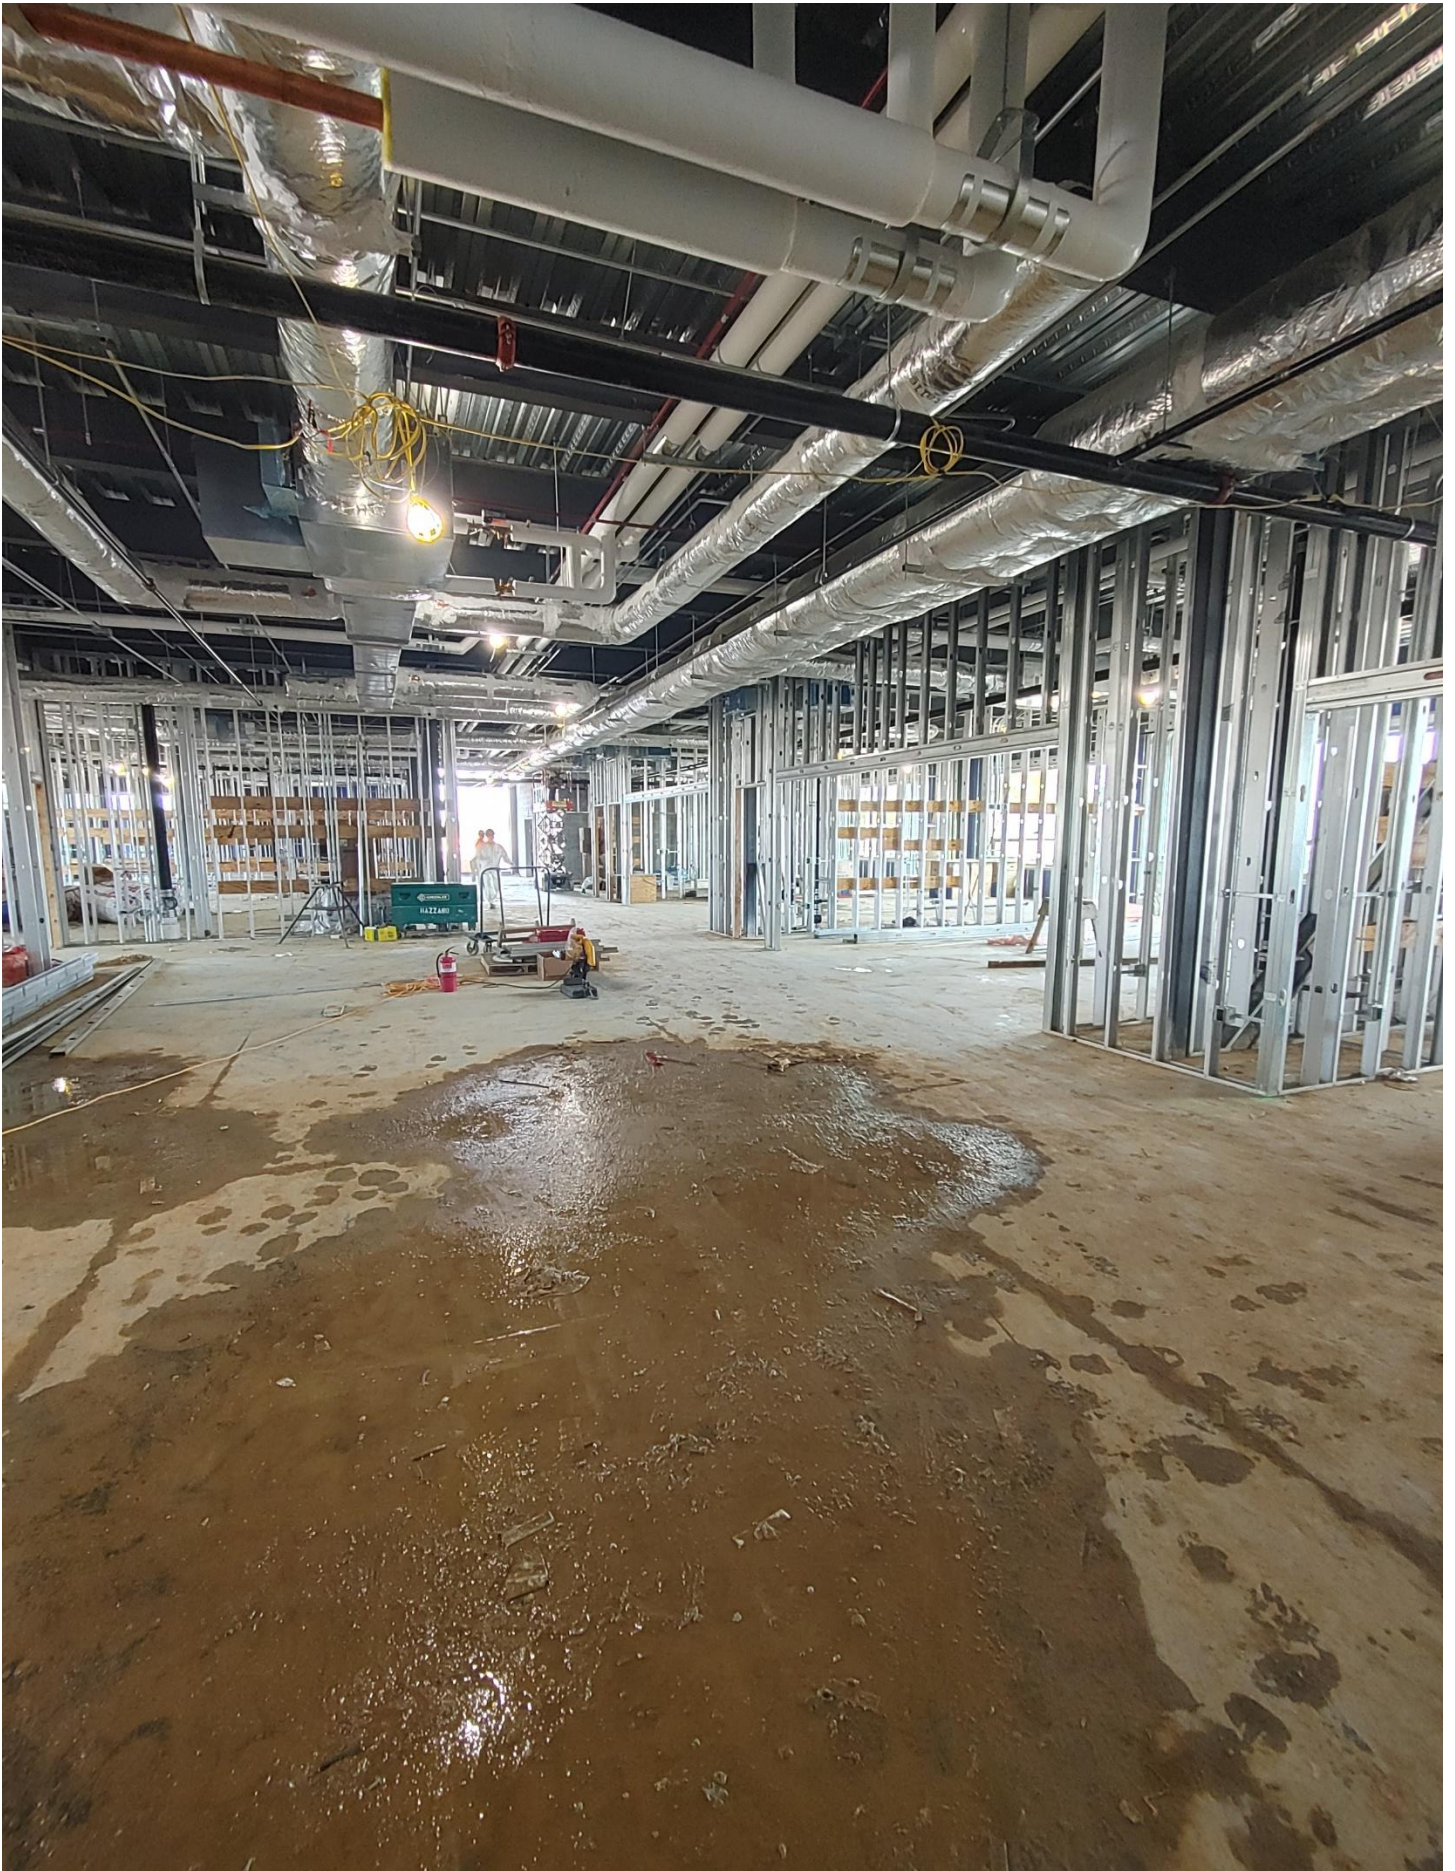


Photo 6 - The fronts of the Learning Studios are being framed in Area B



Photo 7 - Sheetrock is being hung up to the Metal Decking in Area A, 1st floor.



Photo 8 – The Roofers are making progress on the roof from of Area B to Area A.



Photo 9 - Beuchert continues to work on the Westside of the Site.
