



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/21/2021
Weather: 54 degrees at 14:30hrs. Light Rain. High of 59 degrees today.
Hours Worked: 14:30hrs – 16:00hrs (1.5hrs) Site Visit.

I did not visit the site yesterday.

Beuchert Excavation: I counted three (3) men on site today. They continue to move dirt around the site, grading and reworking the Retention Ponds.

Industrial Concrete: Five (5) men are on site today. They are setting the steel rebar for the Loading Dock Wall. The Footer will be poured tomorrow.

J.D. Long, Masons: Fourteen (14) Masons are on site today laying Brick on the South and West sides of Area E.

Hazzard Electric: Seventeen (17) men are on site and they continue to work in Area A & B & D running conduit and pulling wire.

Colonial Webb: Forty-Six (46) men are on site today. They are insulating pipe in Area B, 1st floor, connecting Roof Drains in Areas A & B. They are also running HVAC Duct in Area A, 1st floor.

Weldon Steel: Six (6) men are on site today. They continue to set and weld steel in Area C. A couple of guys are also laying Roof Decking in Area C.

JP Construction: Eighteen (18) men are on site today. They continue to erect interior walls and hanging sheet rock on the 1st floor of Area A. They are also installing batt Insulation in Area A 1st floor. A crew is also framing the Parapet wall on the eastside of Area A Stairwell.

AAR Roofing: Four (4) men are on site today. They have been working on the roof of Area A.

Tailored Foam: Two (2) men are on site today. They have been spraying foam on the Eastside of Area.

FG & M: Four (4) men are on site. They are working on the curtain wall on the Westside of Area B.

United Sprinkler: One (1) man are on site today running Sprinkler pipe on the 2nd floor of Area B.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: Brian left the site early today and was not here when I arrived. I met with Jake and Cooper in the trailer. Jake and I examined the Stair Tread Mockup that was completed yesterday. Copper and I discussed the project and what was going on today.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals – #26 50 00-2.1

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App – PCO #44

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –



Photo 1 – Stair tread Mockup has been completed.



Photo 2 - The East side of Area A has been foamed.



Photo 3 - The Masons are bringing up the brick on the South side of the Gym



Photo 4 - Steel continues to be set in Area C



Photo 5 - Metal Decking is being laid in Area C



Photo 6 - Walls have been insulated and now are being sheet rocked on both sides in Area A, 1st floor.



Photo 7 - Interior walls being framed on the 2nd Floor or Area A



Photo 8 - Roofers are making progress on the Roof of Area A



Photo 9 - Parapet Wall being framed in Area A



Photo 10 - Door Frame has been set at the top of Stairwell #2.

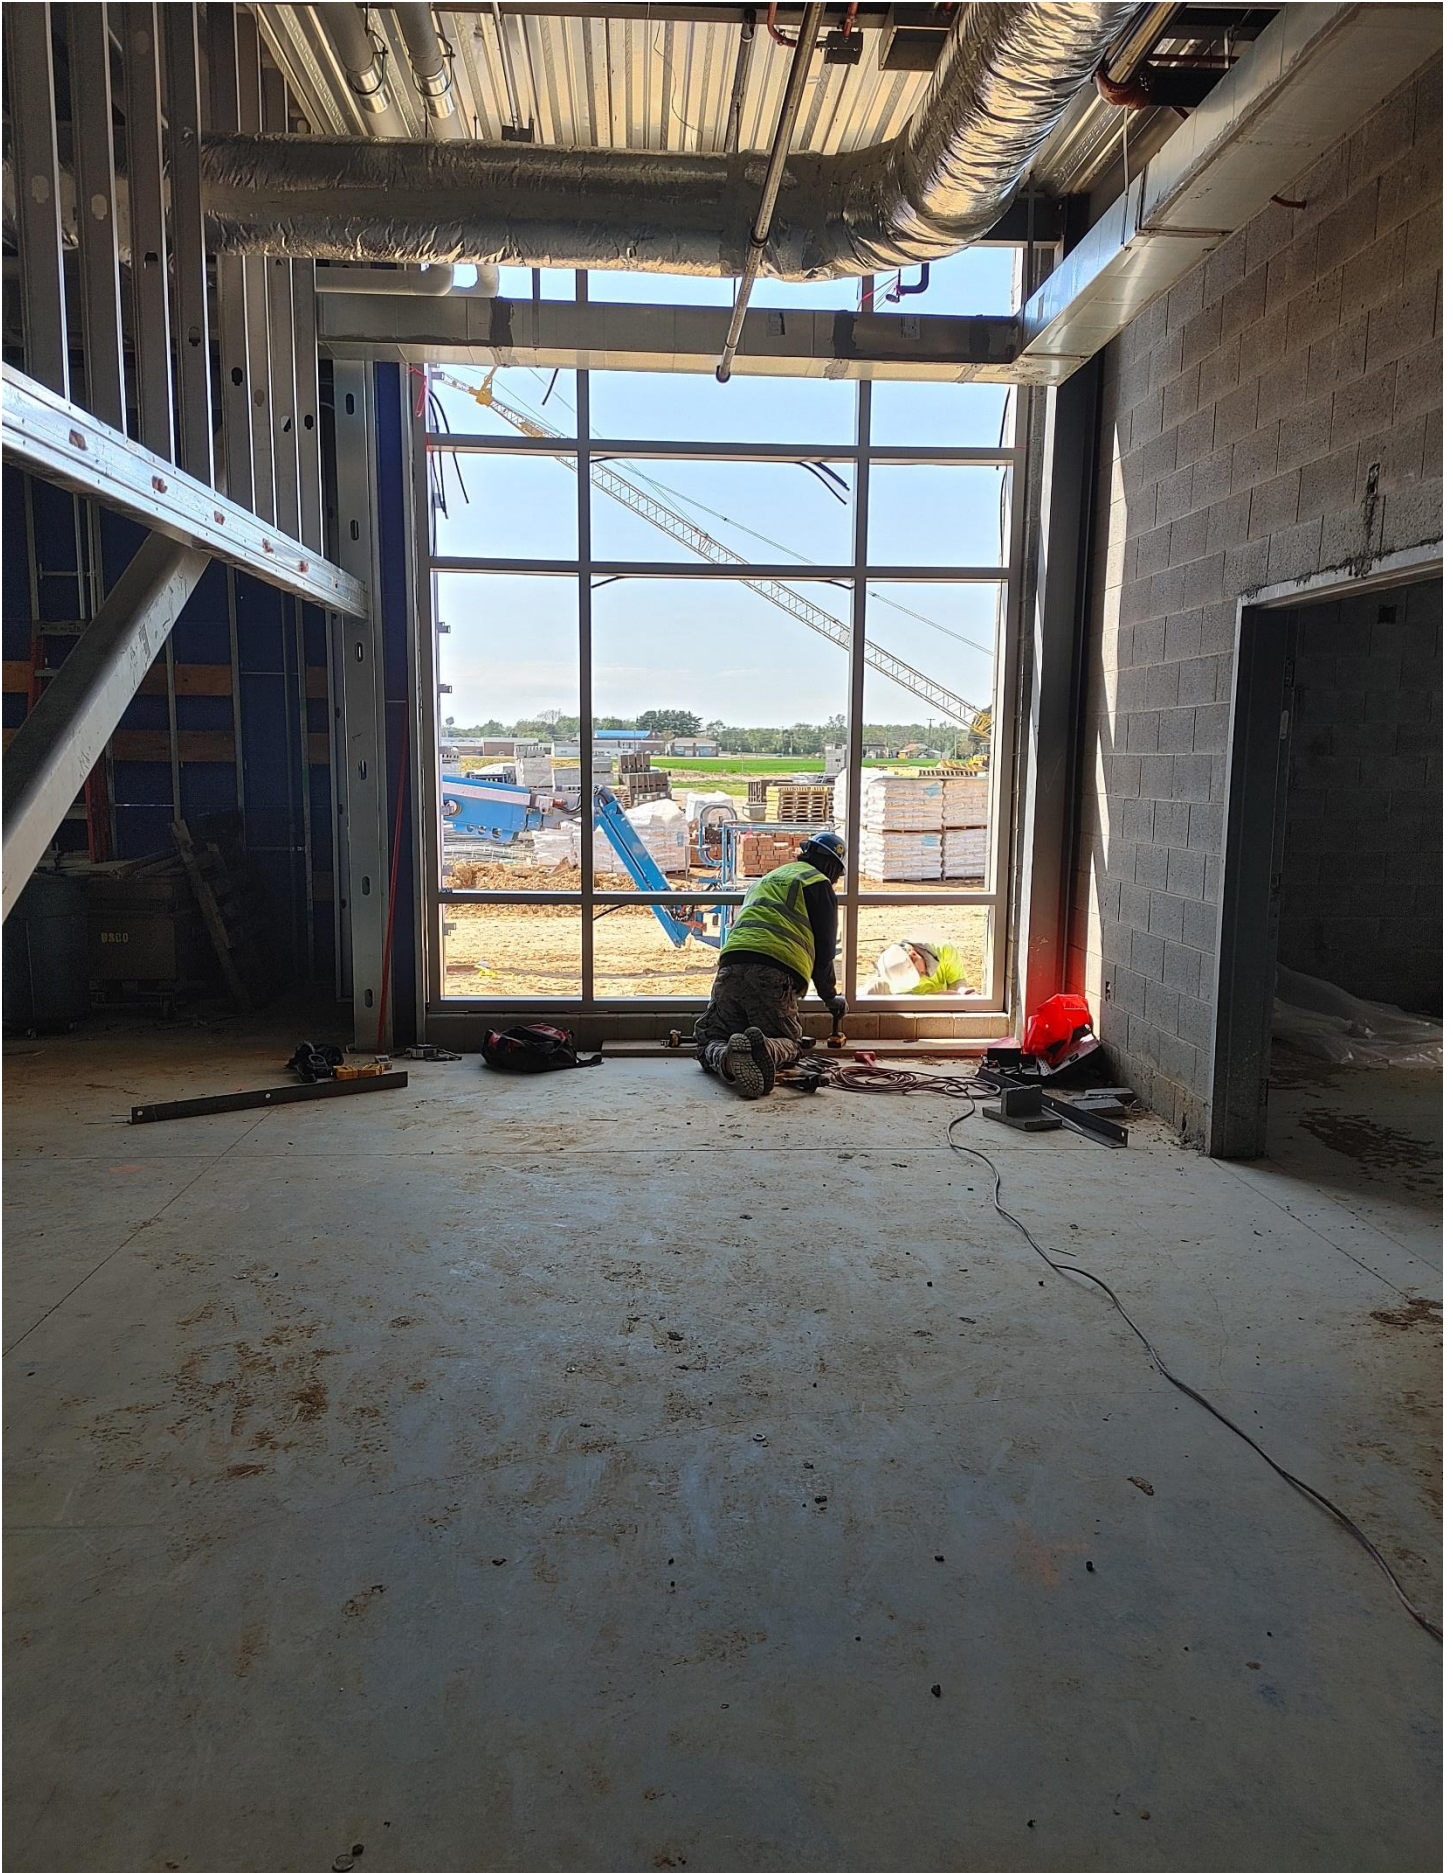


Photo 11 - Frame has been set on the West side of Area B
