



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/23/2021
Weather: 61 degrees at 12:00hrs. High of 64 degrees today.
Hours Worked: 12:00hrs – 14:30hrs (2.5hrs) Site Visit.

Beuchert Excavation: They have a couple of men on site today and they continue to move dirt around the west side of the site, grading and reworking the Retention Ponds.

Industrial Concrete: Three (3) men are on site today. They are setting metal forms for the Concrete Loading Dock Retaining Wall.

J.D. Long, Masons: Fourteen (14) Masons are on site today laying Brick on the East side of Area E and block in Area C, Vestibule C10. A couple of guys are installing brick flashing on the East side of Area A.

Hazzard Electric: Fifteen (15) men are on site and they continue to work in Area B & D running conduit and pulling wire. They have set a couple more Switch Gears in the Electrical Room of Area D.

Colonial Webb: One (1) man is on site today handling administrative matters.

Weldon Steel: Six (6) men are on site today. They continue to set and weld steel in Area C. A couple of guys are also laying Roof Decking in Area C.

JP Construction: Fourteen (14) men are on site today. They continue to erect interior walls and hanging sheet rock in Area A. two men are also installing flashing on the east side of Area A.

AAR Roofing: Four (4) men are on site today. They continue to work on the roof of Area A.

Tailored Foam: Two (2) men are on site today. They have been spraying foam on the South side of Area D.

FG & M: Four (4) men are on site. They continue to work on the curtain wall on the Westside of Area B.

United Sprinkler: One (1) man is on site today running Sprinkler pipe on the 2nd floor of Area A.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: I met with Brian in the trailer. We discussed the project and I pointed out to Brian the areas on the East side of Area A that were either missing caulk or where the caulk had contracted and needed attention. Brian said he would speak to his sub and have it corrected (pictures below).

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs – #248, #253, #255, #257, #260

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report – 04/23/2021

Weekly RFI Status Update – 04/23/2021

Weekly Daily Log Summary – 04/23/2021



Photo 1 - FM&G continues to work on the Curtain Wall on the West side of Area B



Photo 2 - South side of Area D is being Spray Foamed



Photo 3 - The Masons continue to lay Brick on the East side of Gym.



Photo 4 - Pre Cast has been set under the windows of the Gym on the South side.



Photo 5 - The Electricians have set several more Switch Gears since yesterday.



Photo 6 - Industrial Concrete is setting Metal Forms for the Loading Dock Retaining Wall.

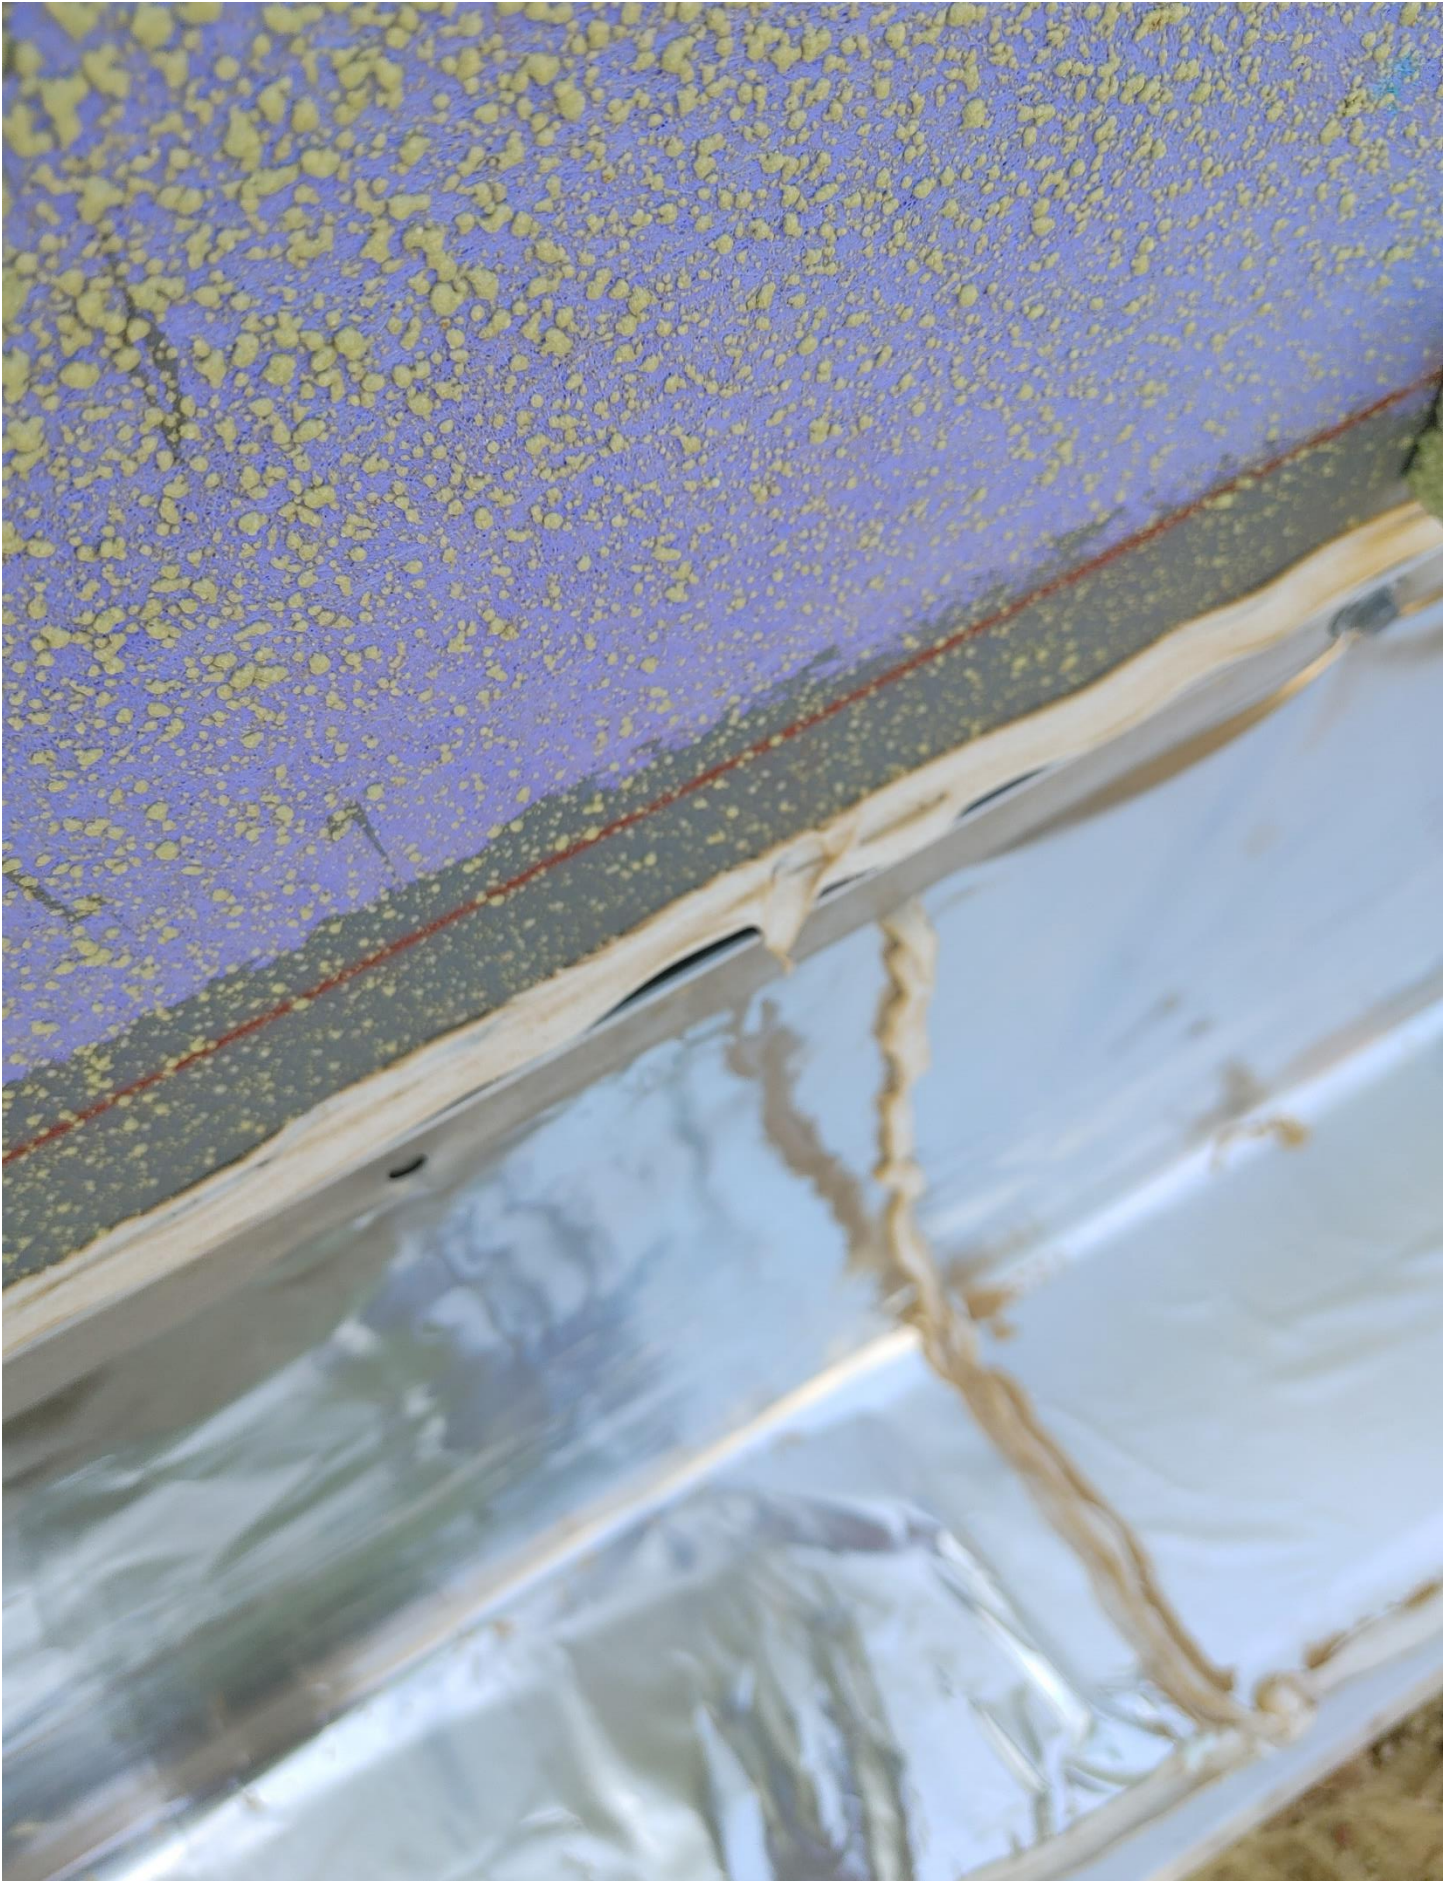


Photo 7 – One of the areas where the caulking has separated from the flashing and wall on the East side of Area A.

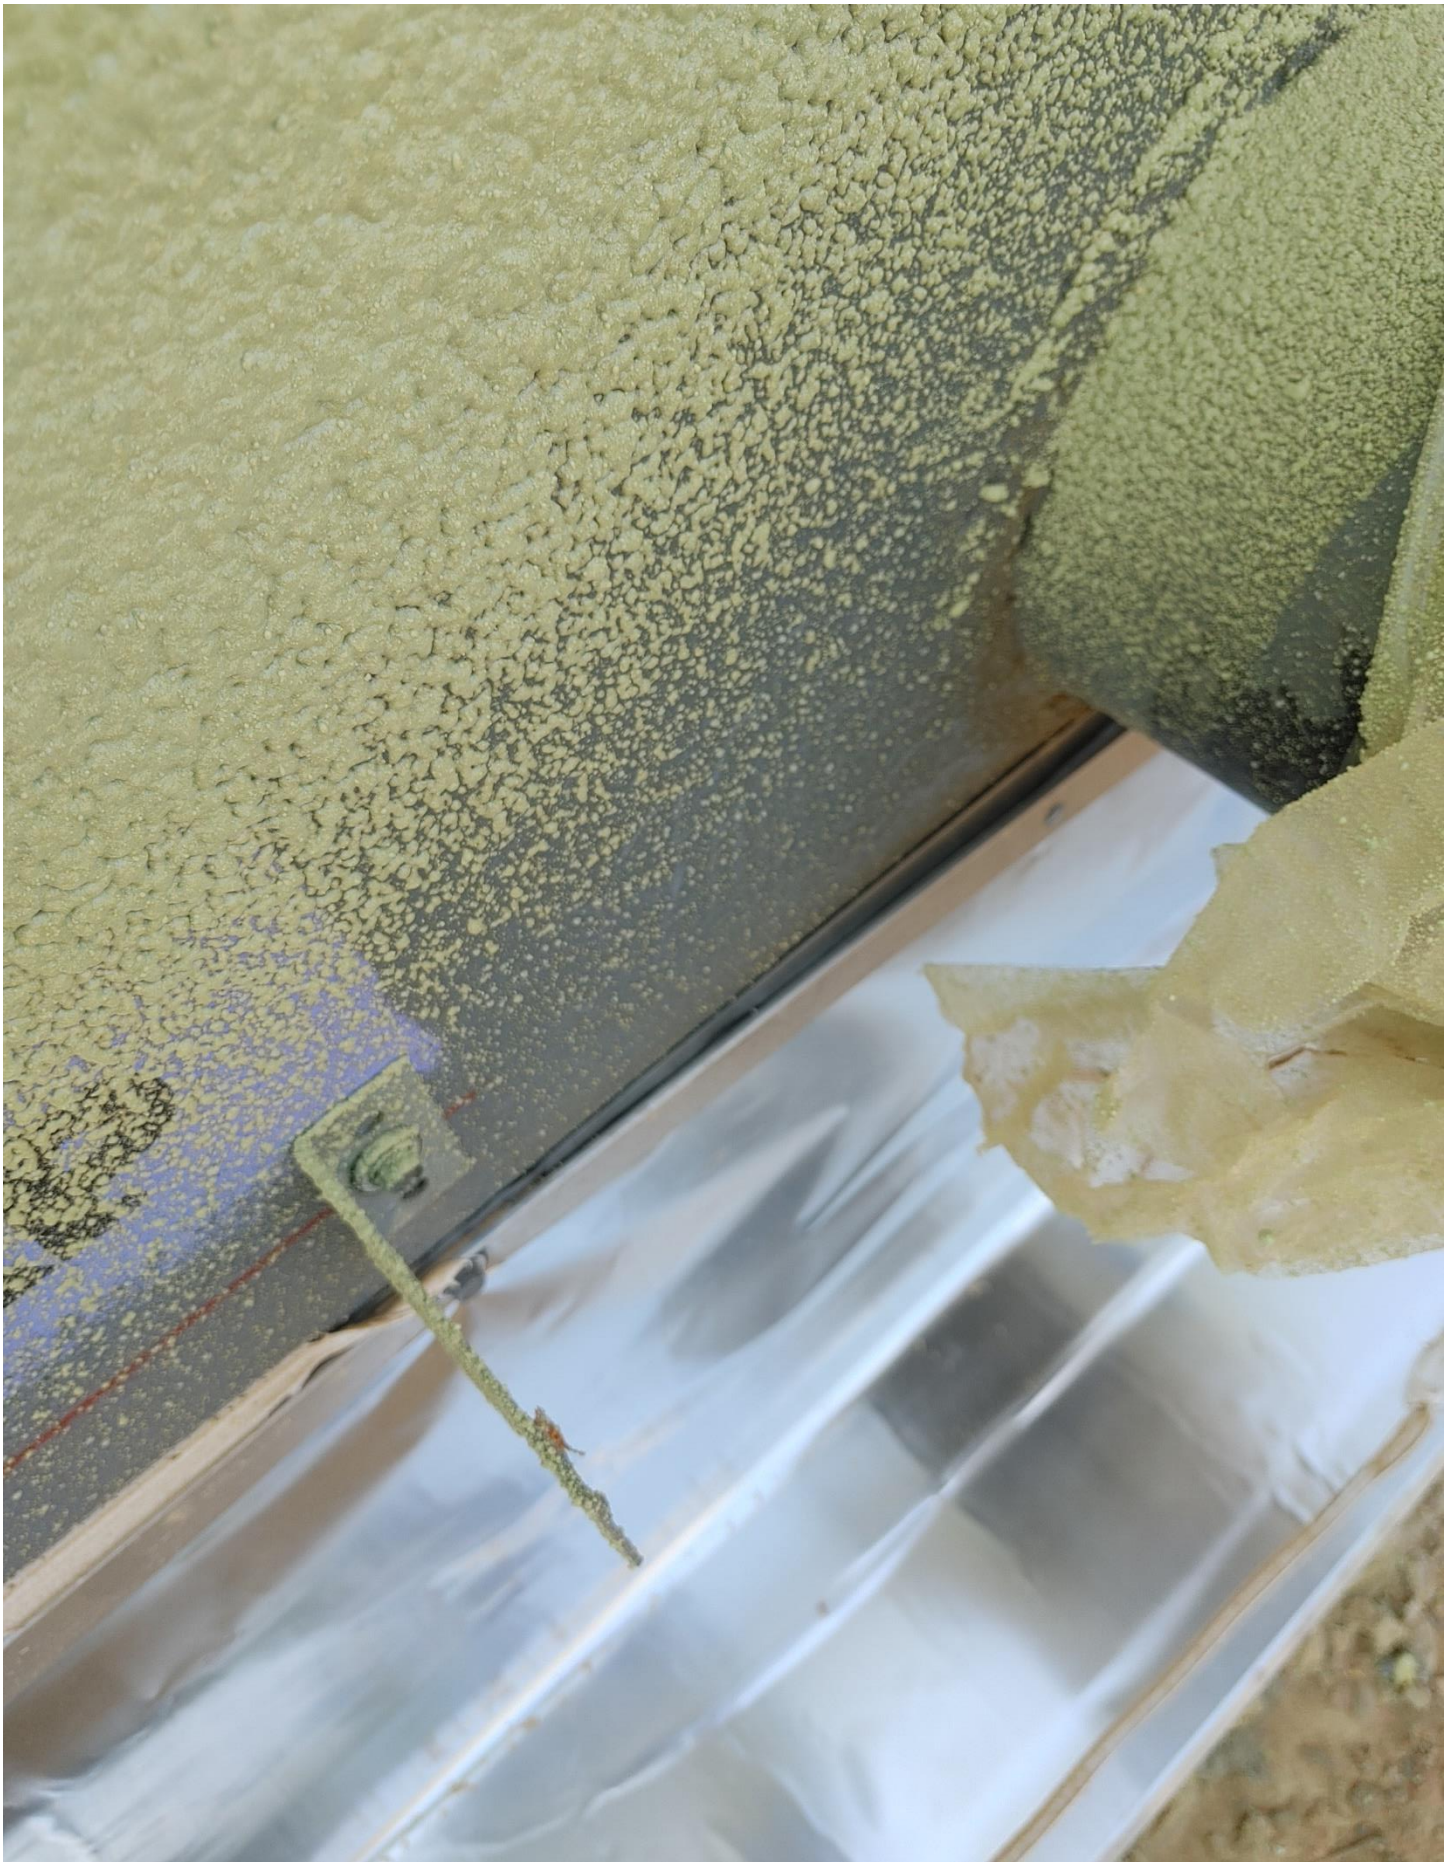


Photo 8 - An area that was missed and not caulked on the East side of Area A

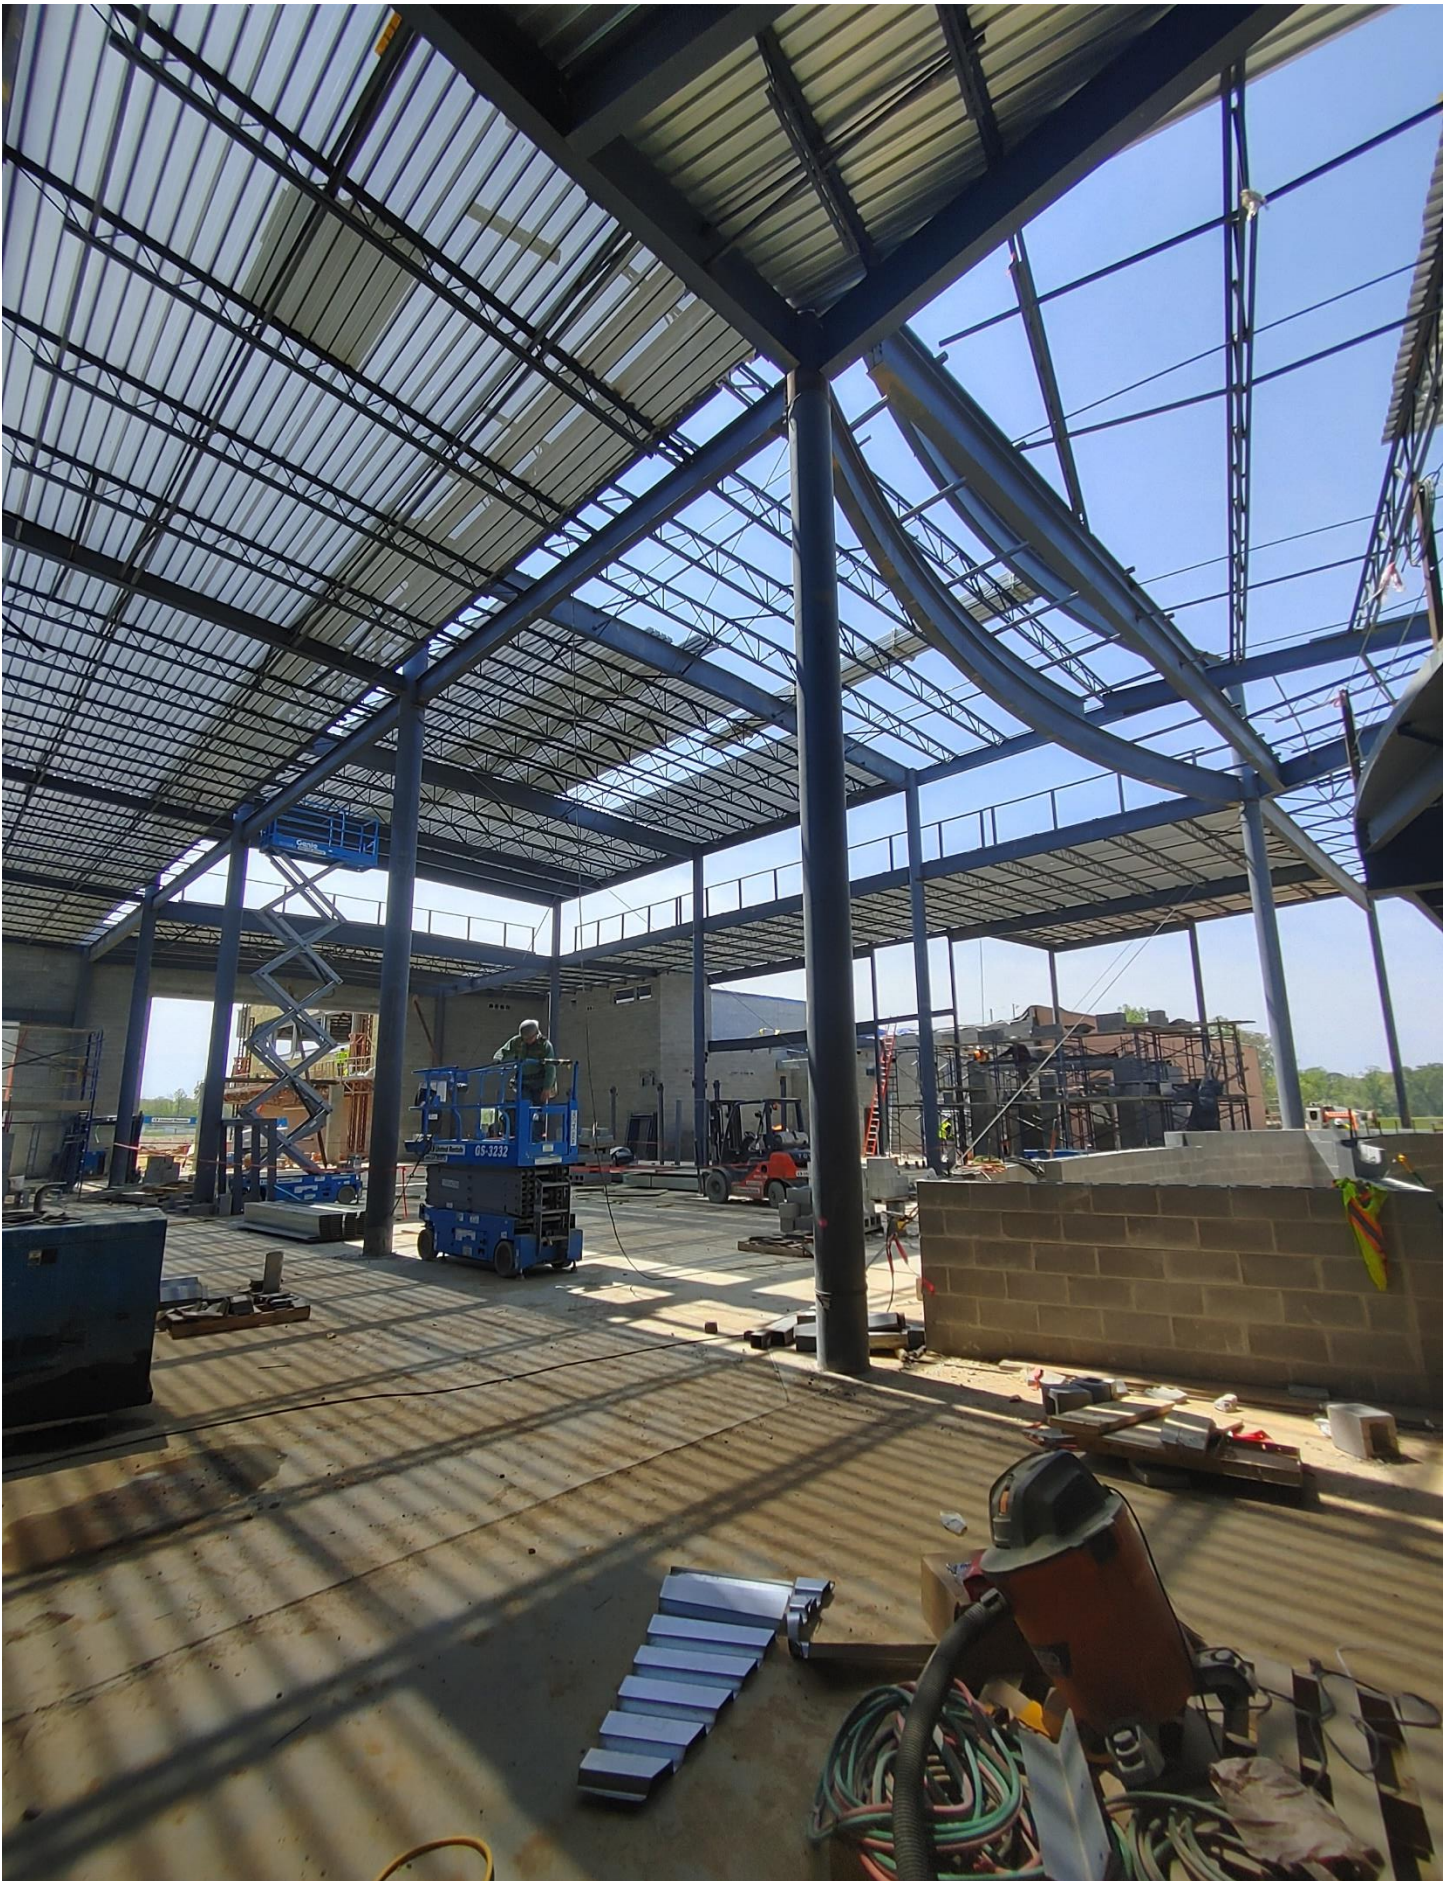


Photo 9 - Metal decking continues to be installed in Area C



Photo 10 - Masons are laying block in Vestibule C10



Photo 11 - Storefront Rough openings are being furred out with plywood for anchoring purposes in Area B.



Photo 12 - Metal Decking is being laid between Areas A & C.
