



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/26/2021
Weather: 46 degrees at 09:00hrs. High of 67 degrees today.
Hours Worked: 09:00hrs – 12:30hrs (3.5hrs) Site Visit.

I walked the site and noted that Loehr Lightening Protection was on site beginning to install the lightening protection on Area E.

Beuchert Excavation: Five (5) men are on site today and they are currently pumping out Retention Pond #1 and they are also grading and reworking the Retention Pond.

Industrial Concrete: Two (2) men are on site today. They continue to work on the metal forms for the Concrete Loading Dock Retaining Wall.

J.D. Long, Masons: Twenty (20) Masons are on site today laying Brick on the East side of Area E and they also continue to lay block in Area C, Vestibule C10. A couple of guys are installing brick flashing on the East side of Area D.

Hazzard Electric: Fifteen (15) men are on site and they continue to work in Area A, & B running conduit and pulling wire. They also continue to work on the Switch Gears in the Electrical Room of Area D.

Colonial Webb: Thirty-Seven (37) men is on site today. They are running waterlines and working on roof top Curbs in Area B. A crew is pressurizing water lines and insulating duct in Area E. They continue to work on running pipe in the Mechanical Room in Area D and they are also insulating pipe in Area A.

Weldon Steel: Six (6) men are on site today. They continue to set and weld roof decking in Area C. One guy continues to install temporary bracing around the high roof of the Cafeteria.

JP Construction: Thirteen (13) men are on site today. They continue to erect interior walls and hanging sheet rock in Area A.

AAR Roofing: Four (4) men are on site today. They are currently working on the roof of Area E.

Tailored Foam: Two (2) men are on site today. The Huddle Board says that they are on site today, but I did not observe them during my visit.

FG & M: No men are on site today.

United Sprinkler: One (1) man is on site today running Sprinkler pipe in Area A.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. A tech was on site this morning.

Questions to or from Branch Builds: When I arrived on site I the Hillis-Carnes Tech, Dean Bunn walking towards his car with Jake, Branch Builds. I walked over and spoke with Dean to see if there were any items of concern that I should be aware of related to the Project. Dean briefed me on what he was inspecting today and a few items that he needs to come back and check on again. At about 09:15hrs Brian Topper and Cooper returned from the local lumber store. Dean, Brian and I then went into the Trailer to review the drawings and outstanding area that Dean needed to either inspect or re-inspect. Brain said he would call him back out when the time came.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test – 04/25/2021

Hillis-Carnes Field Reports (Concrete and Steel) – 04/22/2021

Submittals – #07 95 13-3.1, #28 31 00-3.0

RFIs – #256

Patrick Byrne –

Change Order/PCOs/Pay App – PCO #45:PR #17 Owner VE Revisions, Prime Contract Change Order #008

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –



Photo 1 - Colonial Webb continues to run pipe in the Mechanical Room, Area D.



Photo 2 - J. D. Long are laying Brick on the East side of Area E.



Photo 3 - Weldon Steel continues to install roof decking and temporary railing around the perimeter of the Cafeteria Roof.



Photo 4 - Beuchert continues to work on the West side of the site, Retention Pond #1.

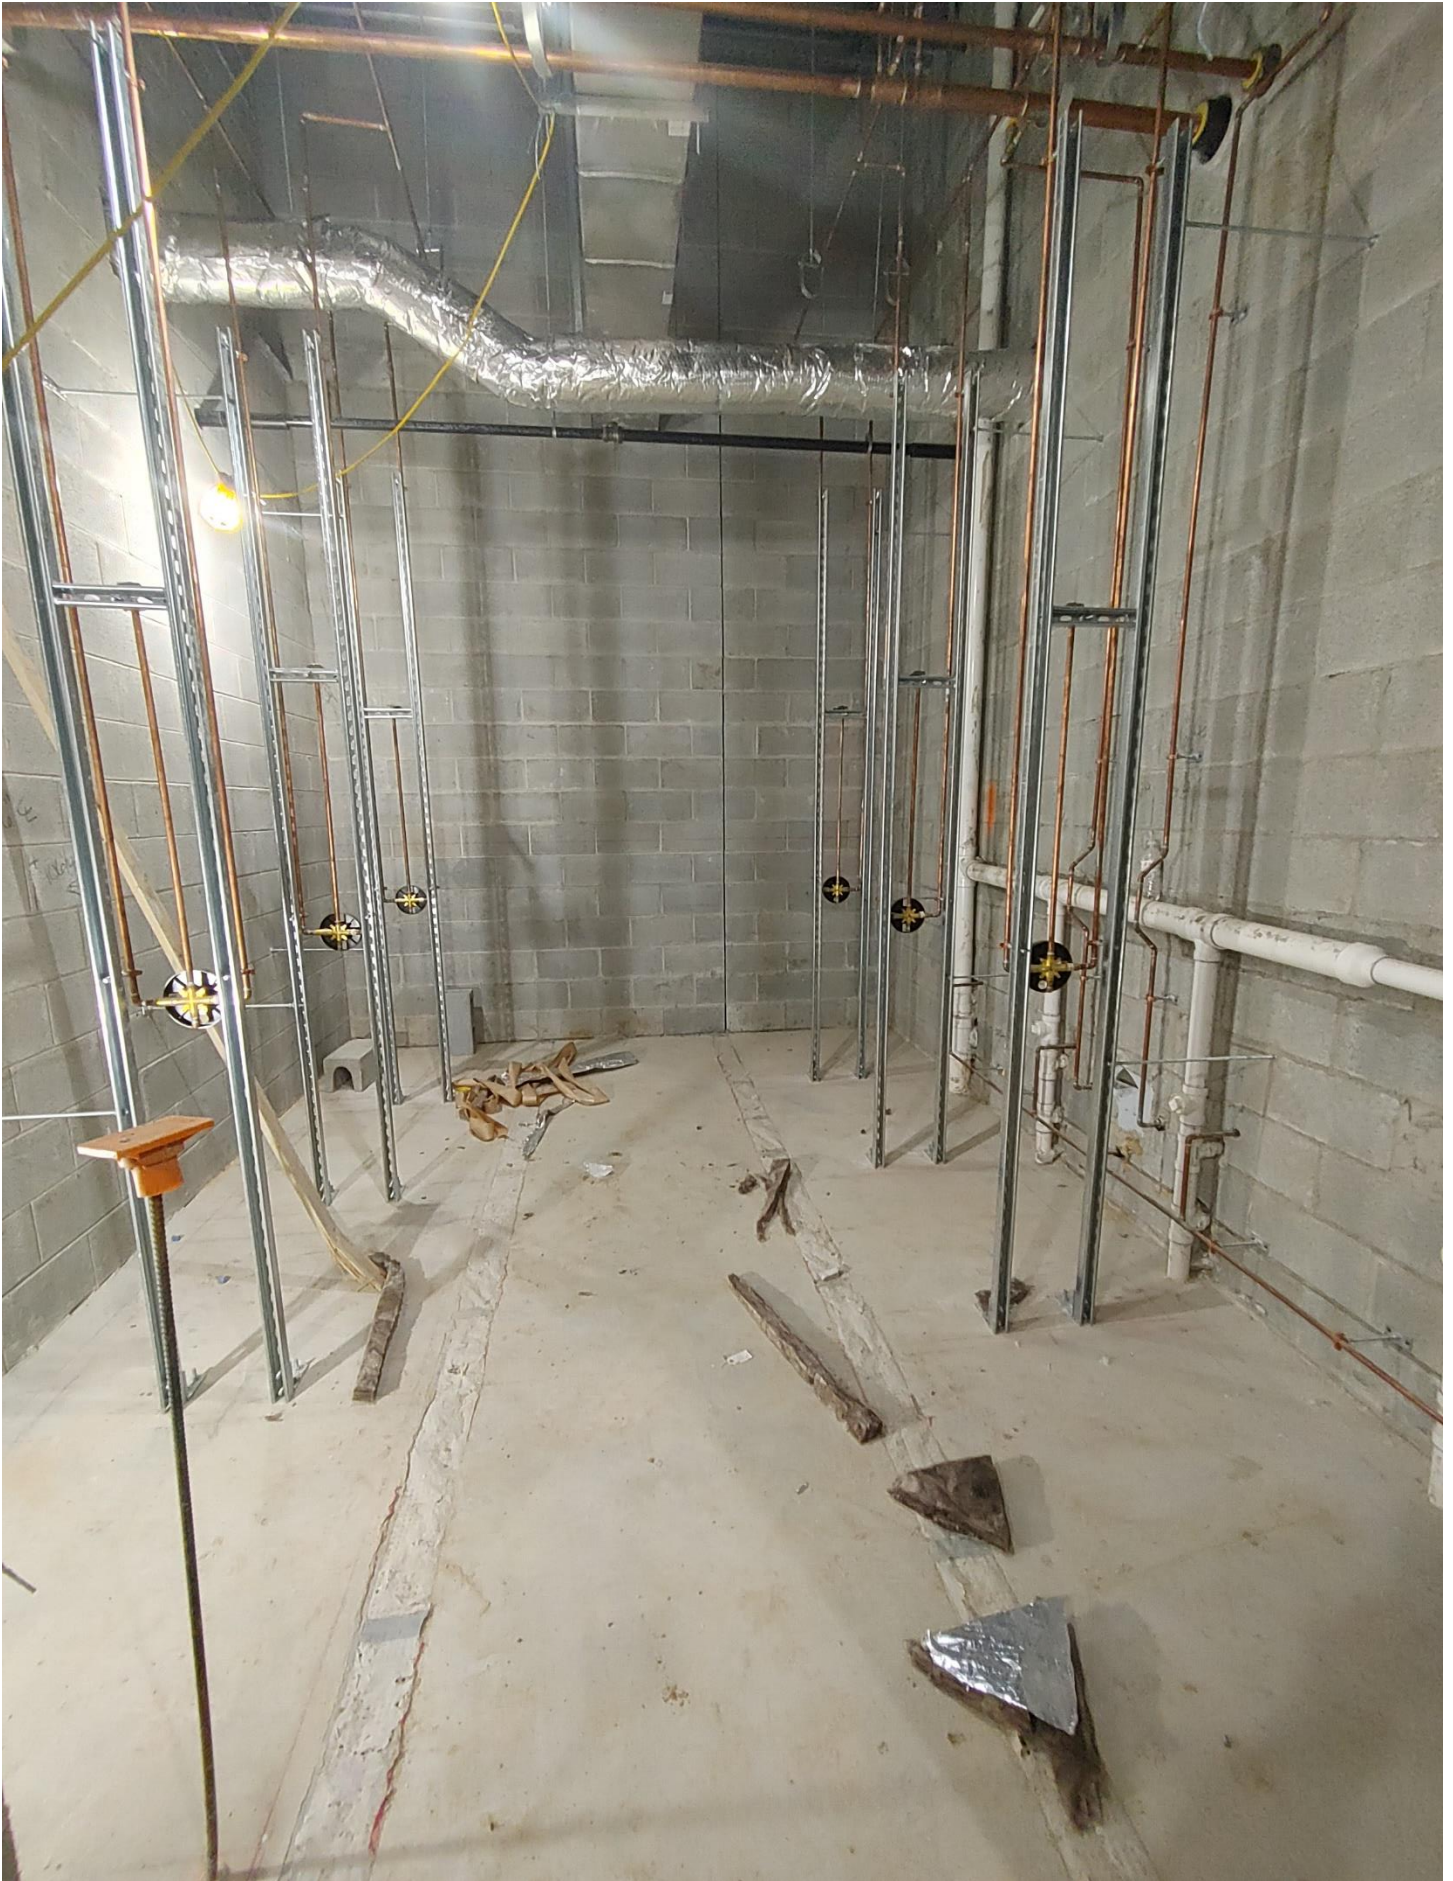


Photo 5 - Plumbing Rough-in in Room E126, Area E.



Photo 6 - J. D. Long laying block in Vestibule c10, Area C.

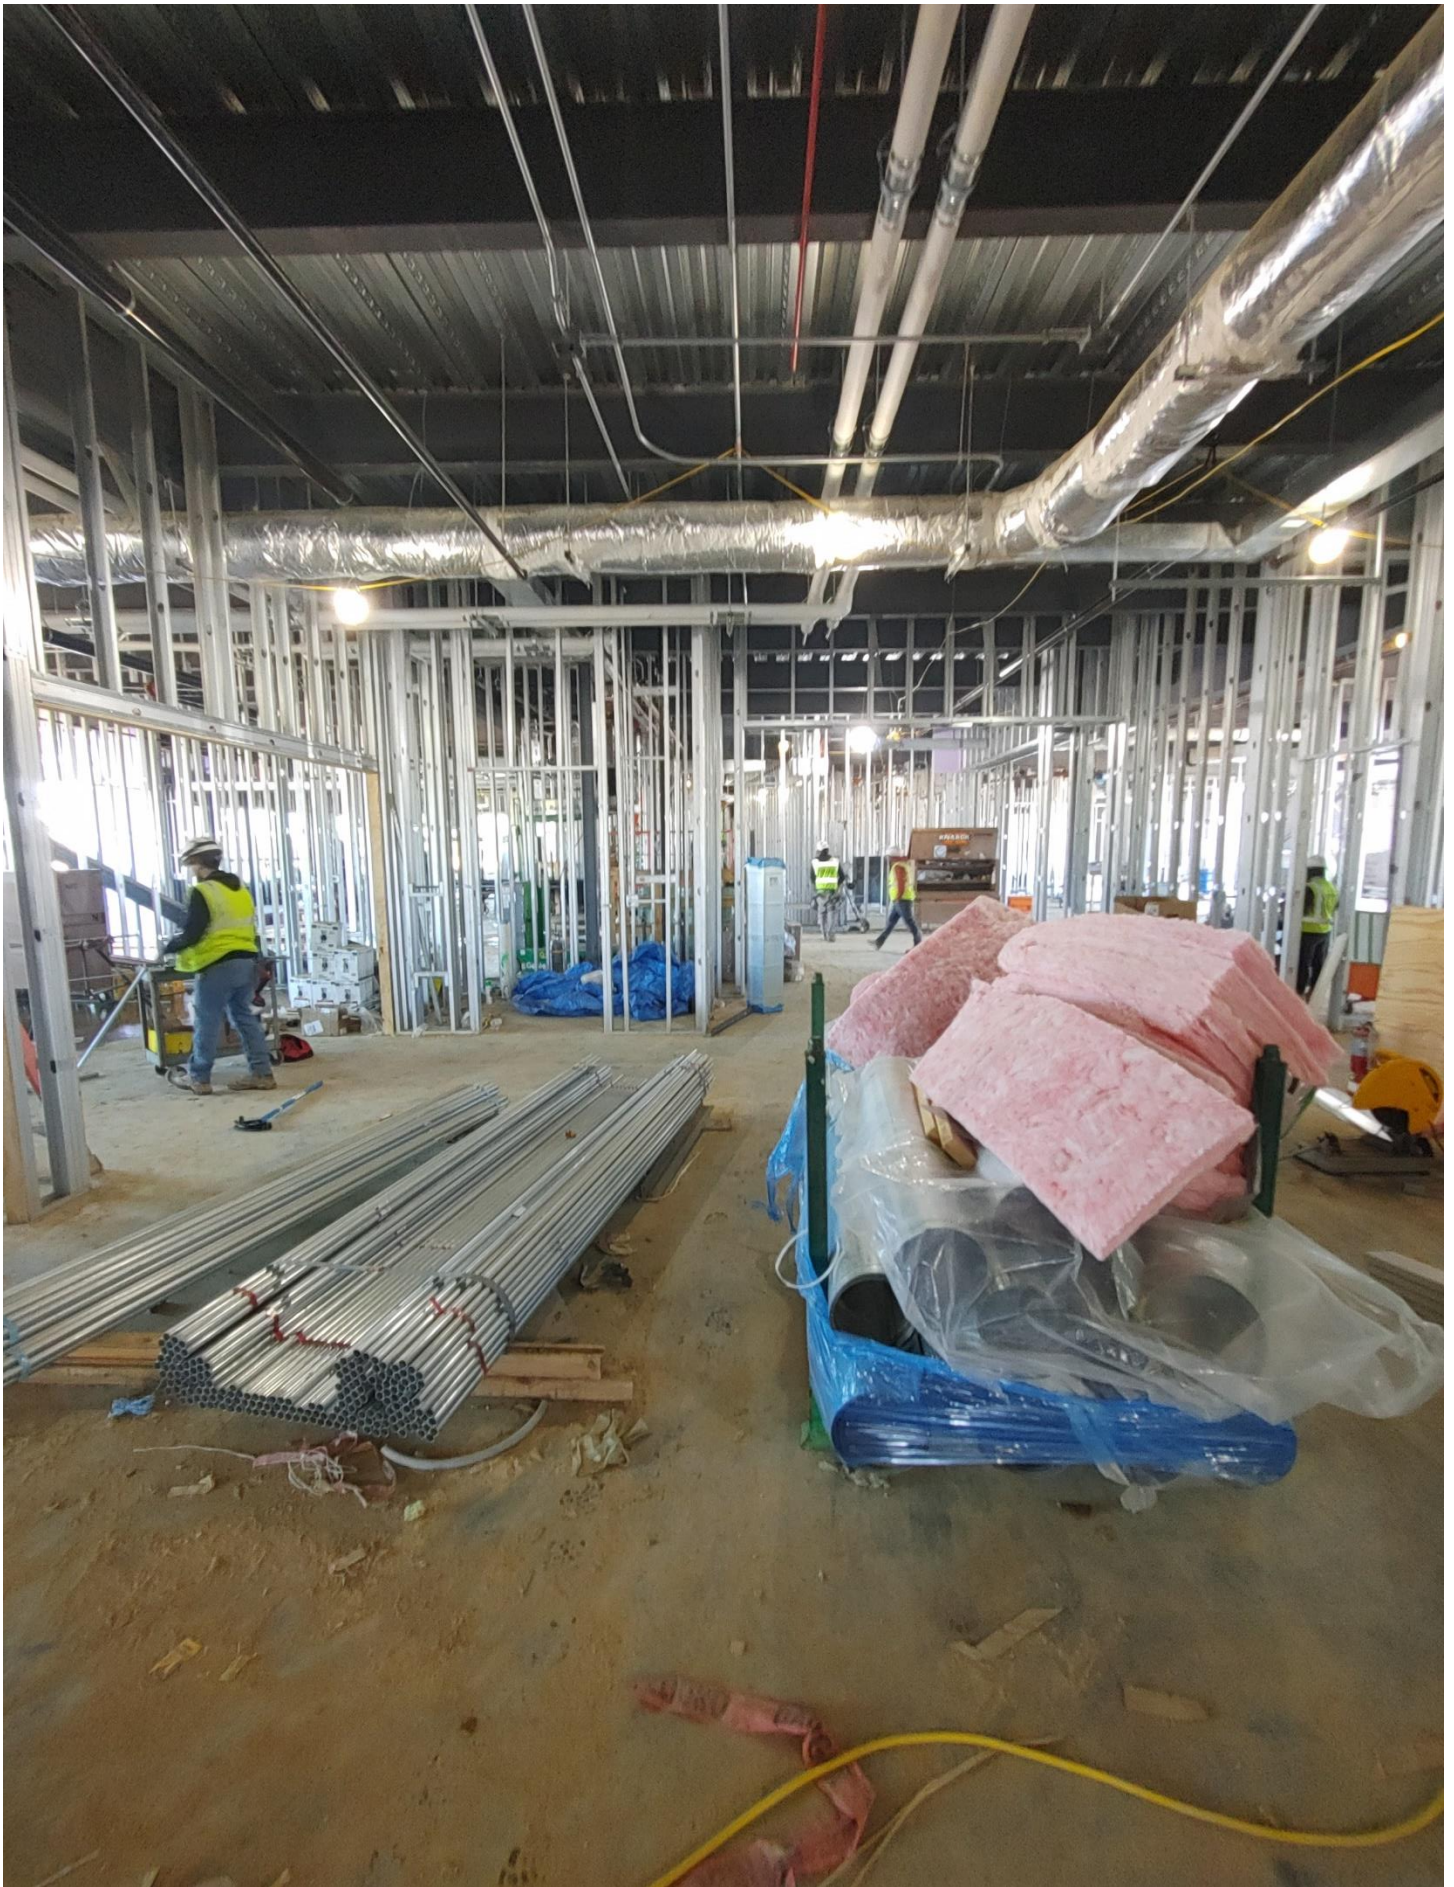


Photo 7 - Framing continues in Area B.



Photo 8 - Weldon Steel installing metal decking , Area A
