



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 04/27/2021  
Weather: 78 degrees at 12:00hrs. High of 86 degrees today.  
Hours Worked: 12:00hrs – 15:00hrs (3hrs) Site Visit.

**Beuchert Excavation:** Five (5) men are on site today and they continue to grade and rework the Retention Pond on the West side of the site..

**Industrial Concrete:** Five (5) men are on site today. They are pouring the Concrete Loading Dock Retaining Wall.

**J.D. Long, Masons:** Sixteen (16) Masons are on site today laying Brick on the North side of Area A and on the Westside of Area E above Store Front SF6. Two men are flashing above the Windows of the Gym on the East side. They are also breaking down Scaffolding in Vestibule #10, Area C.

**Hazzard Electric:** Twelve (12) men are on site and they continue to work in Area A, & B running conduit and pulling wire and also in Electrical Room D158.

**Colonial Webb:** Forty (40) men is on site today. They are running waterlines, working on roof top Curbs and pressurizing water lines and insulating duct in Area B. They continue to work on running pipe in the Mechanical Room in Area D and they are also insulating pipe in Area E.

**Weldon Steel:** Six (6) men are on site today. They continue to set and weld roof decking in Area C.

**JP Construction:** Thirteen (13) men are on site today. They continue to erect interior walls and install wood blocking in Area A. Two guys are framing (Z-Track) the west exterior wall of Stairwell #2.

**AAR Roofing:** Four (4) men are on site today. They are currently working on the low roof of Area D.

**Tailored Foam:** Two (2) men are on site today. They are spraying the East high wall of the Gym Hallway.

**FG & M:** No men are on site today.

**United Sprinkler:** One (1) man is on site today running Sprinkler pipe in Area A.

**S&S Concrete Cutting Company:** I did not observe anyone on site during my visit today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** A tech was on site this morning for the concrete pour.

**Questions to or from Branch Builds:** I met with Brian today and discussed the project. Brian advised that he is expecting a delivery of door hardware later today. We spoke about the concrete pour and where the Roofers are working today. Brian said he is going to invite Dr. Perry, Norm and others to the site in the near future for a tour.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test – 04/26/2021**

**Hillis-Carnes Field Reports (Concrete and Steel) – 04/23/2021, 04/26/2021, Structural Steel 04/26/2021**

**Submittals –**

**RFIs –**

**Patrick Byrne –**

**Change Order/PCOs/Pay App –**

**Changes in Procore – 2021 04-14 WLHS Meeting Minutes #32**

**Weekly Submittal Status Report –**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**



Photo 1 - Preparing to pour the Concrete for the Loading Dock Wall



Photo 2 - Loading Dock wall being poured



Photo 3 - Rebar cage in corner of Loading Dock Wall



Photo 4 - Verification of Rebar in Loading Dock Wall



Photo 5 - Brick being laid on the North side of Area A. Flashing is installed and Precast being laid.



Photo 6 - Brick being laid on the Northside of Area A. Fraco Scaffolding being erected.





Photo 7 - Stairwell #2 being framed for panels.



Photo 8 - Lintel and Precast set above Storefront SF6



Photo 9 - Beuchert continues to work on the West side of the site.



Photo 10 - Area E high wall on the North side being foamed.



Photo 11 - Metal Decking continues to be laid in Area C

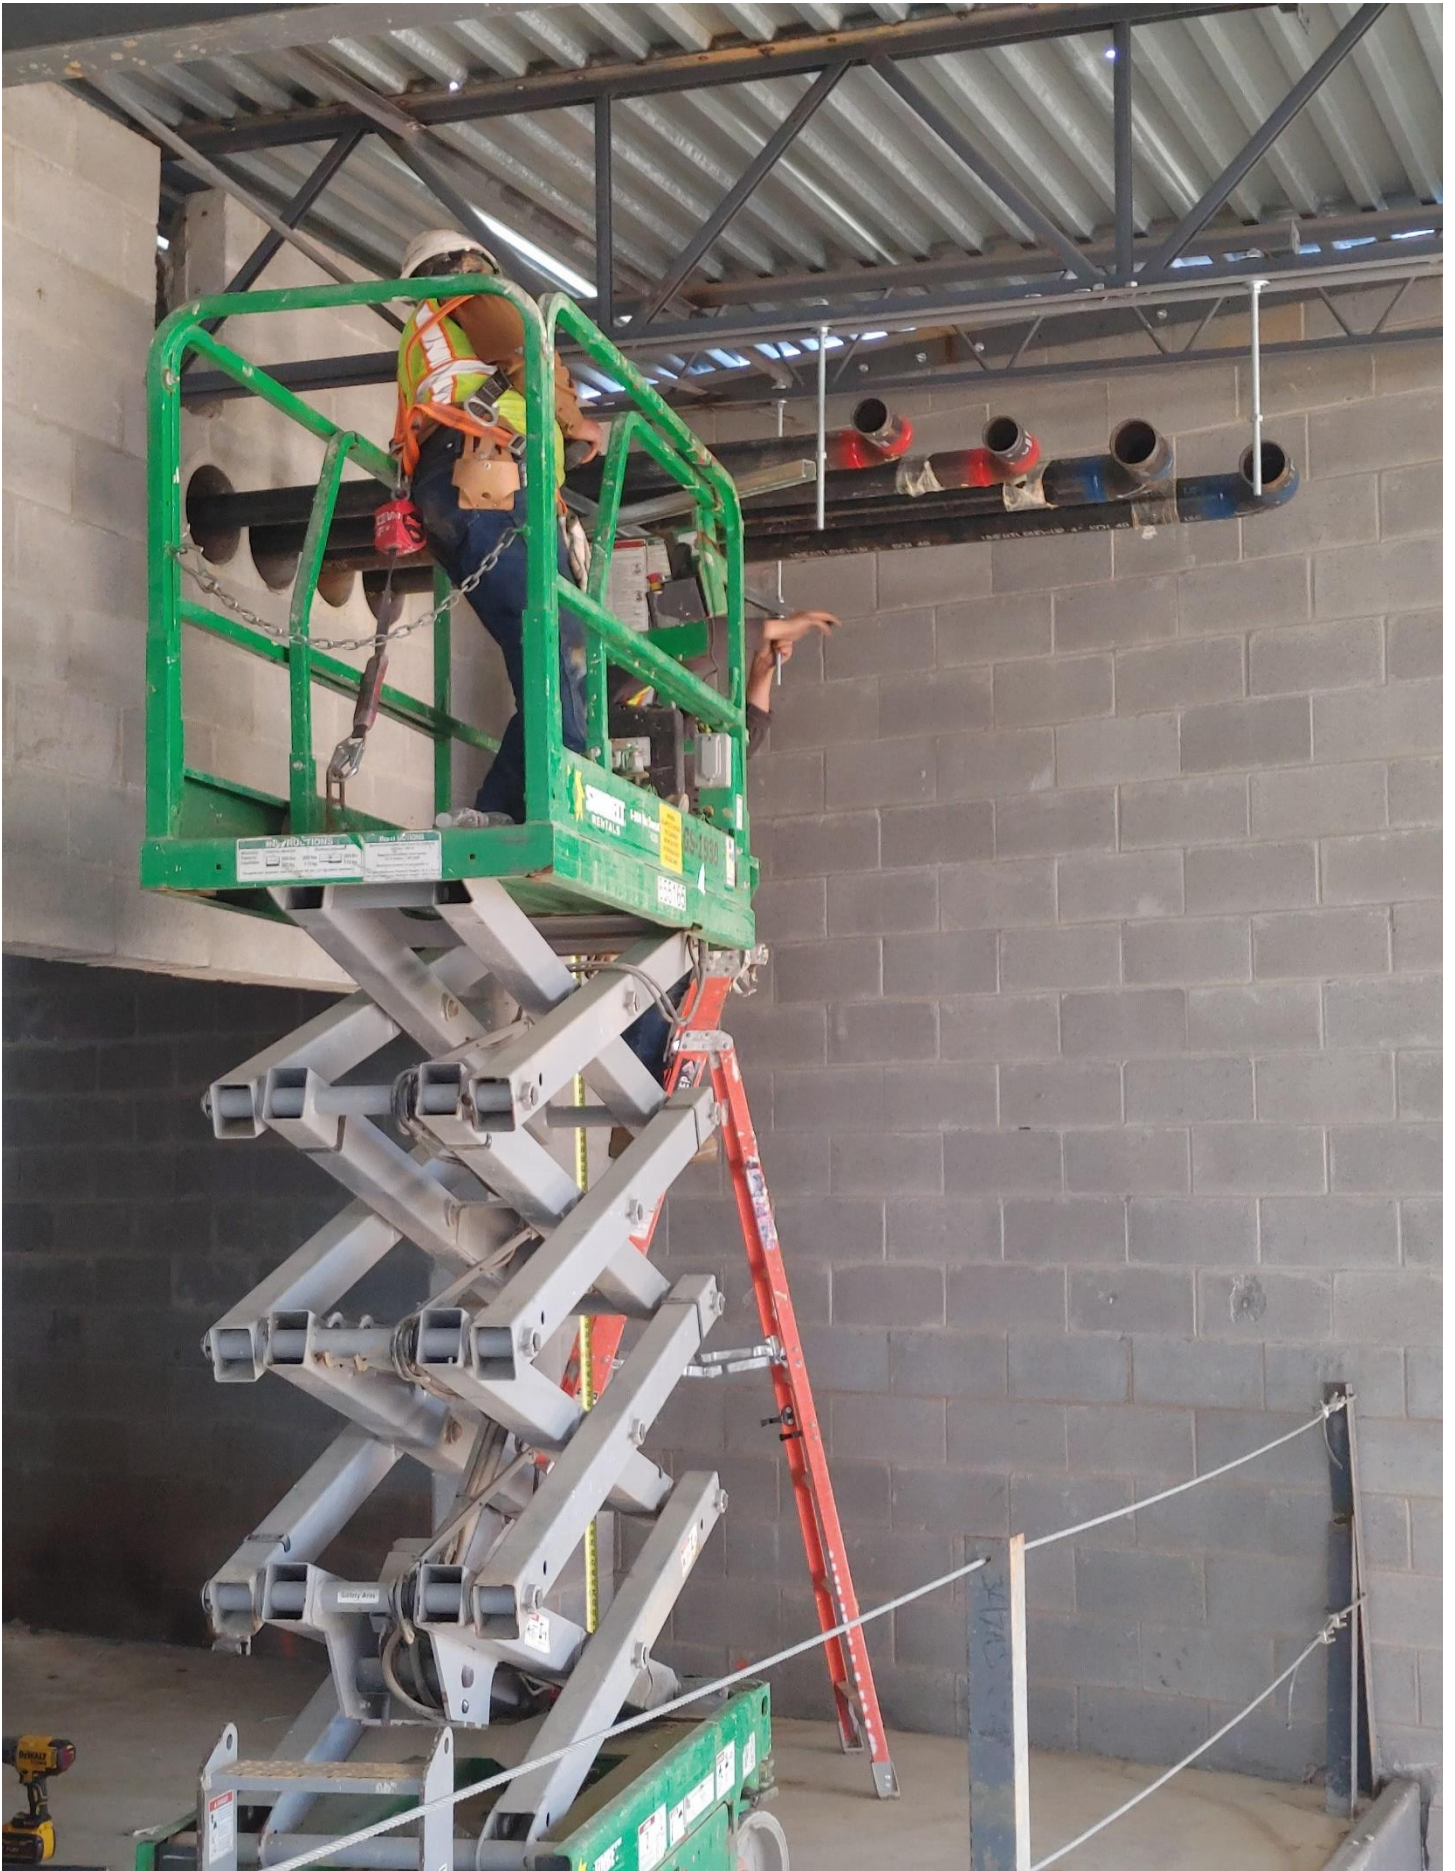


Photo 12 - Colonial running pipe in Area A outside of A229
