



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/28/2021
Weather: 82 degrees. High of 89 degrees today.
Hours Worked: 10:00hrs – 13:30hrs (3.5hrs) Site Visit.

Attended the 10:00hrs Flooring/Paint/Casework: Pre-Installation Conference in Branch Builds' Trailer.

Beuchert Excavation: Four (4) men are on site today and they continue to grade and rework the West side of the site.

Industrial Concrete: No men are on site today.

J.D. Long, Masons: Sixteen (16) Masons are on site today laying Brick on the West side of Area E. They have laid brick on the North side of Area E high roof wall since yesterday. One man continues to install Brick Flashing on the East side of Area D. They have finished installing Plastic over the glass and frames on the Northside of Area A to protect it from mortar and damage.

Hazzard Electric: Twelve (12) men are on site and they continue to work in Area A, & B running conduit and pulling wire and also in Electrical Room D158.

Colonial Webb: Forty-seven (47) men are on site today. They are running copper waterlines, working on roof top Curbs and pressurizing water lines and insulating duct all over the site. Work continues in the Mechanical Room of Area D and they are also insulating pipe in Area E.

Weldon Steel: Six (6) men are on site today. They continue to set and weld roof decking in Area C. They have only a few pieces on decking that remain to be set.

JP Construction: Fifteen (15) men are on site today. They continue to hang sheetrock and have also begun to tape sheetrock in Area A. Two guys continue to frame (Z-Track) the exterior wall of Stairwell #2. They are also framing walls in Area A.

AAR Roofing: Four (4) men are on site today. They are currently working on the low roof on the North side of Area D.

Tailored Foam: Two (2) men are on site today. They are spraying foam on the South side of Area D this morning.

FG & M: No men are on site today.

United Sprinkler: No one is on site today.

CTSI: Four (4) men are on site today running and pulling low voltage (Comm) cabling.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. A tech was on site this morning for the concrete pour.

Questions to or from Branch Builds: I met with Todd this afternoon to discuss COR#46. After discussion, and in light of the fact that the County has depleted all of the initial COVID Funds received from the Federal Government, Todd agreed to hold this PCO until a time that the County receives additional COVID Funds.

I received a phone call today from the Contractor installing the 12" Water line. He wants to meet tomorrow to discuss the location of the Backflow Device & Mater Vault. So I coordinated a meeting with Brian Topper for 10:00AM tomorrow.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –



Photo 1- Roof Decking almost completed in Area C

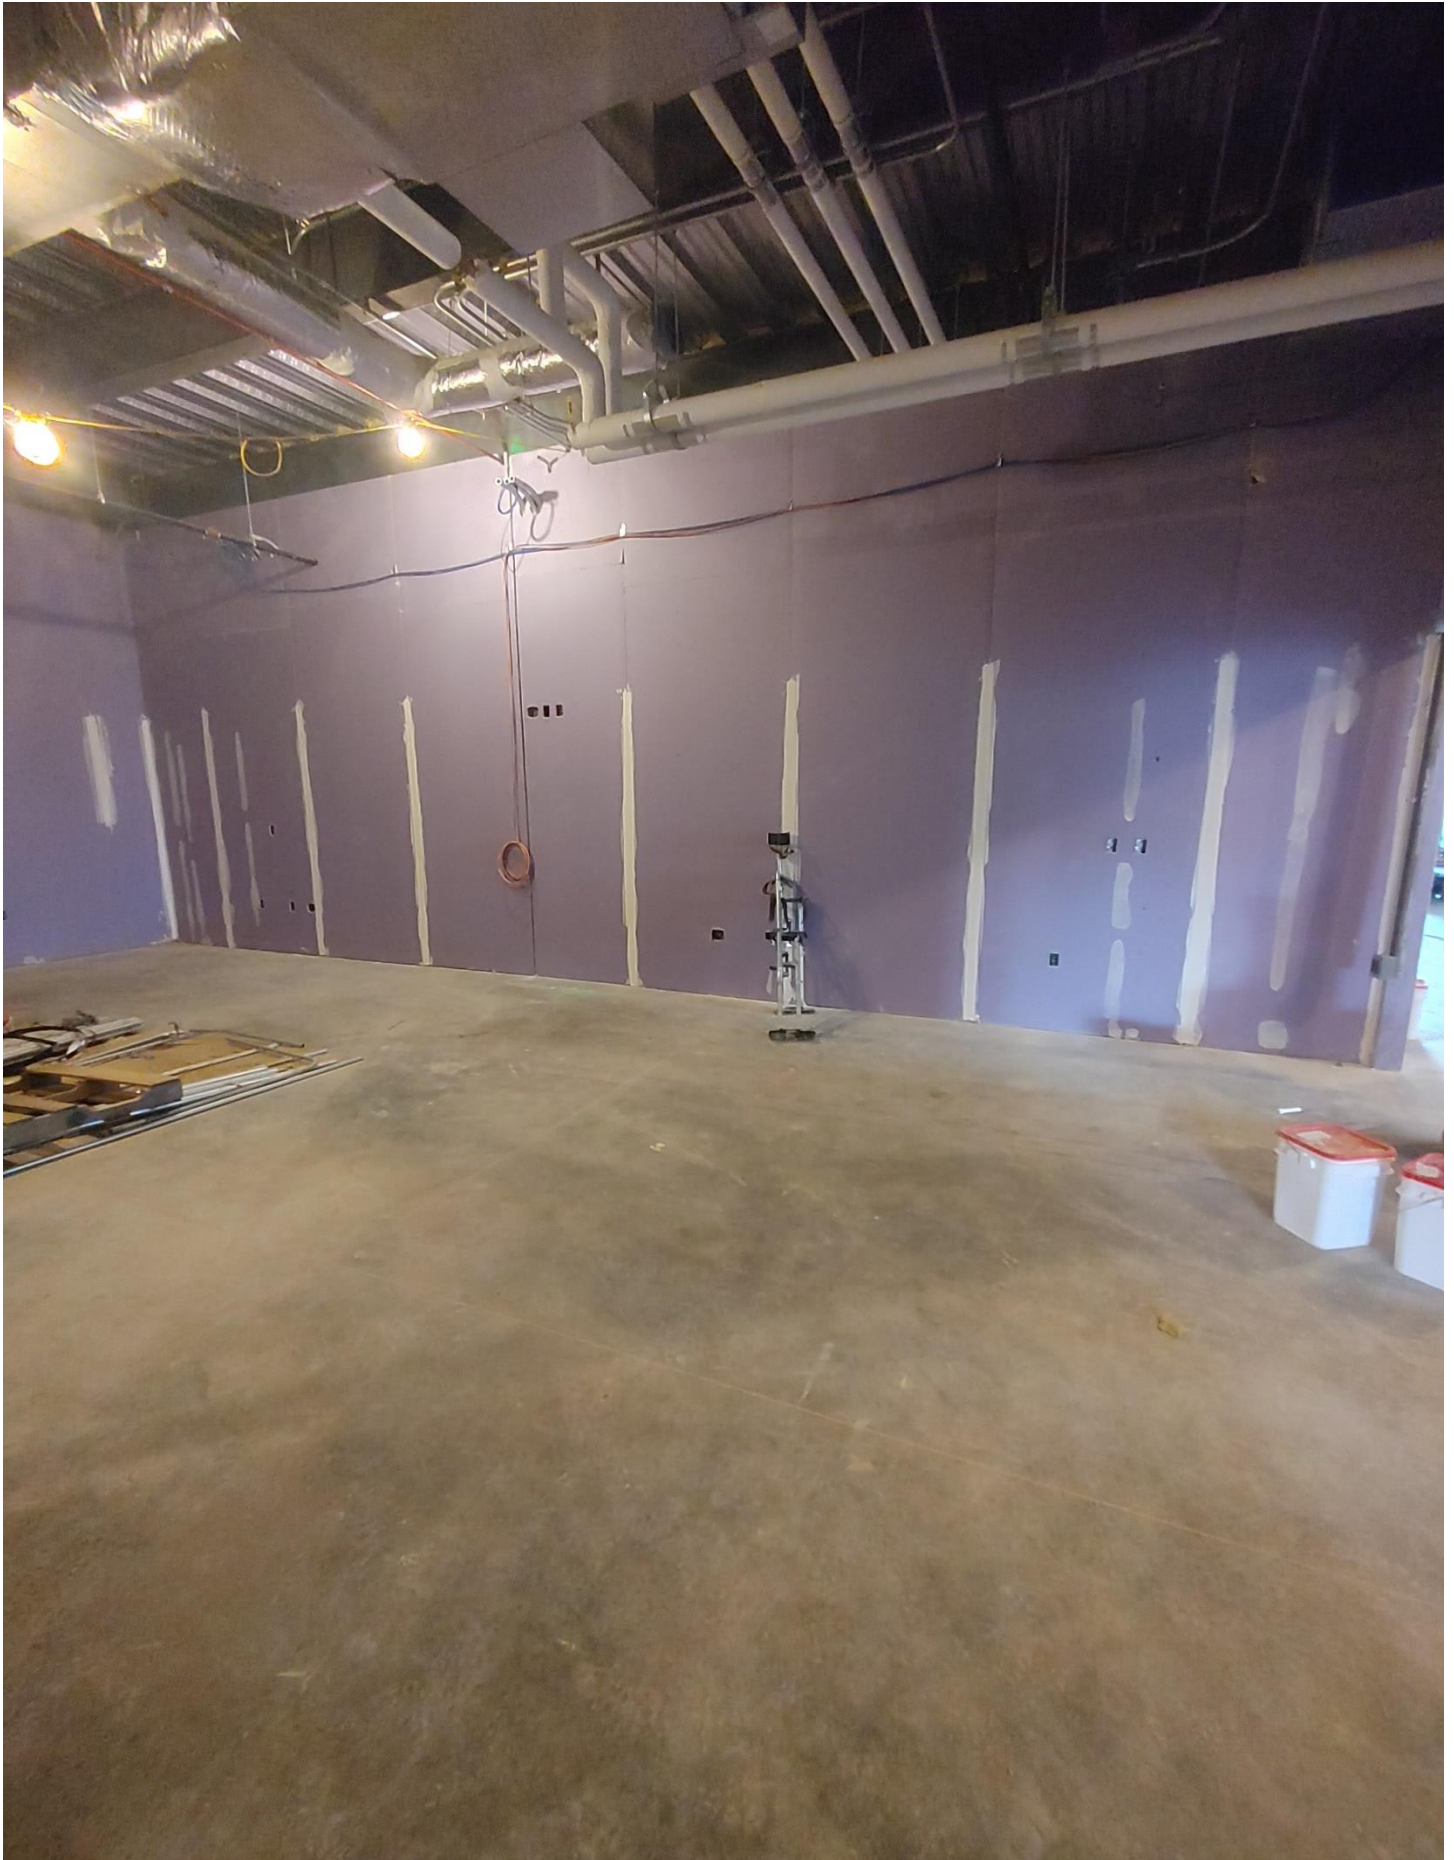


Photo 2 - They have begun to Tape the Sheetrock in Area A



Photo 3 - Loading Dock Wall has waterproof Membrane installed.



Photo 4 - Colonial Webb continues to run pipe in Area A



Photo 5 - J.D. Long has begun to lay Brick above the low roof in Area E



Photo 6 - Z-Channel Framing continues on Stairwell #2



Photo 7 - Colonial Webb continues to run pipe in the Mechanical Room of Area D

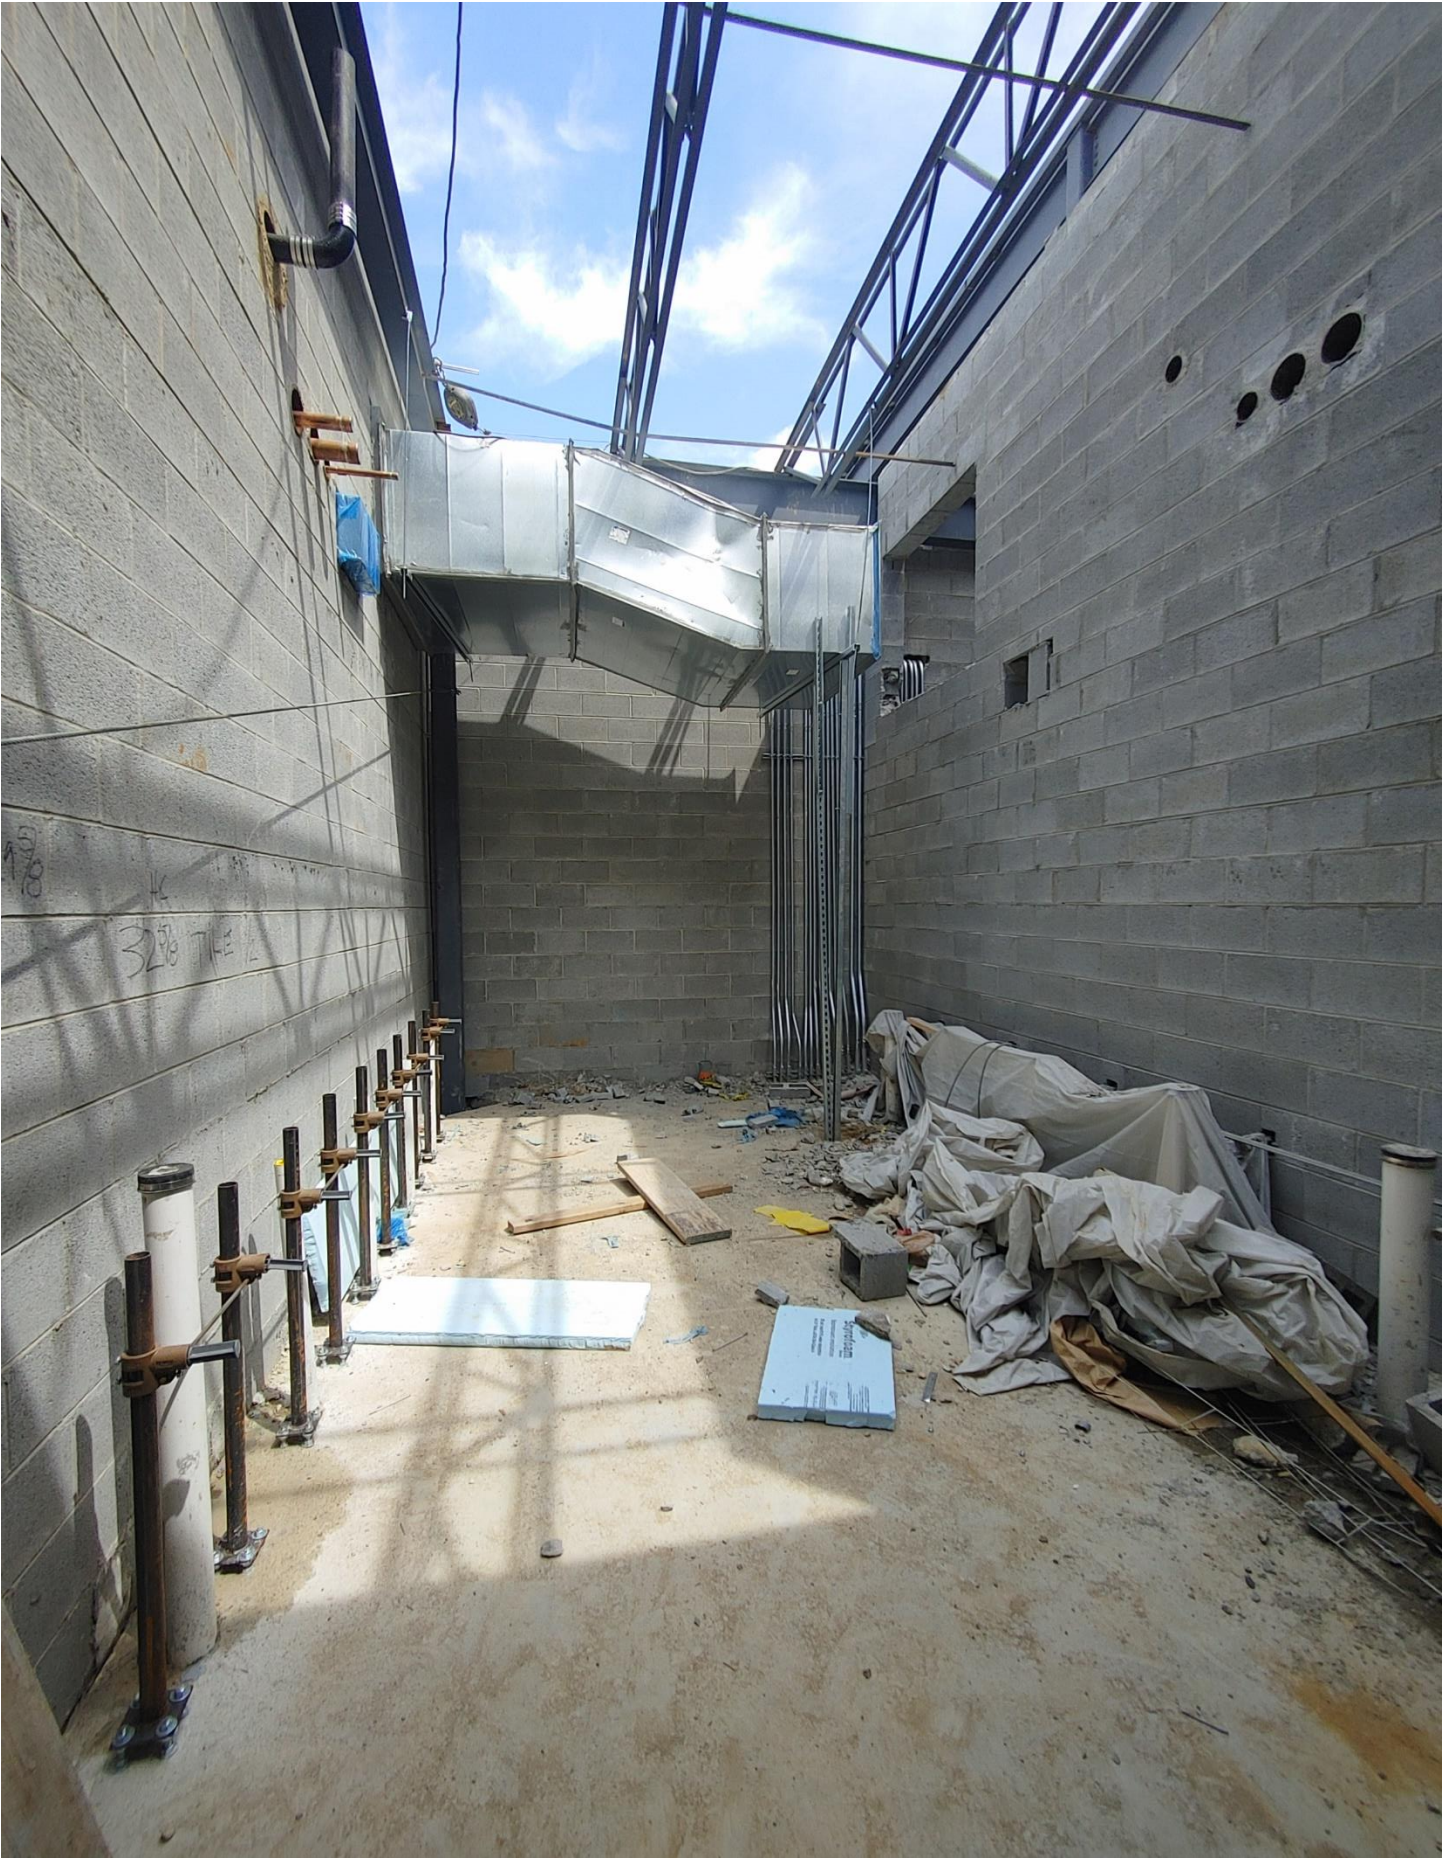


Photo 8 - HVAC Duct is being run in the Girls Toilet E104.



Photo 9 - Masons finishing up Brick work on the East side of Area E.



Photo 10 - Masons are preparing to lay Brick on the West side of Area E.



Photo 11 - Brick being prepped for flashing on the South side of Area D.



Photo 12 - Spray Foam is being applied to the South side of Area D.
