



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/28/2021

Weather: 71 degrees. High of 82 degrees today. A brief shower came through the area at approximately 10:30hrs and lasted about an hour. Rain is called for on and off today.

Hours Worked: 11:00hrs – 13:00hrs (2hrs) Site Visit.

Beuchert Excavation: Four (4) men are on site today and they continue to grade and rework the West side of the site.

Industrial Concrete: No men are on site today.

J.D. Long, Masons: Sixteen (16) Masons are on site today. They are setting up Fraco Scaffolding on the East side of Area A and cleaning brick on the North and East side of Area E. One guy is flashing the brick on the South side of Area D.

Hazzard Electric: Eleven (11) men are on site and they continue to work in Area A, & B running conduit and pulling wire.

Colonial Webb: Thirty-nine (39) men are on site today. They are running copper waterlines, working on roof top Curbs and pressurizing water lines and insulating duct all over the site. Work continues in the Mechanical Room of Area D and they are continue to insulate pipe in Area E.

Weldon Steel: Six (6) men are on site today. They continue to set and weld steel in Area C.

JP Construction: Nineteen (19) men are on site today. They continue to hang sheetrock and are applying the Block Coat of mud to the Vertical Joints of sheetrock in Arwa A. They are also working in Area A framing

AAR Roofing: No men are on site today.

Tailored Foam: According to Branch there are two men are on site today. However, I did not see them during my visit.

FG & M: No men are on site today.

United Sprinkler: One (1) man is on site today running Sprinkler pipe in Area A.

CTSI: Four (4) men are on site today running and pulling low voltage (Comm) cabling.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. A tech was on site this morning for the concrete pour.

Questions to or from Branch Builds: Earlier this morning around 09:00hrs I spoke with Brian about the trash and debris that had blown off of the site onto County Park Road and the adjacent area of the Recreation Park. There were strong winds last week on Friday and it caused a lot of stuff that wasn't tied down to blow off site. Brian sent Cooper and Jake over and together we picked up two pickup truck loads of trash.

While picking up trash I noted three trucks either entering or exiting the High School site via County Park Road. I spoke with Brian about this because we do not have a construction entrance established at that location and mud and dirt could be tracked onto the road. Then we would have to deal with further DEQ violations. Brian had Beuchert pile up some dirt at the entrance to prevent future traffic from entering or exiting the site.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. ***A DEQ Warning Letter was issued on April 30th, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations.***

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test – 04/29/2021

Hillis-Carnes Field Reports (Concrete and Steel) – 04/28/2021

Submittals – #07 62 00-3.0, #33 40 00-5.0

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report – 04/30/2021

Weekly RFI Status Update – 04/30/2021

Weekly Daily Log Summary – 04/30/2021



Photo 1 - Beuchert continues to move dirt on the West side of the site.



Photo 2 - Retention Pond #1 being reworked.



Photo 3 - Weldon Steel working of Stair #3

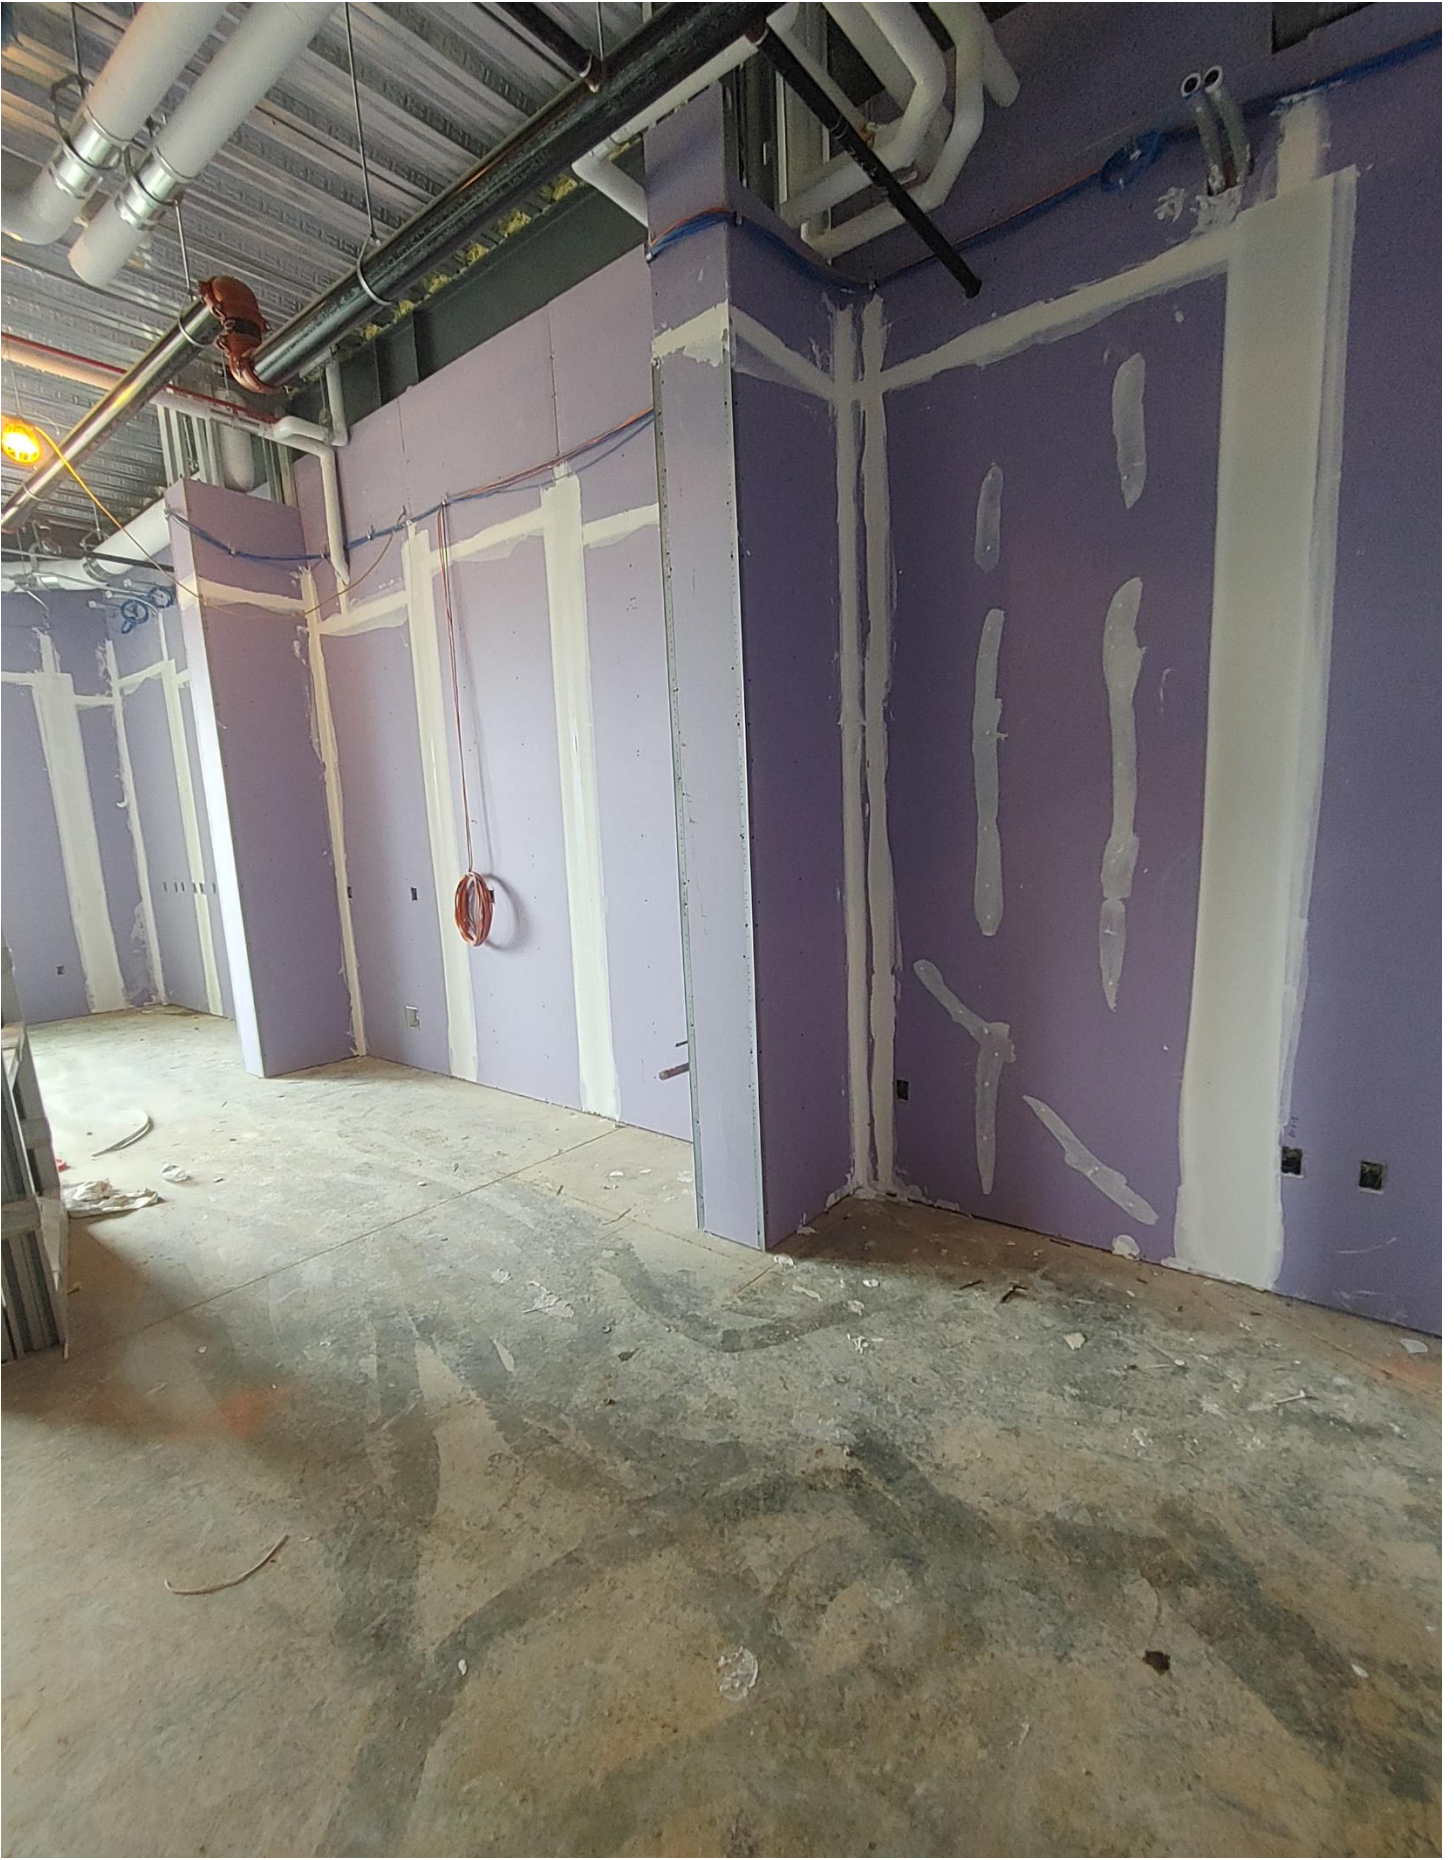


Photo 4 - Block Coat of mud being applied to Vertical Joints in Area A



Photo 5 - Walls being insulated in Area A

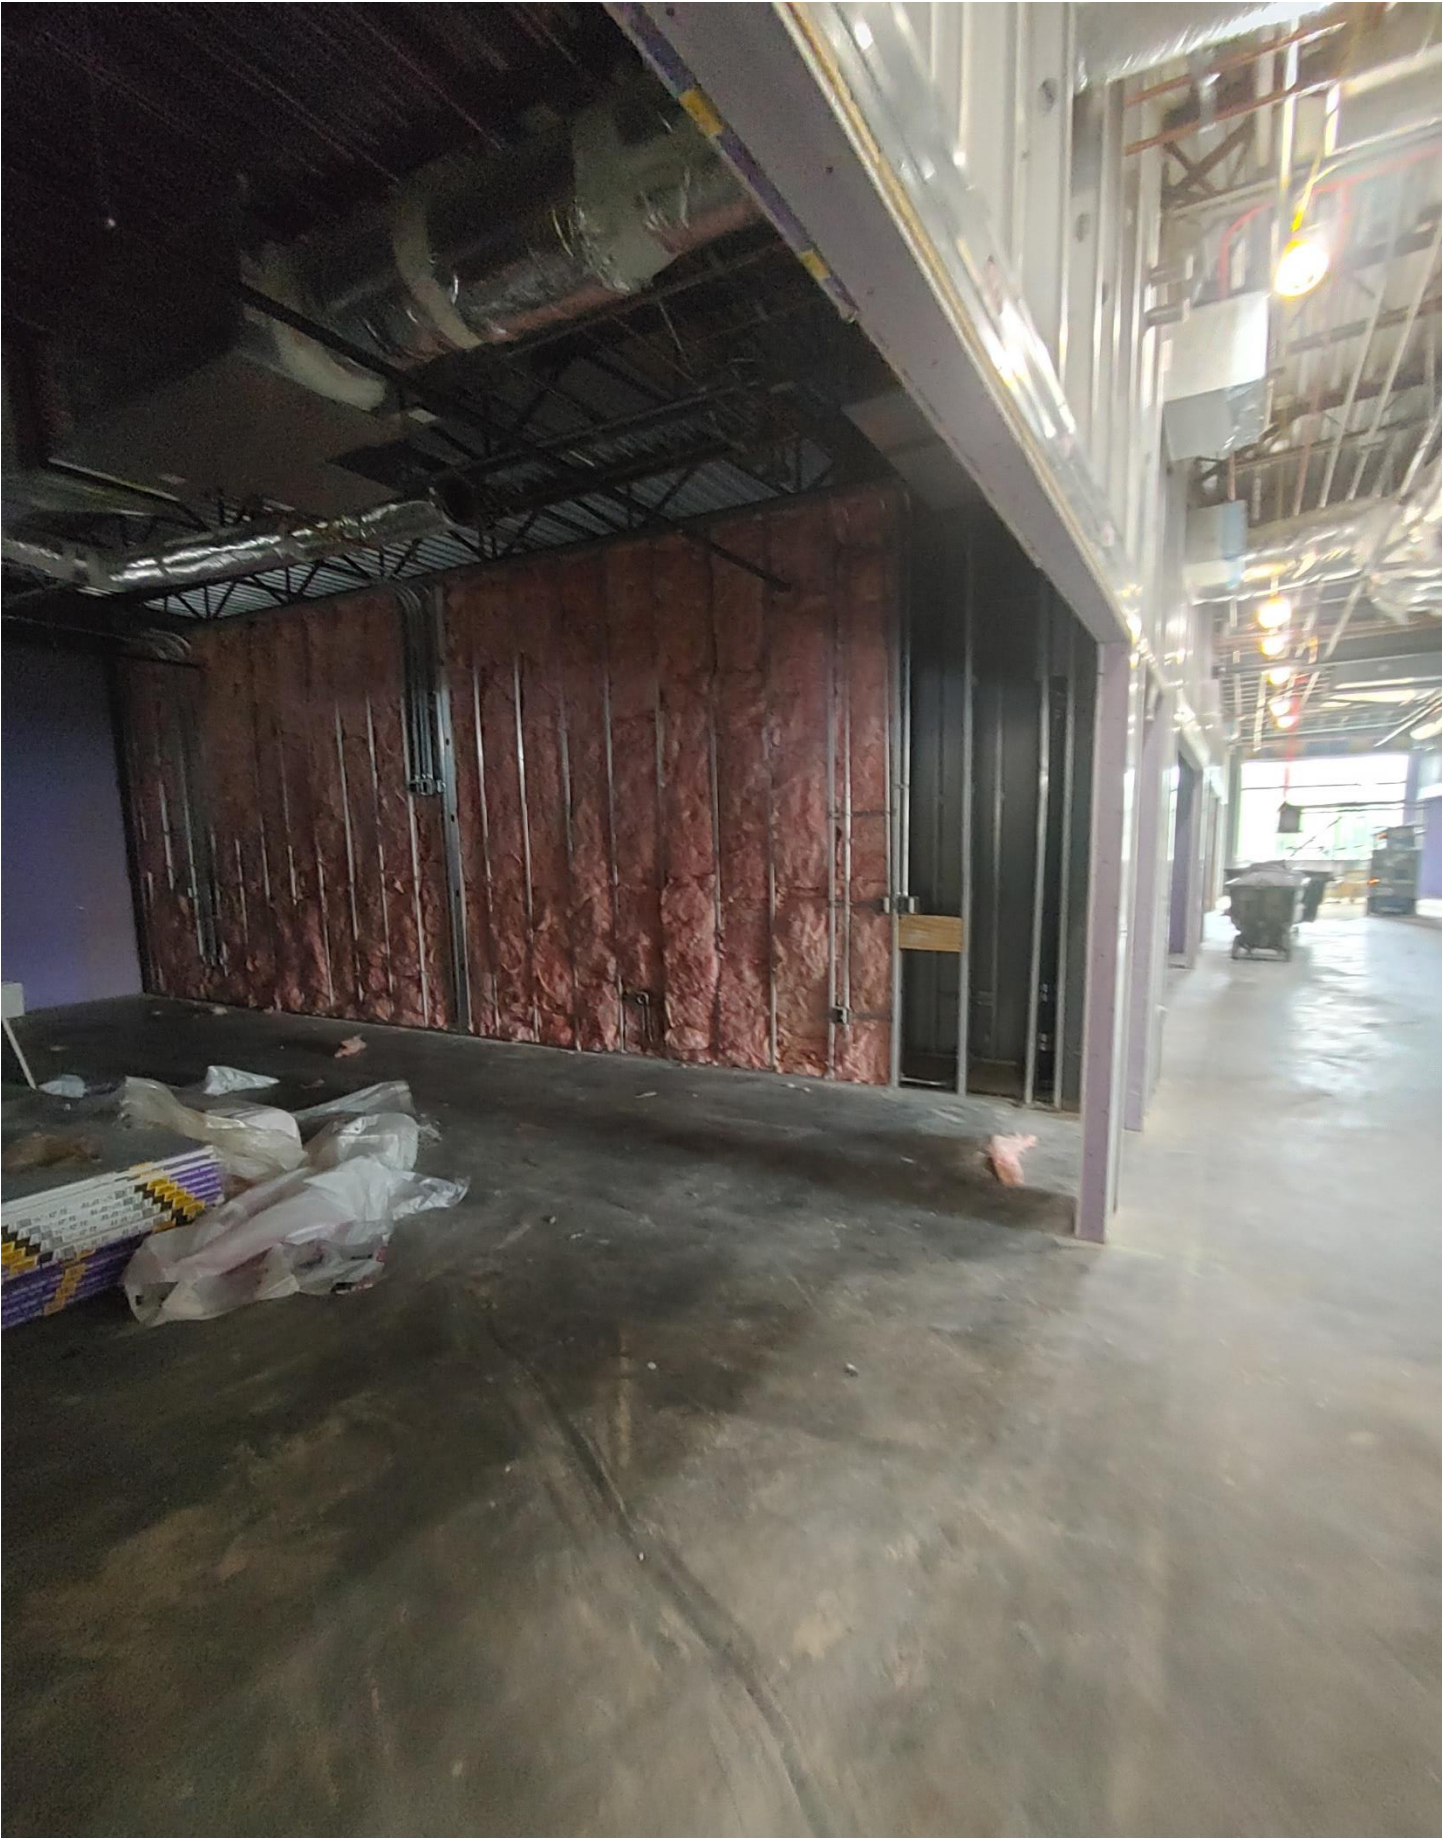


Photo 6 - Area A walls being insulated



Photo 7 - HVAC equipment curbs being constructed above Area A.
