



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 05/06/2021  
Weather: 71 degrees. High of 66 degrees today.  
Hours Worked: 10:30hrs – 12:30hrs (2hrs) Site Visit.

My last report was on May 3, 2021. Branch Builds is currently having a planning meeting with all of the Sub Contractors in the trailer. I am unable to review their Huddle Board to annotate the number of men with each Sub-contractor is on site today.

**Beuchert Excavation:** They are on site today and they continue to grade and rework the West side of the site.

**Industrial Concrete:** I did not notice any men are on site today.

**J.D. Long, Masons:** The Masons now have Fraco Scaffolding set up on the North side of Area A and on the South and East side of Area D. They are currently laying brick on the West side of Area E and two guys are flashing the Display Nook on the West side of Area D.

**Hazzard Electric:** They continue to work in Area A, & B running conduit and pulling wire.

**Colonial Webb:** They are running copper waterlines in Area A; working on roof top Curbs in Areas B & E; pressurizing water lines in Area D; running Duct in Area A; connecting roof top drains in Area D; and setting roof drains in Area c. Work continues in the Mechanical Room of Area D.

**Weldon Steel:** Six (6) men are on site today. They continue to set and weld steel in Area C.

**JP Construction:** They continue to hang sheetrock and are applying the Block Coat of mud to the Vertical Joints of sheetrock in Area A. They are also continue to frame walls in Area A.

**AAR Roofing:** I did not observe anyone on site today.

**Tailored Foam:** I observed two men are on site today. They are spraying foam on the South side of Area A.

**FG & M:** I did not observe anyone on site during my visit.

**United Sprinkler:** One (1) man is on site today and he is attending the Sub-Contractor Planning Meeting.

**CTSI:** I did not observe them on site during my visit.

**S&S Concrete Cutting Company:** I did not observe anyone on site during my visit today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** I did not observe anyone on site during my visit.

**Questions to or from Branch Builds:** I stopped in the Trailer during my visit and Branch is having its weekly Sub-Contractor Planning Meeting. I confirmed with Todd that the Owner's Tour is still scheduled for tomorrow at 10:00hrs. Todd said he has twenty-two people scheduled for the tour.

Earlier this week I received a call from Charlie Shaver who is working with the High School to set up their Radio System in the new High School. Charlie said he wanted to visit the site tomorrow at 10:00hrs with Chris Bankert of Communication Specialists to explore a pathway to run their Radio communication cable. I spoke to Brian yesterday about this meeting and he did not have a problem with them visiting the site.

I received an email from Resource International This morning advising that they would be on site tomorrow to evaluate the tie-in location for the 12" Water Line and a location for the meter vault and Back-flow device.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. A DEQ Warning Letter was issued on April 30<sup>th</sup>, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs –**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**



Photo 1 – Spray foam being applied to the South Side of Area A



Photo 2 - Spray foam being applied to the East side of Area C



Photo 3 - Circulating Pumps set in Area D



Photo 4 - Expansion Tanks Set in Area D



Photo 5 - Switch Gears in the Electrical Room of Area D



Photo 6 - Steel being welded in Area C





Photo 7 - Pipe is being connected to Roof Drains in Area D Auditorium



Photo 8 - Fraco Scaffolding has been erected on the East and South side of Areas D and on the East Side of Area A



Photo 9 - Masons are laying Brick on the West side of Area E



Photo 10 - Display Nook on the West side of Area E is being flashed.

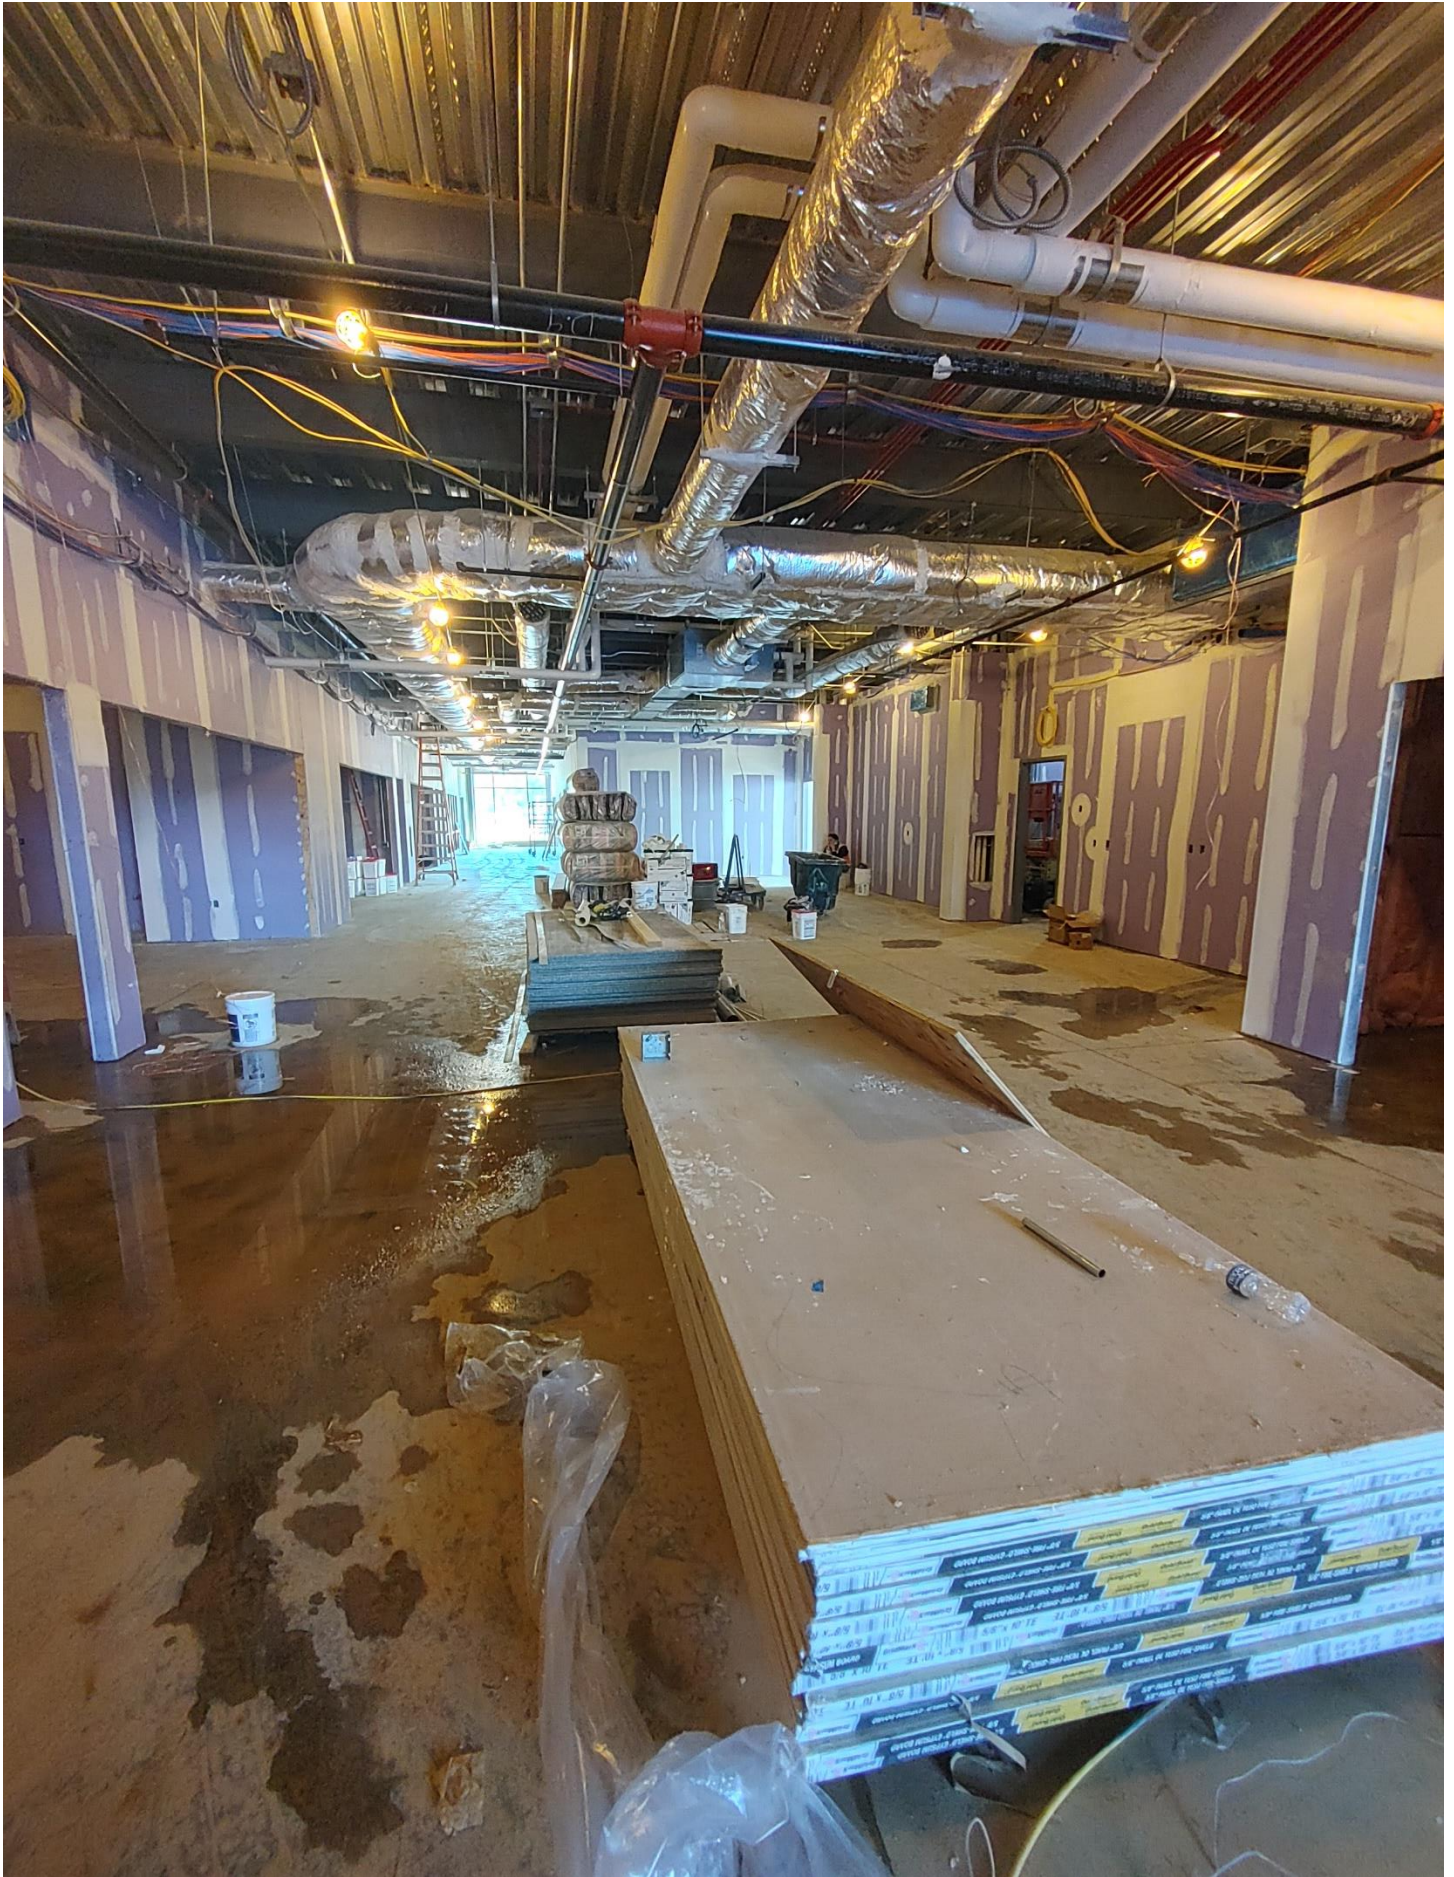


Photo 11 - Sheet Rock continues to be finished in Area A



Photo 12 - Roof Drains being set in Area C



Photo 13 - Colonial Webb working on Curbs on the Roof of Area E



Photo 14 - Colonial Webb working on Curbs on the Roof of Area B
