



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 05/18/2021
Weather: 74 degrees. High of 76 degrees today.
Hours Worked: 11:00hrs – 14:00hrs (3hrs) Site Visit.

My last report was on May 6, 2021. I was on Vacation last week. A lot of work has transpired since my last report. I stopped by Alexes Lee's Office and signed C.O. #8.

Beuchert Excavation: They are on site today and they continue to grade and rework the West side of the site.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: There are Twenty-one (21) men on site today. They are laying Brick on the East and West side of Area D and also on the West side of Area E.

Hazzard Electric: They have Twelve (12) men on site. They continue to run Conduit in Area B and in Area D.

Colonial Webb: There are Forty-two (42) men on site today. Duct is being run and insulated in Area A & B. Crews are also working on Roof top units.

Weldon Steel: No men noted on site today.

JP Construction: They have Sixteen (16) men here today. They are framing in Area A and hanging sheetrock in Areas A & B. A couple of guys are also finishing sheetrock in Area A.

AAR Roofing: Four (4) men are on site today. They are working in Area A.

Tailored Foam: Two (2) men are on site today. They are working on the Southside of Area B.

FG & M: There are Seven (7) men on site today. Work continues in Area E.

United Sprinkler: No one is on site today.

CTSI: Four (4) men are on site today. They are running Low Voltage wire in Areas A & B.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: I stopped in the Trailer during my visit and met with Brian and Jake. Brian briefed me on what had occurred over the past week. Brian said he is currently working on getting some temporary cooling units on site so that he can condition a section of Area A. He also said that a group of people from Stafford County are scheduled to visit the site tomorrow with Grimm & Parker for a tour.

A BMP Preinstallation meeting has been scheduled for 05/20/2021 at 14:00hrs.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. A DEQ Warning Letter was issued on April 30th, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 05/04/2021, 05/05/2021, 05/10/2021, 05/11/2021

Submittals – #07 21 00-1.1, #01 31 14-4.0, #11 66 23-3.2

RFIs – #234, #261, #262, #263, #264, #265, #270

Patrick Byrne –

Change Order/PCOs/Pay App – CO #8

Changes in Procore –

Weekly Submittal Status Report – 05/14/2021

Weekly RFI Status Update – 05/14/2021

Weekly Daily Log Summary – 05/14/2021

PCO Log – 05/14/2021



Photo 1 - Brick continues to be laid on the North side of Area A



Photo 2 - Glass has been installed in the Curtain Wall on the East side of Area A



Photo 3 - Masons are laying brick on the East side of Area D



Photo 4 - Brick is being laid on the South side of Area D



Photo 5 - Progress is being made on the Gymnasium Curtain Walls and Store Fronts



Photo 6 - FG&M working on Curtain Wall on the Southwest corner of Area E



Photo 7 - Brick is being laid on the West side of Area E



Photo 8 - Tailored Foam setting up on the South side of Area B



Photo 9 - Glass is being installed in the Curtain Wall on the West side of Area B

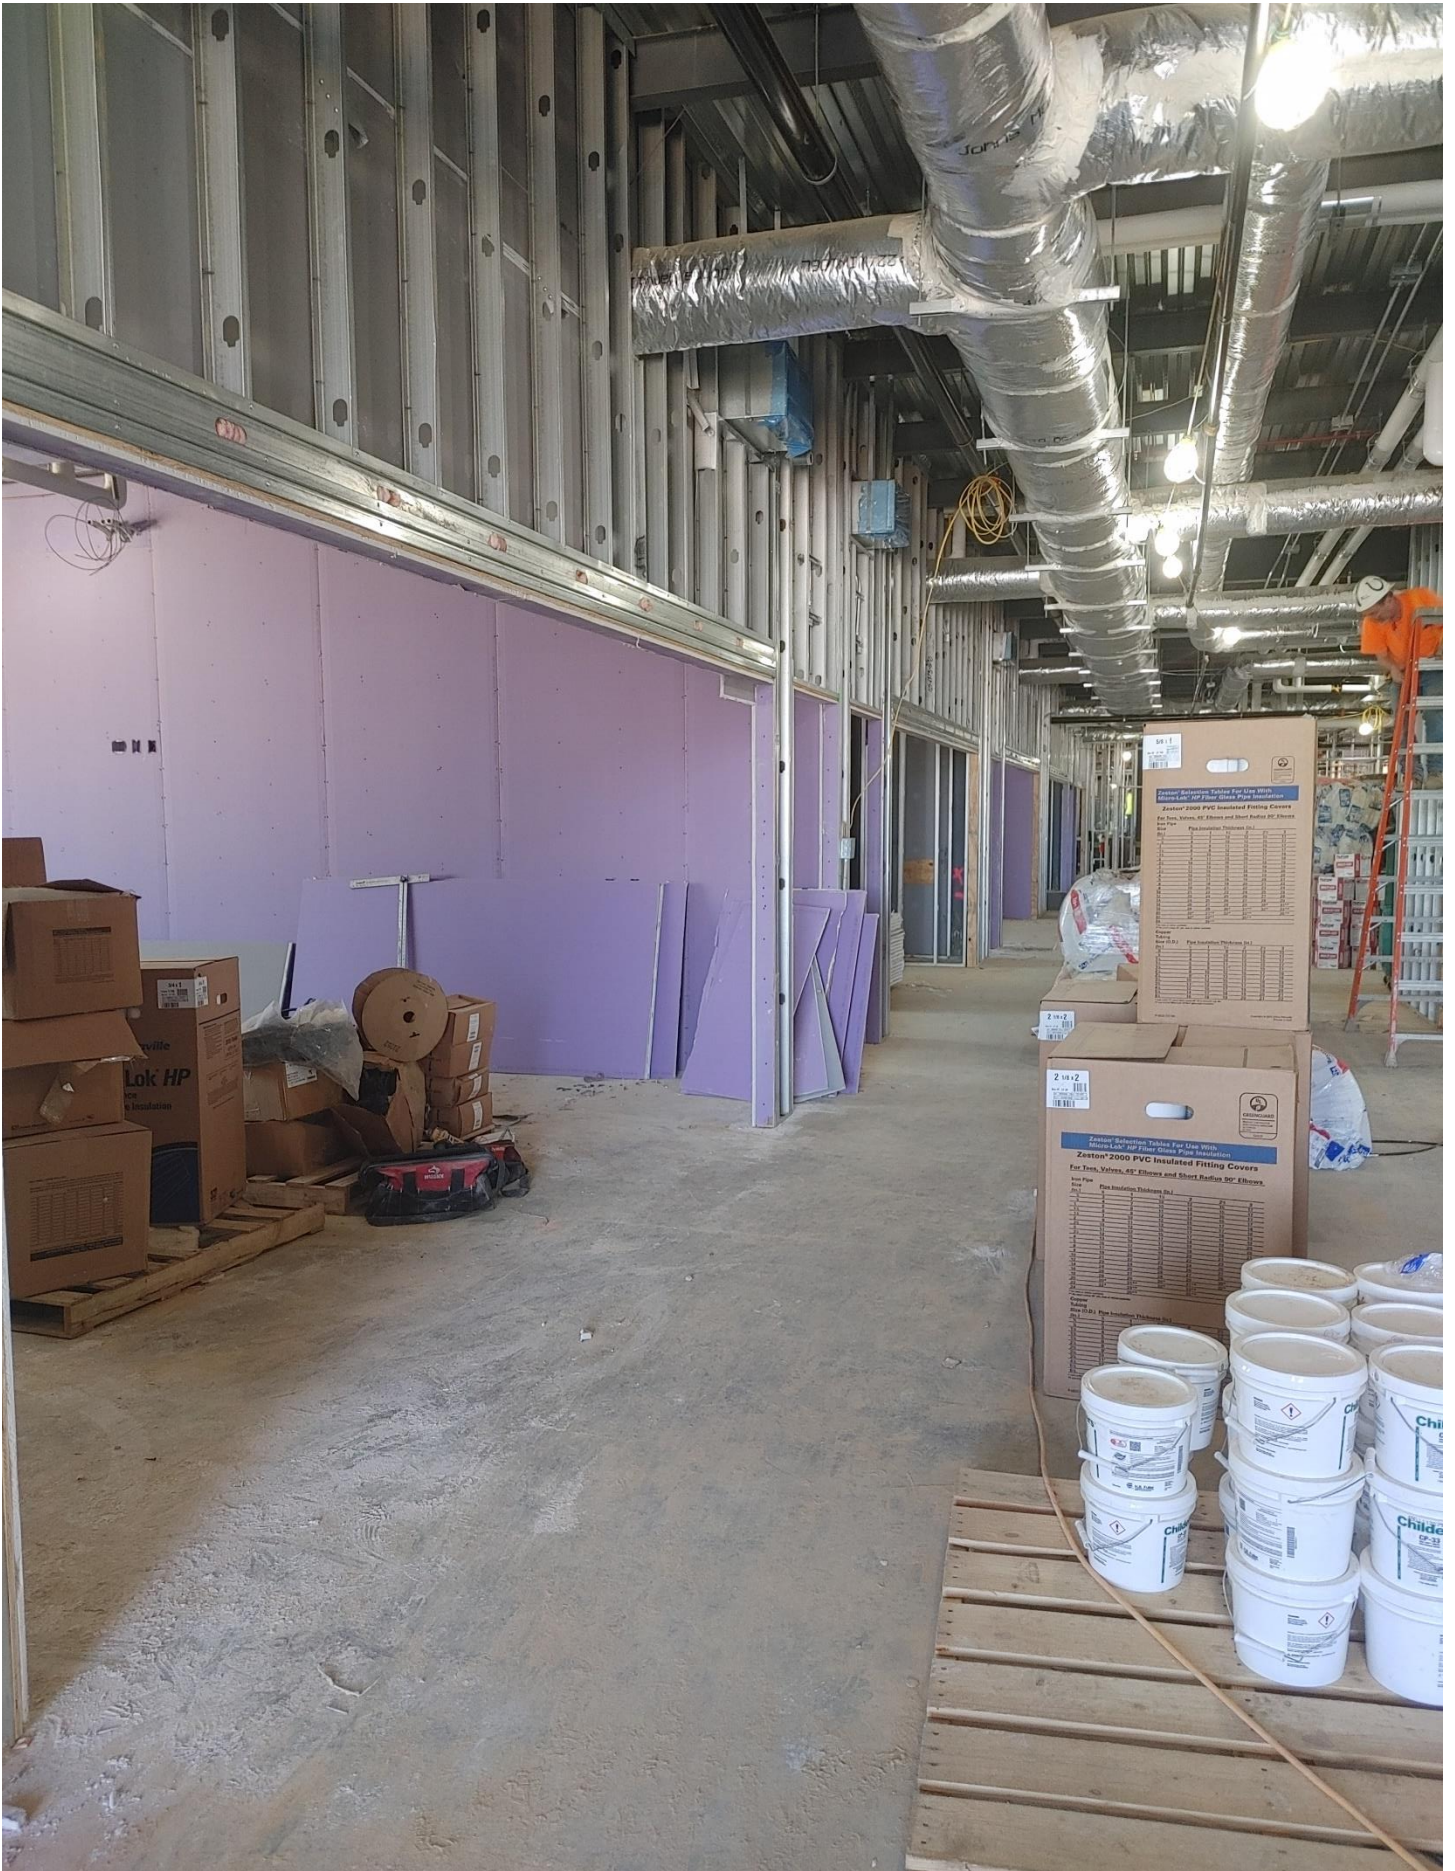


Photo 10 - Sheetrock is now being hung on the 1st floor of Area B



Photo 11 - Glass has been installed in some of the Storefronts on the 1st floor of Area A



Photo 12 - Glass is being installed in the Storefronts on the 2nd floor of Area A



Photo 13 - Roof Top units have been set in Area E



Photo 14 - Roof Top Unit has been set in Area A
