



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 05/20/2021

Weather: 84 degrees. Sunny. High of 85 degrees today.

Hours Worked: 12:30hrs – 14:00hrs (3.5hrs) On Site.

Attended the 14:00hrs.W&L BMP Preinstallation Meeting in the Branch Builds Trailer. The question of when and the frequency of the testing the soils for the BMP was raised. During the discussion it was revealed that the Soil for the BMPs were being mixed on site and not being provided by a third party supplier. Typically, when the material is supplied by a third party that party provides the testing data. Since it is being mixed on site it needs to be tested. I advised the group that I did not think the Owner should have to pay for this testing since the decision was made to mix the soil on site. After some discussion it was agreed that Beuchert would contract with Hillis-Carnes for this testing as required.

Branch did not fill out their Huddle Board today so I am unable to determine the number of men on site today.

Beuchert Excavation: They are working in the Loading Dock area importing soil and compacting it to grade in lifts.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: They continue to lay Brick on the East and West side of Area D today.

Hazzard Electric: They are pulling home runs from Area B to Area D. A couple of guys are also running conduit on the 2nd floor of Area A.

Colonial Webb: Duct is being run and insulated in Area A & B. Crews also continue to work on Roof top units in Area B and water lines are being run in Area A.

Weldon Steel: They continue to work on Joists and welding decking in Area C.

JP Construction: They are framing walls in Area A, hanging Sheet Rock in Area B and finishing sheetrock in Areas A.

AAR Roofing: I did not observe anyone on site today.

Tailored Foam: They are spraying foam on the West side of Area B.

FG & M: They continue to work in Area E on storefronts and curtain walls and on the West side of Area B.

United Sprinkler: No one is on site today.

CTSI: No one is on site today.

S&S Concrete Cutting Company: They are on site drilling and coring concrete in Area A.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. A Tech was on site today checking soil compaction in the Loading Dock Area.

Questions to or from Branch Builds: I spoke with Brian and Jake during my visit today and received a Project Update. No issues of concern were discussed.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. A DEQ Warning Letter was issued on April 30th, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations. I was advised on 05/19/2021 that a response has been sent by Branch Builds to DEQ.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 05/17/2021

Submittals –

RFIs – #251, #269, #271

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Brick continues to be laid on the East side of Area D



Photo 2 - Beuchert continues to remove soils on the East side of the site to be mixed for use in the BMPs.



Photo 3 - The South side of Area C has begun to receive foam.



Photo 4 - Beuchert is compacting soils in the Loading Dock Area.



Photo 5 - the Cap of the Parapet wall is being constructed.

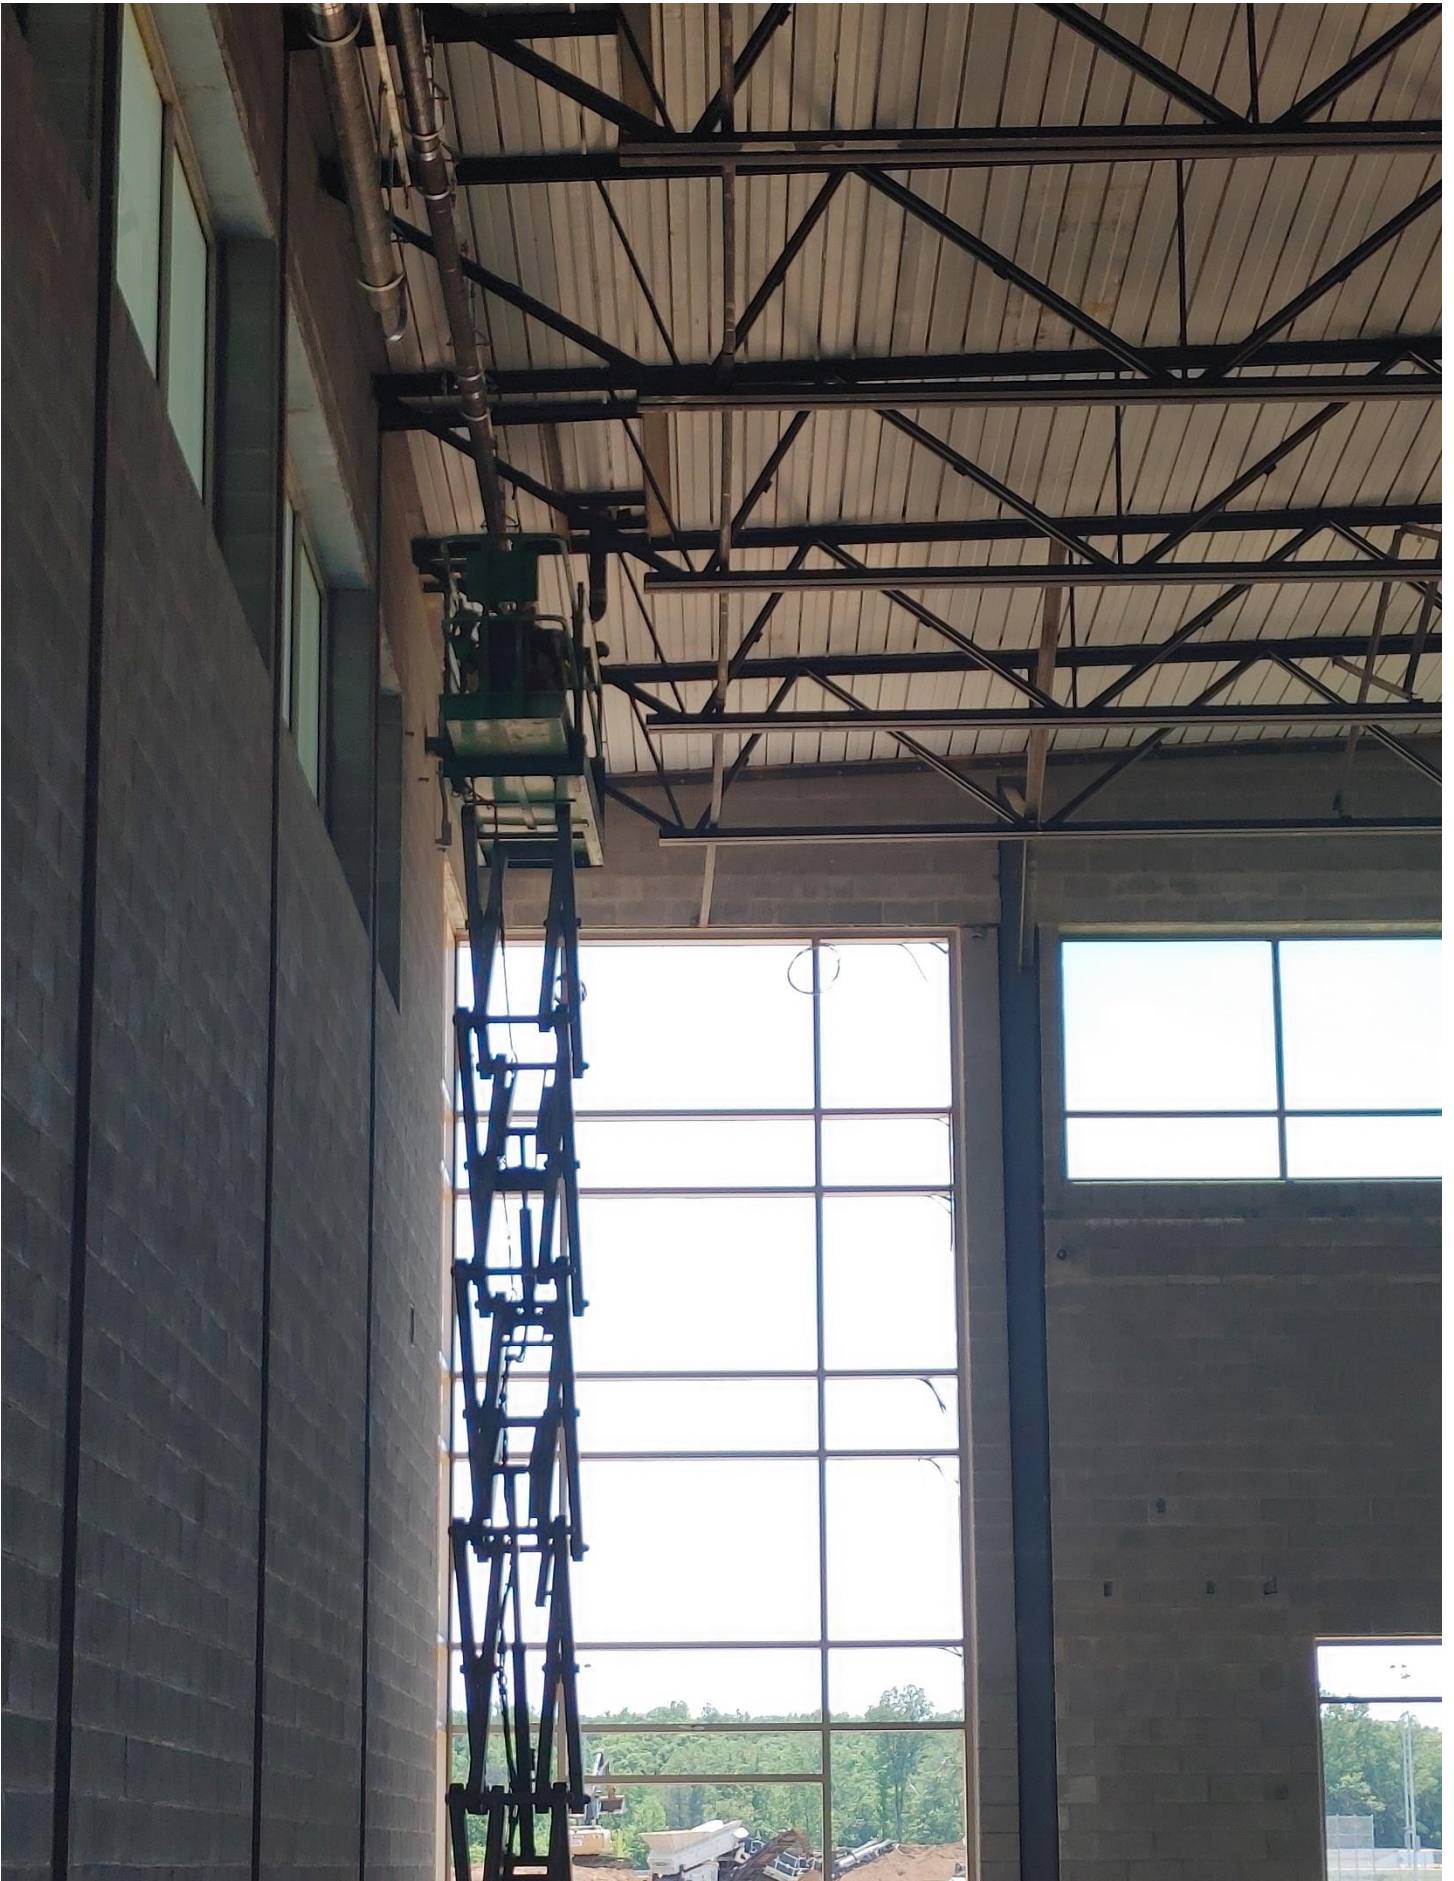


Photo 6 - Roof Drains are being installed in the Gym.



Photo 7 - Steel being welded in Area C.



Photo 8 - Gyp Board being hung on the West side of Area C



Photo 9 - West side of Area B receiving Spray Foam



Photo 10 - Brick being flashed on the North side of Area A
