



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 06/03/2021
Weather: 72 degrees. Partly Sunny. High of 81 degrees today.
Hours Worked: 08:30hrs – 11:30hrs (3hrs) On Site.

It rained here on briefly earlier this morning. The site is muddy. I briefly met with Brian yesterday to discuss the DEQ Re-inspection scheduled for Monday, June 7th. Brian and I also examine a Drop Inlet along Rec Park Road that is experiencing some erosion. I have repaired it twice and Beuchert installed Super Silt Fence around the inlet after working in that area. I did not spend any real time on the High School site yesterday and therefore I did not prepare a Daily Report.

Enviroscapes completed their Bore yesterday under Rec Park Road in preparation of tying the 12" water line into the 8" Waterline and the installation of the Back Flow device.

Beuchert Excavation: No one is on site today.

Industrial Concrete: Two (2) men are on site today. They are forming up diamonds around columns to be poured in Area D, Corridor D15.

J.D. Long, Masons: Eighteen (18) men are here today. They are laying Brick on the North and South side of Area B and on the roof of Area C.

Hazzard Electric: Thirteen (13) men are on site. They continue to pull wire in Area A, B & D. One man is working on the roof of Area A setting Disconnects.

Colonial Webb: Thirty-three (33) men are on site today. They are running duct in Area D; insulating duct and running water lines in Area A; and two men are working on connecting duct work to the large roof top unit in Area A. They have also staged the Hot Water Heater in the Mechanical room and were in the process of off loading the Boilers from a Tractor and Trailer.

Weldon Steel: Four (4) men are on site today. They continue to work in Area C welding Steel.

JP Construction: Twenty-four (24) men are on site today. They are working in Area A, B & C framing walls, bulkheads, and hanging and finishing Sheetrock.

AAR Roofing: Four (4) men are on site today. They continue to work on Area A roof.

Tailored Foam: Two (2) men are on site today. I did not observe what they were doing on site during my visit.

FG & M: Six (6) men are here today. They are currently installing Storefronts in Area D.

United Sprinkler: Two (2) men are on site today. They continue to run pipe in Areas A & B.

CTSI: Two (2) men are on site today. They are pulling low voltage wiring in Areas A & B.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe a Tech on site during my visit.

Questions to or from Branch Builds: I met with Brian before I walked the site this morning. Brian brought me up-to-date on what has transpired since my last visit. Brian also said that Colonial Webb were going to begin installing the Boilers today.

Todd advised me that he would not be visiting the site this week and requested that I send him an email with my questions pertaining to May's Pay Application. I sent him an email outlining my questions that basically pertained to items that are stored. He advised me that some are stored on site and some are off site. He said he would get us the necessary paperwork for those items stored off site. He said Brian would show me the items that are stored on site. He agreed to remove the Wheelchair Lift of \$8,500.00 in Division #14. The amount billed was required when they placed the order. I told him we could only pay for the item if it was stored or installed.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site has been scheduled for 09:00hrs on June 7, 2021.

Reviewed emails:

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs – #271, #276**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



Photo 1 – Roofers are working on Area A's roof.



Photo 2 - Masons are laying block between Area D and C.



Photo 3 - Bulk Head is being framed on the 1st floor of Area A.



Photo 4 - Masons are laying Brick on the North side of Area B.



Photo 5 - Metal Studs are being installed in Area C.



Photo 6 - Sheetrock is being installed in Area B.



Photo 7 - A section of Area A, beginning at the Elevator, has been sealed off so that it can be climatized.



Photo 8 - Finish coat of Mud is being applied around door and storefront frames in Area A.



Photo 9 - Storefront frames being installed in Area D.



Photo 10 - Storefront frames are being installed in Area D.

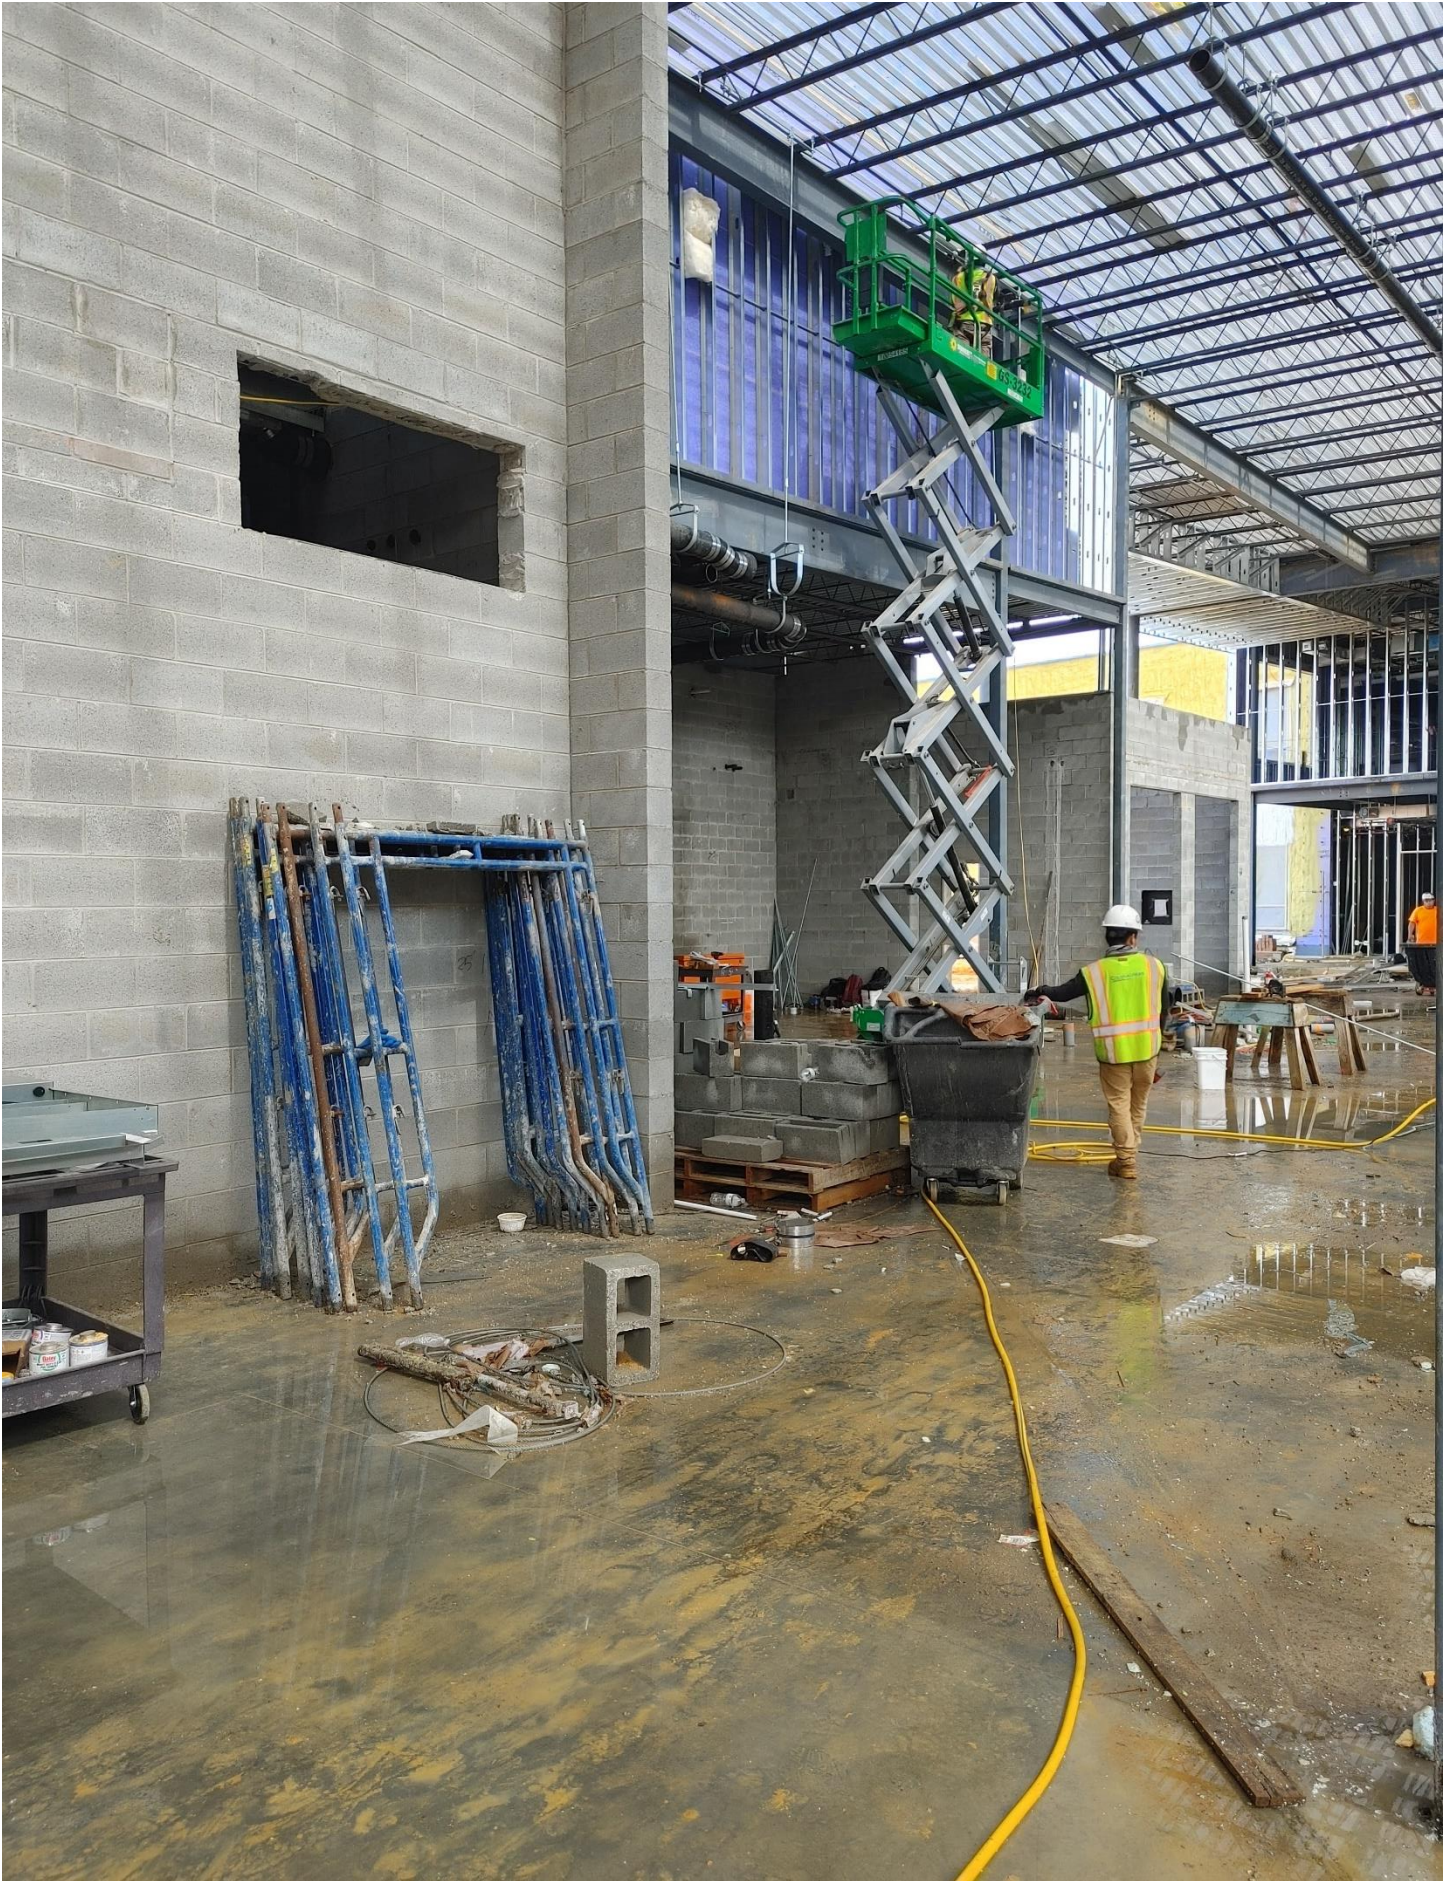


Photo 11 - Colonial Webb is installing hangers and Pipe in Area C.
