



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 06/04/2021

Weather: 74 degrees. Cloudy. High of 78 degrees today.

Hours Worked: 10:30hrs – 13:00hrs (2.5hrs) On Site.

It rained here on last night and early this morning. The site is muddy.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** Four (4) men are on site today. They continue to form up diamonds around columns to be poured in Area D.

**J.D. Long, Masons:** Nineteen (19) men are here today. They are laying Brick on the East side of Area C in the loading dock area. Three men continue to lay block on the roof of Area C. A crew is also laying block in the Kitchen this morning. One man is also washing brick on the North side of Area A.

**Hazzard Electric:** Twelve (12) men are on site. They continue to pull wire in Area A, B & D.

**Colonial Webb:** No one is on site today. They set the Hot Water heater and Boilers yesterday. Pictures below.

**Weldon Steel:** Five (5) men are on site today. They continue to work in Area D & C welding Steel.

**JP Construction:** Twenty-two (22) men are on site today. They continue to work in in Area A, B & C framing walls, bulkheads, and hanging and finishing Sheetrock.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is on site today.

**FG & M:** Two (2) men are here today. They are currently installing Storefronts on the Southside of Area D.

**United Sprinkler:** Two (2) men are on site today. They continue to run pipe in Areas A & B.

**CTSI:** Two (2) men are on site today. They are pulling low voltage wiring in Areas A.

**M. L. Straight:** One (1) man is on site today spraying and back rolling Block sealer in Stairwell #1.

**S&S Concrete Cutting Company:** No one is on site today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** I did not observe a Tech on site during my visit.

**Questions to or from Branch Builds:** I met with Brian this morning and we walked the site. Brian told me that an Engineer associated with Grimm and Parker was on site yesterday. Brian said he thought everything went well. According to Brian the Engineer only noted one small item that needed to be addressed. It was two pipe hanger that supported some copper pipe. The Engineer felt it need additional support.

I told Brian that Todd told me to get with him to verify that several items that are listed on the current Pay App shows are stored on site. I told Brian I needed to see the following items:

**Division #26, Zone #3 - \$59,972.00, 1st Floor Lighting (M).** Todd provided documentation that these items are stored off site.

**Division #26, Zone #4 - \$49,500.00, 1st Floor Lighting (M).** Brain showed me that these items are stored on site in Area A, Zone #4.

**Division #7, Zone #5 - \$17,140.00, Expansion Joint Cover Assembly.** Brian showed me that these items are stored on site in the Construction Trailer and in a Conex Box on site.

**Division #8, \$17,593.00, Door Hardware Sets.** I verified that these items are stored on site in a Conex Box.

**Division #8, \$16,200.00, Hollow Metal Doors.** I verified that these items are stored on site in a Conex Box.

**Division #8, \$9,100.00, Aluminum Door Install.** Brain advised that no Aluminum Doors had been installed. I told Brian I would get back with Todd on this Item.

**Division #8, \$9,900.00, Shadow Box within frames material.** Brian said he is not aware of this material being on site. I told Brian I would get back with Todd on this item.

**Division #14, \$8,500.00, Wheelchair Lifts.** Todd agreed to delete this from the current Pay App.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site has been scheduled for 09:00hrs on June 7, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) –**

**Submittals –**

**RFIs –**

**Patrick Byrne –**  
**Change Order/PCOs/Pay App – PCO #48**  
**Changes in Procore –**  
**Weekly Submittal Status Report – 06/04/2021**  
**Weekly RFI Status Update – 06/04/2021**  
**Weekly Daily Log Summary – 06/04/2021**  
**PCO Log – 06/04/2021**





Photo 1 - Masons are laying Brick on the East side of Area C in the Loading Dock Area





Photo 2 - Water Heater was set yesterday in the Mechanical Room of Area D.





Photo 3 - The Boilers were set yesterday in the Mechanical Room of Area D.



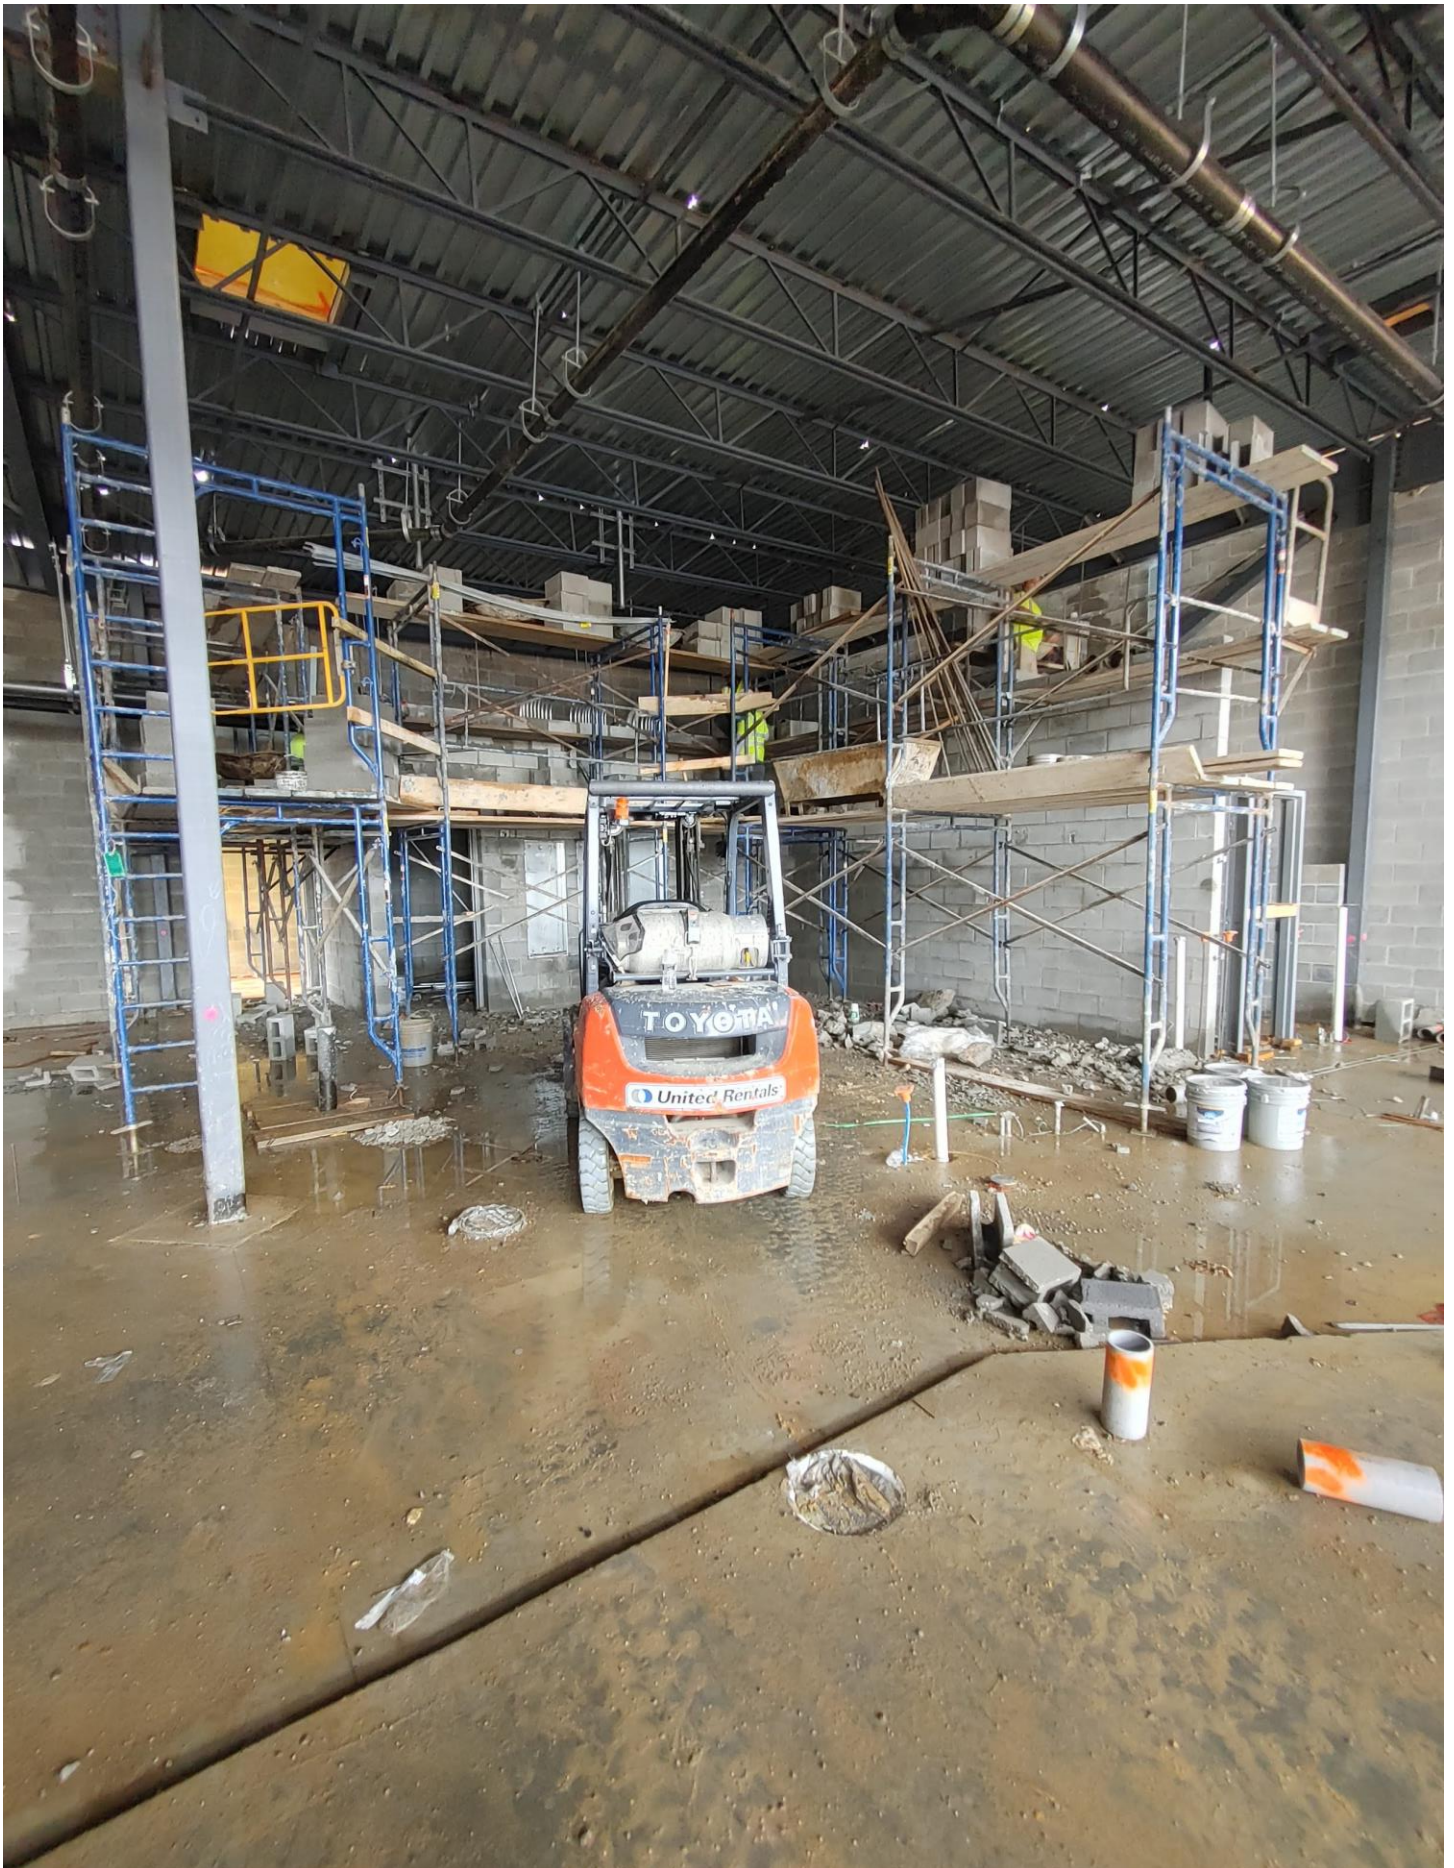


Photo 4 - The Masons are laying block in the Kitchen.





Photo 5 - Storefront being set on the South side of Area D.
