



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 06/08/2021
Weather: 82 degrees. Mostly Cloudy. High of 90 degrees today.
Hours Worked: 08:30hrs – 11:00hrs (2.5hrs) On Site.

08:30hrs – 10:30hrs (2hrs) on 06/07/2021

Yesterday I attended the Daily Huddle Meeting with Branch Builds and the Subcontractors at 08:30hrs. Brook Philpy, DEQ Inspector and Beth McDowell, Director, Westmoreland County Land Use arrived at 09:00hrs to conduct a SWPPP inspection of the High School site, Rec Park Road and the Recreation Park. Brian, Cooper, Jake and I walked the entire site with the inspectors. The inspection of the High School Site concluded at 10:30hrs. I did not prepare a report for yesterday.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one site today.

J.D. Long, Masons: Twenty-four (24) men are here today. They are laying Brick on the East side of Area C in the loading dock area. A crew also continues laying block in the Kitchen area this morning. Brick is also being laid on the North side of Area B and the West side of Area D.

Hazzard Electric: Fifteen (15) men are on site. They continue to pull wire in Area A, B, C & D.

Colonial Webb: Thirty (30) men are on site today. They are insulating pipe and running HVAC Duct in Area D. Running and insulating copper pipe in Area A and B and installing roof drains in Area C

Weldon Steel: No one is site today.

JP Construction: Twenty-two (22) men are on site today. They continue to work in in Area A, B & C framing walls, bulkheads, and hanging and finishing Sheetrock. Two men are also framing parapet walls on the roof of Area C.

AAR Roofing: No one is on site today.

Tailored Foam: No one is on site today.

FG & M: Seven (7) men are here today. They are currently installing glass in Area E and working on the Storefront on the West side of Area B.

United Sprinkler: Two (2) men are on site today. They continue to run pipe in Areas A & B.

CTSI: Two (2) men are on site today. They are pulling low voltage wiring in Areas A.

M. L. Straight: Two (2) men are on site today spraying and back rolling Block sealer in Stairwell #2.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe a Tech on site during my visit.

Questions to or from Branch Builds: I met with Brian this morning and we discussed yesterday's DEQ Inspection. I told Brian that DEQ had noted that I had some silt in a drop inlet along Rec Park Road. I told Brian that I have been having a constant problem with silt getting into the pipe and the area around the inlet eroding away. It wasn't until yesterday that I realized that there is a hole in the drop inlet. It is on the same side of the Inlet that Beuchert tied their temporary pipe. I told Brian that I believe they may not have sealed around pipe when they installed it and when they removed it they may not have sealed the hole. I am going to remove the grate later today and inspect the manhole. I will let Brian know what I find.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site conducted yesterday, June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals – #08 33 23-1.1, #08 33 23-2.1, #08 33 26-3.1, #08 33 13-4.0, #08 33 26-3.0, #08 33 23-4.0, #09 64 66-1.1, 09 75 00-7.0, #09 75 00-8.0, #10 21 23-1.1, #11 61 43-9.0, #11 61 42-5.0

RFIs – #266, #268,

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Temporary Cooling Units have been run into Area A to condition the space.



Photo 2 - Block sealer being sprayed and rolled on walls in Stairwell #2



Photo 3 - Parapet Walls are being constructed



Photo 4 - Walls being framed in Area C.



Photo 5 - Brick is being laid on the West side of Area D.



Photo 6 - Roof Drains being installed in Area C.



Photo 7 - Block continues to be laid in the Kitchen.



Photo 8 - Brick is being laid on the North side of Area D and the East side of Area C.

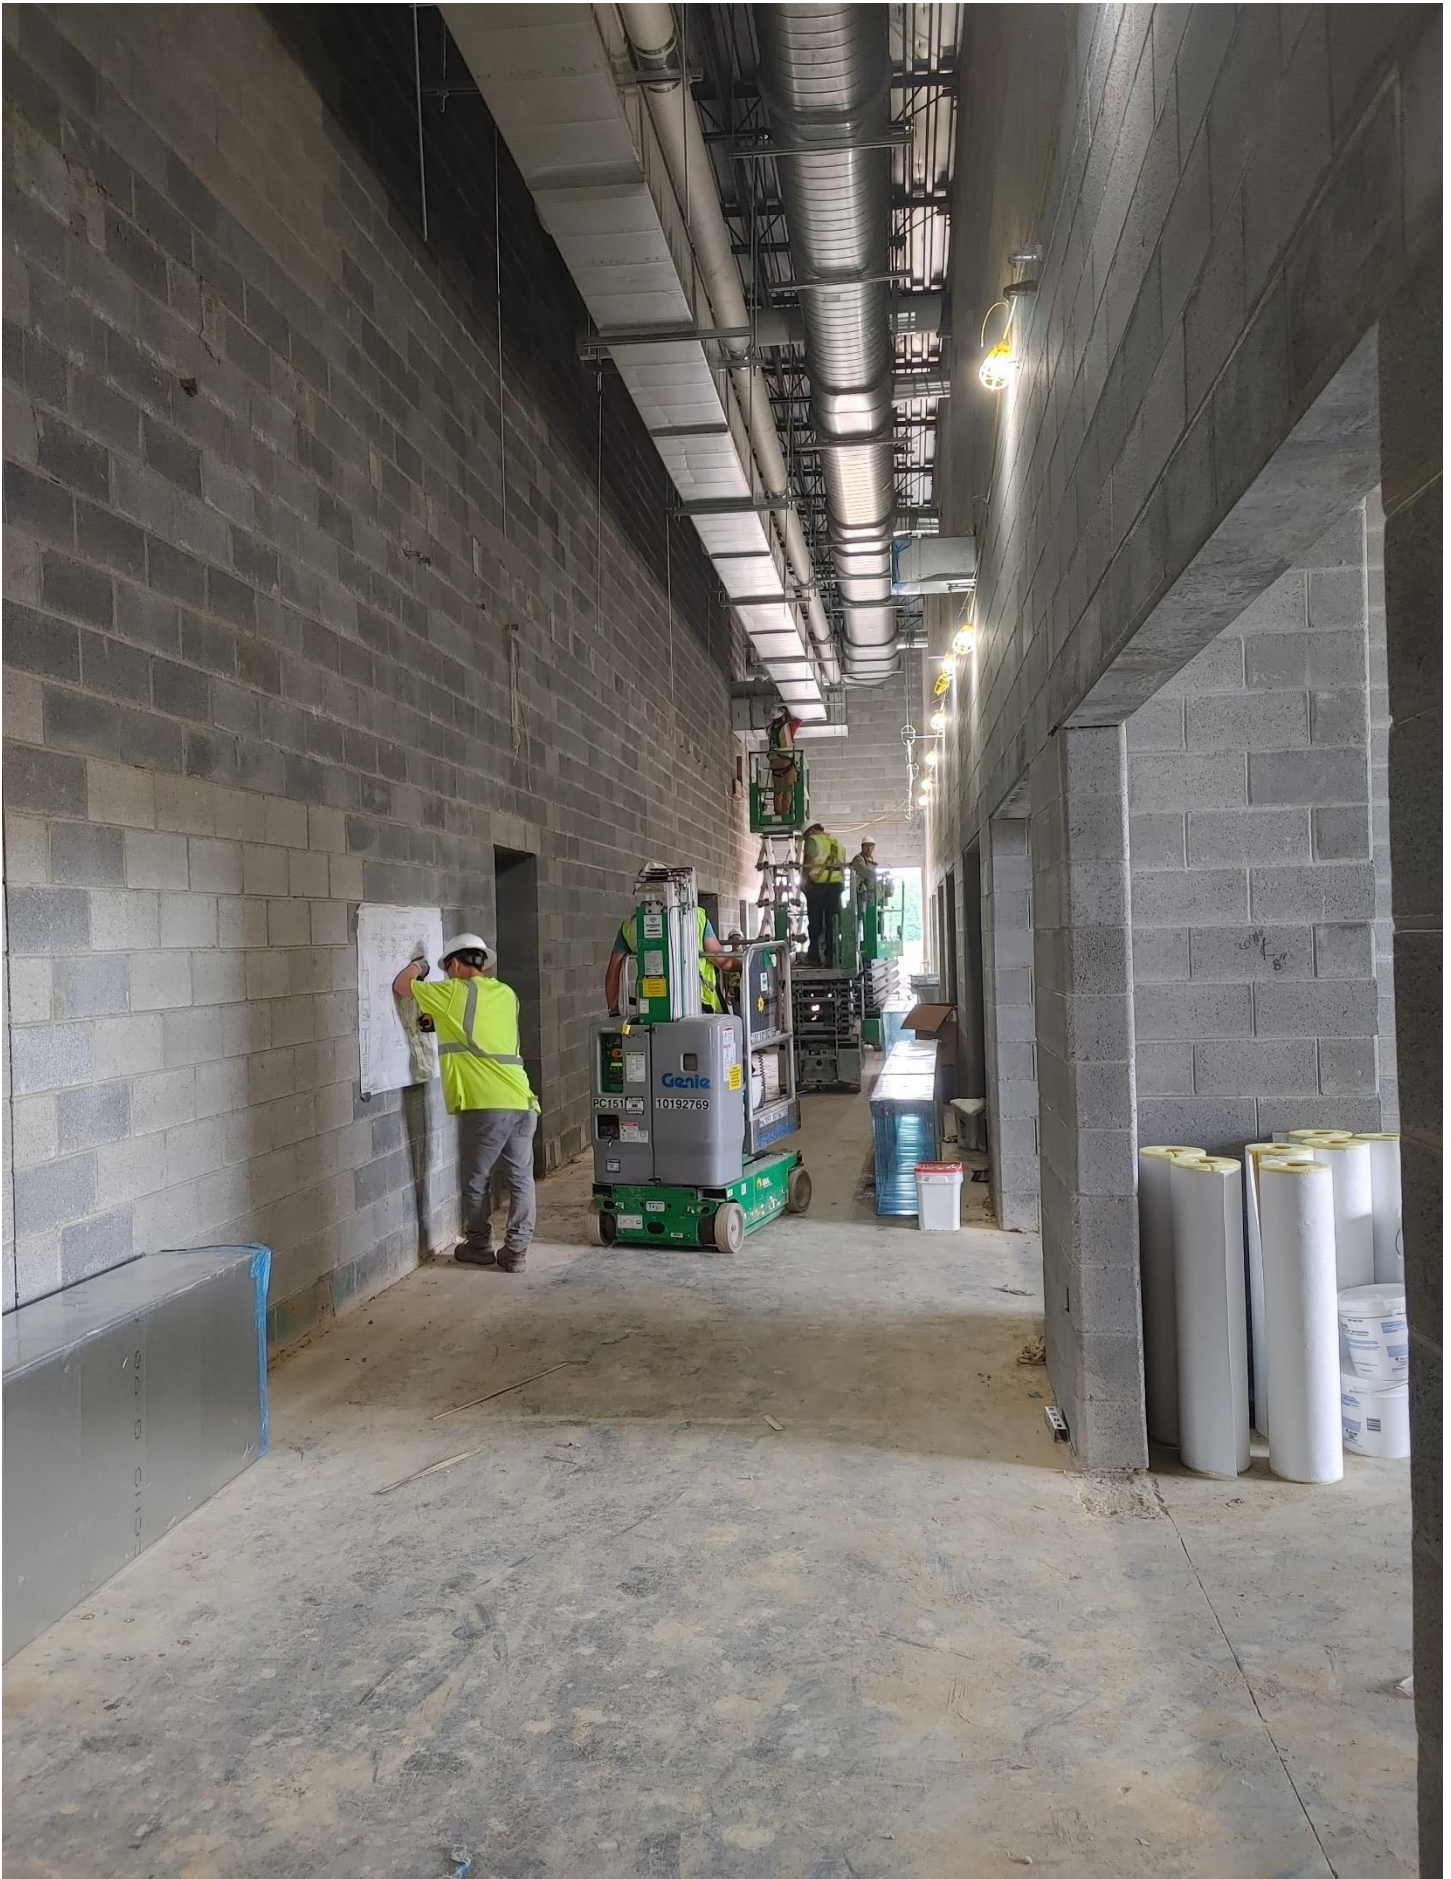


Photo 9 - HVAC Duct is being run in Area D.



Photo 10 - The Masons are grouting block in Area C.



Photo 11 FG&M is working on the Curtainwall on the West side of Area B.



Photo 12 - Brick is being laid on the North side of Area B.
