



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 06/17/2021
Weather: 70 degrees. Sunny. High of 80 degrees today.
Hours Worked: 09:00hrs – 12:00hrs (3hrs) On Site.

I met with Todd Demetriou yesterday afternoon to discuss the status of the 12" water line and the Third Party Inspections of the BMPs. The Contractor installing the Water Line said that best case he would be ready for the line to be tested in Mid-August. Worst Case would be October. We will discuss this at the next Progress Meeting on June 23, 2021. Hillis-Carnes is also requesting a Schedule for the BMPs and Todd is working on getting it together.

Beuchert Excavation: No one is on site today.

Industrial Concrete: I counted eight (8) men on site today. They poured the Generator Pad yesterday and are now forming up the Fuel Tank and Chiller Pads.

J.D. Long, Masons: Twenty-one (21) men are here today. They are laying Brick on the West and South side of Area B and they are Laying Block in Area D.

Hazzard Electric: Thirteen (13) men are on site. They continue to pull wire in Area A, B, C & D and continue to install light fixtures in Area A. One man is installing Disconnects on H-frames on the roof of Area B.

Colonial Webb: Thirty (30) men are on site today. They continue to insulate pipe and run HVAC Duct in Area A.

Weldon Steel: No one is on site today.

JP Construction: Twenty-two (22) men are on site today. They continue to work in in Area A & B framing walls, bulkheads, installing blocking and hanging and finishing Sheetrock.

AAR Roofing: Three (3) men are on site today working on the Parapet Wall between Area A & C.

Tailored Foam: Two (2) men are on site today.

FG & M: Six (6) men are on site today. They are installing Backer Rod on the Northside of Area A. All but two panes of glass has been installed in the Gymnasium.

United Sprinkler: Two (2) men are on site today. They continue to run pipe in Area A.

CTSI: No one is on site today.

M. L. Straight: Two (2) men are on site today spraying and rolling Block Filer in Area E.

S&S Concrete Cutting Company: Two (2) men are on site today coring concrete.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: I briefly met with Todd today and we discussed the Schedule for the BMPs and the Testing of the 12" Water Line. I told him that the Contractor installing the line is supposed to have me something in writing tomorrow indicating when he will be ready for the line to be tested.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. Follow-up Inspection Report received today from Emmett Philpy, DEQ.

Reviewed emails:

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals – #03 30 00-17.0**
- RFIs –**
- Patrick Byrne –**
- Change Order/PCOs/Pay App – PCO #52, #53**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



Photo 1 - Generator Pad has been poured. Forming up the Fuel Tank and Chiller slabs.



Photo 2 - Brick is being power washed on the West side of Area D.



Photo 3 - All but two pieces of glass has been installed in the Gym.



Photo 4 - Masons are laying brick on the West and South side of Area B.



Photo 5 - FM&G installing Backer Rod around windows in Area A.

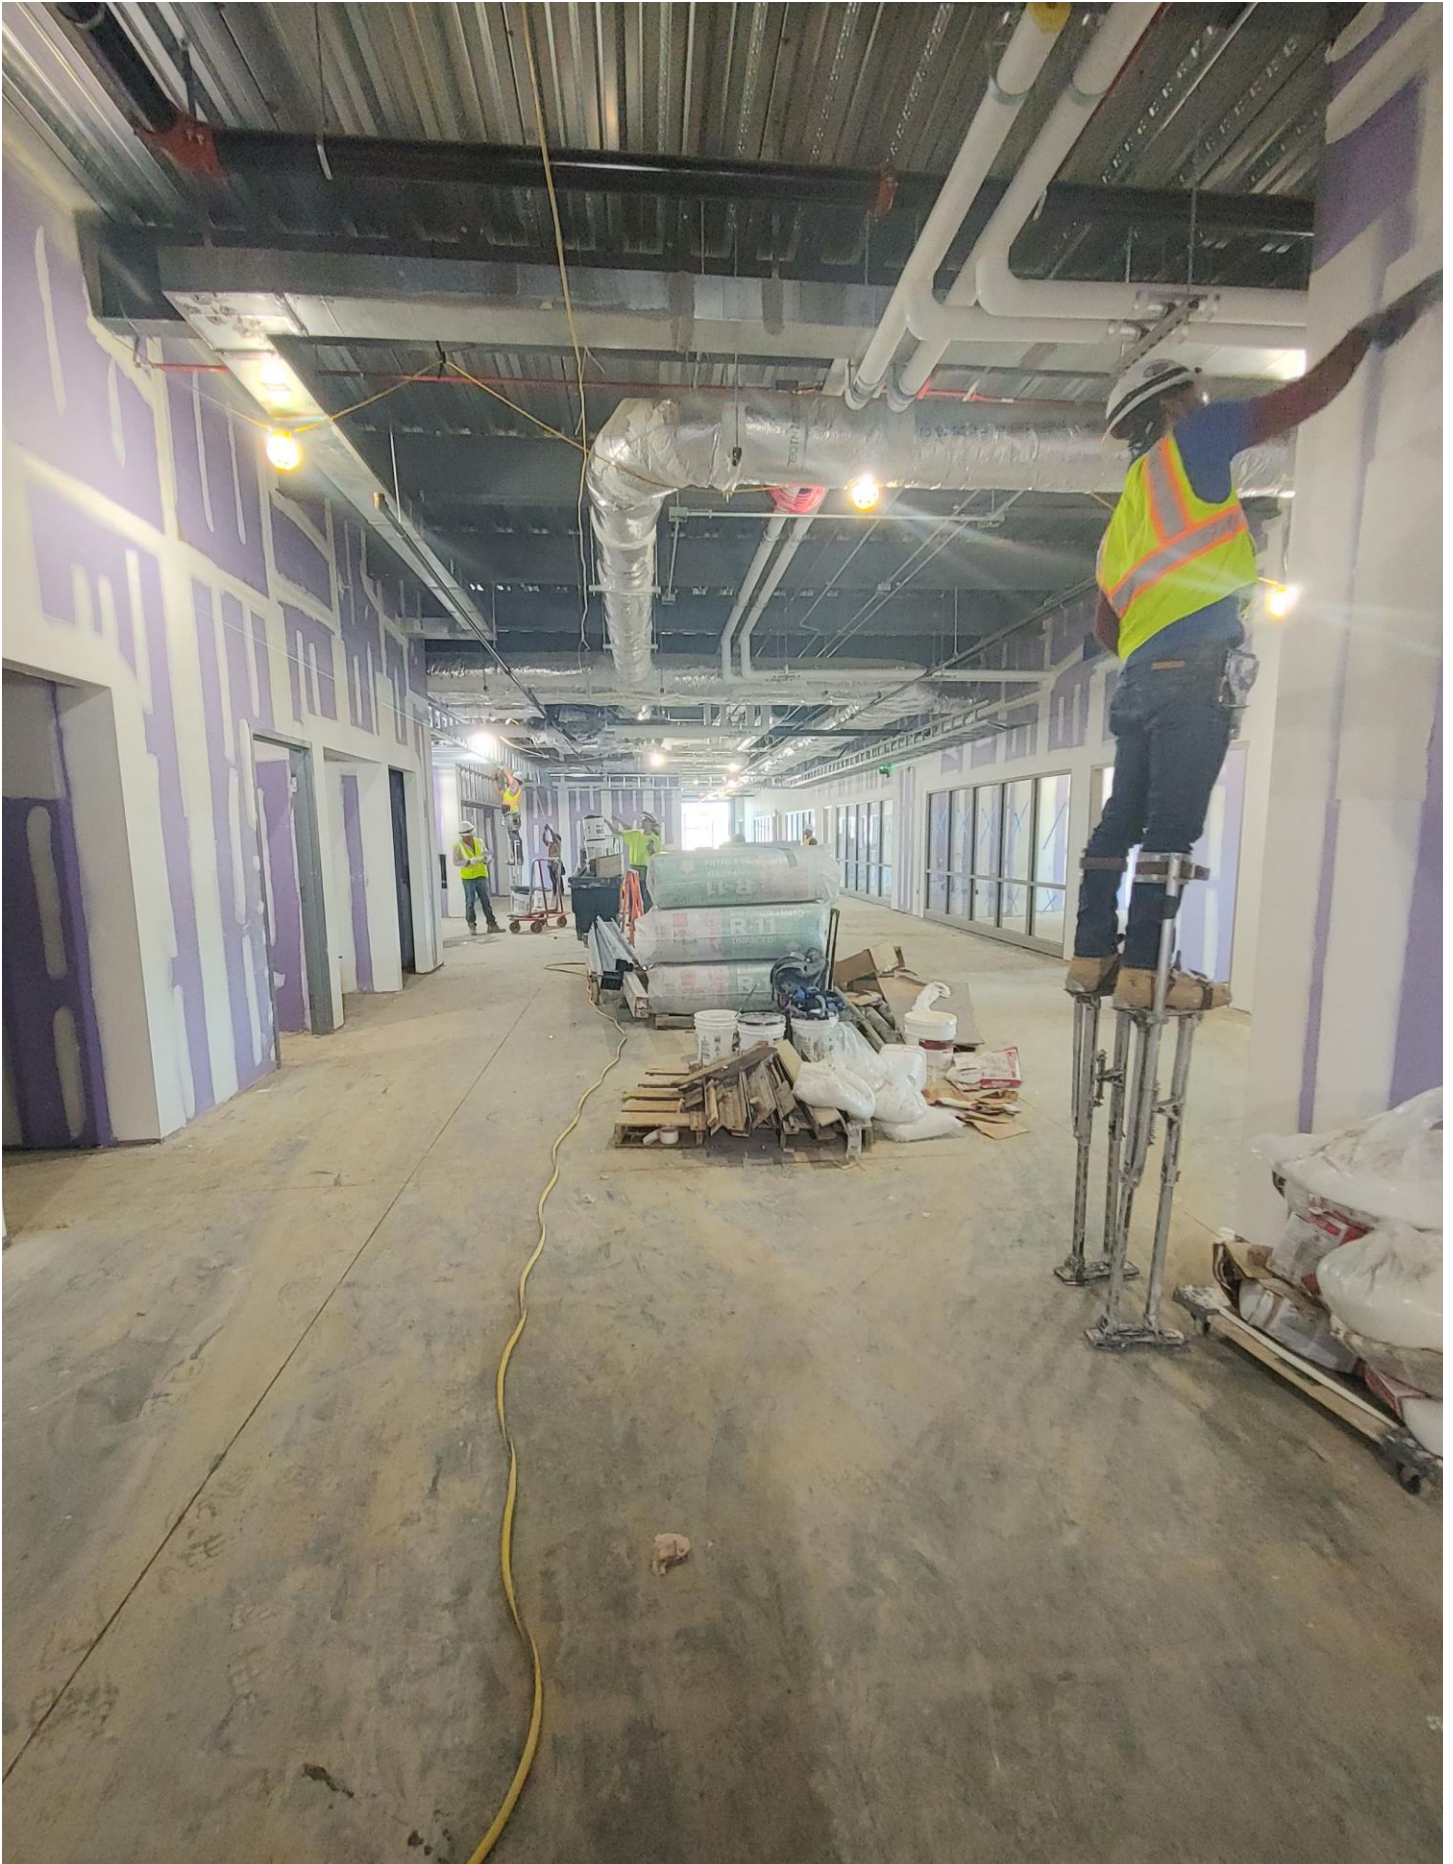


Photo 6 - Sheetrock is being finished and Bulk Heads constructed on the 1st floor of Area B.



Photo 7 - Duct work is being run and pipe is being insulated in Area A.



Photo 8 - Ceiling Grid is being run on the 1st floor of Area A.



Photo 9 - Roofers are working on the Parapet Wall between Area A & C.



Photo 10 Masons are laying Block in Area D.



Photo 11 - Pre-cast is being laid on the East side of Stairwell #1.
