



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 06/23/2021

Weather: 65 degrees. Sunny. High of 76 degrees today.

Hours Worked: 09:00hrs – 13:00hrs (4hrs)

Dr. Perry stopped by the site this morning. We spoke about today's Progress meeting, the current status of the project and about the 12" Water Line.

I attended the Virtual Progress Meeting in Norm Risavi's Conference Room at 11:00AM.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Twenty-one (21) men are here today. They continue to lay Brick on the South side of Area B and they are also laying Block in room D117.

**Hazzard Electric:** Thirteen (13) men are on site. They continue to pull wire in Area A, B, C & D and continue to install light fixtures in Area A. One man continues to install Disconnects on H-frames on the roof of Area B.

**Colonial Webb:** Thirty-two (32) men are on site today. They continue to insulate pipe and run HVAC Duct in Area A. A crew is also installing metal Duct in Area D.

**Weldon Steel:** Six (6) men are on site today. They are installing and welding steel between D110 & D112 for the Operatable Partition.

**JP Construction:** Twenty-one (21) men are on site today. They continue to work in in Area A & B framing bulkheads and hanging and finishing Sheetrock.

**AAR Roofing:** Four (4) men are on site today working on the Roof of Area C.

**Tailored Foam:** No men are on site today.

**FG & M:** Seven (7) men are on site today. They are installing the window frames on the West side of Area D and also installing the Storefront SF21 on the East side of Area D.

**United Sprinkler:** Two (2) men are on site today. They continue to run pipe in Area A.

**CTSI:** Two (2) men are on site today pulling low voltage wire.

**M. L. Straight:** Two (2) men are on site today spraying and rolling Block Filer in Area D.

**S&S Concrete Cutting Company:** No one is on site today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes:** I did not observe a Tech on site today.

**Questions to or from Branch Builds:** I met with Todd today and we discussed the Schedule for the Testing of the 12" Water Line. I briefed him on the status and told him that the best case scenario would be late August or potential as late as October. After some discussion and after speaking with the Engineer installing the 12" water line, Todd agreed to get with the Engineer designing the Fire Suppression System and determine how accurate the Pressure Test needs to be. Another words, does everything need to be installed and connected (meter vault, Back flow device, 12" and 8" tied in to the school) for the engineer to design the pump or can some estimations be made. We will regroup after he obtains that information.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. Follow-up Inspection Report received today from Emmett Philpy, DEQ.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs – #263, #265, #281**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**

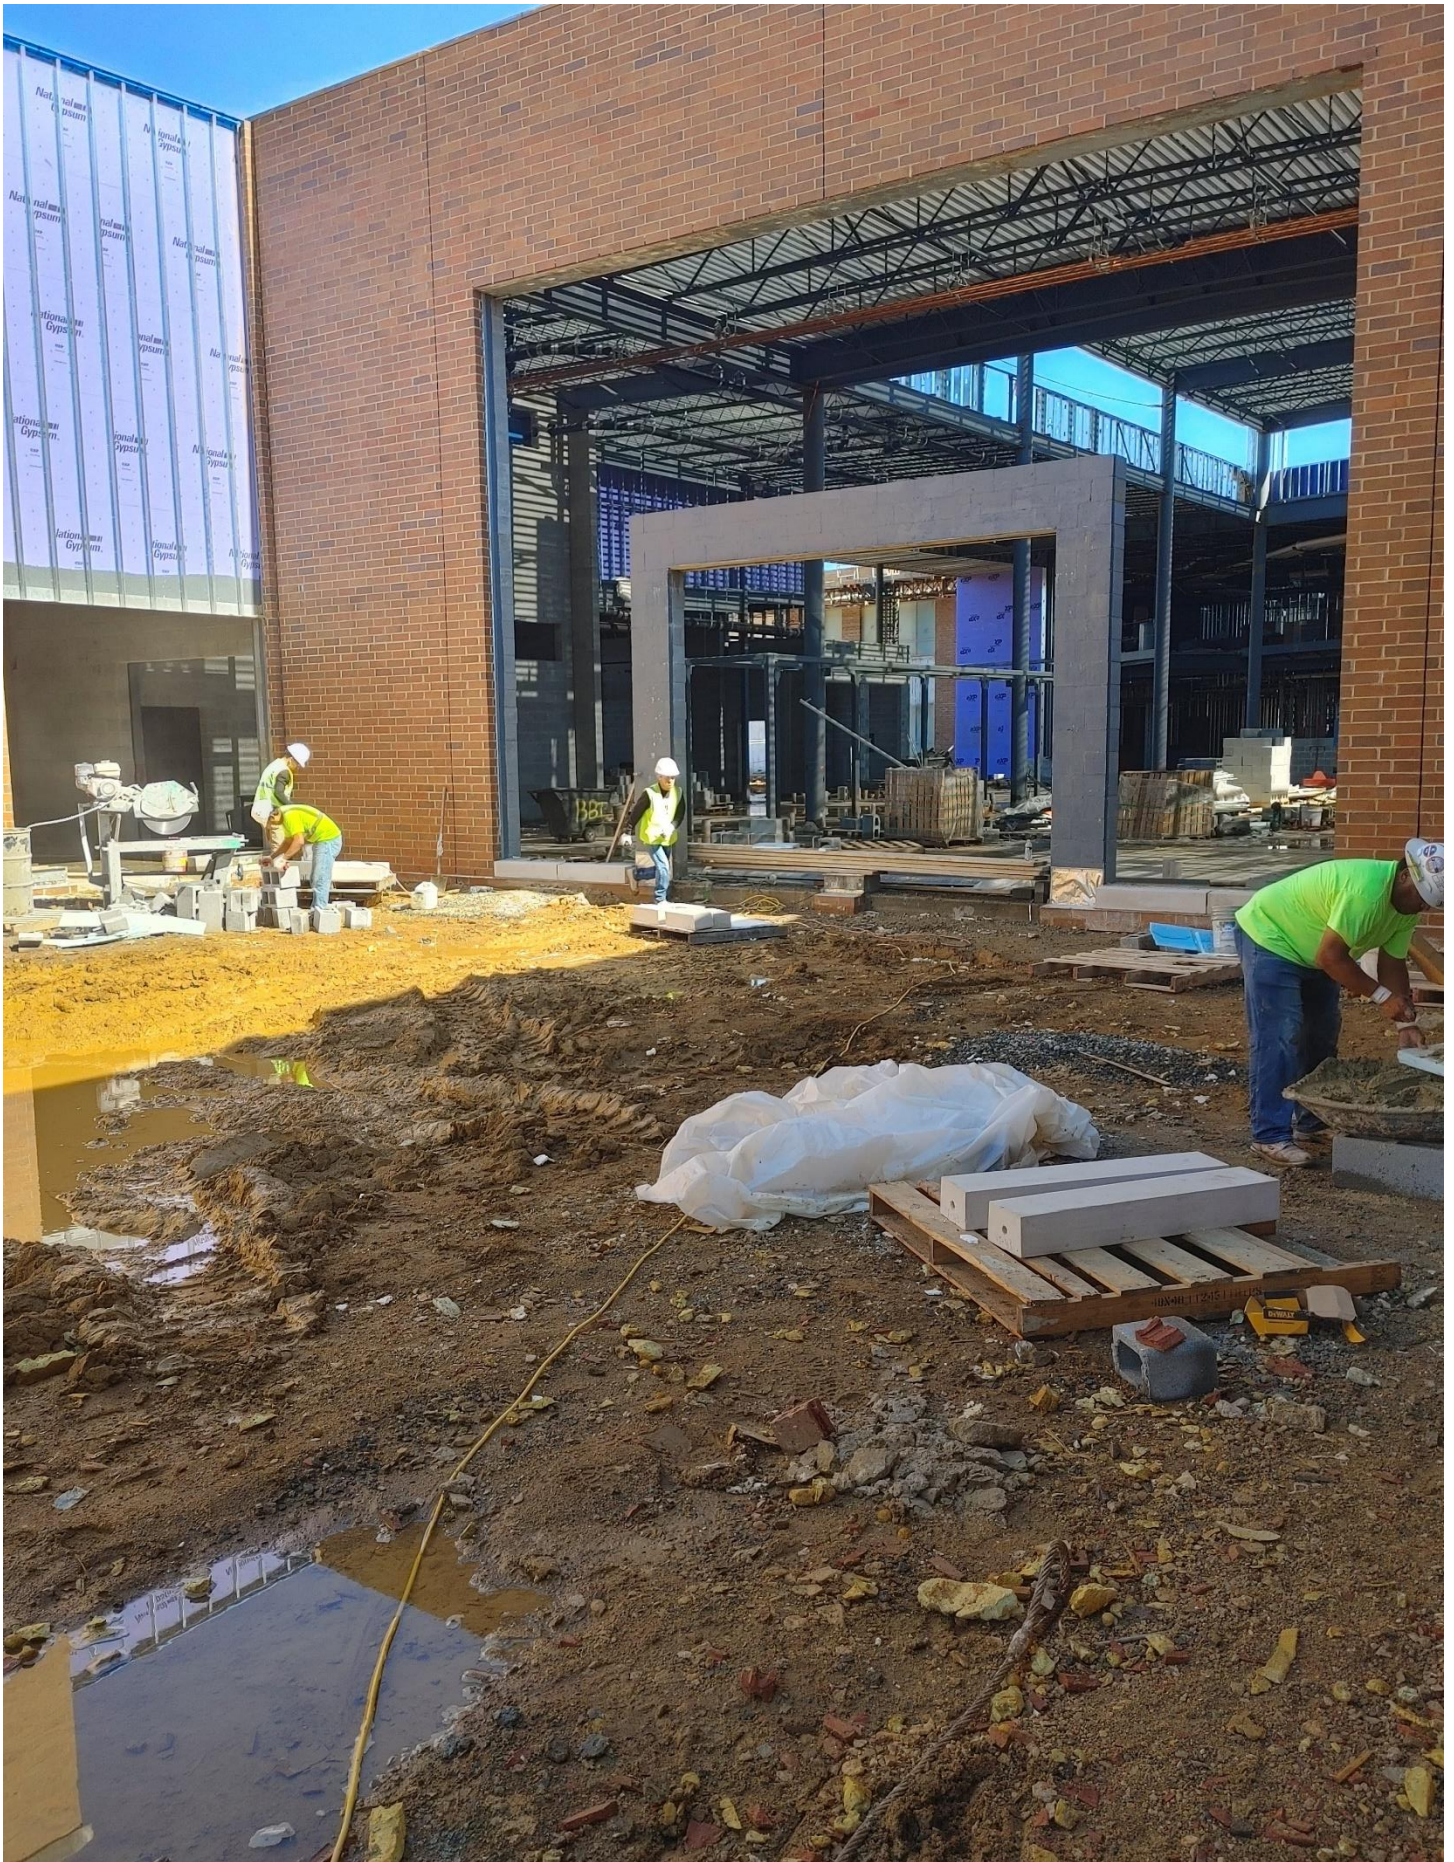


Photo 1 - Masons are laying Pre-cast on the South side of Area C



Photo 2 - View from the 2nd floor of Area A into Area C



Photo 3 - Roofers are working on the Roof of Area C.



Photo 4 - Mason are laying Brick on the South side of Area B.



Photo 5 - Frames being installed by FG&M on the West side of Area D



Photo 6 - Block is being laid in Area D, D117.





Photo 7 - Storefront SF21 is being set on the East side of Area D.



Photo 8 - Block filler is being sprayed and rolled in Area D, in room D125B
