



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West
Aylett, Virginia 23009
Phone: 804-761-4248
FrazierConsulting@gmail.com
Licensed Class A - RBC/CBC
DEPOR # 2705169996
EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 06/25/2021

Weather: 73 degrees. Sunny. High of 80 degrees today.

Hours Worked: 10:30hrs – 12:30hrs (2hrs)

I did not visit the site yesterday, June 24, 2021. Yesterday, I received the Design information on the 12" water line and I forwarded it to that Todd. Todd said he would get it to the Engineer and get back to me.

Branch did not have a Huddle Meeting with their Subs this morning, so the number of people on site was not obtained today.

I sent an email to Hillis-Carnes reminding them to provide the Owner with a cost to perform the work on the BMPs before actually starting the work. Note: we are waiting on a schedule from Branch Builds before Hillis-Carnes can provide the Owner with a cost for Services.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: They are laying brick on the East side of Area A and laying block in Area D in the Kitchen, Auditorium, and the Ticket room. One man is also laying brick on the low roof of Area E.

Hazzard Electric: They continue to pull wire in Area A, B, C & D and continue to install light fixtures in Area A. One man continues to install Disconnects on H-frames on the roof of Area B. A couple of guys are installing conduit in Area C ahead of the Mason.

Colonial Webb: No one is on site today.

Weldon Steel: I did not observe anyone on site today during my visit.

JP Construction: No one is on site today.

AAR Roofing: No one is on site today.

Tailored Foam: No men are on site today. They are scheduled to return on Monday.

FG & M: They are installing the Storefronts on the West side of Area D. Exterior doors have been installed on the East and South side of Area D.

United Sprinkler: Two (2) men are on site today. They are running Sprinkler pipe in Area D.

CTSI: Two (2) men are on site today pulling low voltage wire.

M. L. Straight: Two (2) men are on site today spraying and rolling Wall Primer in Area B.

S&S Concrete Cutting Company: Two (2) men are on site today coring walls in Electrical Room D158 for United Sprinkler .

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: Brian Topper is on Vacation. I met with Cooper and Jake in Branch Builds Trailer. Cooper briefed me on what was happening today.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. Follow-up Inspection Report received today from Emmett Philpy, DEQ.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test – 06/23/2021

Hillis-Carnes Field Reports (Concrete and Steel) – 6/24/2021

Submittals –

RFIs – #277, #278, #279, #282, #283, #285, #286, #287, #288

Patrick Byrne –

Change Order/PCOs/Pay App – PCCO #10, PCOs #49, #52, #53, #54

Changes in Procore –

Weekly Submittal Status Report – 06/25/2021

Weekly RFI Status Update – 06/25/2021

Weekly Daily Log Summary – 06/25/2021

PCO Log – 06/25/2021



Photo 1 - Brick is being laid on the East side of Area A



Photo 2 - Mason laying Brick on the North side of the Gym.



Photo 3 - Masons have begun to lay block for the wall that separates the dishwashing area from the Kitchen. Electricians are running conduit in this picture.

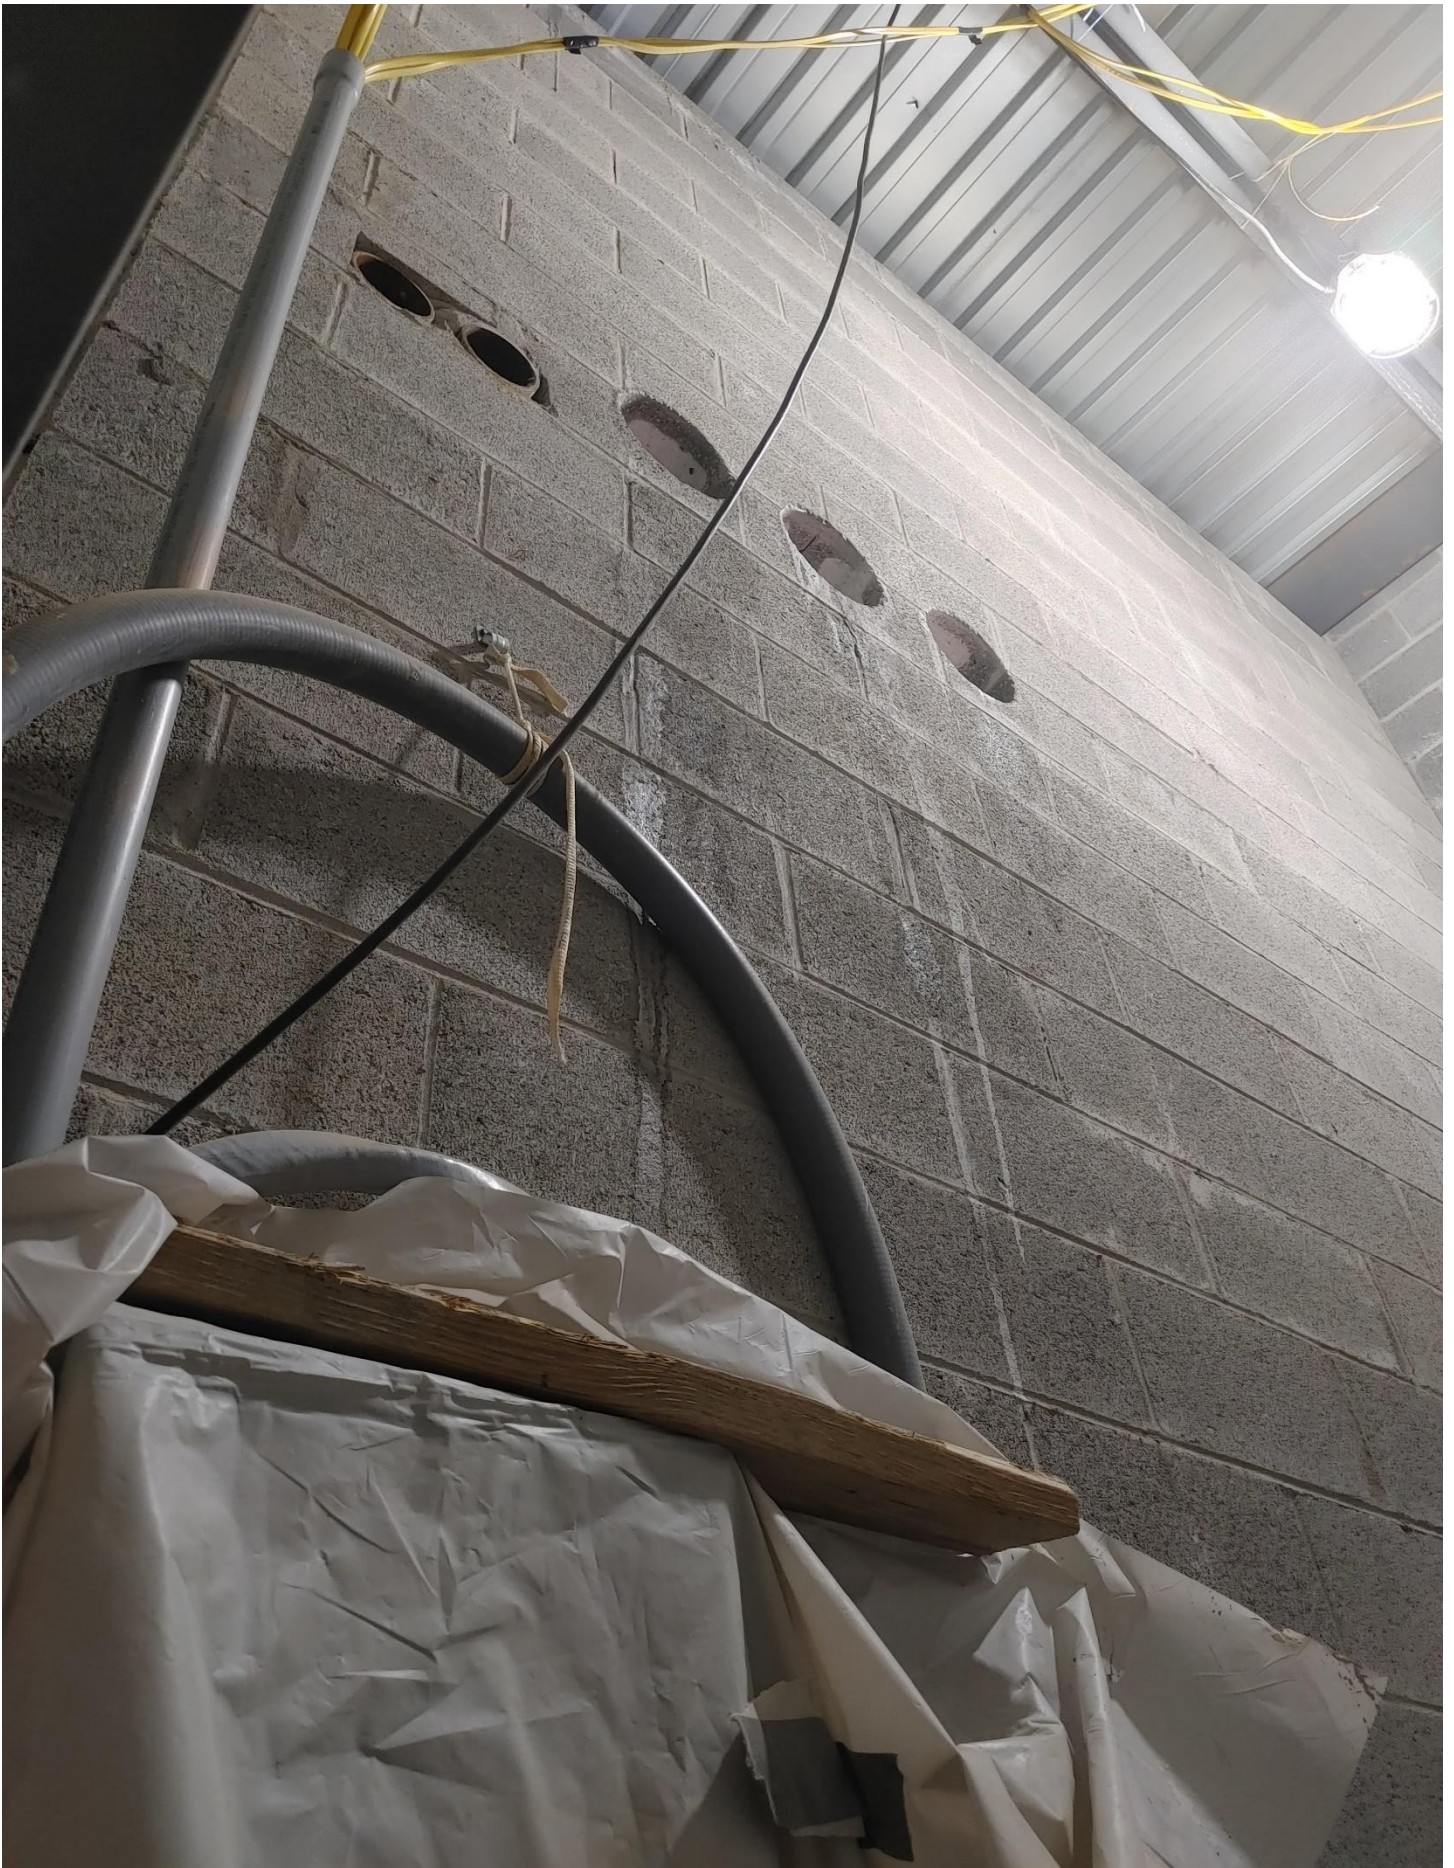


Photo 4 - S&S Concrete is coring walls in Area D for Sprinkler Pipe.



Photo 5 - Mason is laying block in the Auditorium.



Photo 6 - Doors have been set in SF21.



Photo 7 - Doors have been set in CW6 & CW7 on the South side of Area D



Photo 8 - FG&M is preparing openings to set SF22 & SF23

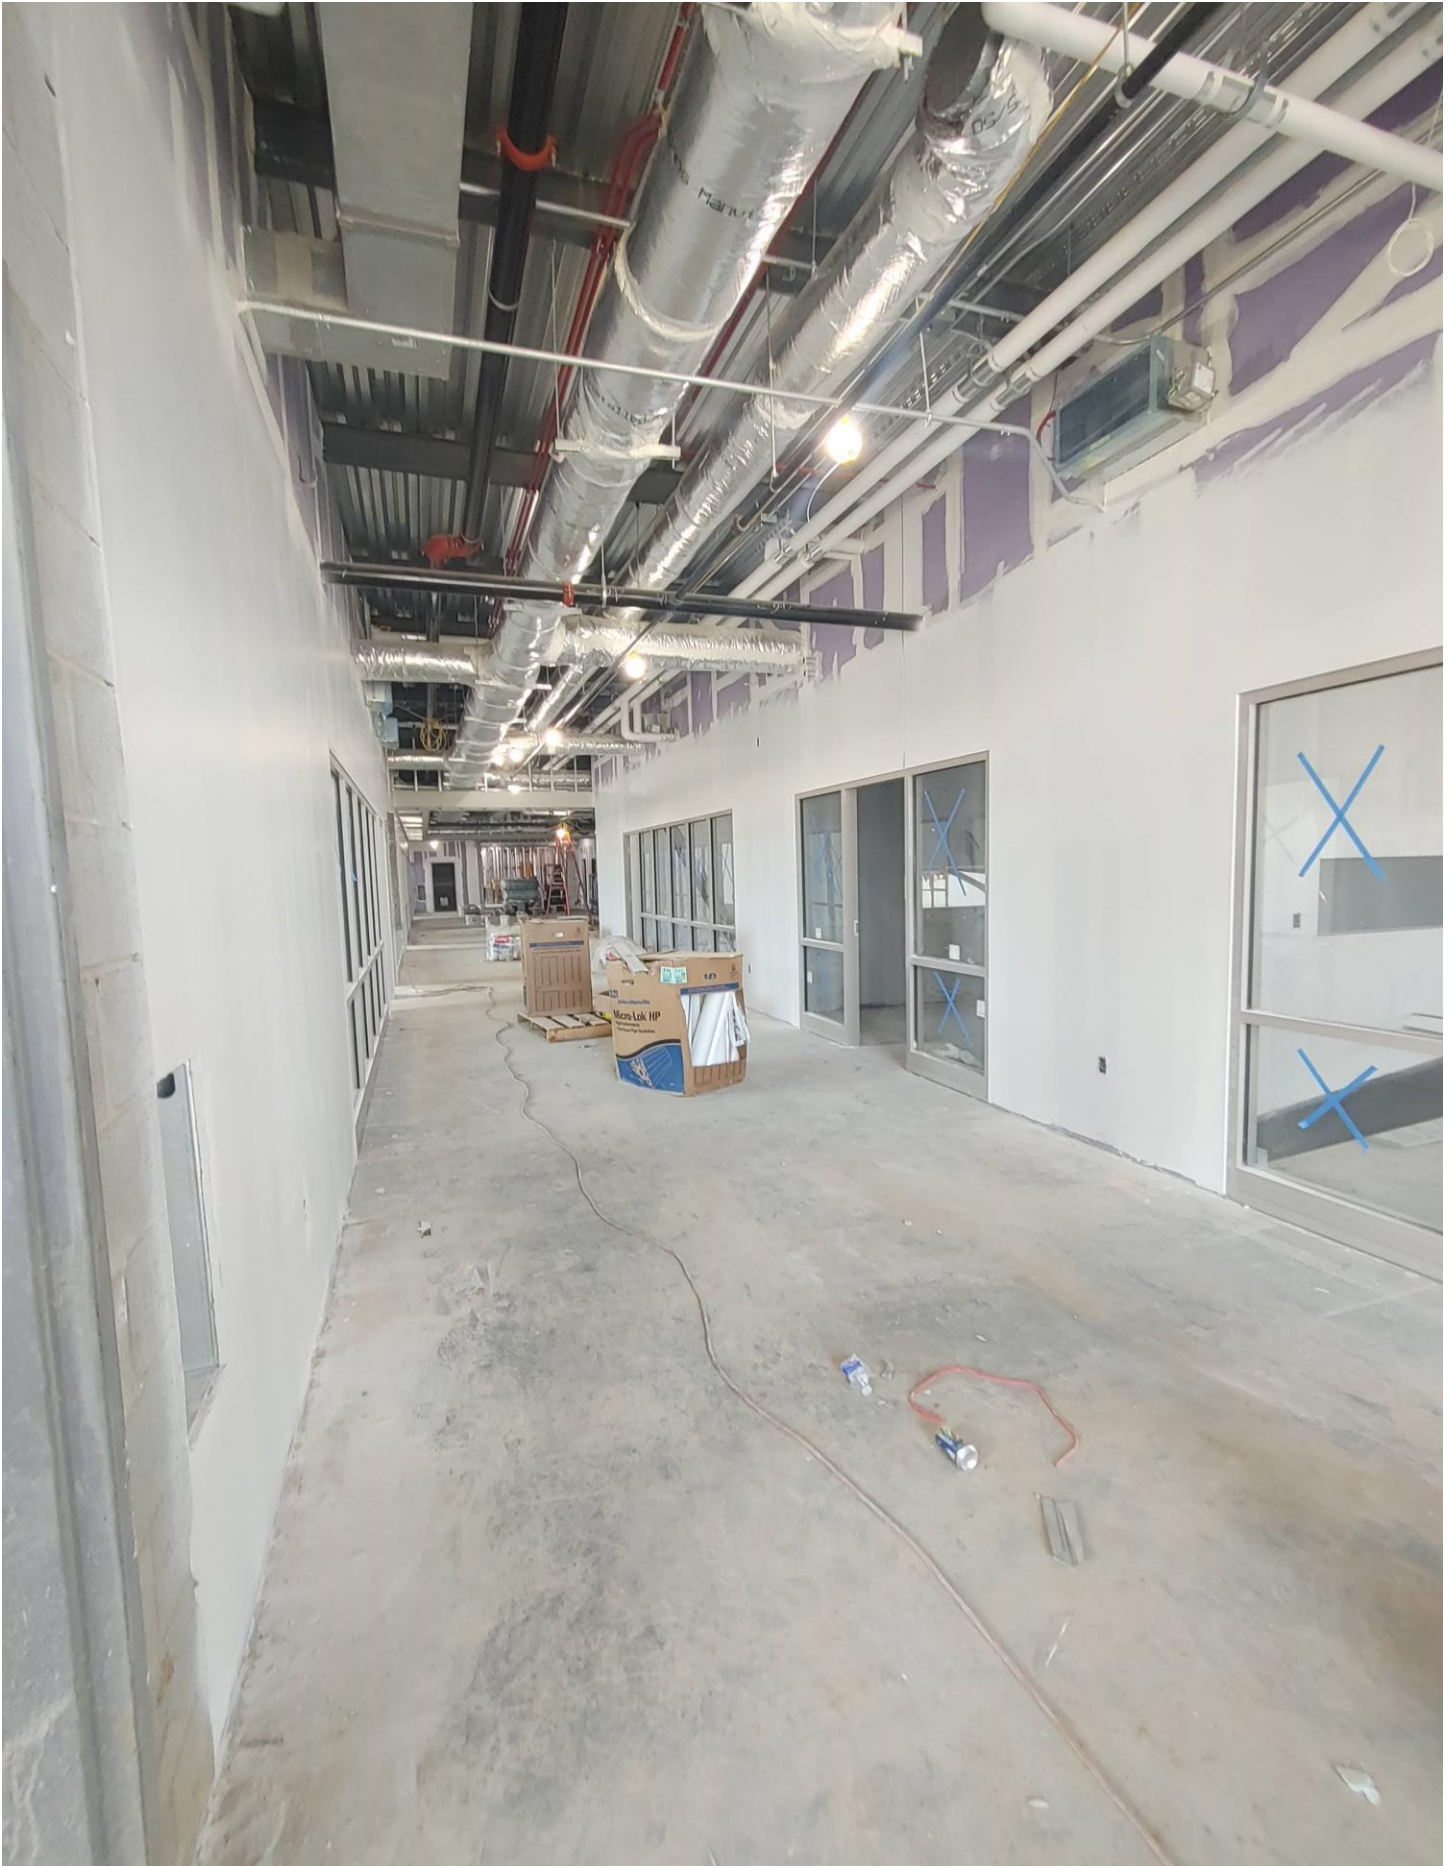


Photo 9 - Painters are priming Gyp board in Area B
