



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 06/30/2021

Weather: 86 degrees. Sunny. High of 95 degrees today.

Hours Worked: 10:00hrs – 12:00hrs (2hrs)

I walked the site and observed the work being performed.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Fourteen (14) men are on site today. They continue to lay block in Area D, in the Kitchen and in D103. One man is also laying precast on the West Side of Area C. They are also power washing brick on the South side of Area B.

**Hazzard Electric:** Thirteen (13) men are on site today. They continue to pull wire in Area A, B, C & D. One man continues to install Disconnects on H-frames on the roof of Area B. A couple of guys are installing conduit in the Kitchen ahead of the Mason. They are also setting Light Fixtures in Area A.

**Colonial Webb:** Twenty-one (21) are on site today. They are setting three rooftop units and installing Duct in Area D, Auditorium. A crew is also running pipe in D107.

**Weldon Steel:** Three (3) men are on site today. They continue to set Steel in the Auditorium.

**JP Construction:** Fifteen (15) men are on site today. They are hanging ceiling grid in Area A & B and working on roof blocking in Area C.

**AAR Roofing:** Five (5) men are on site today. They have begun to work on the high Roof of Area C.

**Tailored Foam:** Two (2) men are on site today and are up on the low roof of Area E spraying foam.

**FG & M:** Five (5) men are on site today. They continue to work on Curtain walls and are also prepping SF8 to be set.

**United Sprinkler:** Three (3) men are on site today. They are running Sprinkler pipe in Area D.

**CTSI:** Two (2) men are on site today pulling low voltage wire in various locations.

**M. L. Straight:** No one is on site today.

**S&S Concrete Cutting Company:** I did not observe anyone on site today during my visit.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes:** I did not observe a Tech on site today.

**Questions to or from Branch Builds:** I met with Brian Topper this morning. He advised me that the Crane was on site this morning setting three Roof Top HVAC Units and would also be setting the Chillers this morning. He also told me that he is targeting September 1<sup>st</sup> as the date to have all of the Construction Trailers moved off site.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. Follow-up Inspection Report received today from Emmett Philpy, DEQ.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs –**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



*Photo 1 - Two Roof Top Units have been set on the Roof of Area A*

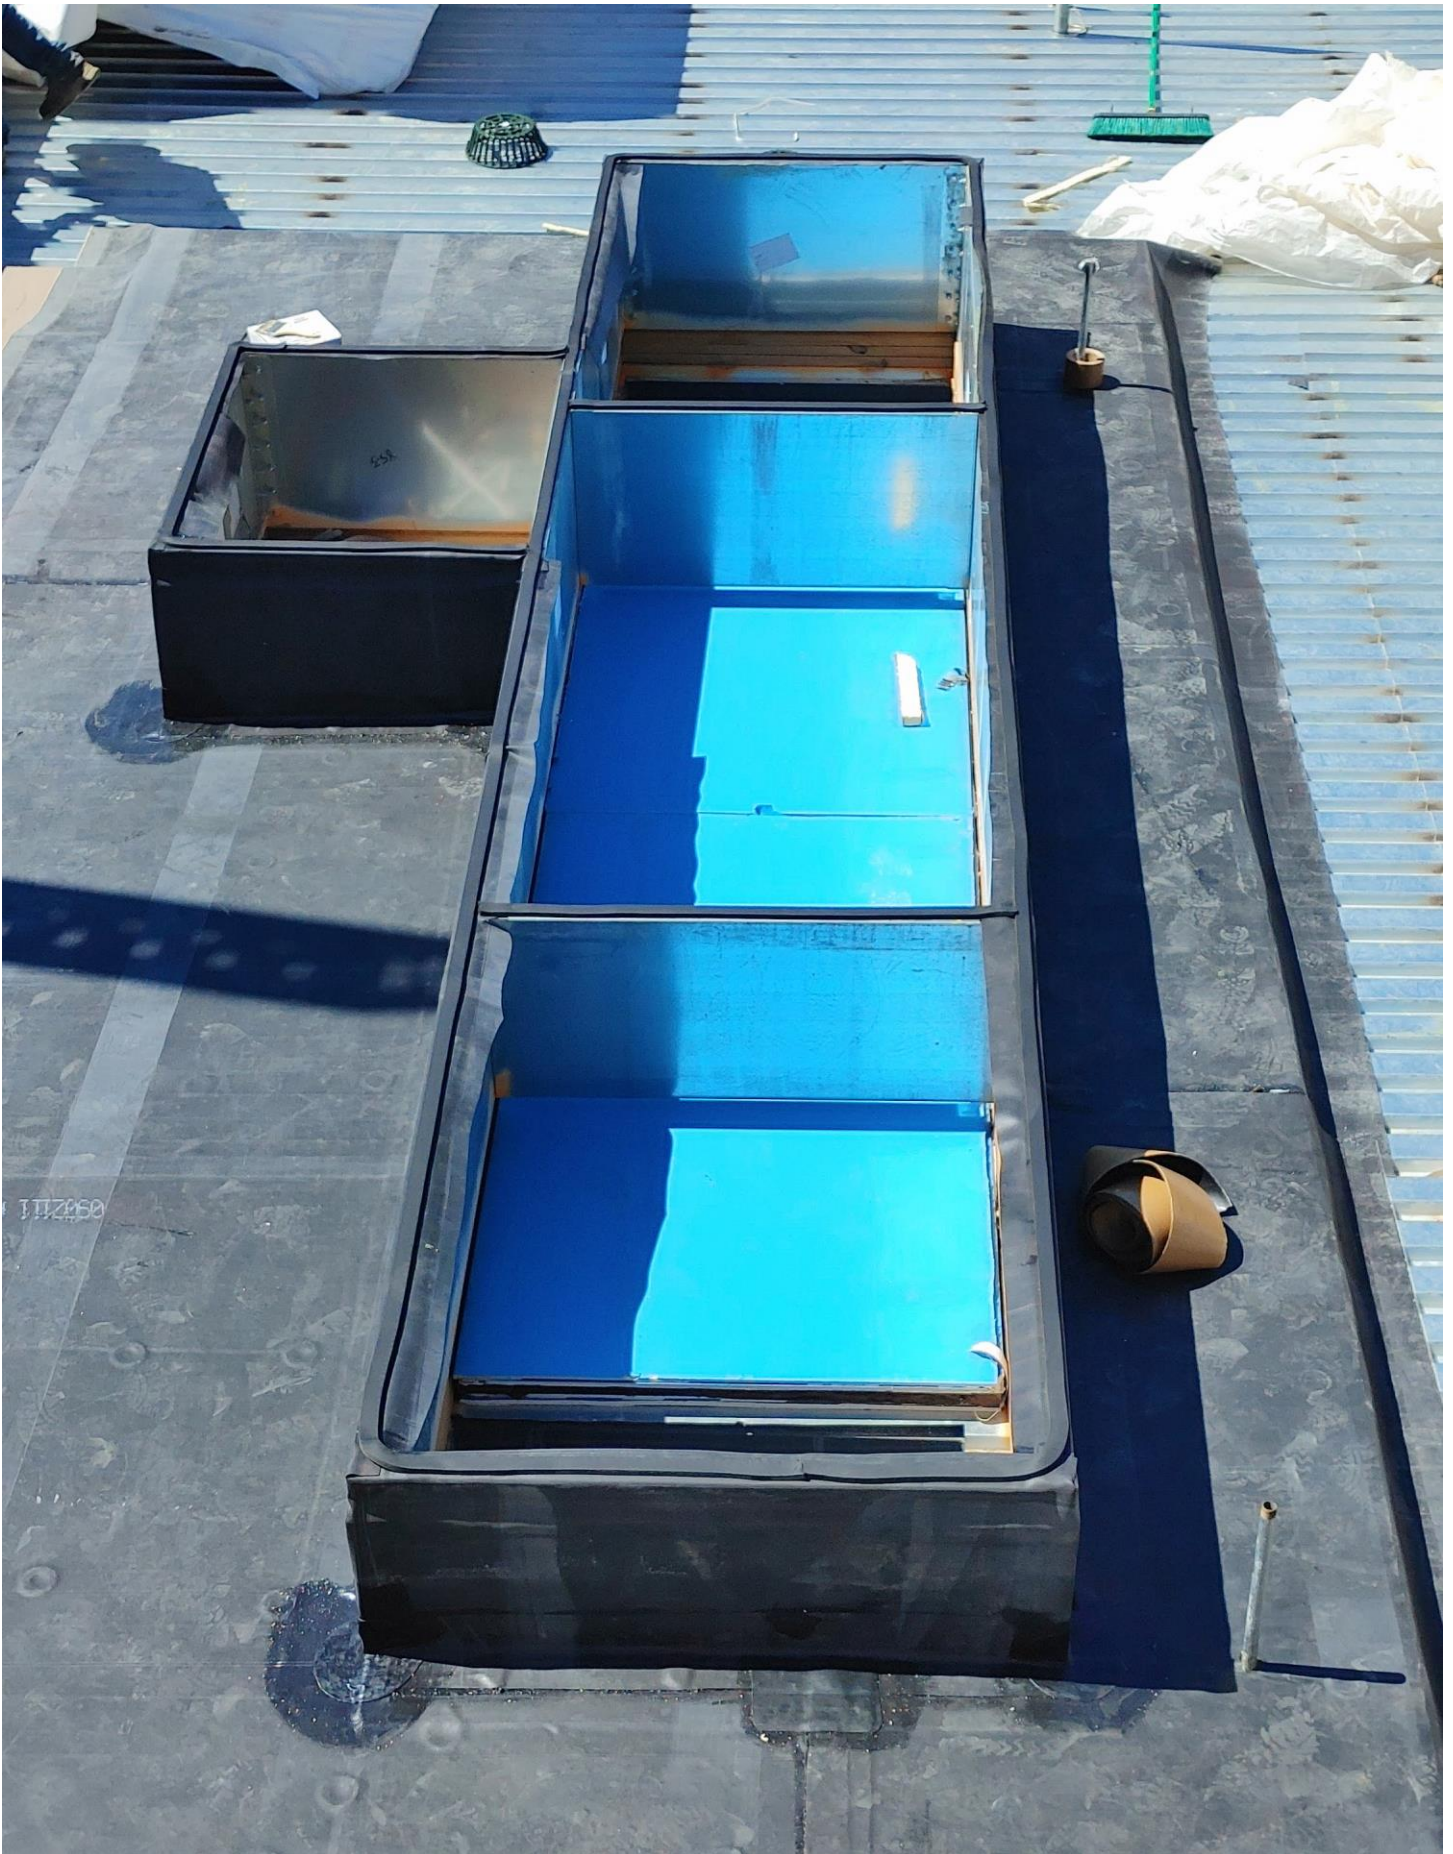


Photo 2 - Curb prepped to receive Rooftop HVAC Unit on the Low roof of Area D.



*Photo 3 - Roofers are working on the high roof of Area C.*



Photo 4 - SF8 opening being prepped.

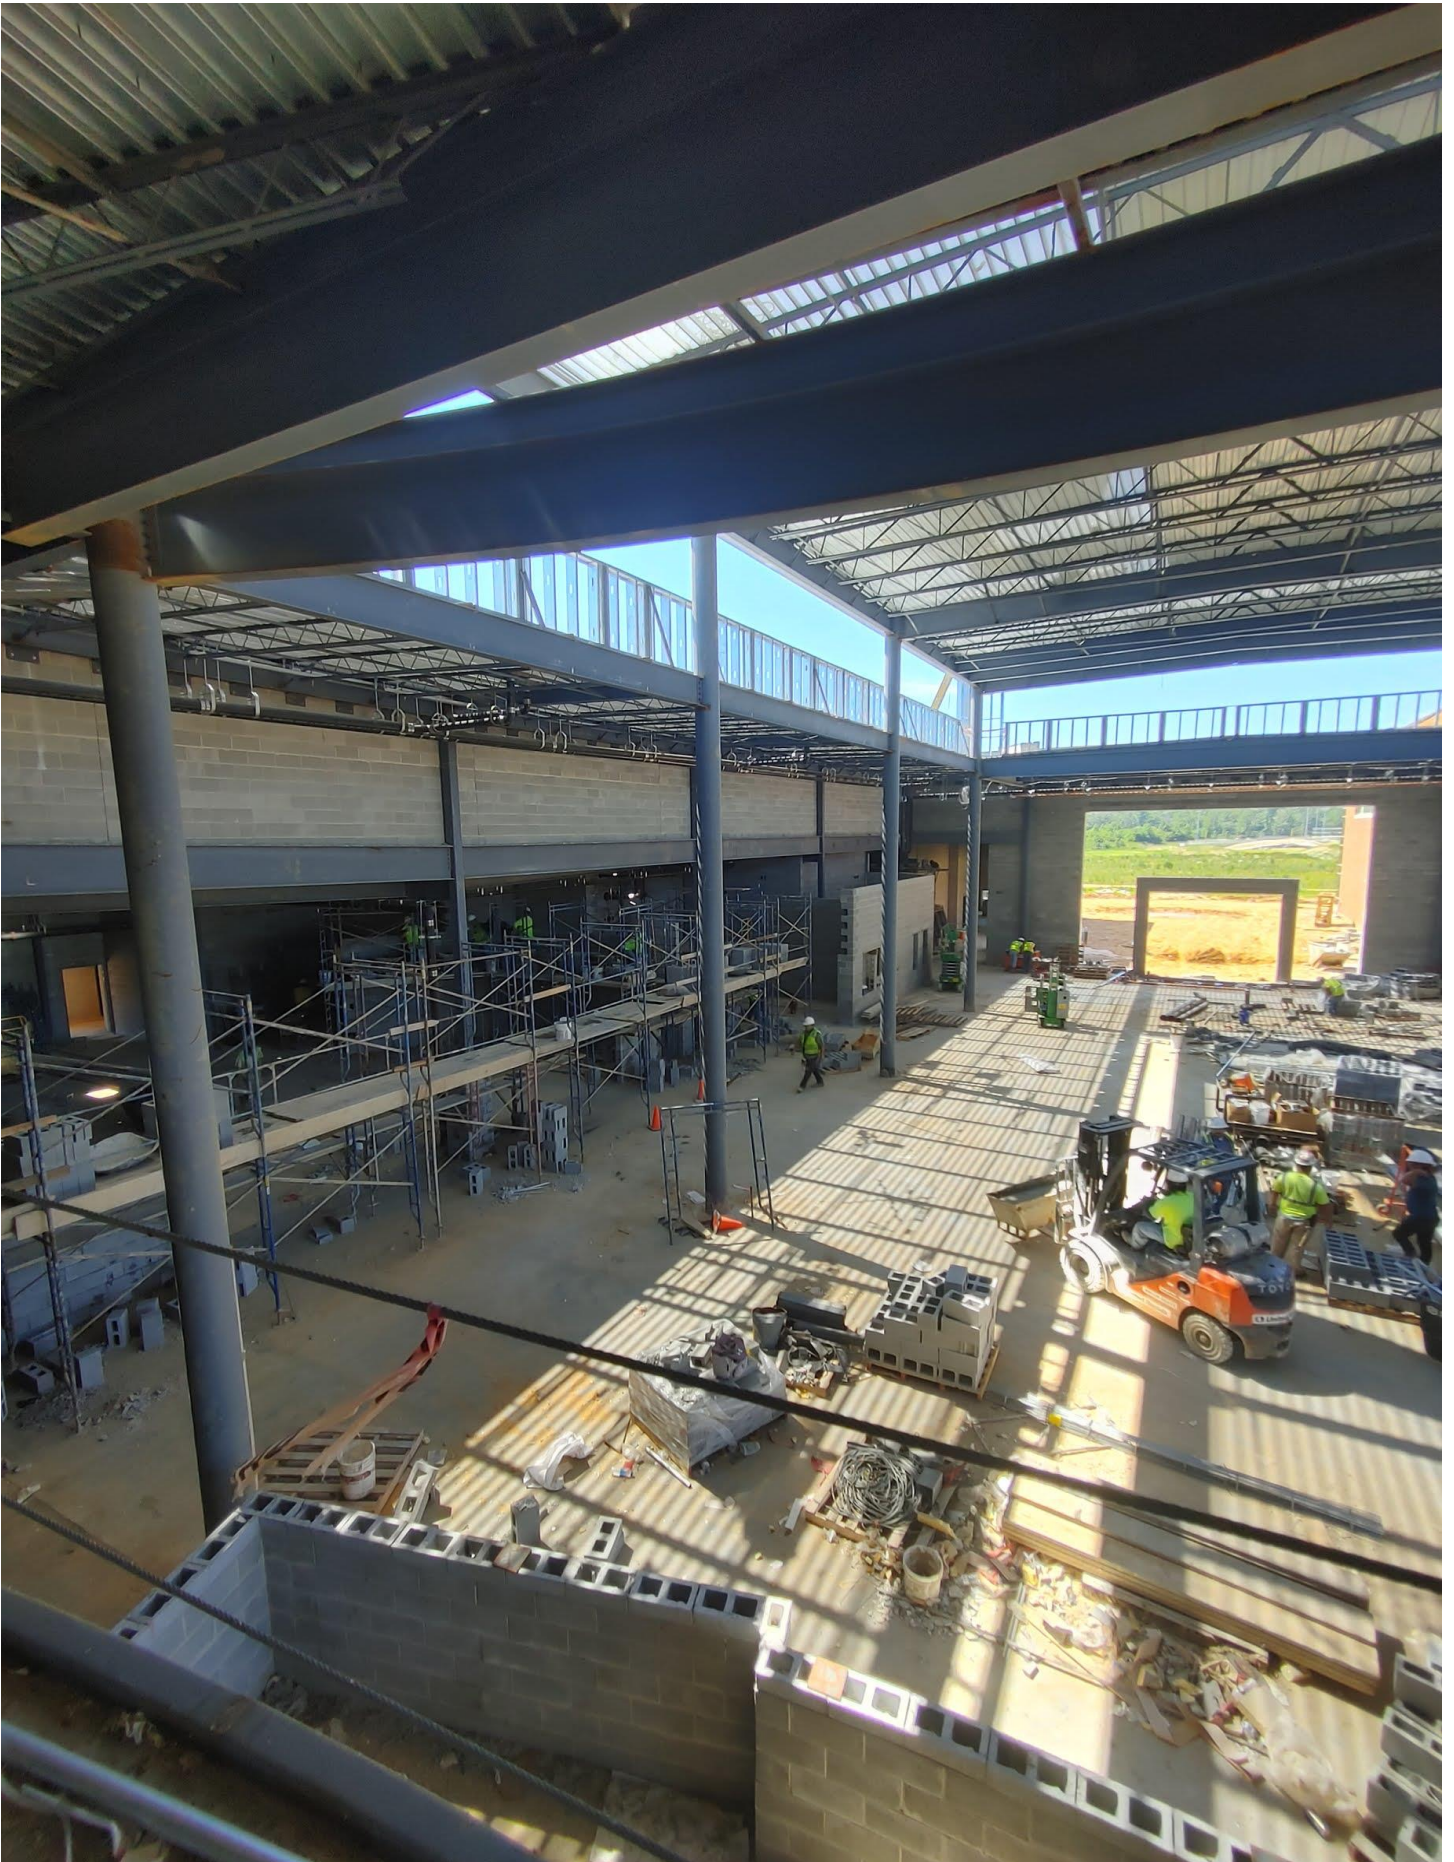


Photo 5 - Masons continue to lay block in the Kitchen



Photo 6 - Brick and Precast is being Power Washed on the South side of Area B.





Photo 7 - Steel is being set in the Auditorium.

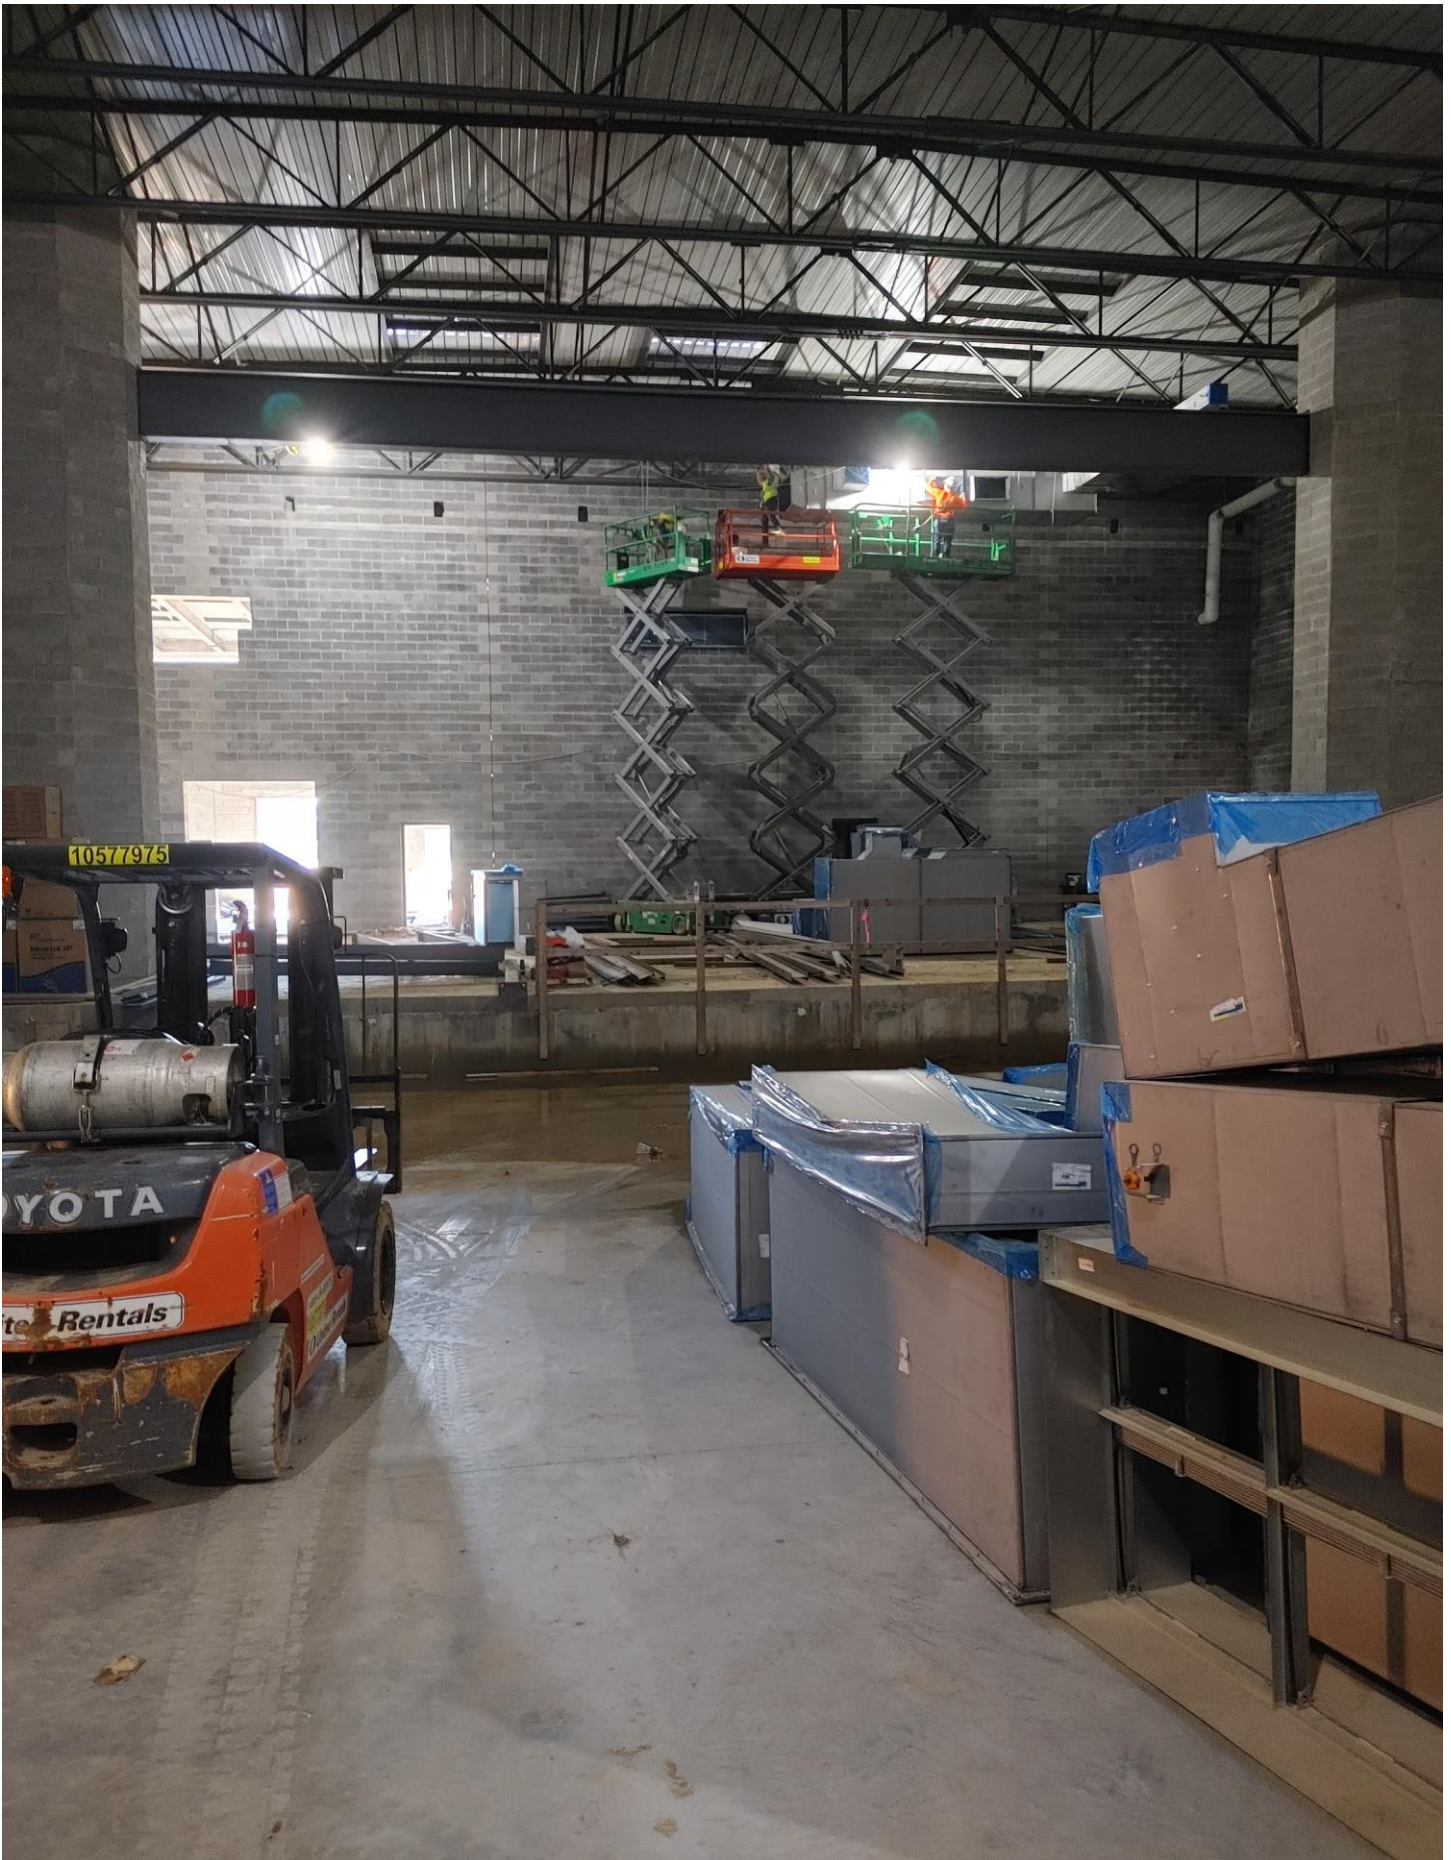


Photo 8 - HVAC Duct is being run above the Stage in the Auditorium.



Photo 9 - Roof Top HVAC Unit is being set on the low roof of Area D.



Photo 10 - One of two Chillers being set.
