



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West
Aylett, Virginia 23009
Phone: 804-761-4248
FrazierConsulting@gmail.com
Licensed Class A - RBC/CBC
DEPOR # 2705169996
EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 07/02/2021

Weather: 75 degrees. Mostly Cloudy. High of 79 degrees today. It rained last night and today. Site is muddy with water ponding in various locations.

Hours Worked: 13:00hrs – 14:30hrs (1.5hrs)

I walked the site and observed the work being performed. I did not visit the site yesterday July 1st, 2021.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Six (6) men are on site today. They continue to lay block in Area D, in the Kitchen.

Hazzard Electric: Thirteen (13) men are on site today. They continue to pull wire in Area A, B, C & D. They also continue to set Light Fixtures in Area A.

Colonial Webb: No one is on site today.

Weldon Steel: Three (3) men are on site today. They continue to set Steel in the Auditorium.

JP Construction: No one is on site today.

AAR Roofing: No one is on site today.

Tailored Foam: No one is on site today.

FG & M: Six (6) men are on site today. They continue to work on Curtain walls and are also are setting glass on the South side of Area B and the West side of Area C.

United Sprinkler: Two (2) men are on site today. They continue to run Sprinkler pipe in Area D.

CTSI: No one is on site today.

M. L. Straight: No one is on site today.

S&S Concrete Cutting Company: I did not observe anyone on site today during my visit.

Linear Surveyors: One man is on site today laying out the four column location on the South side of Area C.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: I met with Brian Topper and he advised me that the Chiller and Generator have been set. He said that many of the subs are off today. We spoke about the water ponding in front of the Construction Trailers. Branch was cited by DEQ for cutting a relief ditch into the retention pond behind the trailer. So, they filled in the ditch and now water ponds. Brian said he was going to send pictures to DEQ.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. Follow-up Inspection Report received today from Emmett Philpy, DEQ.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs – #289,

Patrick Byrne –

Change Order/PCOs/Pay App – PCCO #009

Changes in Procore –

Weekly Submittal Status Report – 07/02/2021

Weekly RFI Status Update – 07/02/2021

Weekly Daily Log Summary – 07/02/2021

PCO Log – 07/02/2021



Photo 1 - Chillers and Generator have been set



Photo 2 - FRACO has been set up on the South side of Area A

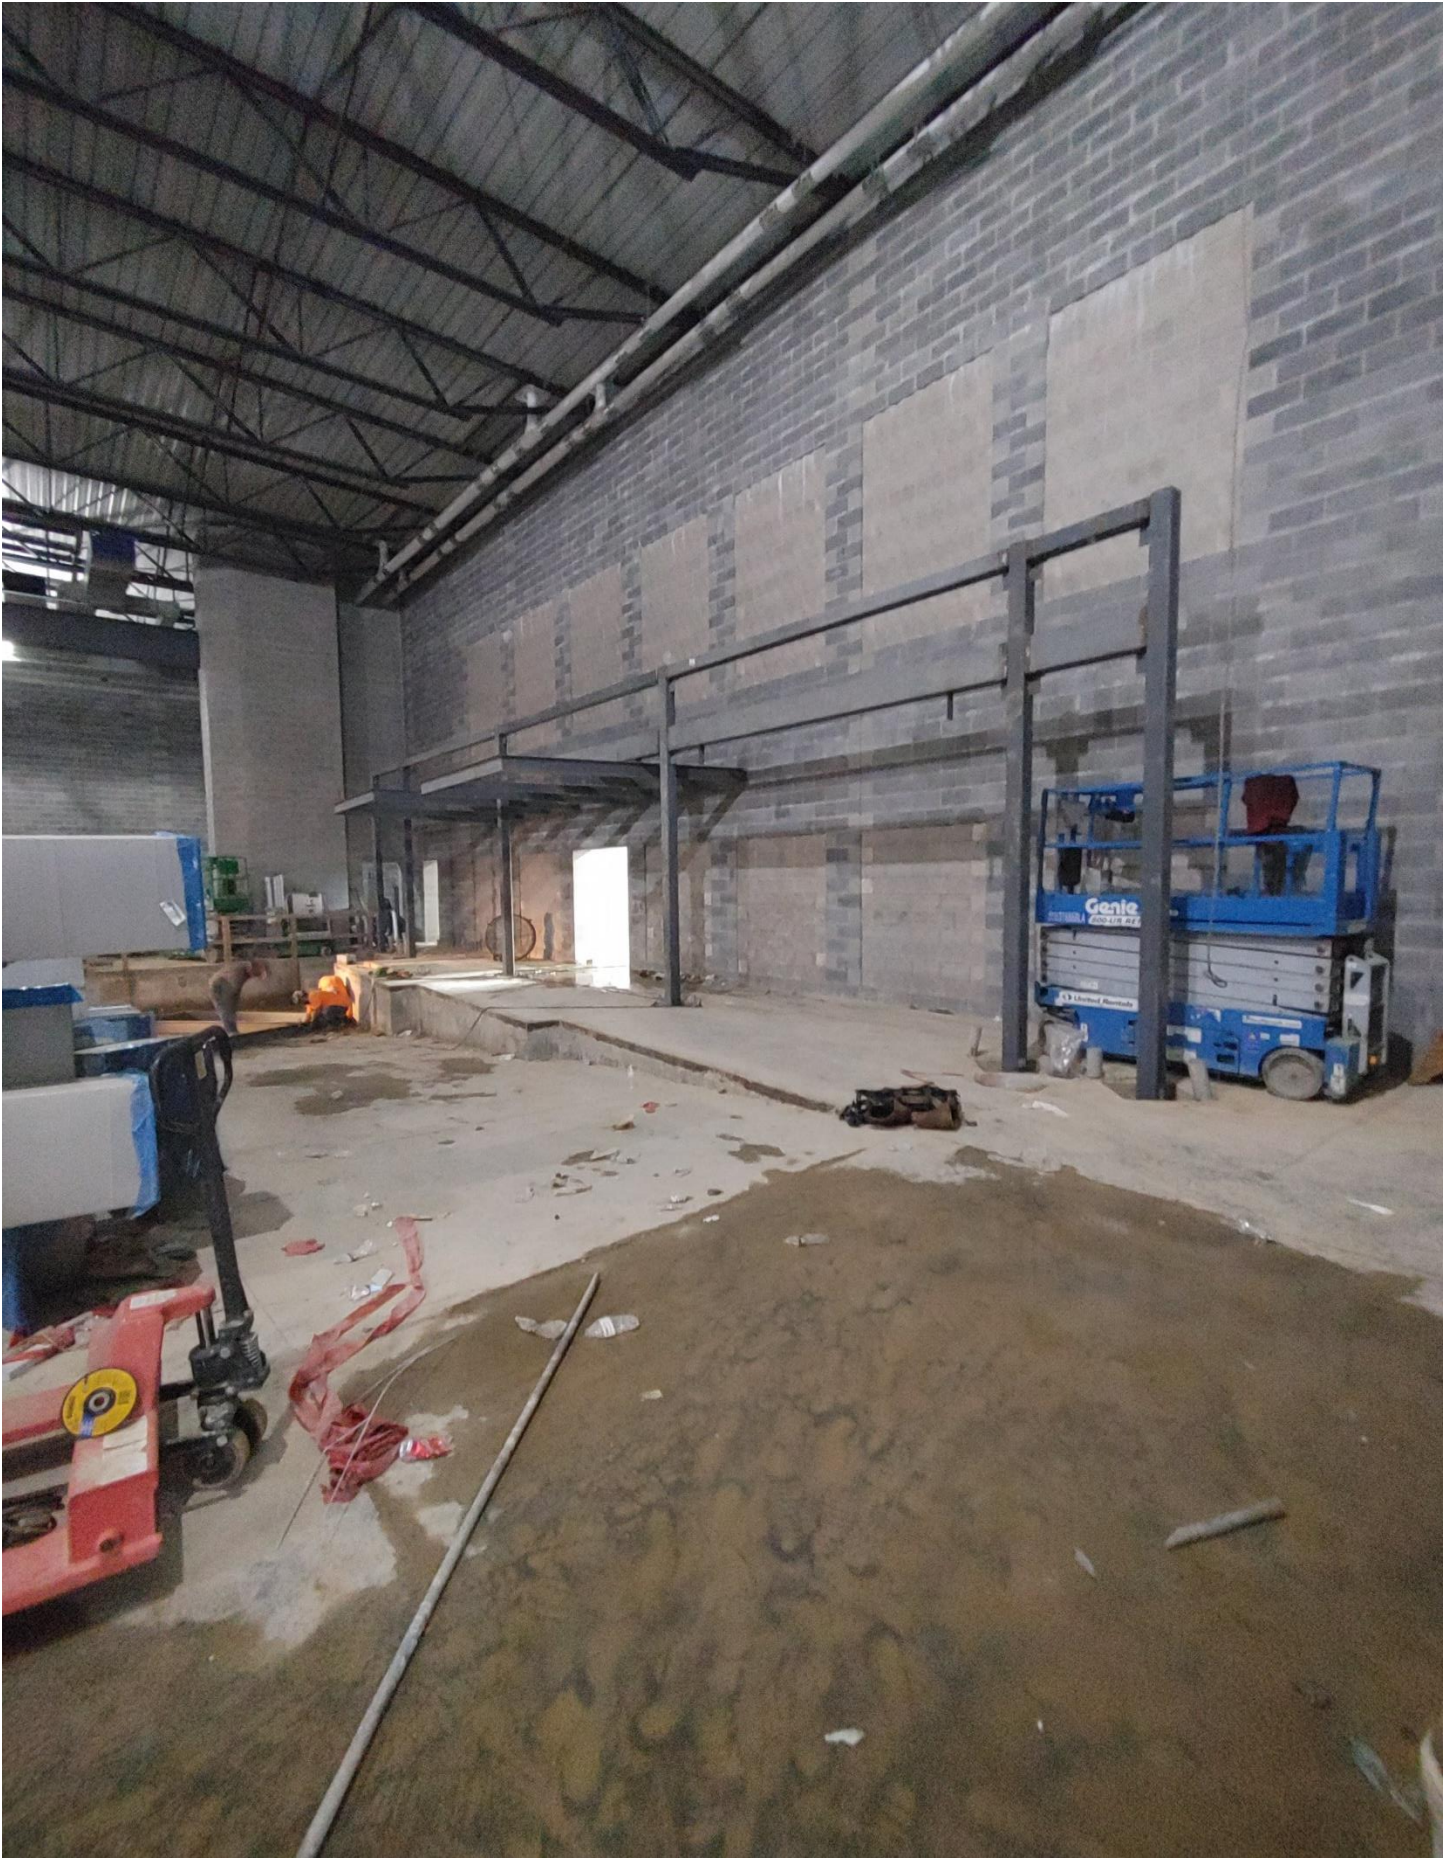


Photo 3 - Steel continue to be set in the Auditorium.



Photo 4 - Masons continue to lay block in the Kitchen



Photo 5 - Glass being set on the South side of Area B and the West side of Area C.



Photo 6 - Water is ponding in front of the Construction Trailers from the storms we received.
