



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 07/21/2021

Weather: 87 degrees. Sunny. High of 90 degrees today.

Hours Worked: 09:30hrs – 13:30hrs (4hrs)

I walked the site and observed the work being performed. I did not visit the site yesterday. I attended the 11:00hrs Progress meeting today at Norm's Conference Room.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Twelve (12) men are on site today. They are also laying block in Area C and also in Area E pipe chases.

Hazzard Electric: Eleven (11) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D. Three men are working on the Conduit Bank to the Transformer and Generator.

Colonial Webb: Sixteen (16) men are on site. They continue to run Duct and insulating pipe in Area D. A crew is also running and insulating duct & pipe in Area A.

Weldon Steel: No one is on site today.

JP Construction: Twenty-three (23) men are on site today. They are installing insulation and hanging & finishing sheetrock in Areas A & B, Framing metal studs in Area A and installing Acoustical Ceiling grid in Area B. They are also off-loading and staging sheetrock in Area C.

AAR Roofing: Six (6) men are on site today. They continue to work on the roof above the Kitchen in Area C.

Tailored Foam: No one is on site today.

FG & M: Five (5) men are on site today. They are working on Curtain Wall #9 on the North side of Area A.

United Sprinkler: Three (3) men are on site today. They are running pipe in Area D.

CTSI: Three (3) men are on site today running low voltage wire throughout the site.

M. L. Straight: Three (3) men are on site today painting and back rolling in Areas D and B.

K-Plus: One (1) man is here caulking control joints in area E.

S&S Concrete Cutting Company: I did not observe anyone on site today during my visit.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: Met with Todd this morning upon arriving on site. We discussed the time line for the Parking lot and the removal of the office trailer. I told him I would have my office moved by August 31, 2021. We also discuss today Progress meeting and the 12" Water line.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs – #291

Patrick Byrne –

Change Order/PCOs/Pay App – PCO #43 – PR #18 Book Storage Rooms Revisions

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Curtain Wall #9 going up.

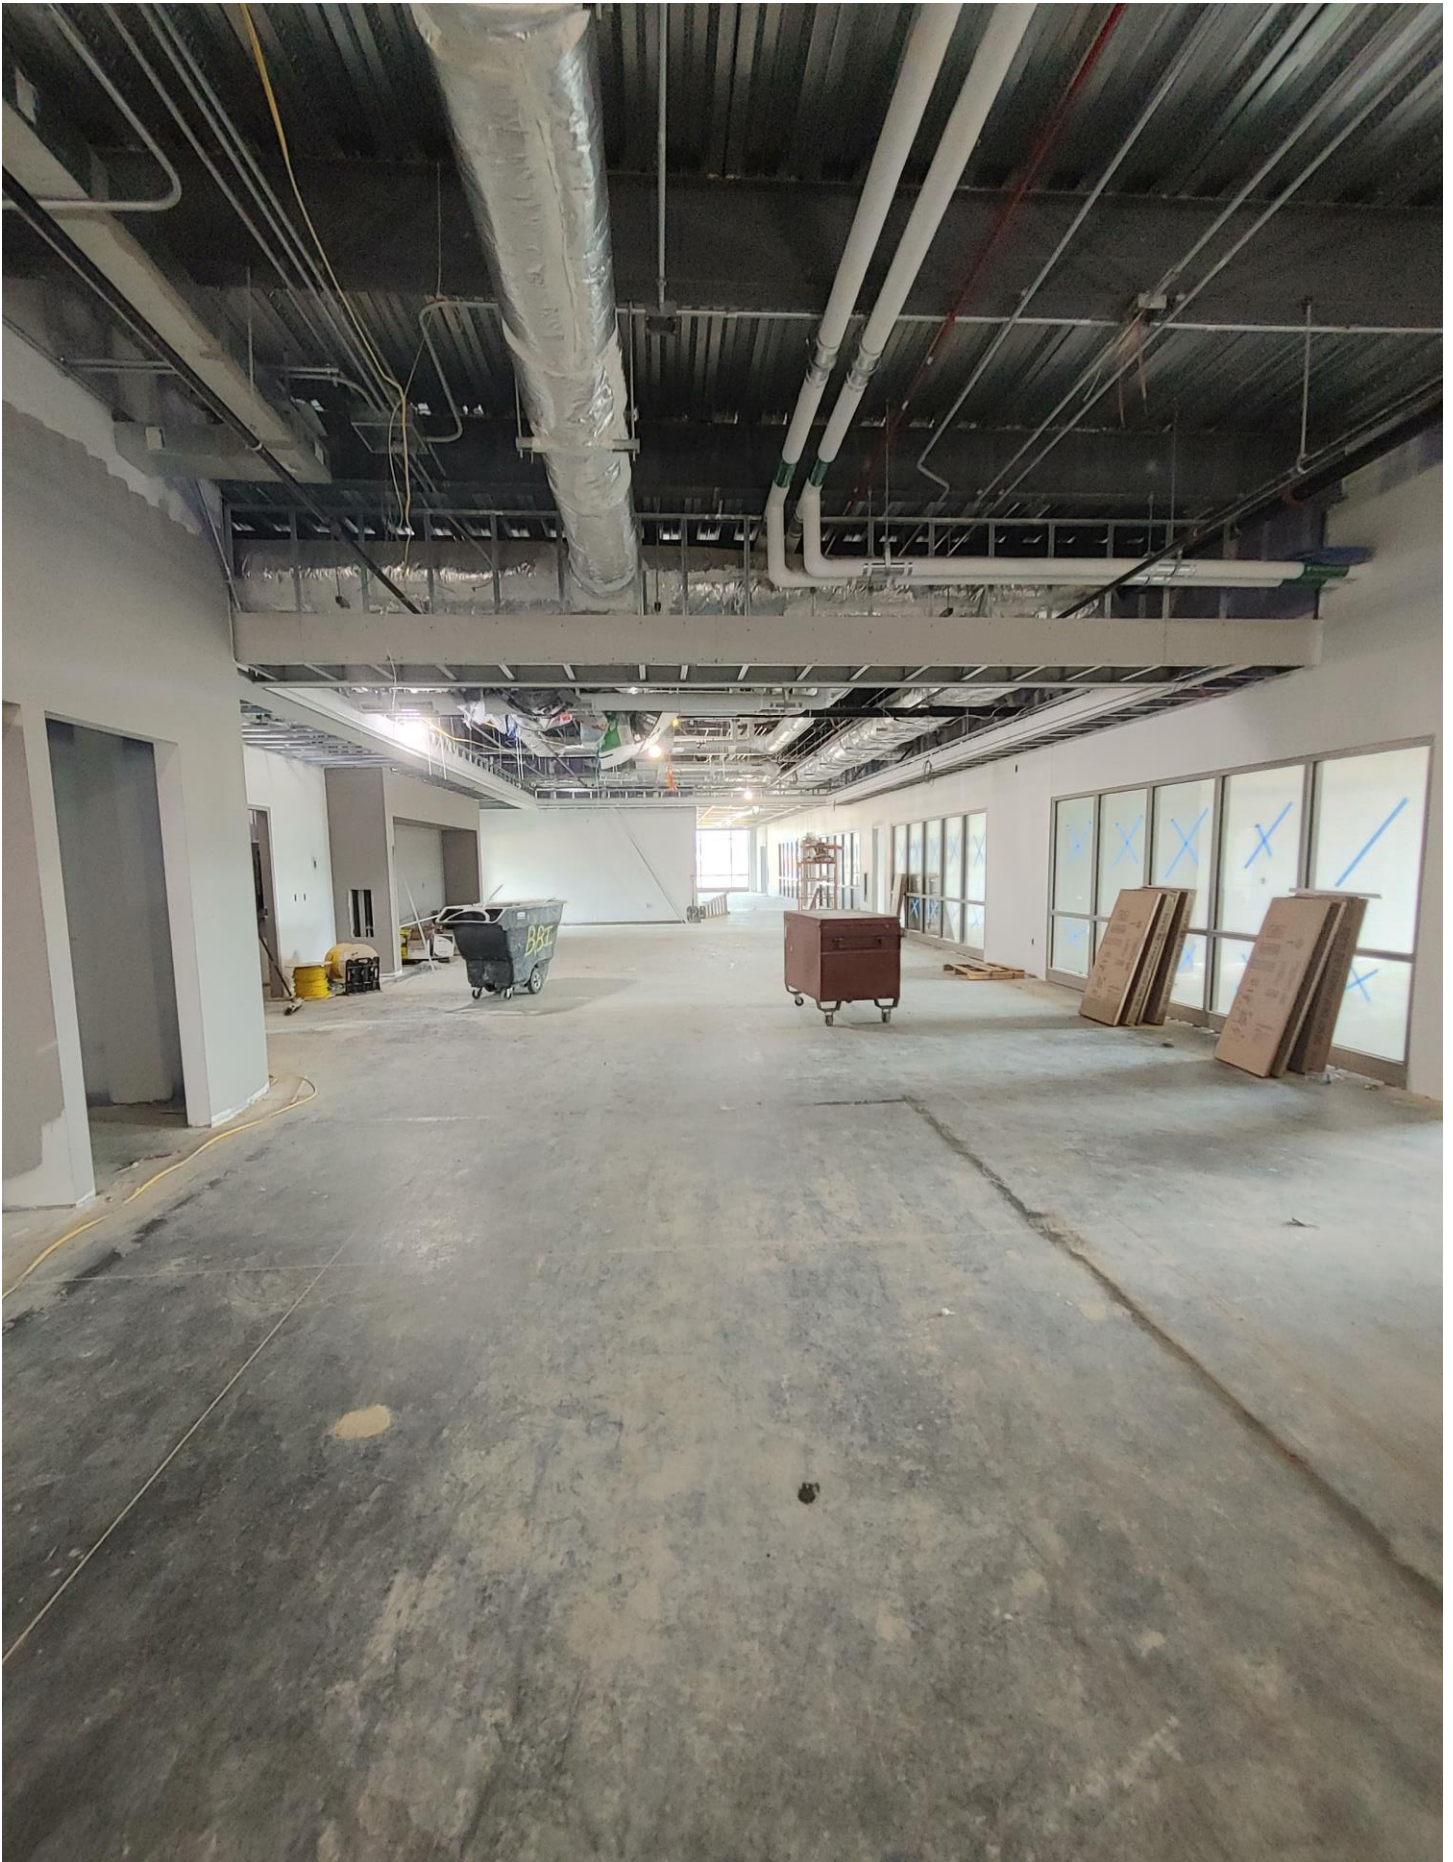


Photo 2 - Bulk Head completed in Area B



Photo 3 - Area in the North East Corner of Area A, Administrative Offices that still needs to be poured.



Photo 4 - Diffusers continue to be installed in Area A.



Photo 5 - Cement Board is being hung in rooms A216 & A218

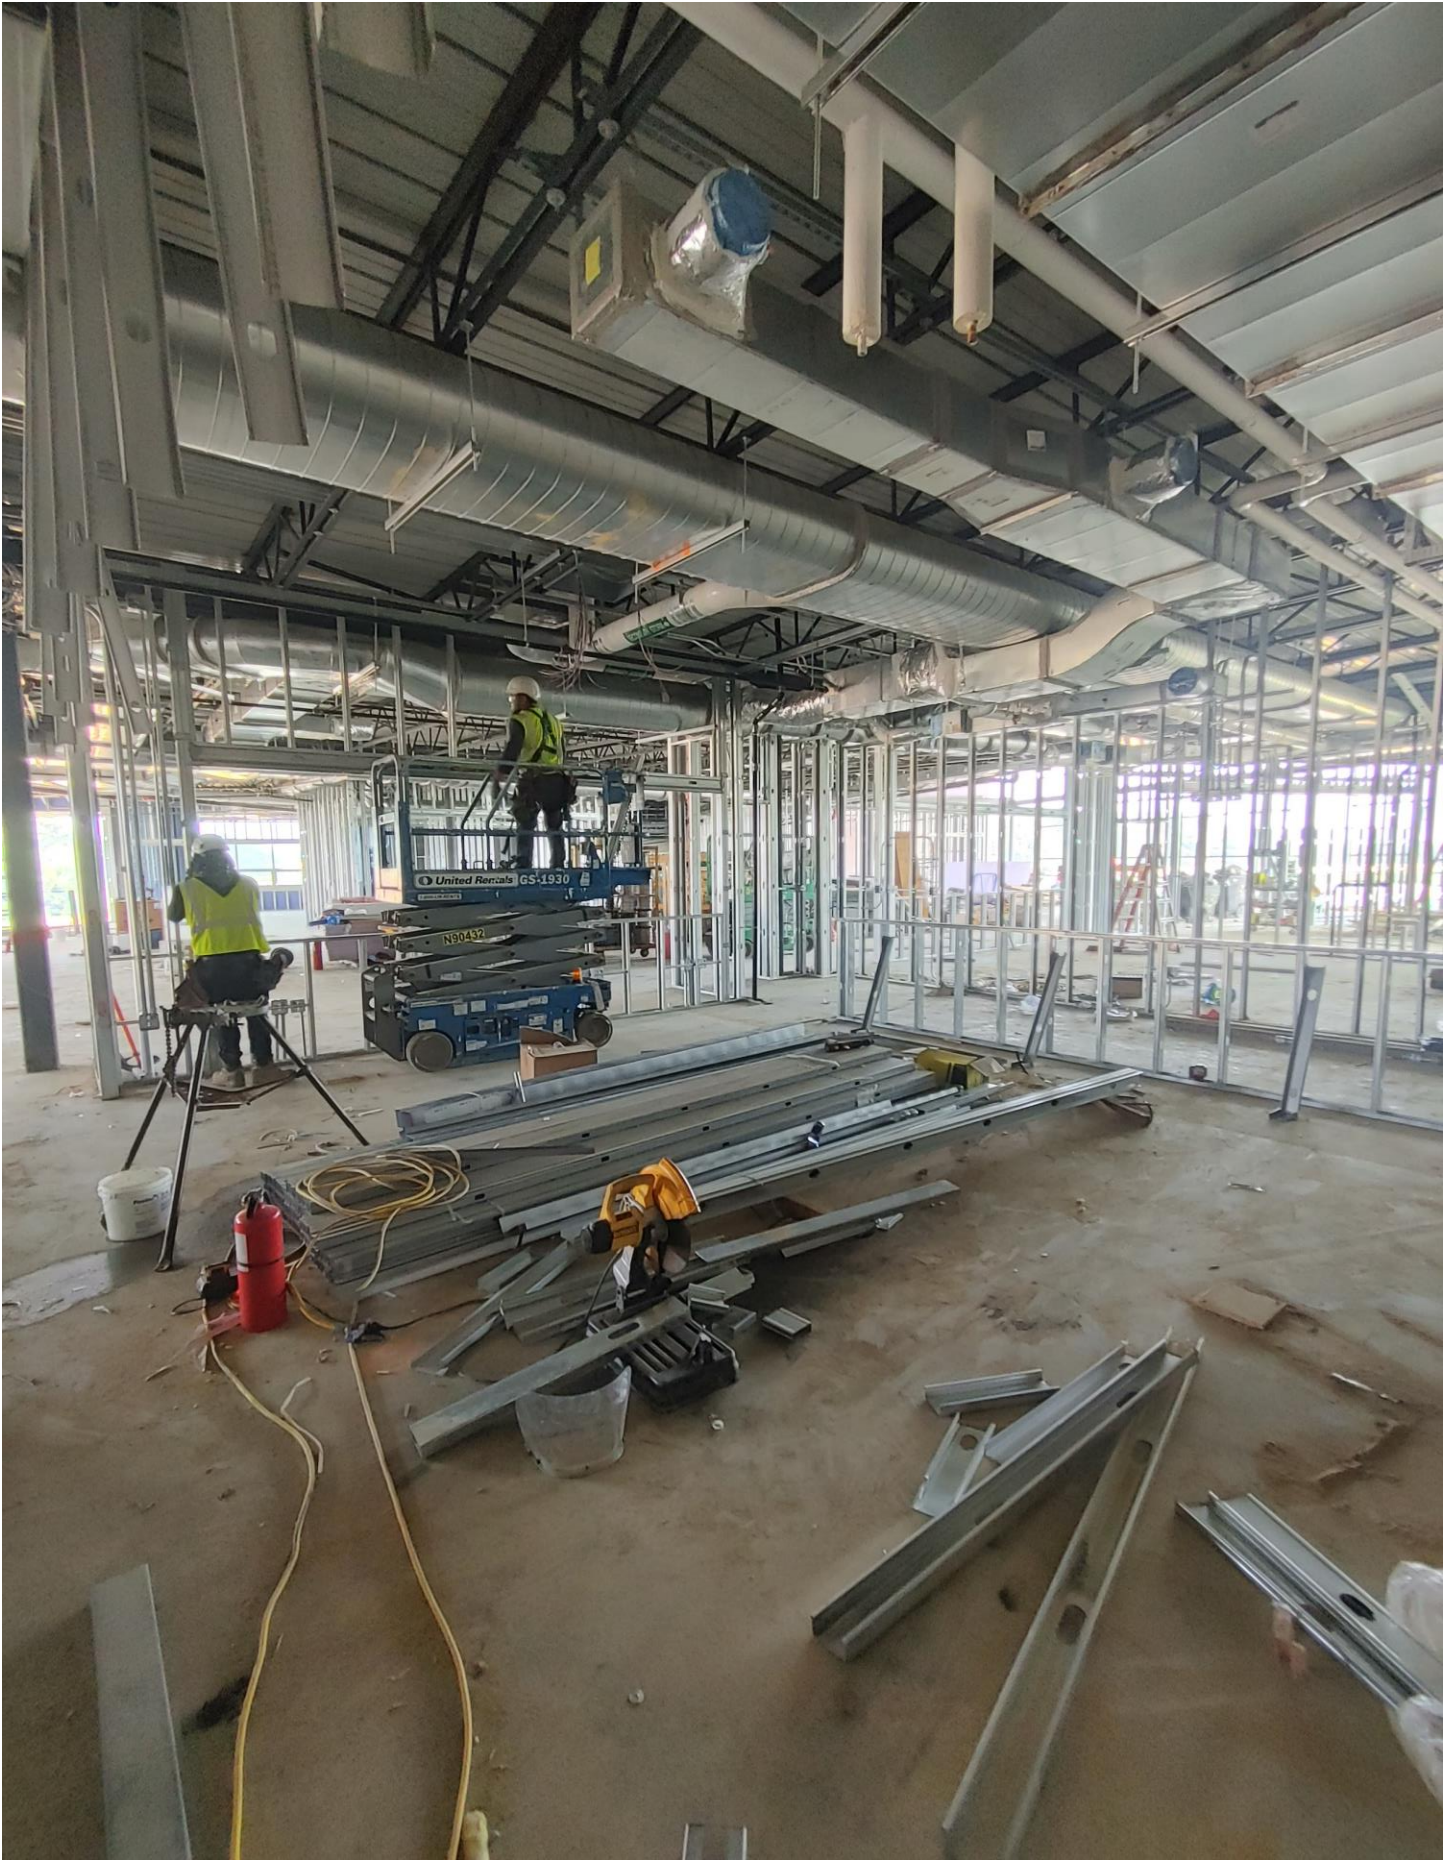


Photo 6 - Walls are being framed on the 2nd floor of Area A



Photo 7 - Curtain Wall #9 being installed.



Photo 8 - Bulkhead being constructed on the 2nd floor of Area B



Photo 9 - Door frames are being primed in Area B



Photo 10 - Roofers continue to work on the roof above the Kitchen.



Photo 11 - Masons are laying block around door frame #E13.

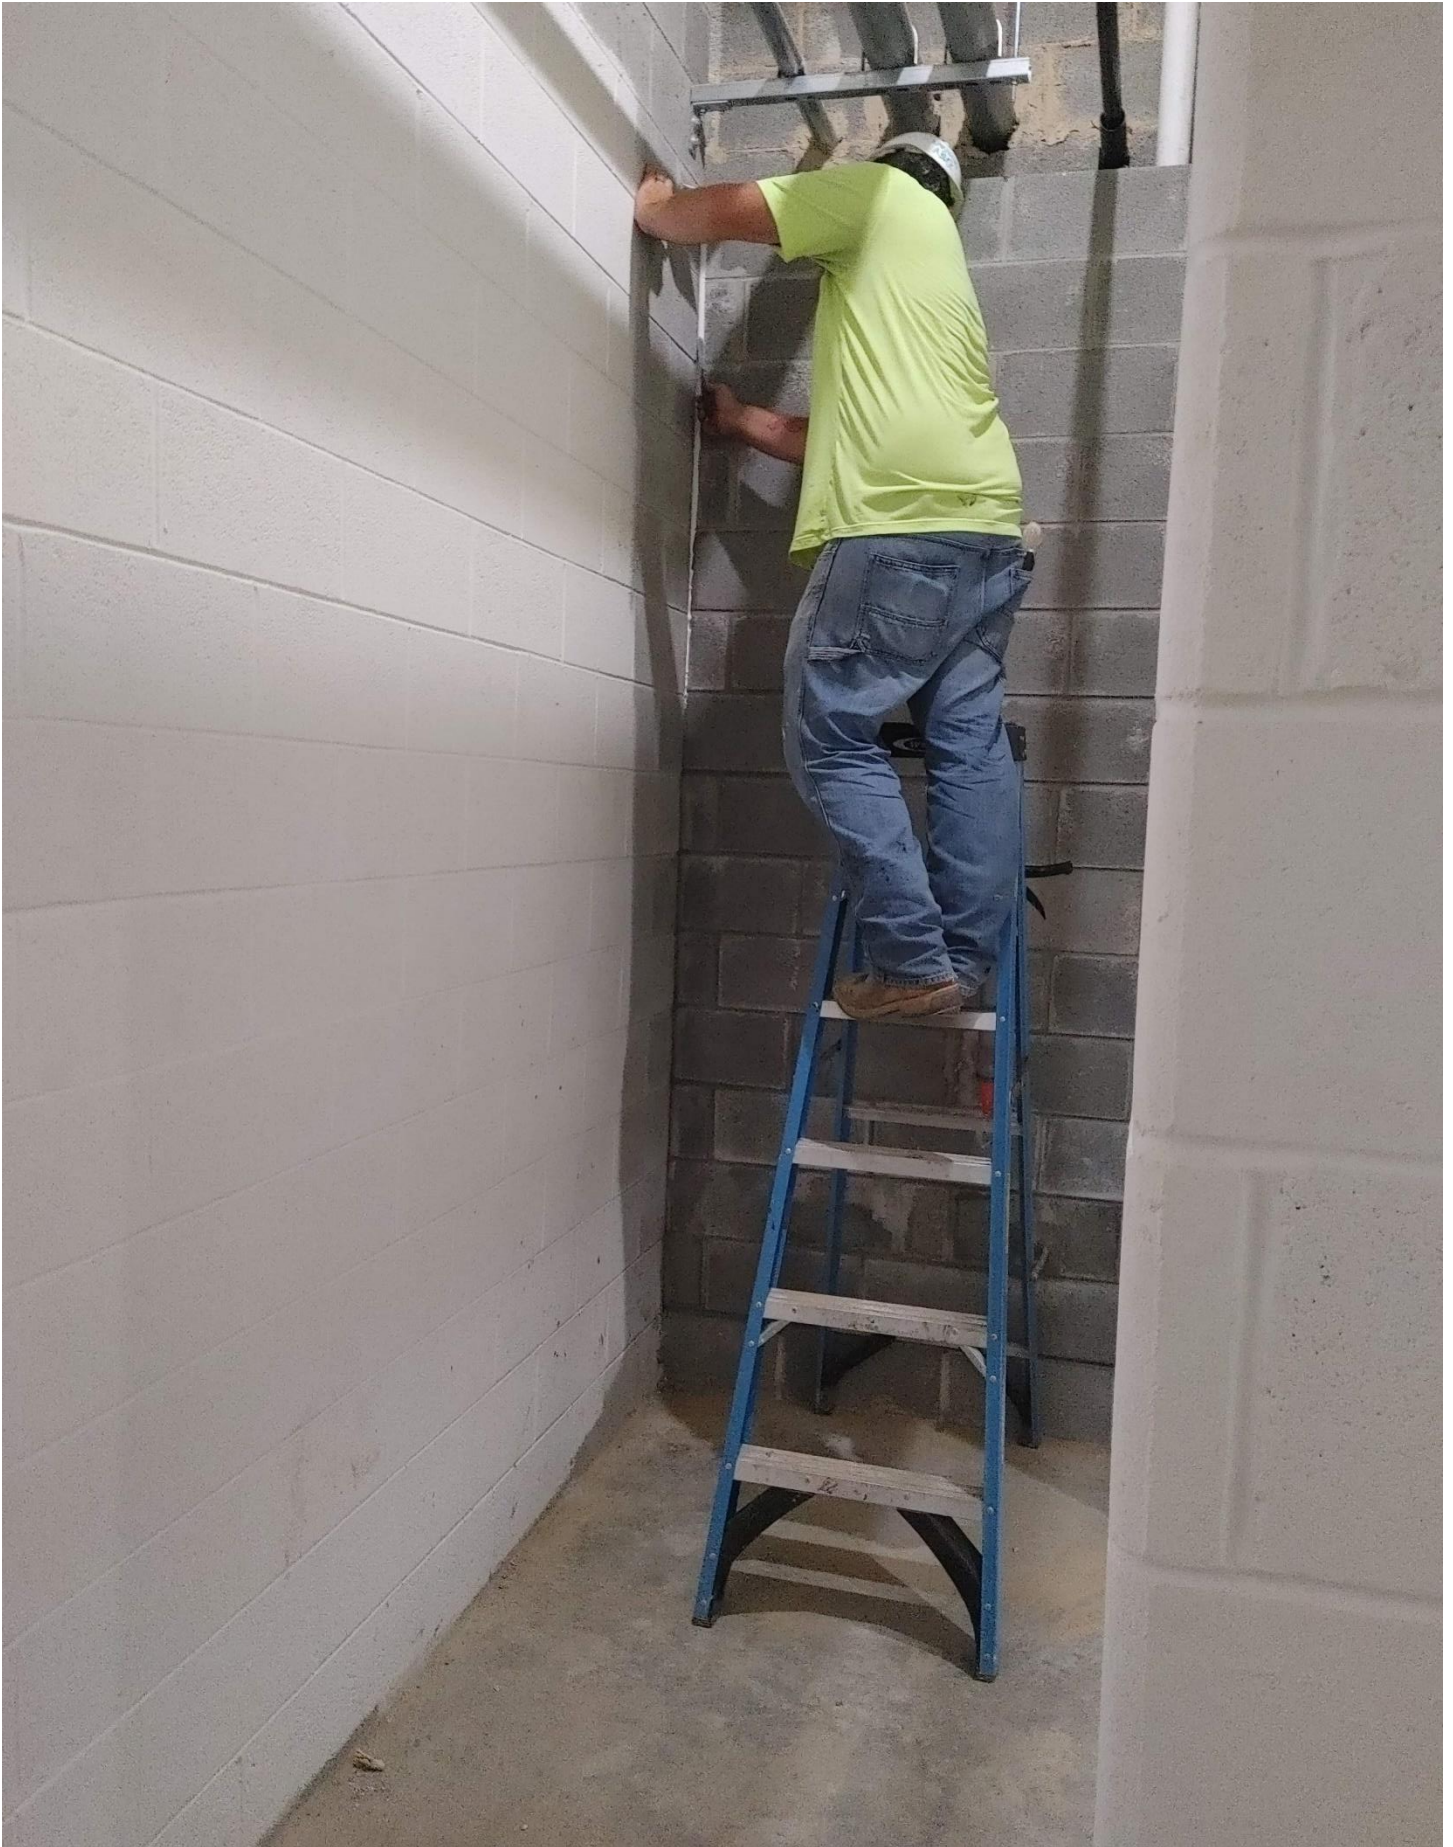


Photo 12 - Control Joints being caulked in Area E.



Photo 13 - HVAC Duct continues to be installed in the Auditorium.

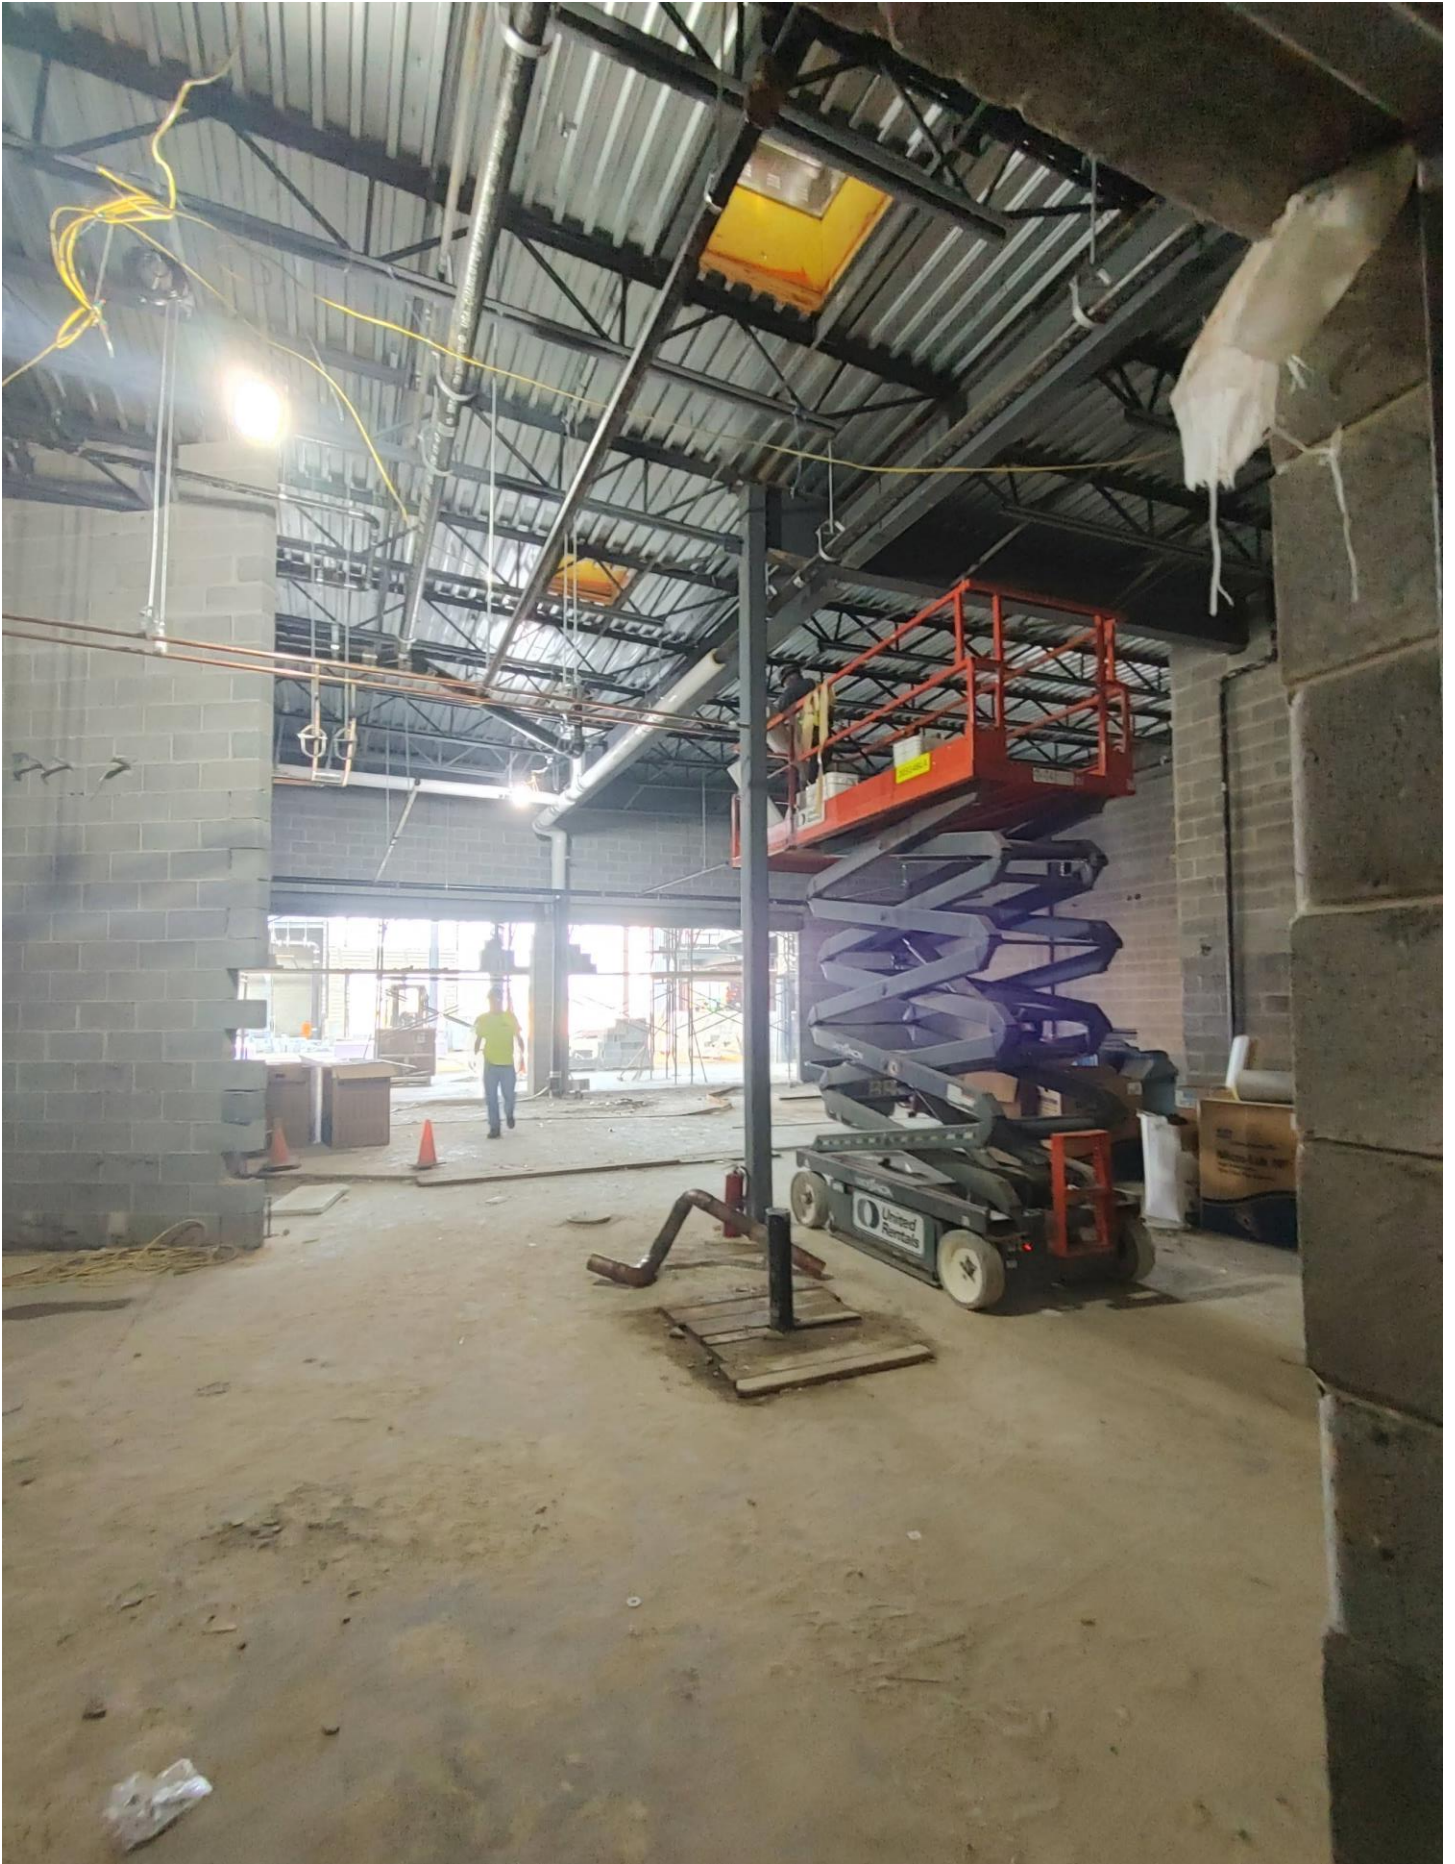


Photo 14 - Pipe being insulated in the Kitchen.
