



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 08/06/2021

Weather: 87 degrees. Sunny. High of 90 degrees today.

Hours Worked: 13:00hrs – 15:00hrs (2hrs)

I walked the site and observed the work being performed. Very few people are on site today.

**Beuchert Excavation:** Is on site today working on Retention Pond #1.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Are on site today. They are laying block in Area C for Curtain Wall #2 and in Corridor E11 for SF48 and for E11A & E11B. They are also staging block and scaffolding to lay the Chase Wall in D122.

**Hazzard Electric:** They continue to pull wire and run conduit in Area A, B, C & D. They are also working on the lights outside the front Main Entrance.

**Colonial Webb:** No one is on site.

**Weldon Steel:** No one is on site today.

**JP Construction:** No one is on site

**AAR Roofing:** No one is on site.

**Tailored Foam:** No one is on site today.

**FG & M:** No one is on site.

**United Sprinkler:** They are on site today running pipe in Area D.

**CTSI:** They are here today running low voltage wire throughout the site.

**M. L. Straight:** No one is on site.

**K-Plus:** No one is here today.

**S&S Concrete Cutting Company:** I did not observe anyone on site today during my visit.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe a Tech on site today.

**Questions to or from Branch Builds:** Brian Topper took off today and Monday of next week. I met with Jake in the trailer. Jake said not much was happening today.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) – 07/30/2021, 08/04/2021**

**Submittals – #03 30 00-2.5, #08 44 13-3.0**

**RFIs – #295, #296, #297**

**Patrick Byrne –**

**Change Order/PCOs/Pay App – July Pay App, PCO #56**

**Changes in Procore –**

**Weekly Submittal Status Report – 08/06/2021**

**Weekly RFI Status Update – 08/06/2021**

**Weekly Daily Log Summary – 08/06/2021**

**PCO Log – 08/06/2021**



*Photo 1 - Electricians are installing exterior lighting fixtures in Area A*



Photo 2 - They have begun to install Ceiling tiles in Area A



Photo 3 - The Masons have laid the block for Curtain Wall #2 in Area C.



Photo 4 - Beuchert is working on the Retention pond on the West Side of the property

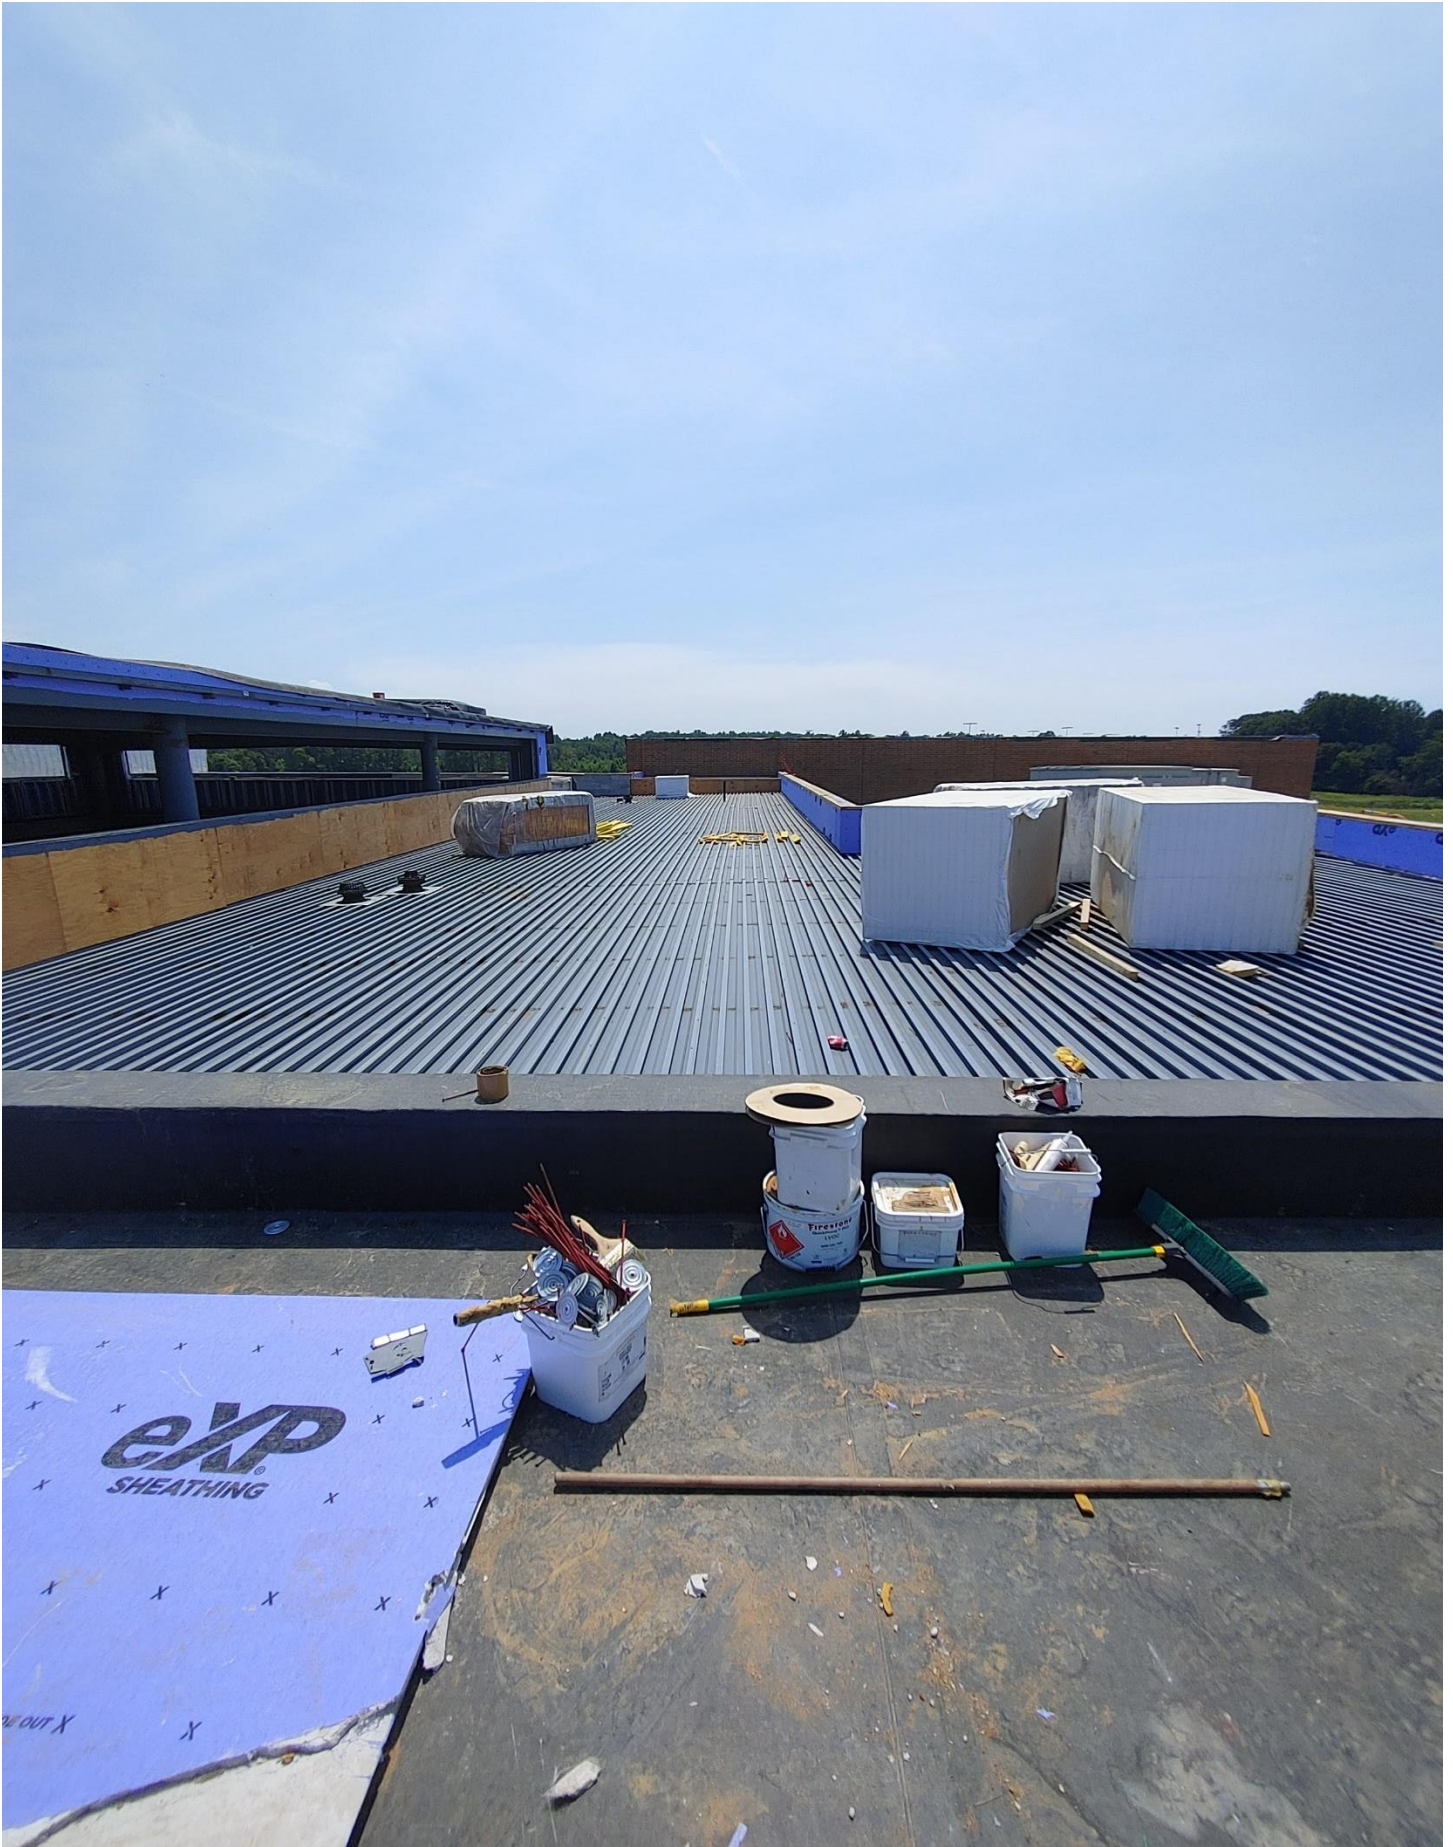


Photo 5 - The Roofer has not completed the Roof in Area C.

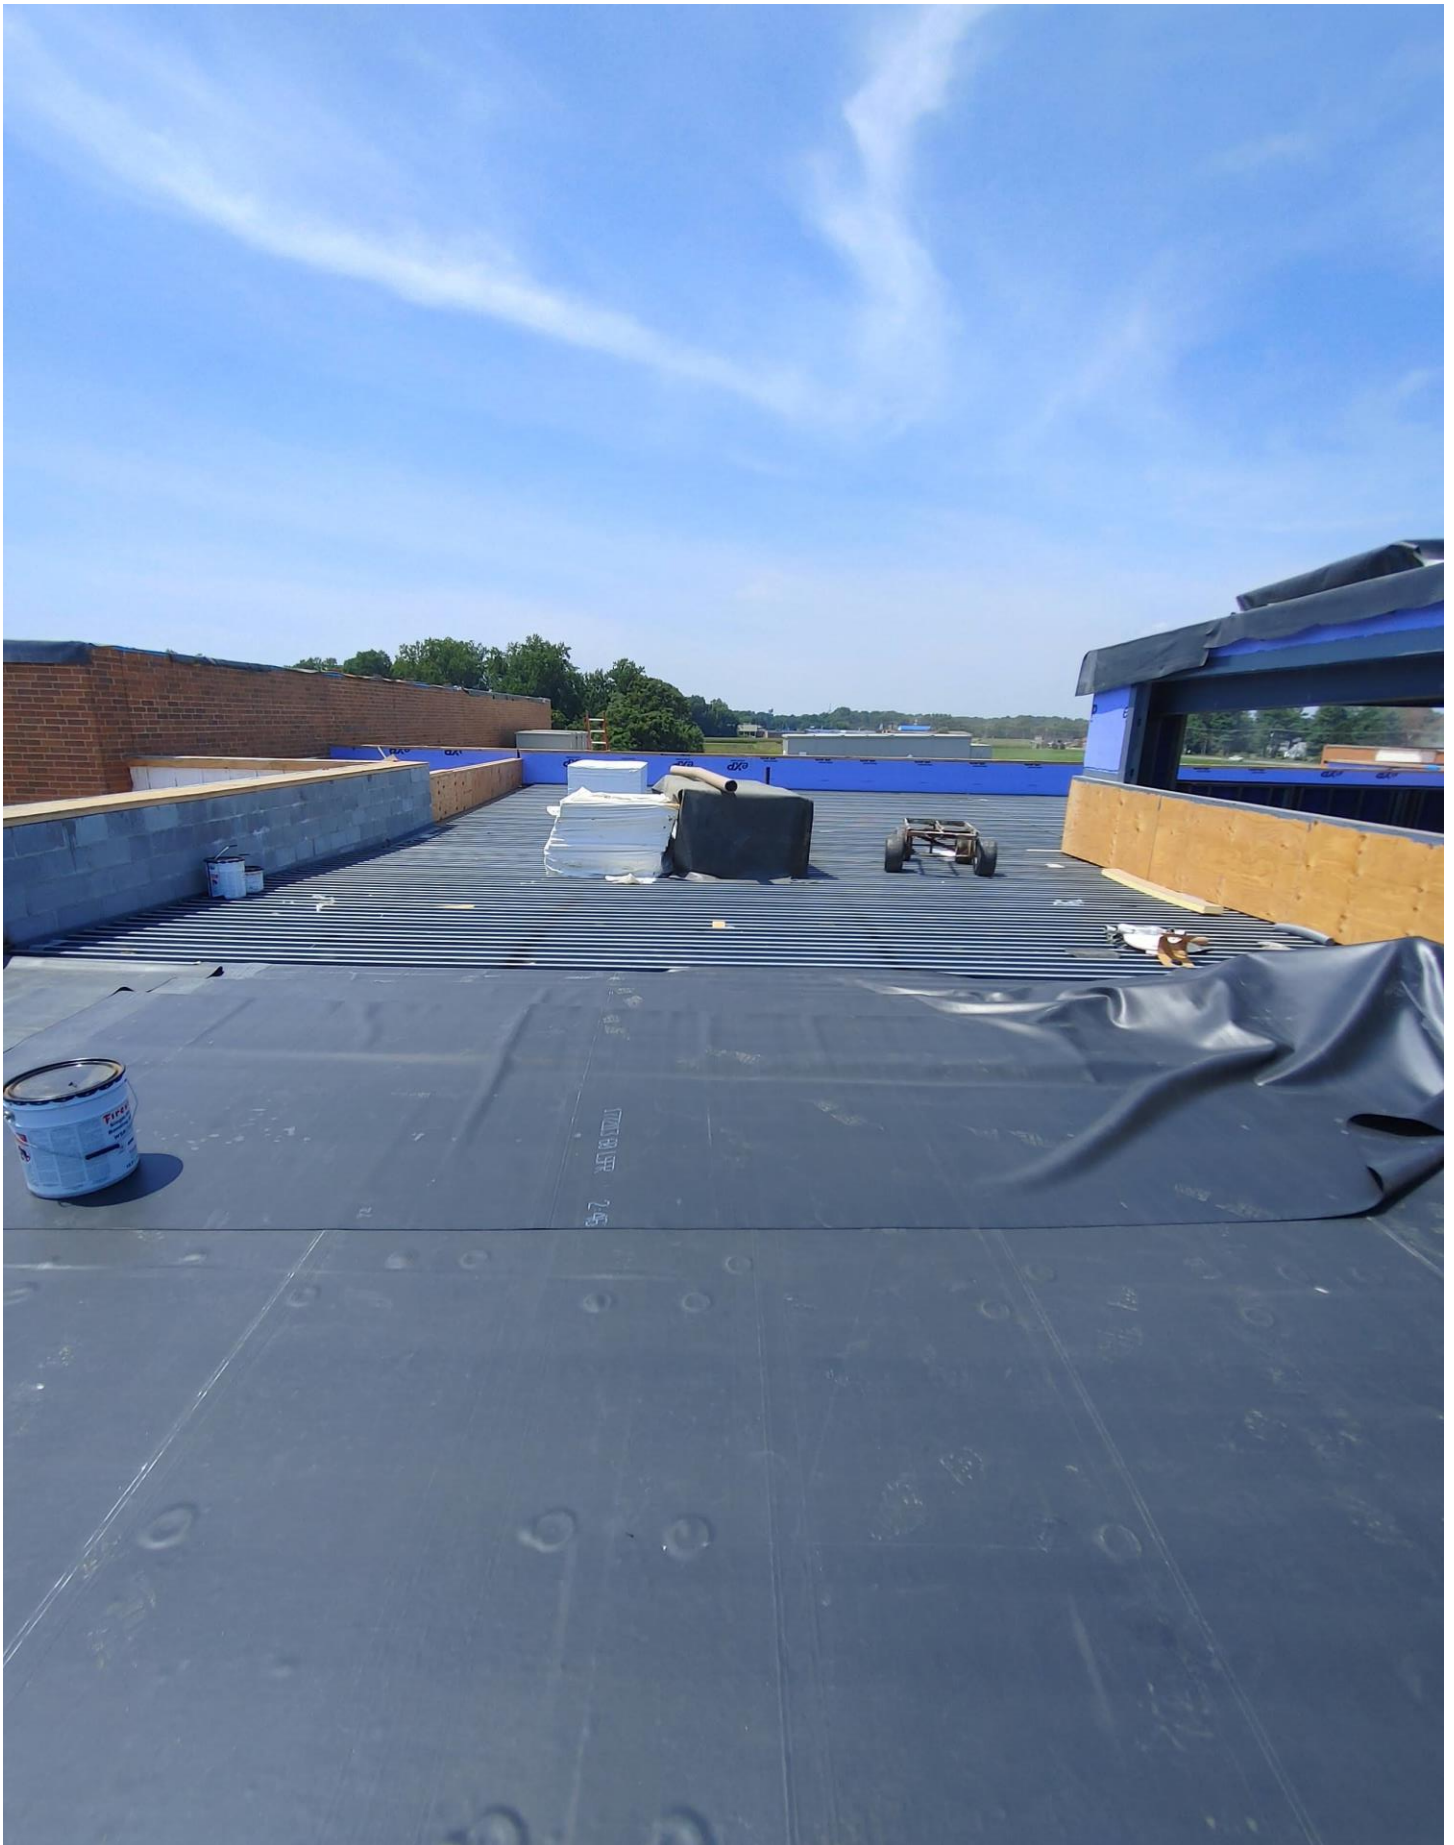


Photo 6 - Area C Roof has yet to be completed.



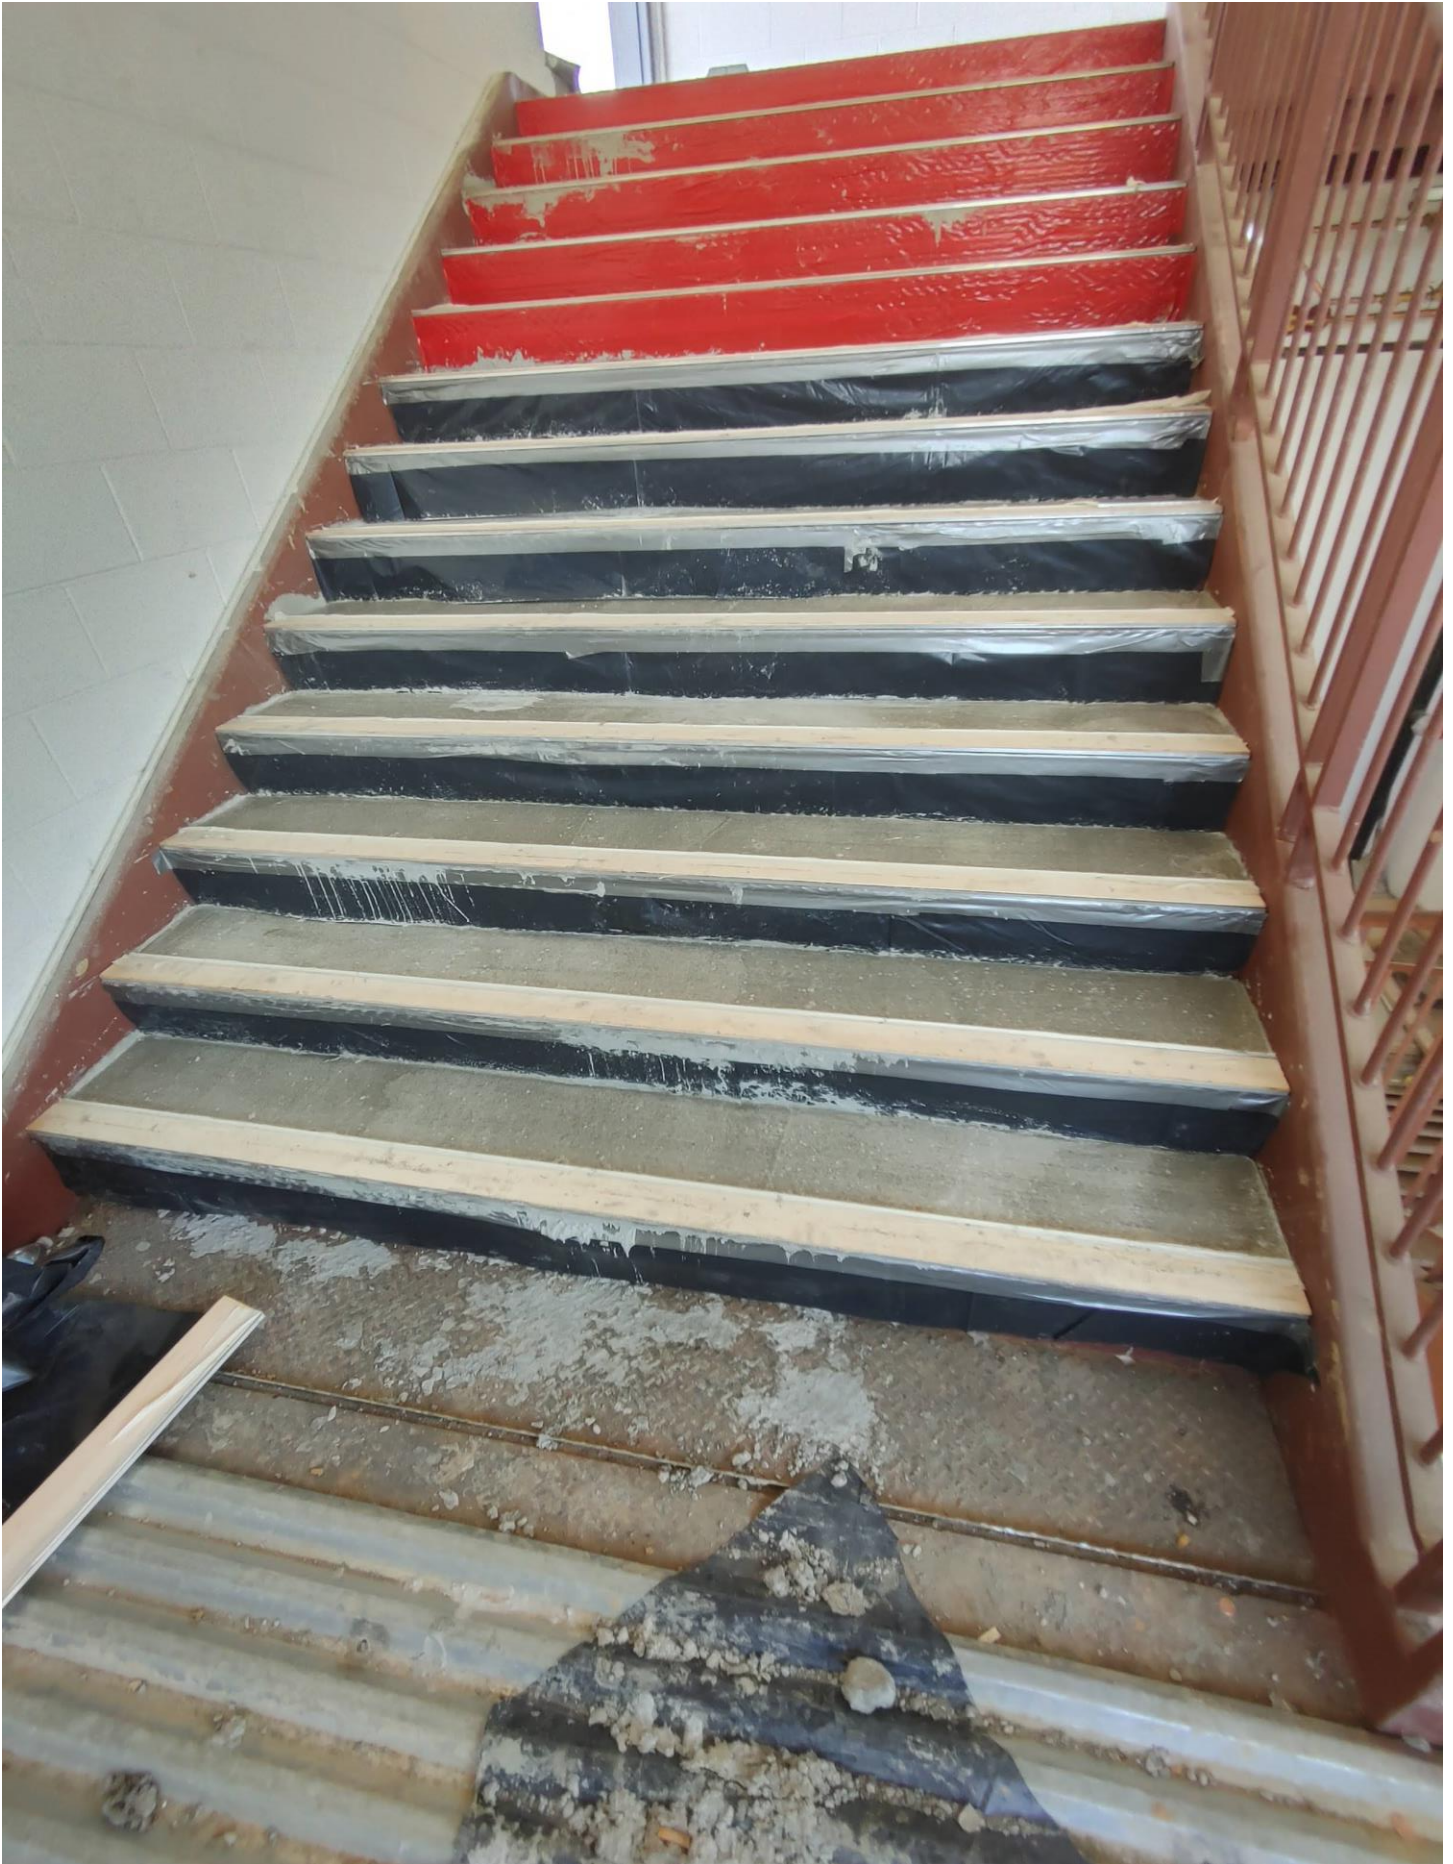


Photo 7 - They have begun to pour the stairs in Stairwell #2



Photo 8 - Masons laying block in Corridor E11



Photo 9 - Site prepped for Transformer Pad.
