



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 08/11/2021

Weather: 90 degrees. Sunny. High of 95 degrees today. Heat index of 107 today.

Hours Worked: 12:00hrs – 14:30hrs (2.5hrs)

I walked the site and observed the work being performed.

Beuchert Excavation: Is on site today and they continue to work on Retention Pond #1.

Industrial Concrete: they have approximately five (5) men on site today. They are forming up the footers for the Columns that will support the rear Canopy off of Area C.

J.D. Long, Masons: They have eleven (11) men on site today. They are laying block in Area D, Chase Walls.

Hazzard Electric: They have fourteen (14) men on site today. They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: They have sixteen (16) men on site today. They are running HVAC Duct in Area D and insulating pipe in Area A.

Weldon Steel: No one is on site today.

JP Construction: There are sixteen (16) men on site. They are laying Acoustical tile in Area A, 1st & 2nd floors. They are also installing acoustical ceiling grid in Area B. A few men are also finishing sheetrock in Area A & B.

AAR Roofing: I counted four men working on the roof of Area C.

Tailored Foam: No one is on site today.

FG & M: Seven (7) men are here today installing glass on the front of Area A.

United Sprinkler: Two men are on site running pipe in Area D.

CTSI: Three men are here today running low voltage wire throughout the site.

M. L. Straight: Two men are painting in Area B.

K-Plus: No one is here today.

S&S Concrete Cutting Company: I did not observe anyone on site today during my visit.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: Brian Topper is not here today. I met John, Branch Builds Superintendent who will eventually replace Brian Topper. I met with John, Jake and Cooper in the trailer. I was told that Dominion Power's Transformer had been set and that a delivery of metal panels were being off loader from a Tractor Trailer.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 08/10/2021

Submittals –

RFIs – #294

Patrick Byrne – Asphalt Thickness

Change Order/PCOs/Pay App – July's Pay Application

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Glass is being installed on the front of Area A



Photo 2 - They have begun to install the elevator



Photo 3 - Acoustical Ceiling tiles are being installed in Area A

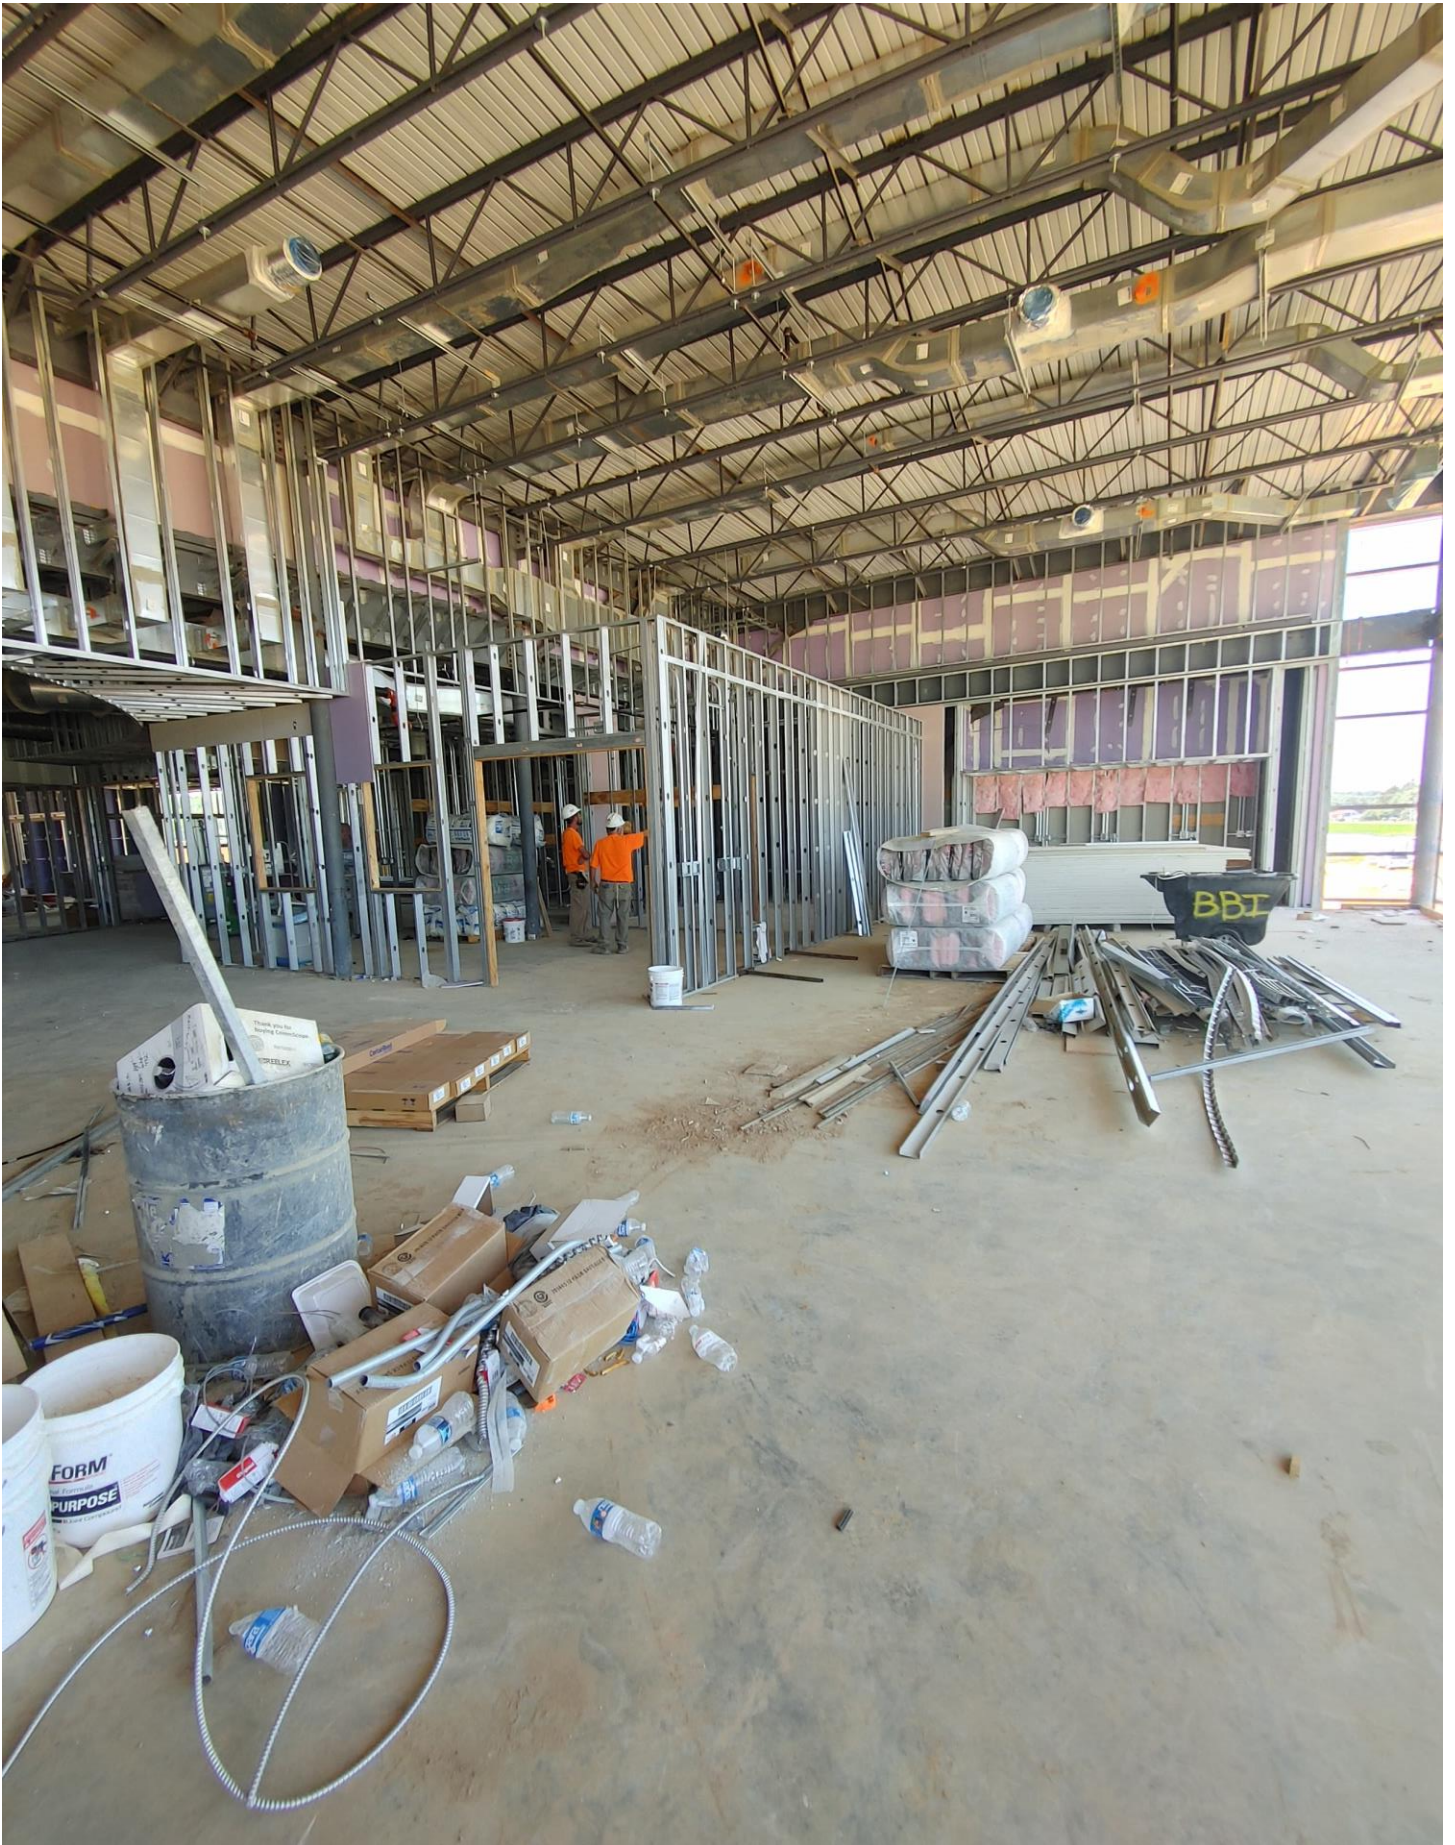


Photo 4 - Metal Stud framing continues in Area A

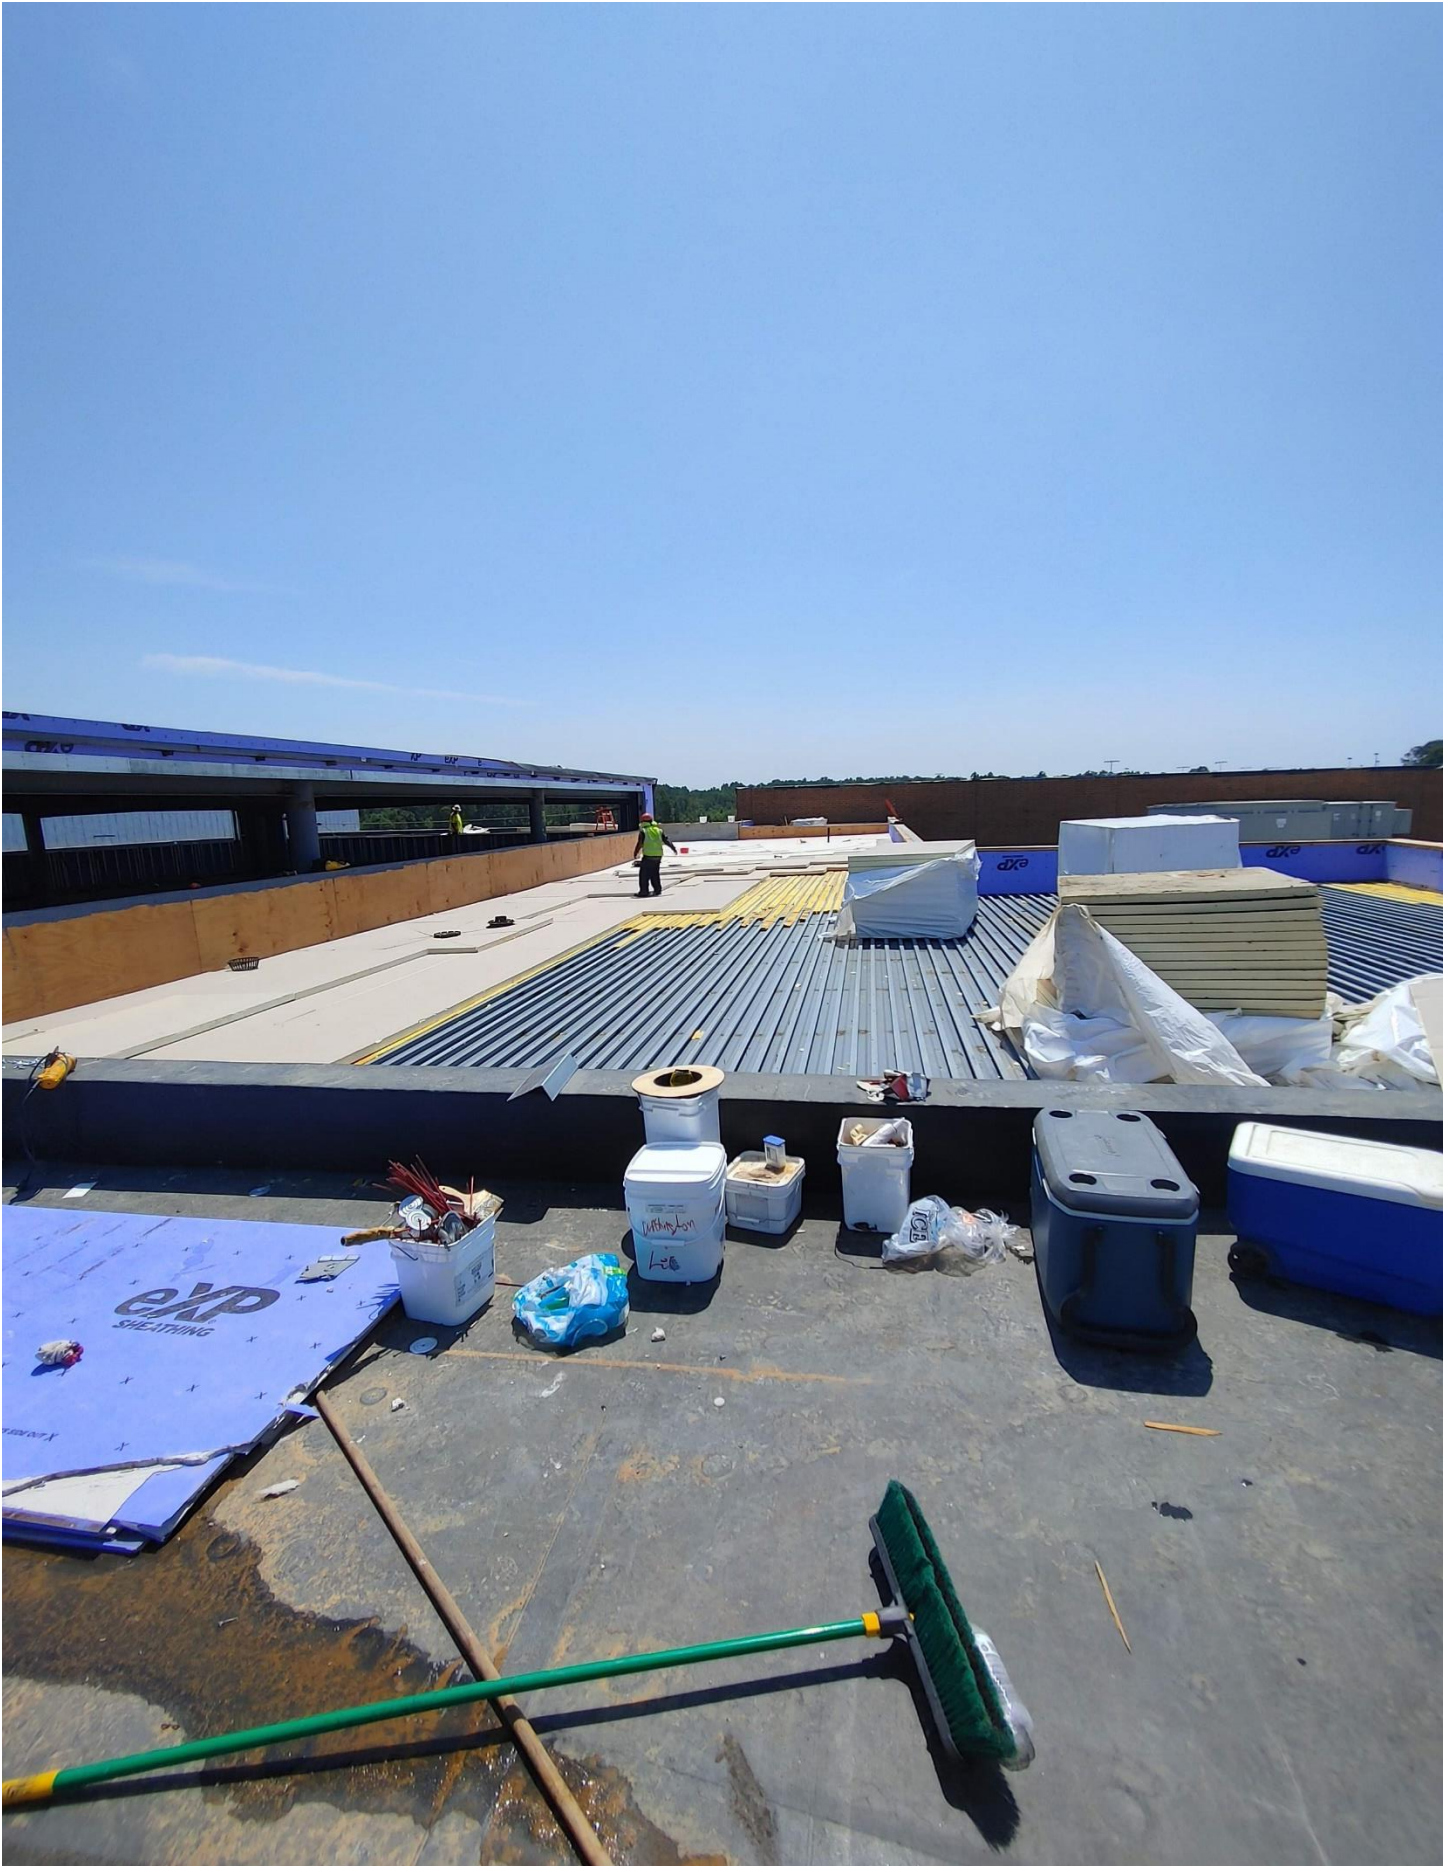


Photo 5 - Roofer are working on the Roof of Area C.



Photo 6 - Ceiling grid is being installed on the 2nd floor of Area B.



Photo 7 - Footers are being formed on the South side of Area C for the Canopy Columns.



Photo 8 - HVAC duct is being installed in Area D



Photo 9 - Dominion Power Transformer has been set



Photo 10 - Metal Panels are being off loaded and staged.
