



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West
Aylett, Virginia 23009
Phone: 804-761-4248
FrazierConsulting@gmail.com
Licensed Class A - RBC/CBC
DEPOR # 2705169996
EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 08/13/2021

Weather: 93 degrees. Sunny. High of 95 degrees today. Heat index of 106 today.

Hours Worked: 13:00hrs – 14:30hrs (1.5hrs)

I walked the site and observed the work being performed. Not many people are working today.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: They are laying block in Areas C & D, Chase Walls.

Hazzard Electric: They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: No one is on site today.

Weldon Steel: No one is on site today.

JP Construction: No one is on site today.

AAR Roofing: I counted three men working on the roof of Area C.

Tailored Foam: No one is on site today.

FG & M: They are installing the Curtain Wall Framing on the South side of Area C.

United Sprinkler: Three (3) men are on site running pipe in Area D.

CTSI: Three men are here today running low voltage wire throughout the site.

M. L. Straight: I did not observe anyone on site today.

K-Plus: No one is here today.

S&S Concrete Cutting Company: I did not observe anyone on site today during my visit.

Linear Surveyors: They are on site laying out reference points around the site.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: I met with Brian Topper. I informed hi that I had set up a meeting with Franklin Mechanical for 09:00hrs on Tuesday of next week to discuss the installation of the Sewage Pump Station. Brain said that he had cleaned up the area for Franklin and was ready to proceed. Brain said that everything was ready to turn the power on to the building. He is just waiting on Dominion to make the final tie-in across Rt. #3

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs – #295, #296, #297, #300

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report – 08/13/2021

Weekly RFI Status Update –08/13/2021

Weekly Daily Log Summary – 08/13/2021

PCO Log – 08/13/2021



Photo 1 - Surveyors laying out reference points.

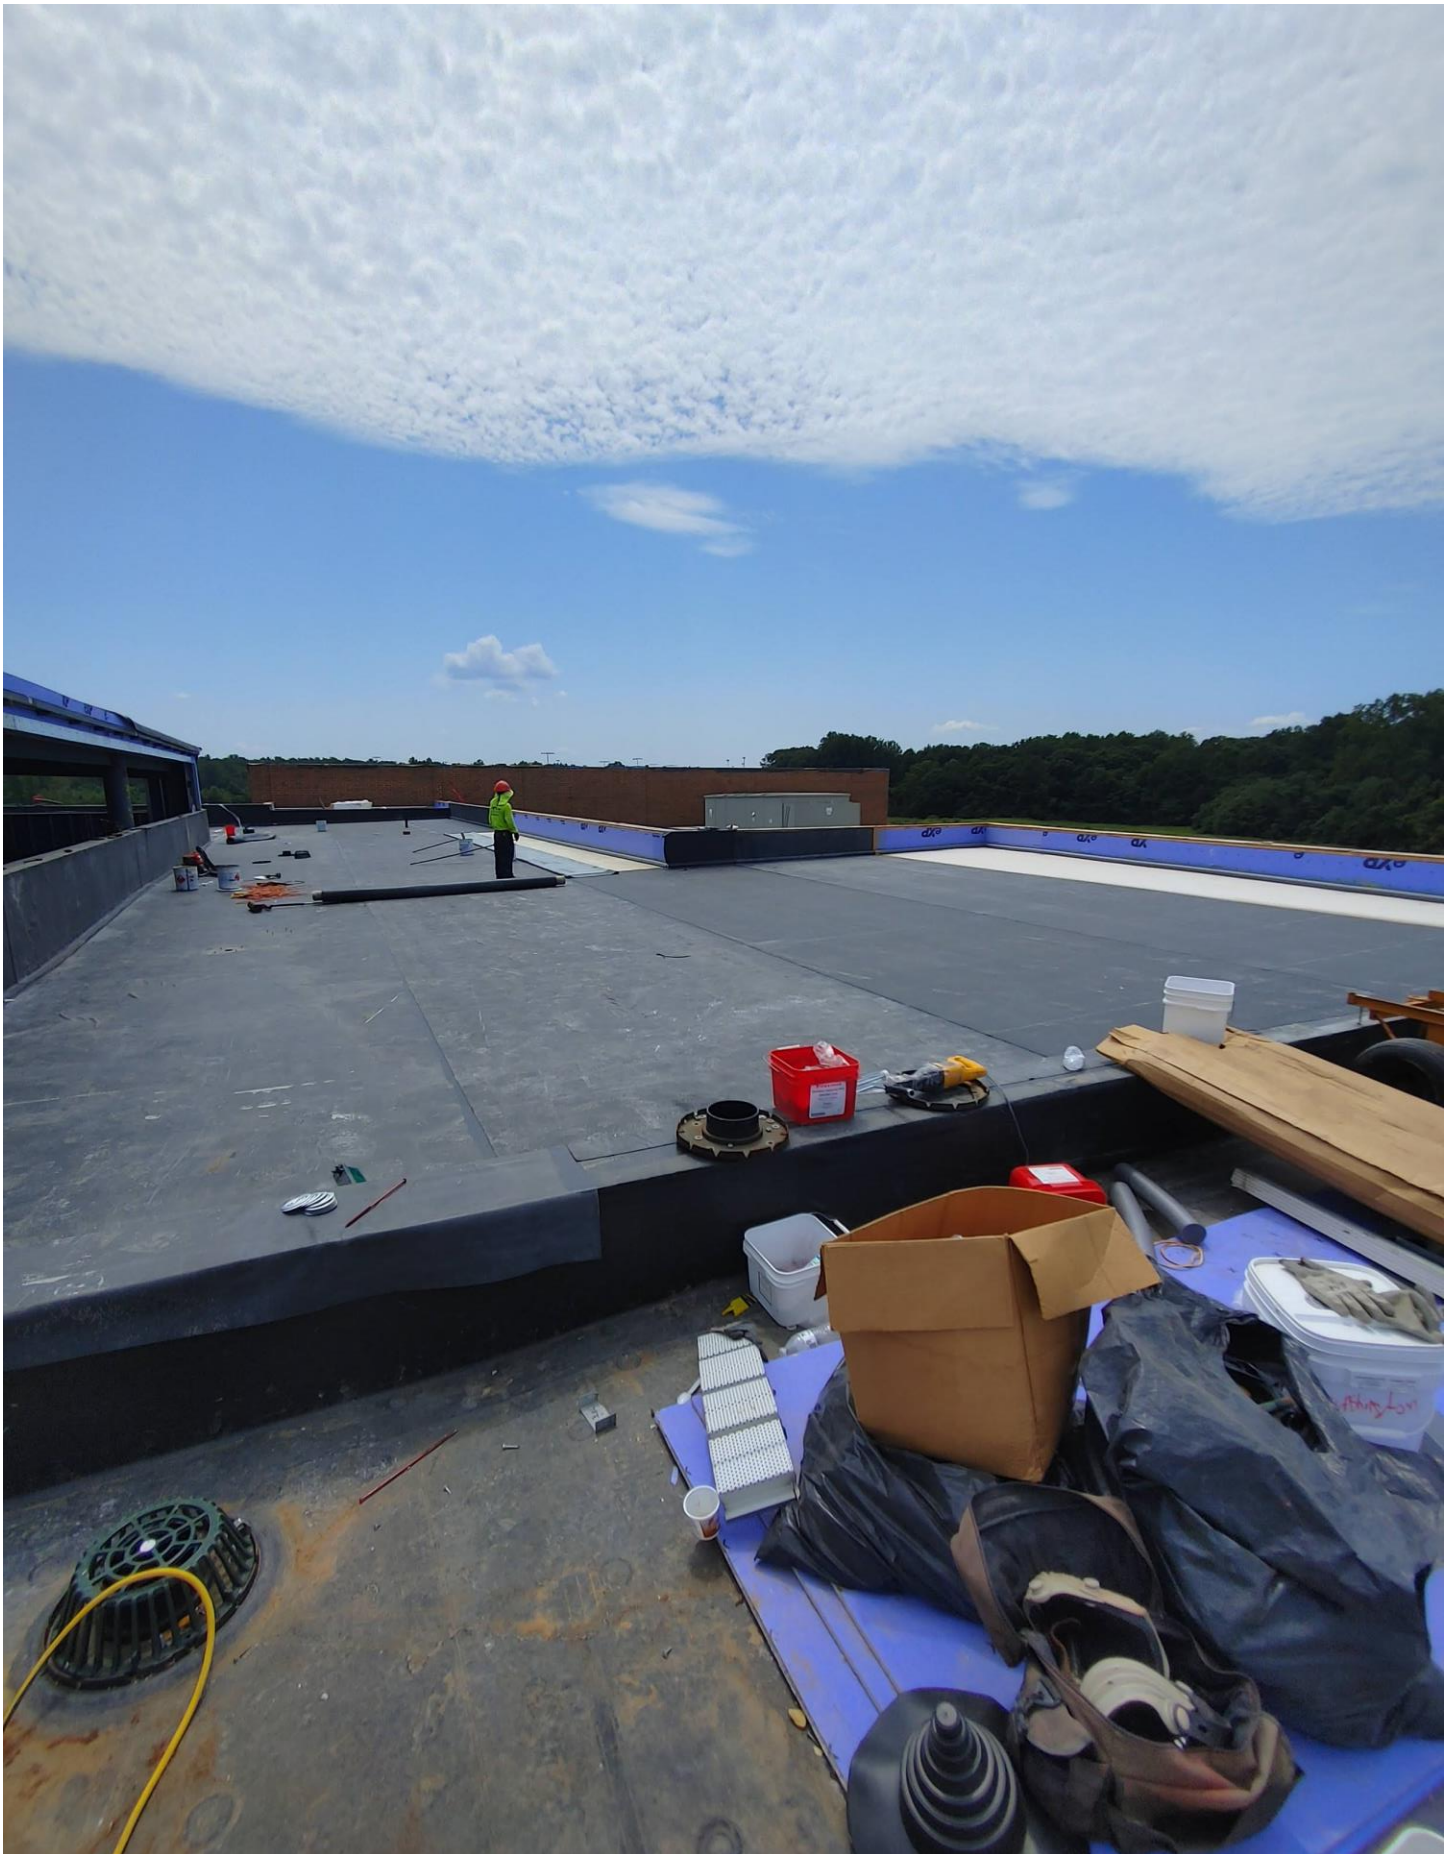


Photo 2 - Roofers are working on Area C.



Photo 3 - Curtain wall framing going up on the South side of Area C.



Photo 4 Roofers working on Area C Roof.



Photo 5 - Window frames have been staged on the roof of Area C.



Photo 6 - Soffit has been painted in Area A.
