



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 08/18/2021

Weather: 87 degrees. Mostly Cloudy. High of 88 degrees today. Heat index of 98 today.

Hours Worked: 11:00hrs – 15:00hrs (4hrs)

Attended the 11:00AM Progress Meeting in Norm's Conference Room.

I walked the site and observed the work being performed.

Beuchert Excavation: No one is on site today.

Industrial Concrete: I counted five (5) men on site today. They poured the footers for the Canopy Columns on the rear of Area C and are currently pouring the stairs in Stair #1. today.

J.D. Long, Masons: They are laying block in Areas E & D, Chase Walls.

Hazzard Electric: Fifteen (15) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: Fourteen (14) are on site today. They are insulating pipe in Areas A & C. Crews are also running HVAC Duct and copper water lines in Area D.

Weldon Steel: No one is on site today.

JP Construction: Three (3) men are on site today. They are pointing up sheetrock in Area A and installing ceiling grid in Area B.

AAR Roofing: No one is on site today.

Tailored Foam: No one is on site today.

FG & M: Nine men are on site. They are installing the Curtain #1 Wall Framing on the South side of Area C. They are also installing Storefront #17 and A10 frame.

United Sprinkler: Two (2) men are on site running pipe in Area D.

CTSI: I counted three men are here today running low voltage wire throughout the site.

M. L. Straight: Four (4) men are here today painting in Area A.

K-Plus: No one is here today.

S&S Concrete Cutting Company: Two guys are here coring walls in Area D.

Linear Surveyors: They are on site laying out reference points around the site.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: I met with Brian Topper and Todd Demetriou in the construction trailer. During the progress meeting Todd requested that I reach out to the Contractor installing the 12" water line and get an update on their schedule. I email Jim Aldous with Enviroscares. Jim responded and said that they had found a leak in the pipe under Rt. #3. He said his subcontractor Webb will need to help them remove the pipe in the casing and reinstall it and that work is tentatively scheduled for August 30th. He said pressure testing and disinfecting will follow. A second flusher will also be added to the 6" line to the Rec Park line so that we can get a pressure reading. The double detector check vault should be ready around that time also.

Brian requested me to reach out to Franklin Mechanical to determine when they plan on starting the work for the Sewage Pump Station. Franklin said that they are waiting on a delivery date for the Pump Station. Once they have that they will schedule the work and he is expecting that to take place next month.

I told Brian and Todd that I noted that there was a lot of condensation occurring in Area A because Industrial Concrete had stairwell #1 doors open while pouring the stairs and FG& M were installing A10 Frame on the opposite end of the building. Note: Branch has put up a trap in front of A10 to help to mitigate the problem. I told Brian I was concerned with the potential of Ceiling tiles curling. We agreed that we would continue to monitor that area. Branch also trying to expedite the work to minimize that amount of time that they area is open.

I emailed Brian yesterday about erosion that is occurring around a Drop Inlet along Rec Park road because of the Schools Retention Pond. Brian said he would take care of the problem.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 08/10/2021, 08/12/2021, 08/13/2021, 08/16/2021

Submittals – #09 52 50-2.1

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App – Change Order #11

Changes in Procore –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Curtain Wall #1 is being installed



Photo 2 - Footers for Canopy Columns have been poured on the South side of Area C.



Photo 3 - Masons are laying block around columns in Auditorium.

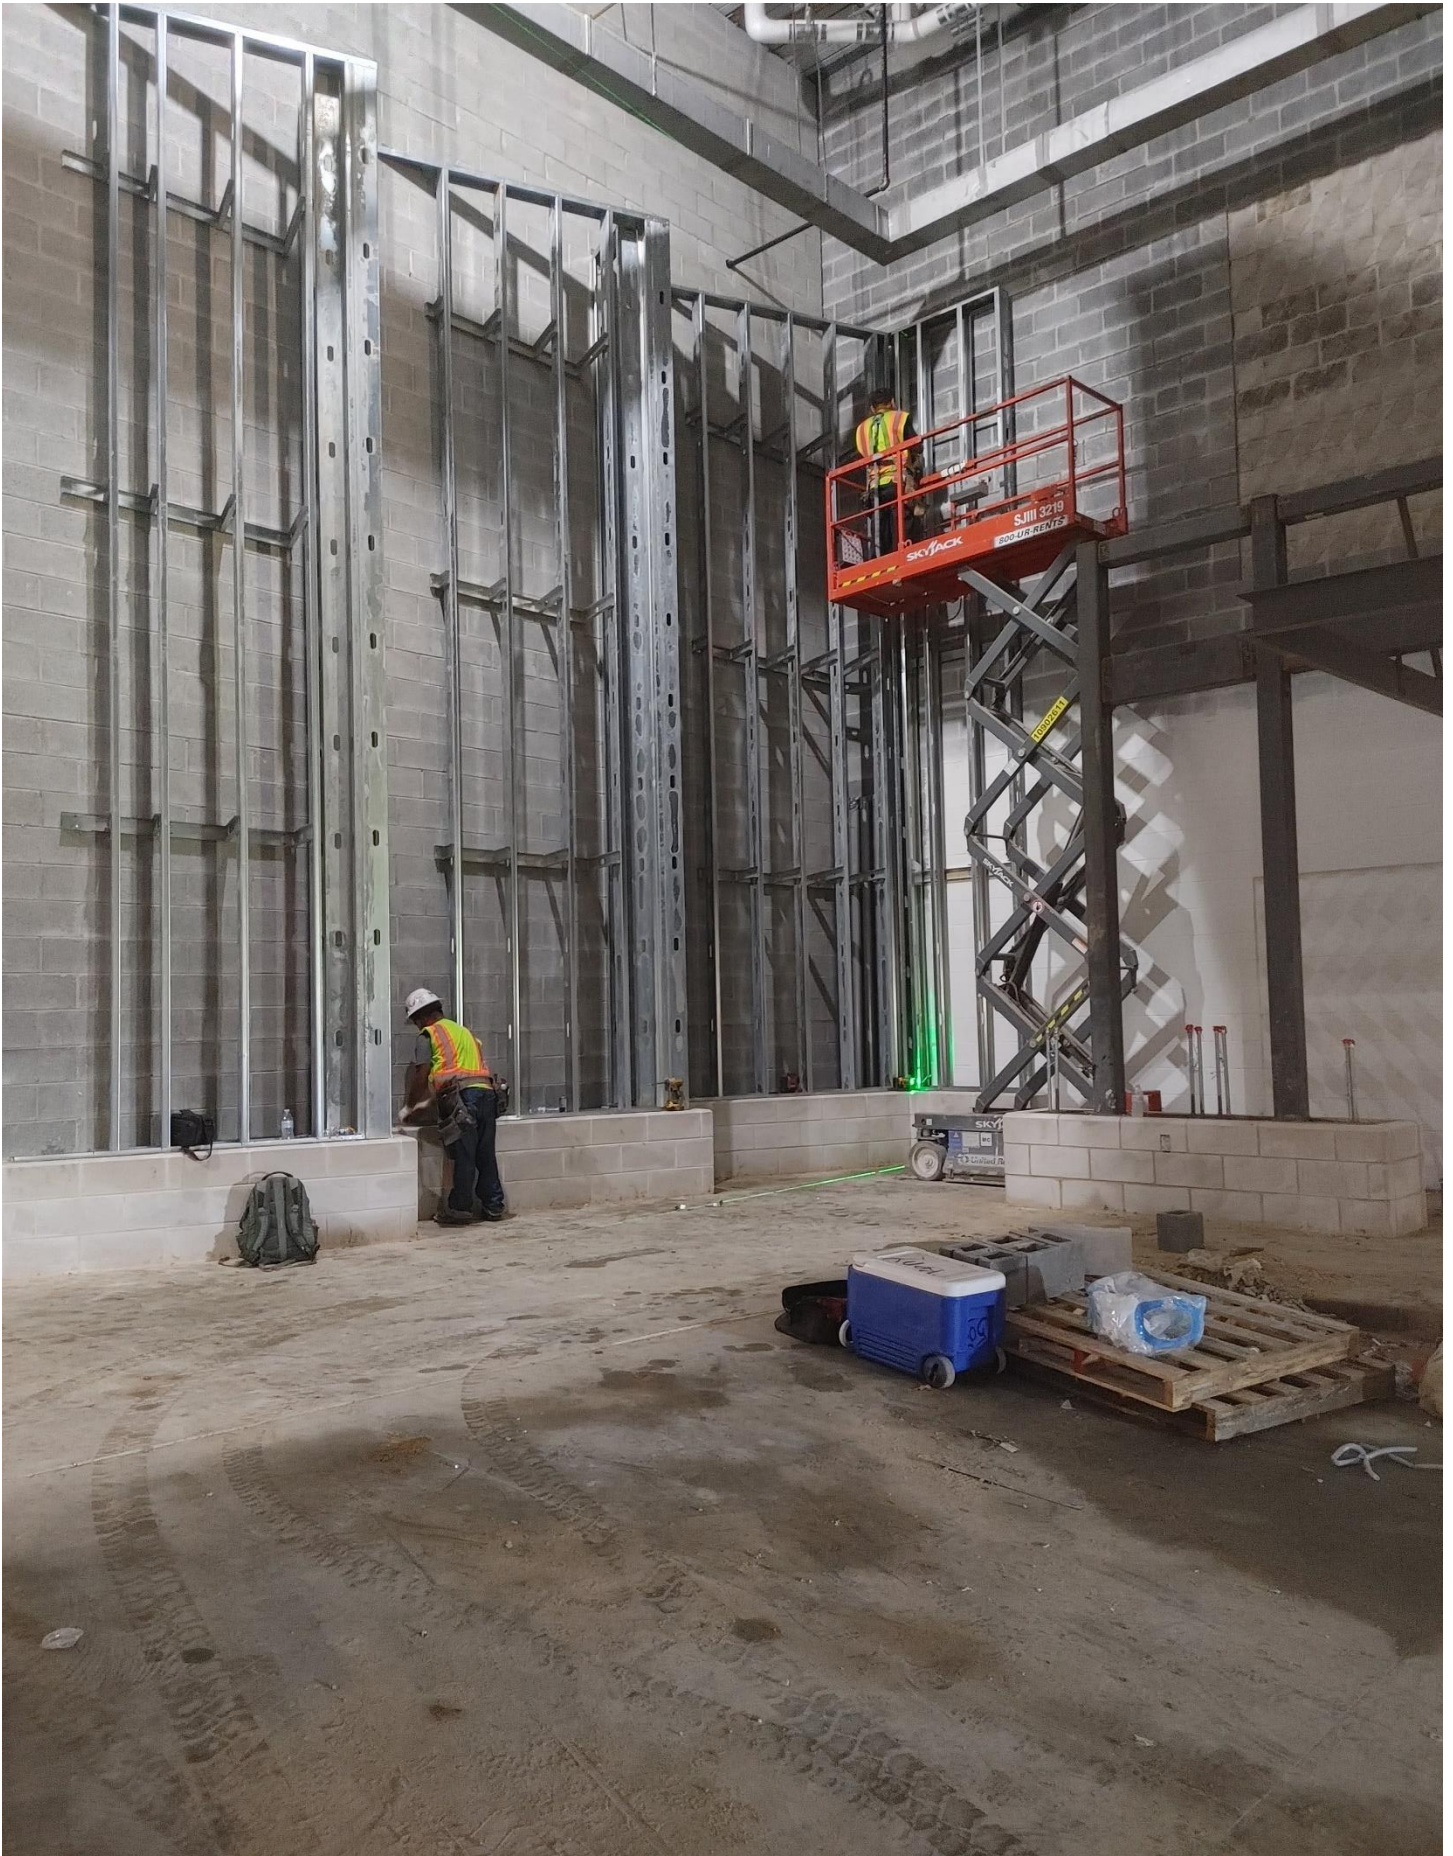


Photo 4 - Walls being framed in the rear of the Auditorium.



Photo 5 - Canopy has been framed in Area C as you enter Area E.



Photo 6 - Raised concrete slabs have been poured in E126 for lockers.



Photo 7 - Pipes are being labeled



Photo 8 - The radius bulkhead has been completed on the 2nd floor of Area A.

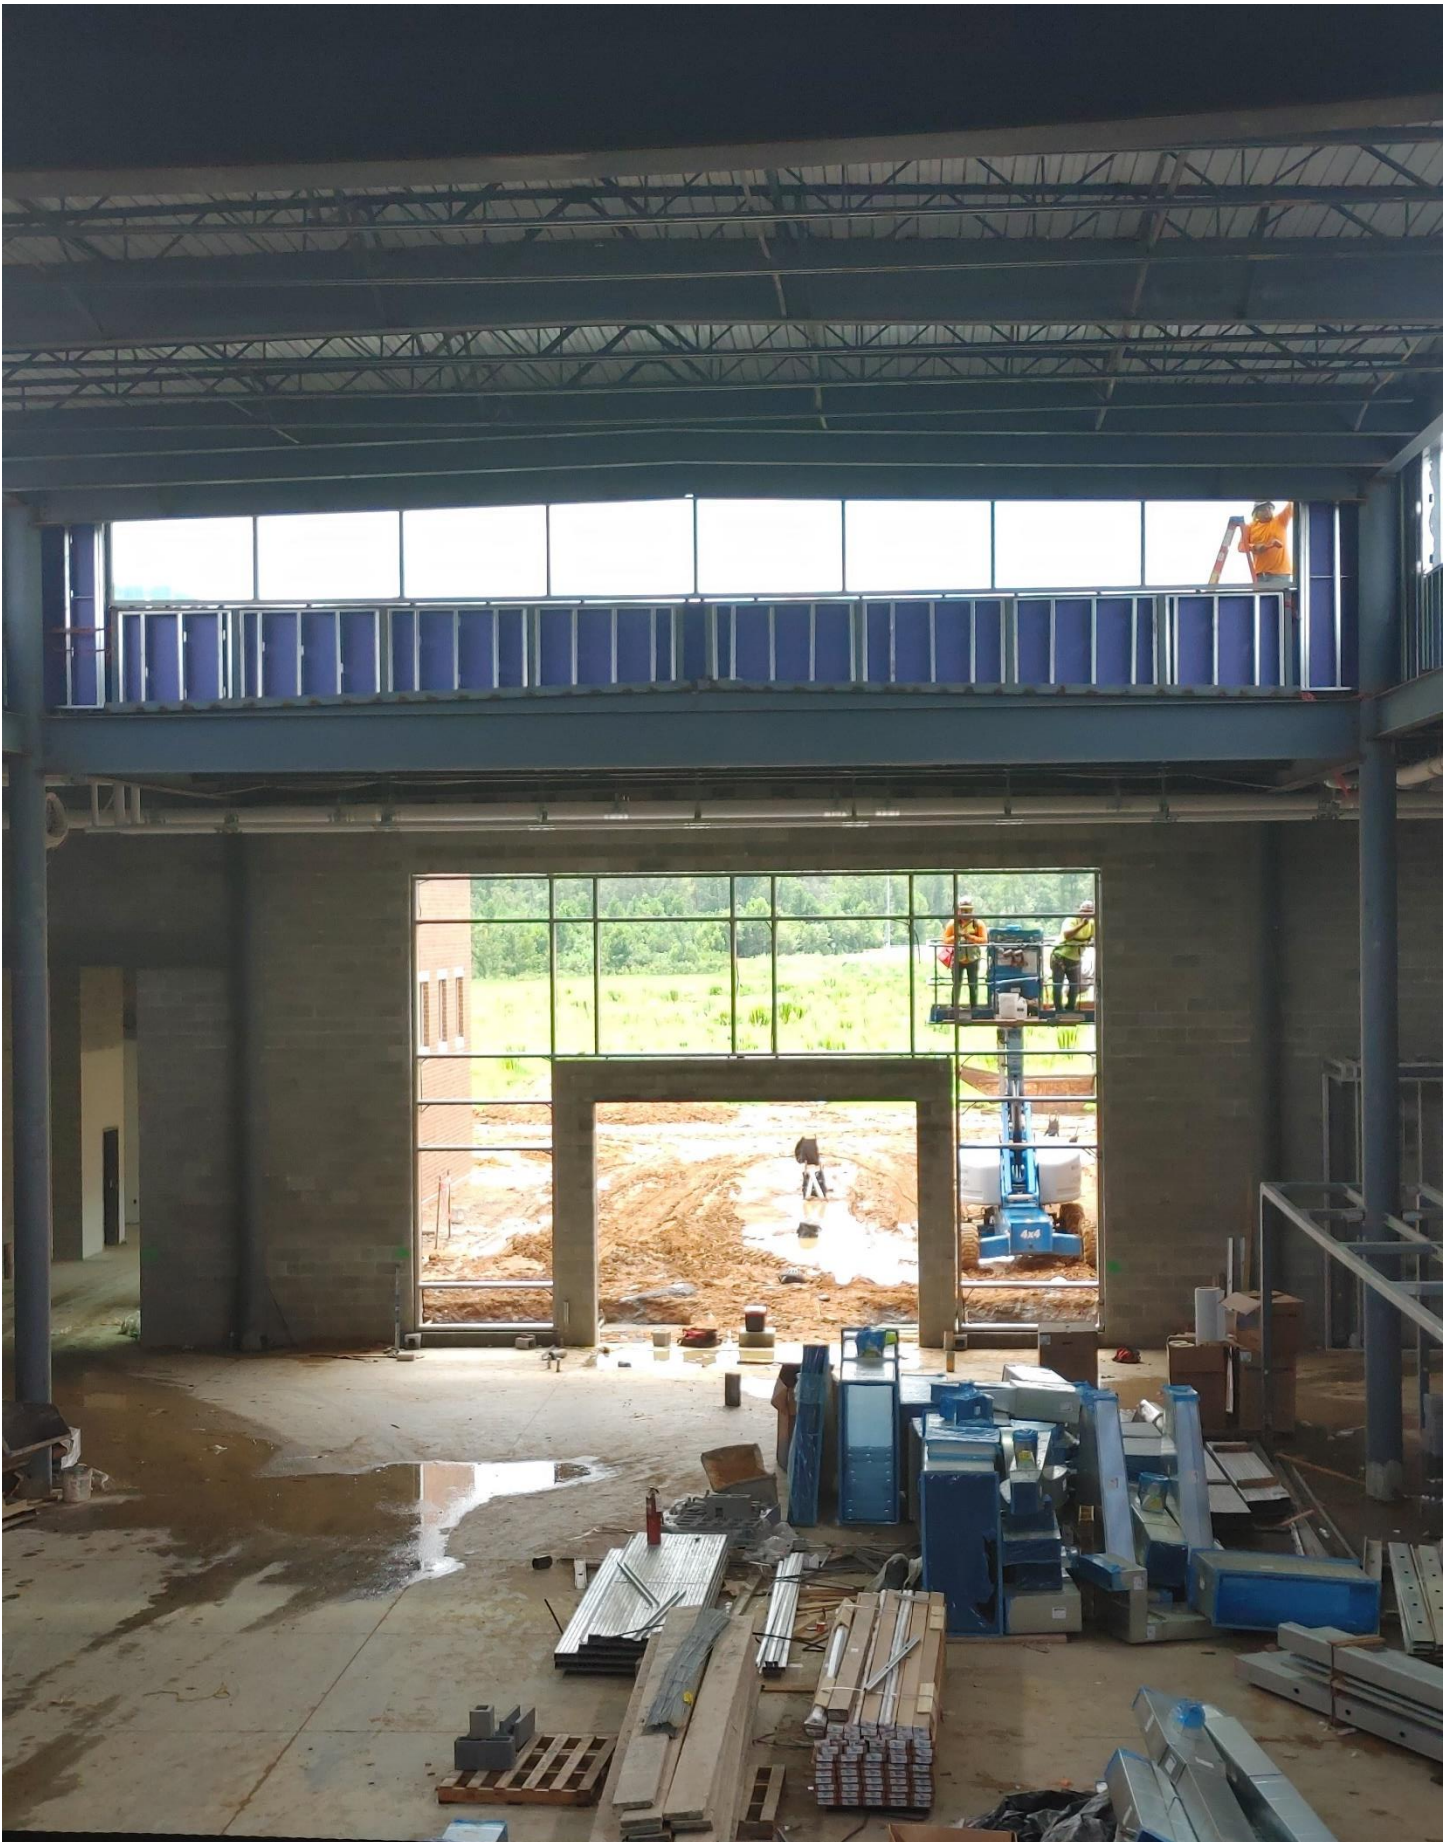


Photo 9 – Crews working on Curtain Wall #1 and Storefront #17



Photo 10 - Glass being installed in Storefront #17



Photo 11 - A10 Frame is being installed. A tarp has been hung to help maintain conditioned space.



Photo 12 - VCT is being laid in A106



Photo 13 - Accumulation of condensation on the first floor of Area A.
