



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 09/22/2021

Weather: 80 degrees. Light Rain. High of 82 degrees today.

Hours Worked: 10:00hrs – 13:30hrs (3.5hrs)

I arrived on Site today for the MEP/IT Mockup meeting. Not sure if I had the wrong day, but no one from the School showed for the meeting.

Beuchert Excavation: Four (4) men are on site today. They are working on the main travel and drop off loop lane in front of the school.

Industrial Concrete: No men are on site today.

J.D. Long, Masons: Seven (7) They are laying brick on the West side of Area C and they are cleaning block.

Hazzard Electric: Fourteen (14) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D. They are also trenching on the West Side of Area C and running Conduit.

Colonial Webb: Twelve (12) men are on site today. Running duct and insulating pipe in Areas A, C and in Area E.

Weldon Steel: A couple of guys are on site welding steel in Area A & D.

JP Construction: Seventeen (15) men are on site today. They are hanging & finishing sheetrock and framing walls in Area A & D.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: Five (5) men are on site. They are installing glass in various areas.

United Sprinkler: One (1) man continues to run pipe in Area D.

CTSI: Four (4) men are on site pulling wire throughout the site.

M. L. Straight: Four (4) men are on site today painting in Area C.

K-Plus: One (1) man is on site caulking in various area around the site.

AAM: Five (5) men are on site today. They are installing metal panels on the North side of Area A and on the West side of Area B.

Hodgemen: No one is here.

Deleware Elevator: Two (2) men are on site working on the elevator.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site during my visit.

Conversations with Branch Builds: I met with John, Jake and Cooper in the Branch Builds Trailer. Brian was attending a meeting off site this morning. John said that they have a 10:00AM meeting scheduled with the Landscaper to discuss their work. I asked about the MEP/IT Mockup meeting and John was not aware of the Meeting. Jake said he knew about the meeting but there was some confusion as to if it was scheduled for today or not. John said they are working on getting Industrial Concrete on site to begin the curb and gutter on the front of the site. John said Beuchert is continues to work o the BMPs and is working on importing the BMP material needed to finish the two BMPs on the West side of the site. They have installed the 57 stone and pea gravel. Hillis-Carnes has been on site to document the process.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test – 09/15/2021

Hillis-Carnes Field Reports (Concrete and Steel) – 09/15/2021, 09/21/2021

Submittals –

RFIs – #301, #306, #309, #310, #312, #313, #321, #322

Patrick Byrne –

Change Order/PCOs/Pay App – PCO #58:CE #98-PR#22

Changes in Procore –

Weekly Submittal Status Report: 09/17/2021

Weekly RFI Status Update – 09/17/2021

Weekly Daily Log Summary – 09/17/2021

PCO Log – 09/17/2021



Photo 1 - Metal Panels are being installed on the North side of Area A



Photo 2 - Insulation is being installed in the Entrance area on the Northside of Area A.



Photo 3 - Frames have been installed A134



Photo 4 - Block Filler/Sealer is being applied in Area C.



Photo 5 - Work continues on the Boilers in the Mechanical room.



Photo 6 - Metal Stud framing has been completed on the North and South side of the Auditorium.



Photo 7 - Metal Beams are being welded in the Auditorium.



Photo 8 - Vestibule has been constructed on the South Side of Area C



Photo 9 - Metal Pan has been installed on the Canopy on the South side of Area C.



Photo 10 - Metal Stud Framing on the North wall of the Gym.



Photo 11 - Pea Gravel has been installed in BMP



Photo 12 - Pea Gravel installed in smaller BMP



Photo 13 - Metal Panels are being installed on the West side of Area B.



Photo 14 - Glass has been installed in the Curtain Wall on the West side of Area C.

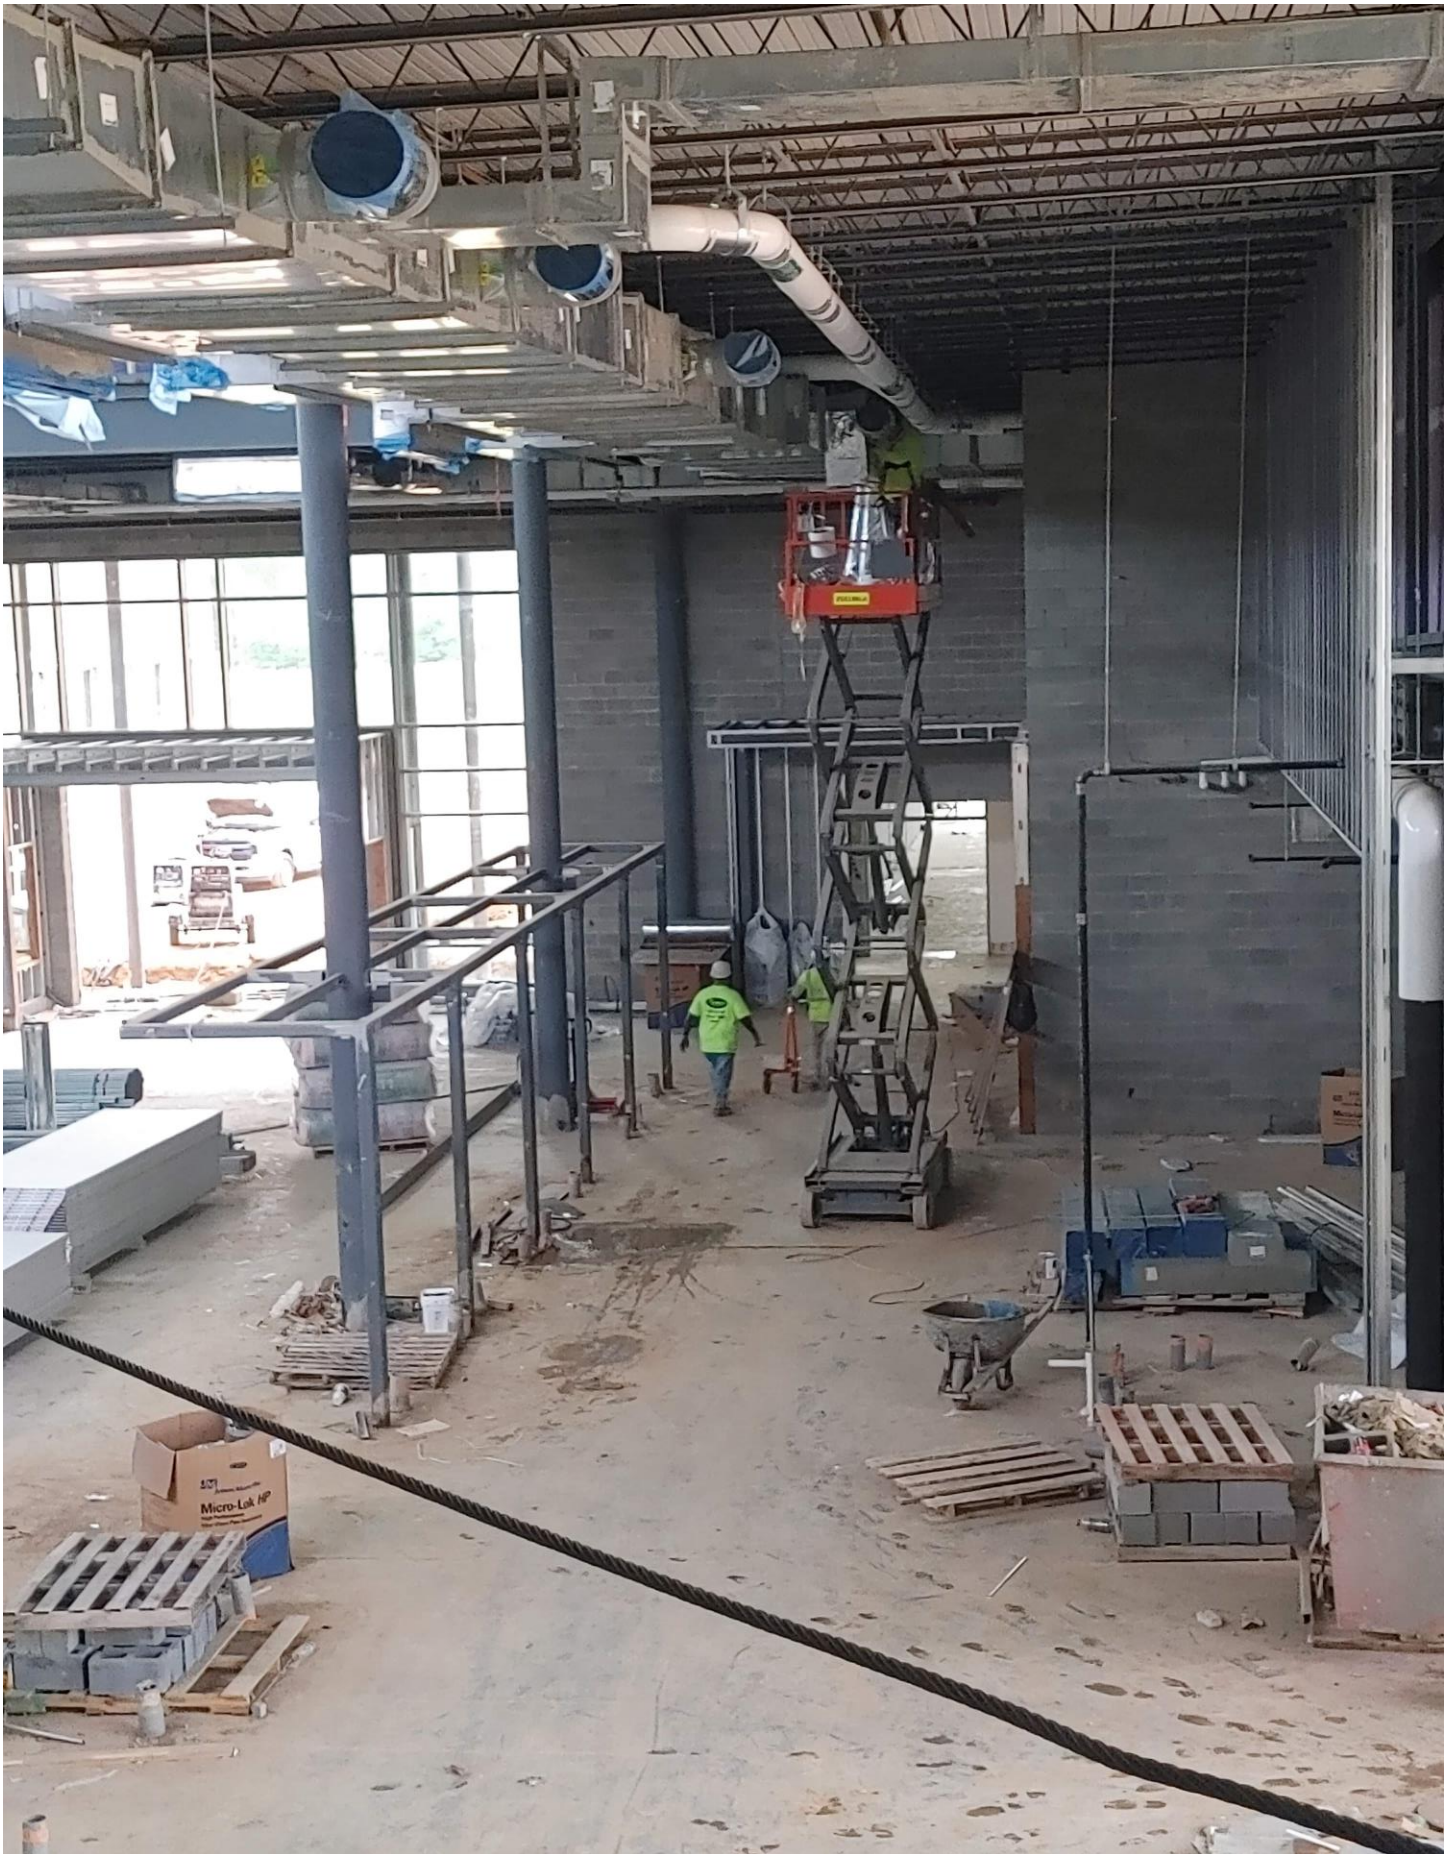


Photo 15 - HVAC Duct is being insulated in Area C.



Photo 16 - Sheetrock continues to be hung and finished on the 2nd floor of Area A.



Photo 17 - Metal Deck and Duct has been sprayed in Area A.

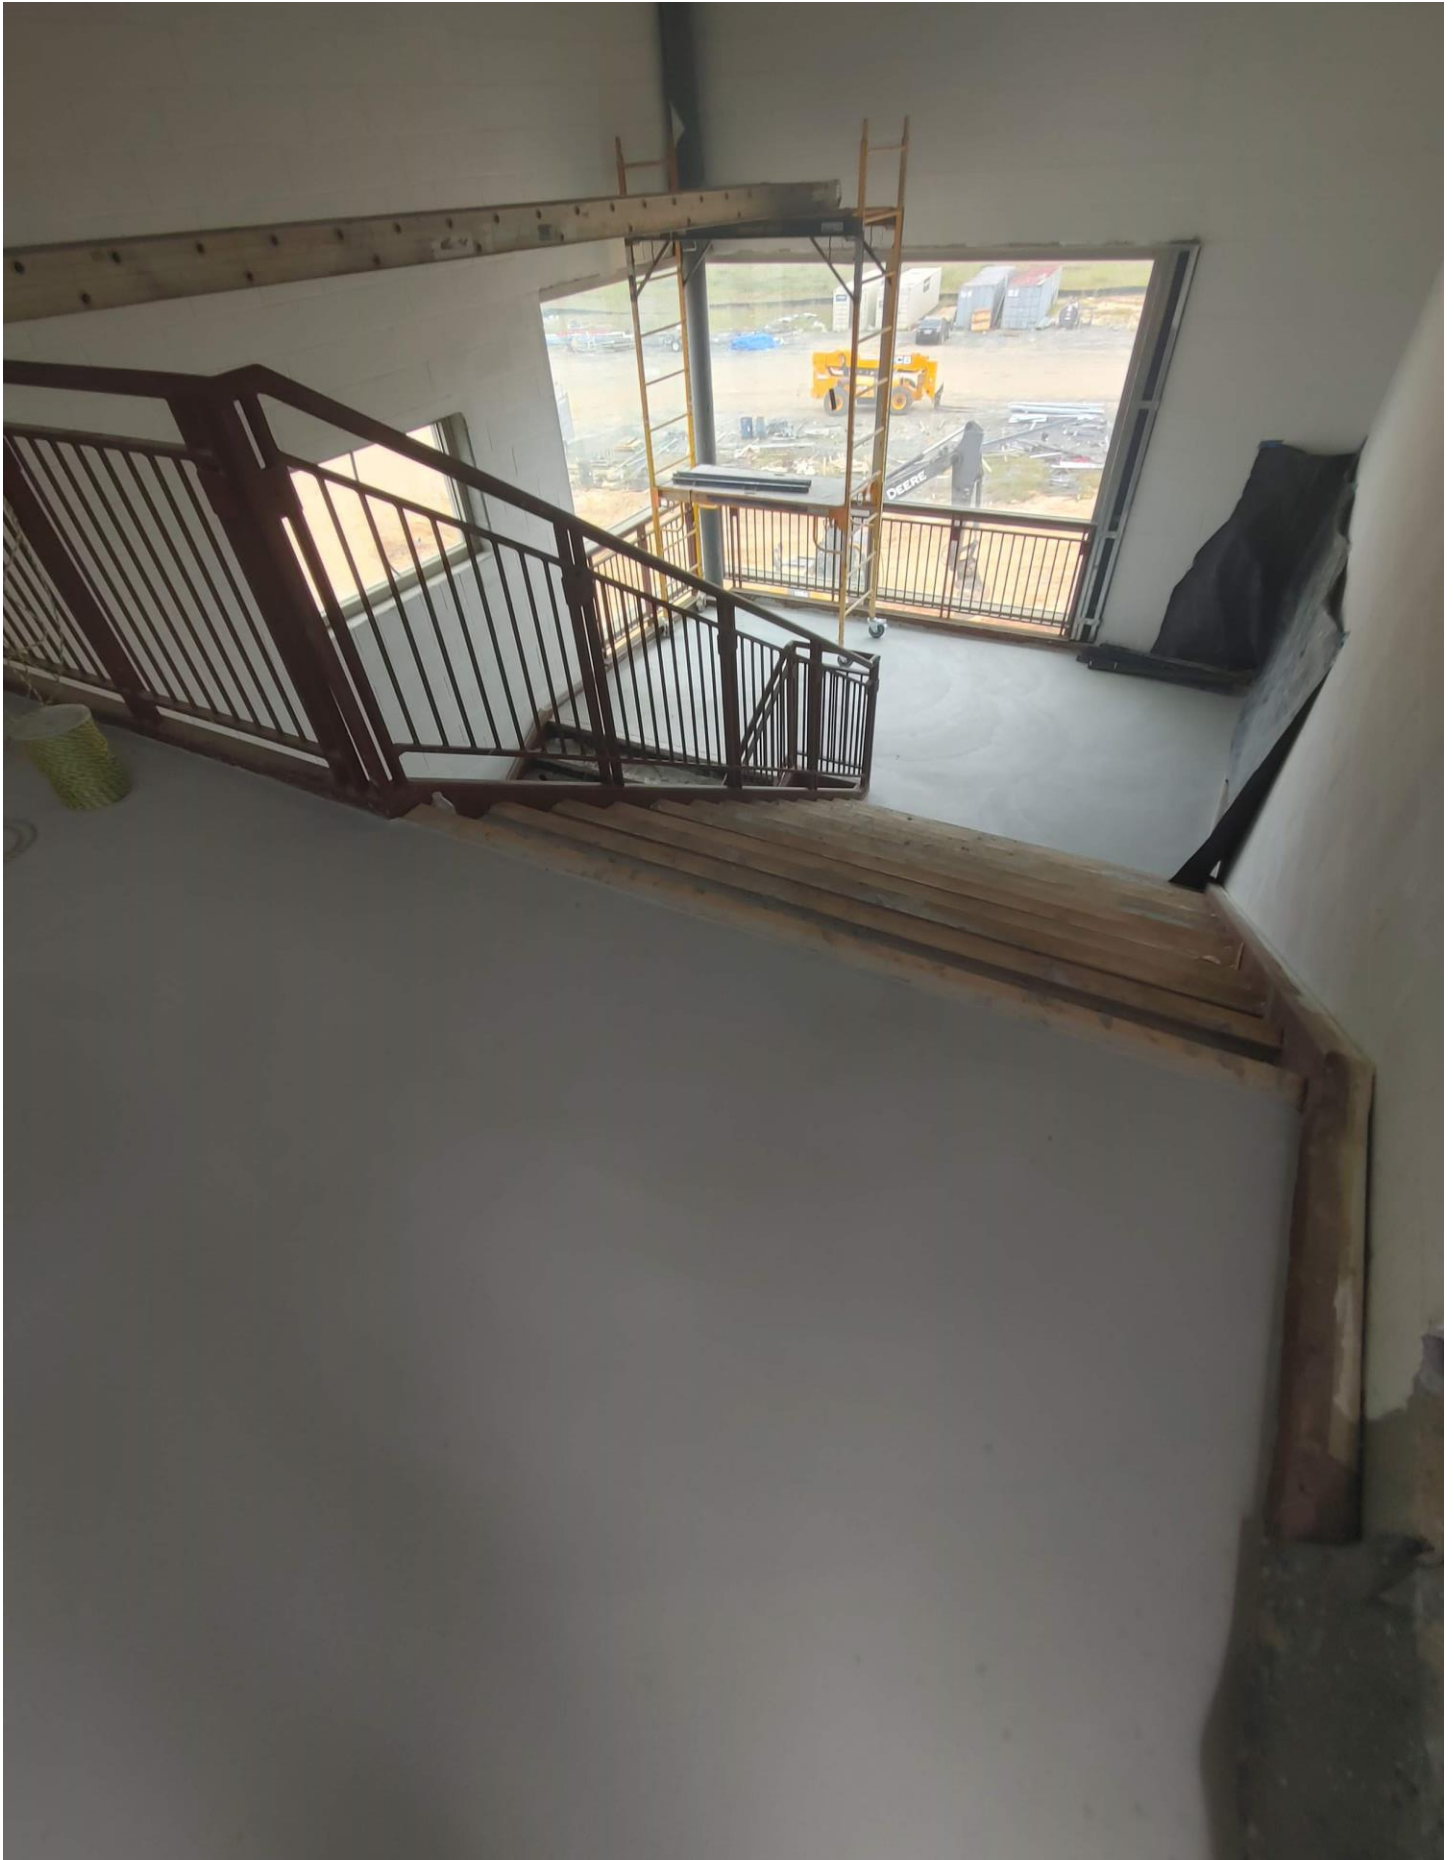


Photo 18 - All of the landings in Stairwell #2 have been poured. Two of the three landings have been poured in Stairwell #1.



Photo 19 - Drive lane and drop off loop has been rough graded. Stone has been placed for curb and gutter.



Photo 20 - BMPs and Bus Parking area.



Photo 21 - Glass has been installed in three of the four sides of Area C.
