



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 09/28/2021

Weather: 80 degrees. Cloudy. High of 86 degrees today. Rain is in the forecast for this afternoon.

Hours Worked: 08:30hrs – 11:30hrs (3hrs)

**Beuchert Excavation:** Is on site and they are working on the Main Entrance area off of Route #3 and the student drop off area in front of the School. Their Sub-Contractor is also forming Curb and Gutter at the Main Bus Loop Entrance off of Route #3. The Sub is also pour curb in the Bus Loop area and also poured some sidewalks in front of Area A & Area B this morning.

**Industrial Concrete:** No one is on site this morning.

**J.D. Long, Masons:** Seven (7) men are on site today. They are cleaning block in various locations.

**Hazzard Electric:** Fourteen (14) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D. They are also trenching and running conduit in front of the Main Entrance of Area A.

**Colonial Webb:** They are running HVAC Duct in Area D and Area C and also installing the Utility Distribution System (UDS) in Area C, Kitchen.

**Weldon Steel:** I did not observe anyone on site.

**JP Construction:** Fifteen (15) men are on site today. They are studding out the Canopy Roof on the South side of Area C; laying out walls in Area C; hanging sheetrock in Area C and finishing Sheetrock in Area E.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is here today.

**FG & M:** Five (5) men are on site today. They are on site setting glass in various locations and two men are setting SF#53B.

**United Sprinkler:** One (1) man continues to run pipe in Area C&D.

**CTSI:** Three (3) men are on site. They are on site pulling low voltage wiring.

**M. L. Straight:** Three (3) men are on site today. I observed two men on site painting in Area D.

**K-Plus:** One (1) man is on site today caulking Control Joints in various locations.

**AAM:** They are installing metal panels on the North side of Area B.

**Hodgemen:** No one is here.

**Deleware Elevator:** No one is on site.

**S&S Concrete Cutting Company:** No one is on site today.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** A Tech was on site this morning inspecting Concrete and obtaining samples for the Lab.

**Conversations with Branch Builds:** I met with John, Brian, Cooper and Jake in the trailer. Brian asked me again if I had heard anything from the Contractor who is installing the Sewage Pump Station. I advised him I had not. I spoke with John about the width of Bus Entrance. I thought it appeared small. John said he thought the same thing, but it is being formed for curb and gutter according to plans. We also spoke briefly about the UDS being installed in the Kitchen.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel)**

**Submittals –**

**RFIs – #312**

**Patrick Byrne –**

**Change Order/PCOs/Pay App –**

**Changes in Procore –**

**Weekly Submittal Status Report:**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**

**PCO Log –**



Photo 1 - Bus Loop Entrance Curb & Gutter is being formed





Photo 2 - Sidewalk is being poured in front of Area A.





Photo 3 - Sidewalk poured in front of Area B and Metal Panels are being installed.





Photo 4 - Curb is being poured in the Bus Loop area.





Photo 5 - Curb is being poured in the Bus Loop Area.





Photo 6 - Millwork delivery is being unloaded.





Photo 7 - Sheetrock is being finished in the Gym.





Photo 8 - Metal Stud Framing of the Canopy on the South side of Area C.





Photo 9 - HVAC Duct is being installed in the Auditorium.





*Photo 10 - Metal Studs have been erected between Areas C & D.*





Photo 11 - One of two Range hoods has been delivered.





Photo 12 - 2nd Range Hood.



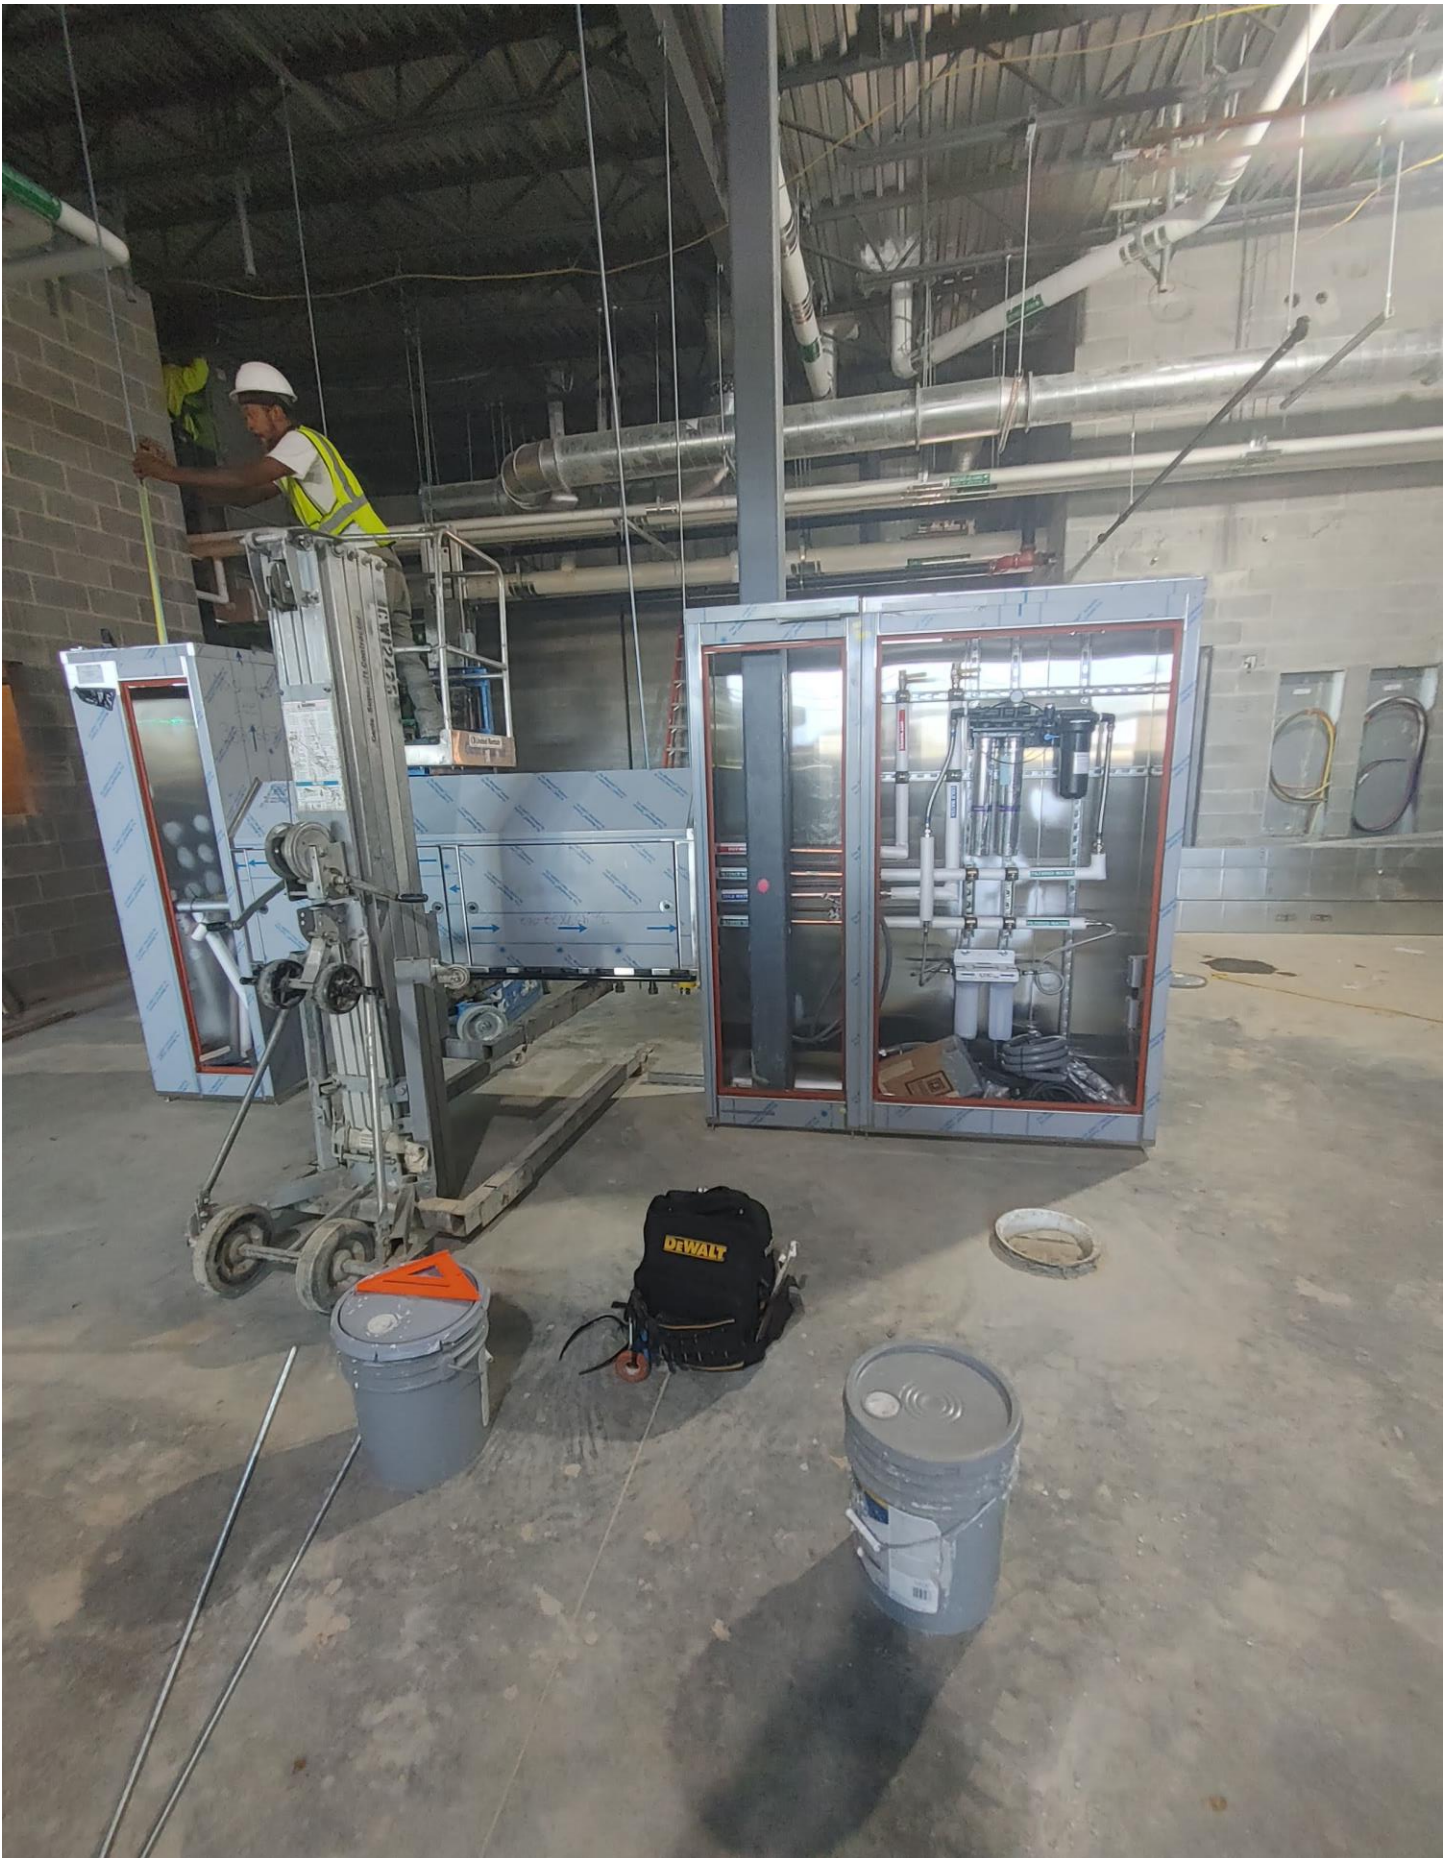


Photo 13 - Utility Distribution System and Water Filtration system is being installed.





Photo 14 - Lighting installed and energized in Area A, 1st floor.



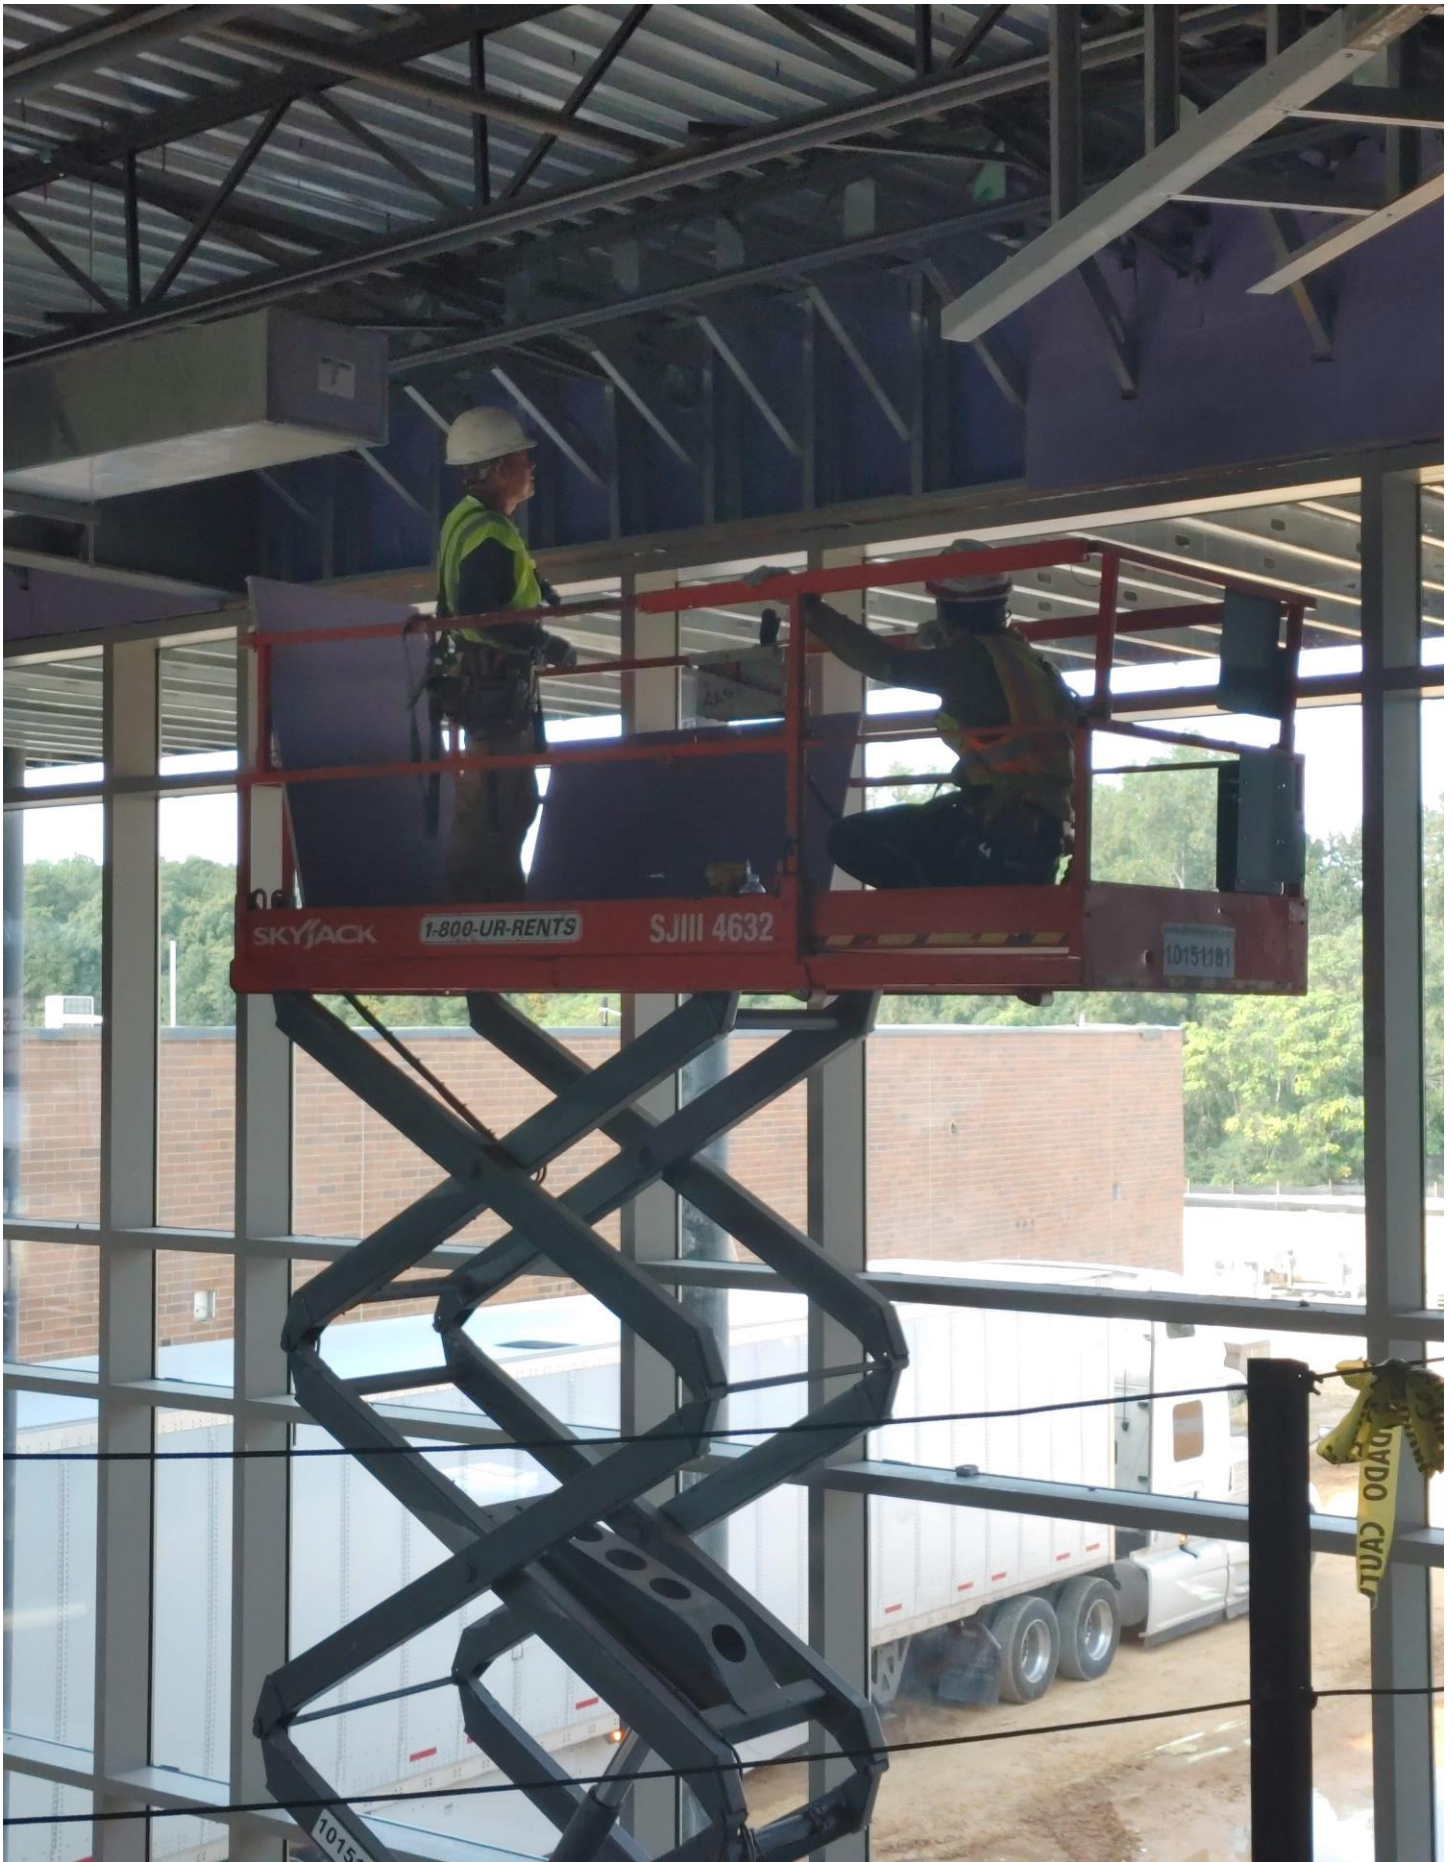


Photo 15 - Sheetrock is being hung in Area C.





Photo 16 - Utility Distribution System





Photo 17 - Trenching for Conduit at the Main Entrance
