



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 10/20/2021

Weather: 75 degrees. Sunny. High of 77 degrees today.

Hours Worked: 09:30hrs – 13:30hrs (4hrs)

Franklin Mechanical is on site today boring the Sewer line under Route #3 and digging the hole to place the Sewage tank. During the excavation for the tank they uncovered two 4" Low Voltage conduits. After meeting with Brian Topper and Hazzard it was agreed to shift the Tank a couple feet further into the green space to avoid the Low Voltage conduits.

Beuchert Excavation: Five (5) men are on site. They are grading between Areas A and B. I spoke with the Foreman and he advised that they started installing Bio Mix but that the third party supplier was having Trucking problems today and therefore they would not be receiving anymore Bio Mix today. Brain Topper advised the Hillis-Carnes Tech that he was no longer needed today.

Industrial Concrete: No one is on site this morning.

J.D. Long, Masons: I did not observe anyone on site during my visit.

Hazzard Electric: They have fourteen (14) men on site and they continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: They have nine (9) men on site today and they are running HVAC duct in Areas A, D & E. They are also running Storm water pipe on the South side of Area C.

Weldon Steel: I did not observe anyone on site.

JP Construction: Sixteen (16) men are on site working in various areas hanging Acoustical Ceiling Grid, hanging and finishing sheetrock.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: Six (6) men are on site. They continue to set frames and glass in various locations and are working on the Front Entrance SF69.

United Sprinkler: One (1) man is on site working on the Sprinkler System.

CTSI: Five (5) men are on site and are pulling low voltage wiring.

M. L. Straight: Five (5) men are on site Painting in Area A & C.

K-Plus: One man is on site caulking.

AAM: Four (4) men continue to install Metal Panels.

Hodgemen: Three (3) men are prepping and leveling floors in Area B today.

Deleware Elevator: One (1) man is on site working on the Elevator.

S&S Concrete Cutting Company: Two (2) men are on site coring the concrete slab in the Gym for Volley Ball pole sleeves.

TJ Distributers, INC: Four (4) men are here today installing Equipment in the Gym.

Linear Surveyors: No one is on site today.

Hillis-Carnes: A Tech was on site this morning to observe the placement of Bio Material. Ttransportation issue arose from the Bio Material Supplier, so the Tech was advised he could leave.

Conversations with Branch Builds: I met Brian, John, Jake and Cooper in the office they have established in Area A. briefly with Todd and Jacob on site. We discussed the installation of the Sewer line by Franklin Mechanical. We also discussed the work that was currently under way. I asked Brian when he thought they may be pouring the Grand Stairway landing and setting the steps. He said he thought it would be happening in December. John asked if I knew the status of Atlantic Broadband being brought into the building. I told him that Dr. Perry was handling that matter.

Finally, Brian and I spoke yesterday. Brian wanted to know if I or the County had any pull with Dominion Power to expedite the removal of the Temp Service & pole that was installed at the beginning of the project. Brian said he was being told that it may be five weeks before Dominion could remove the Temp Service. I asked Brian to get me the Work Order number and I would see if there was anything I could do.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) Two Reports for 10/18/2021

Submittals –

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report:

Weekly RFI Status Update –
Weekly Daily Log Summary –
PCO Log –



Photo 1 - Sewage Tank is being off loaded



Photo 2 - Storm Water Pipe is being laid on the South side of Area C



Photo 3 - They have begun to lay stone between Areas D & E.

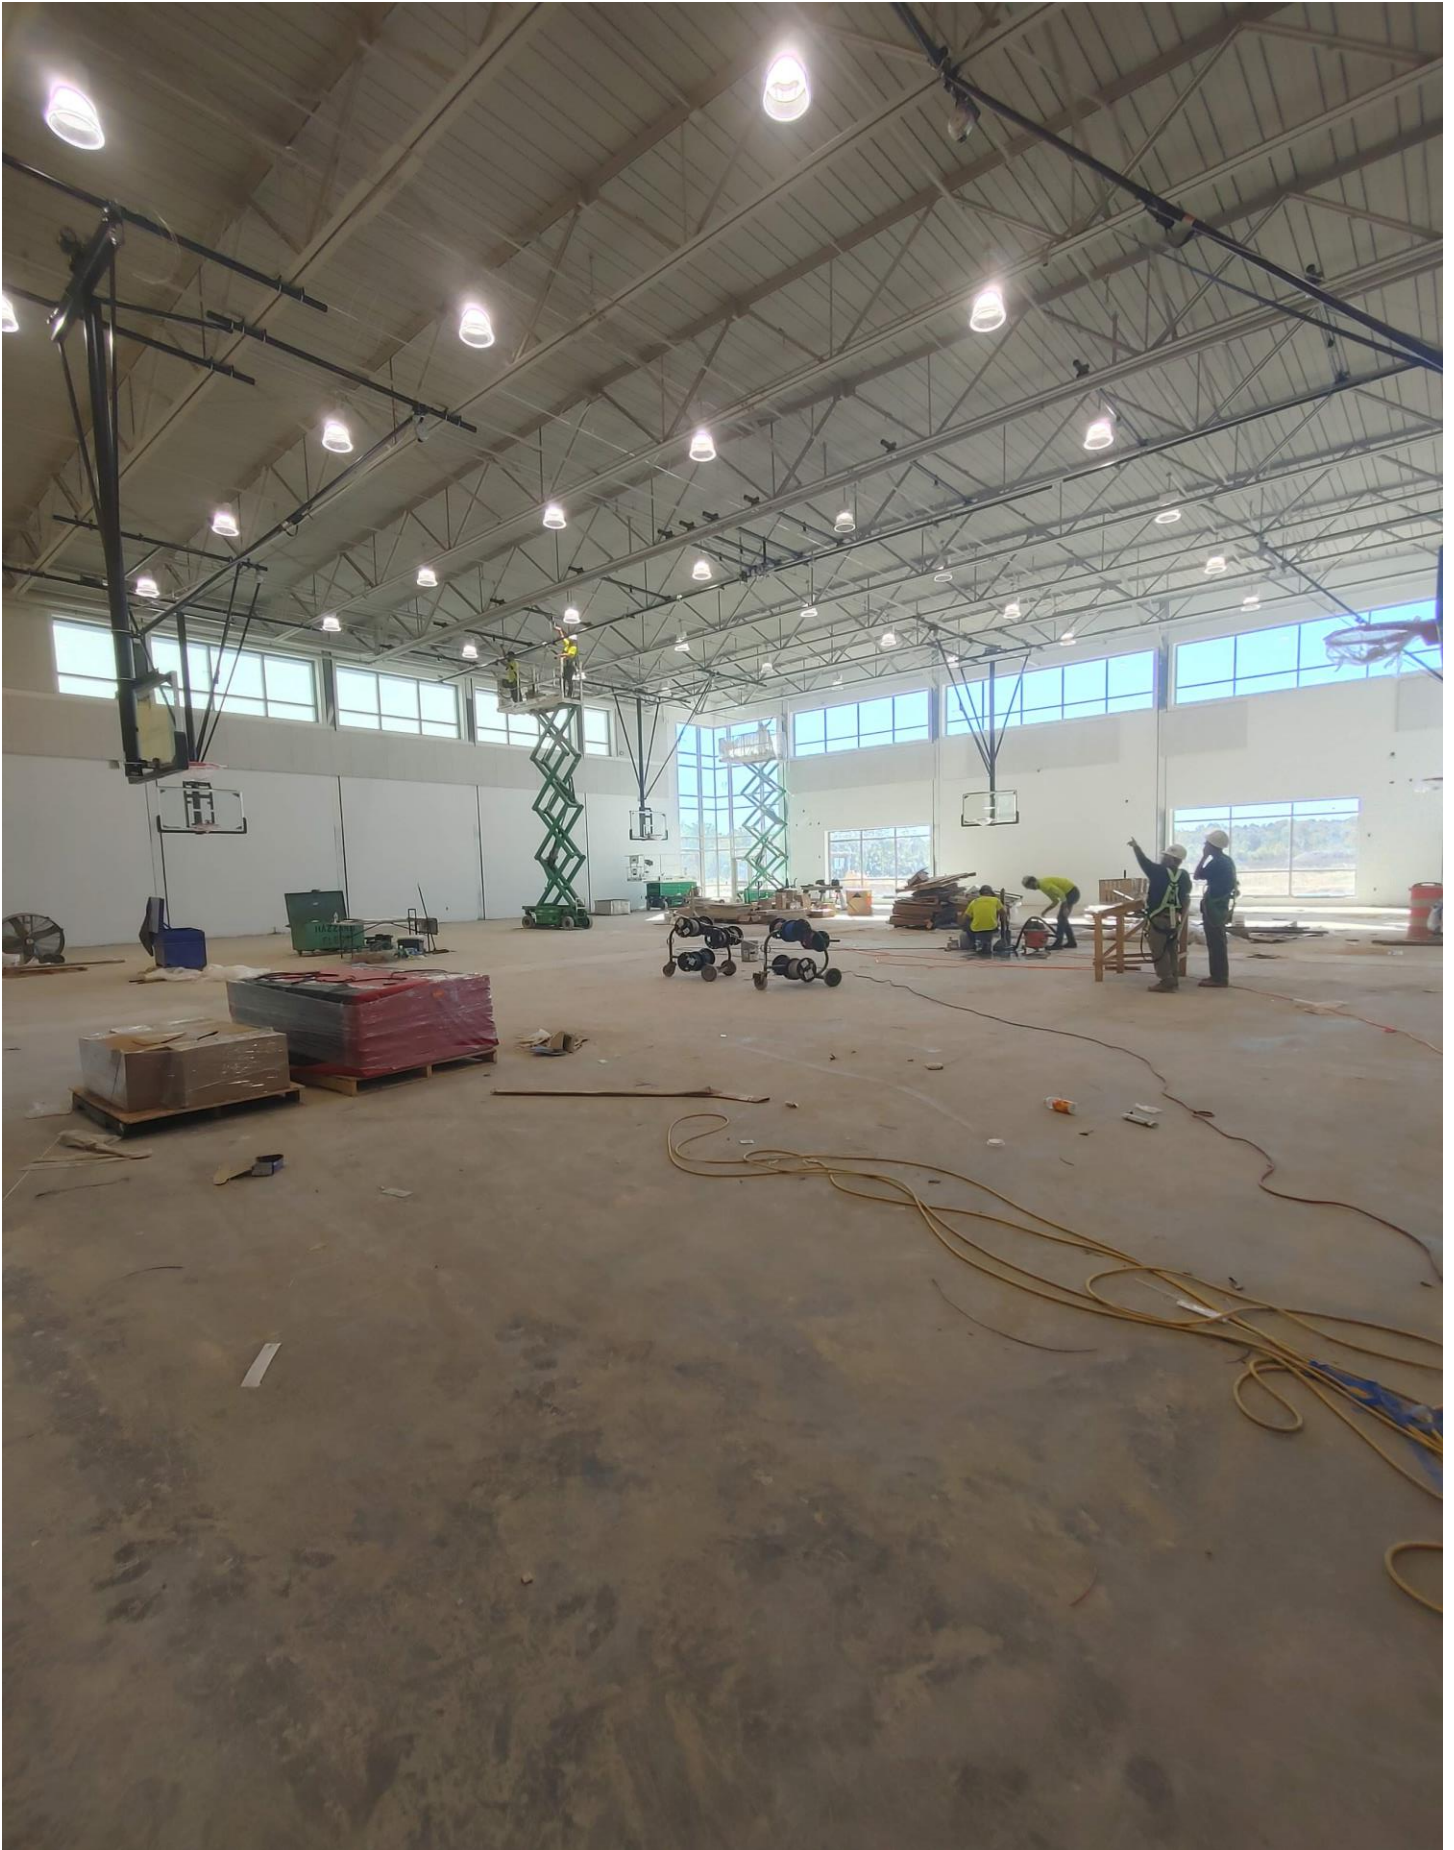


Photo 4 - Gym Equipment is being installed.



Photo 5 - Gym Floor is being cored for Volley Ball Pole Sleeves.



Photo 6 - North wall of Gym has received a coat of paint.



Photo 7 - Beuchert is working on the West side of Area C.



Photo 8 - First lift of Bio Material has been installed.



Photo 9 - Acoustical Ceiling Grid has been installed throughout Area E.



Photo 10 - FG&M is working on SF69

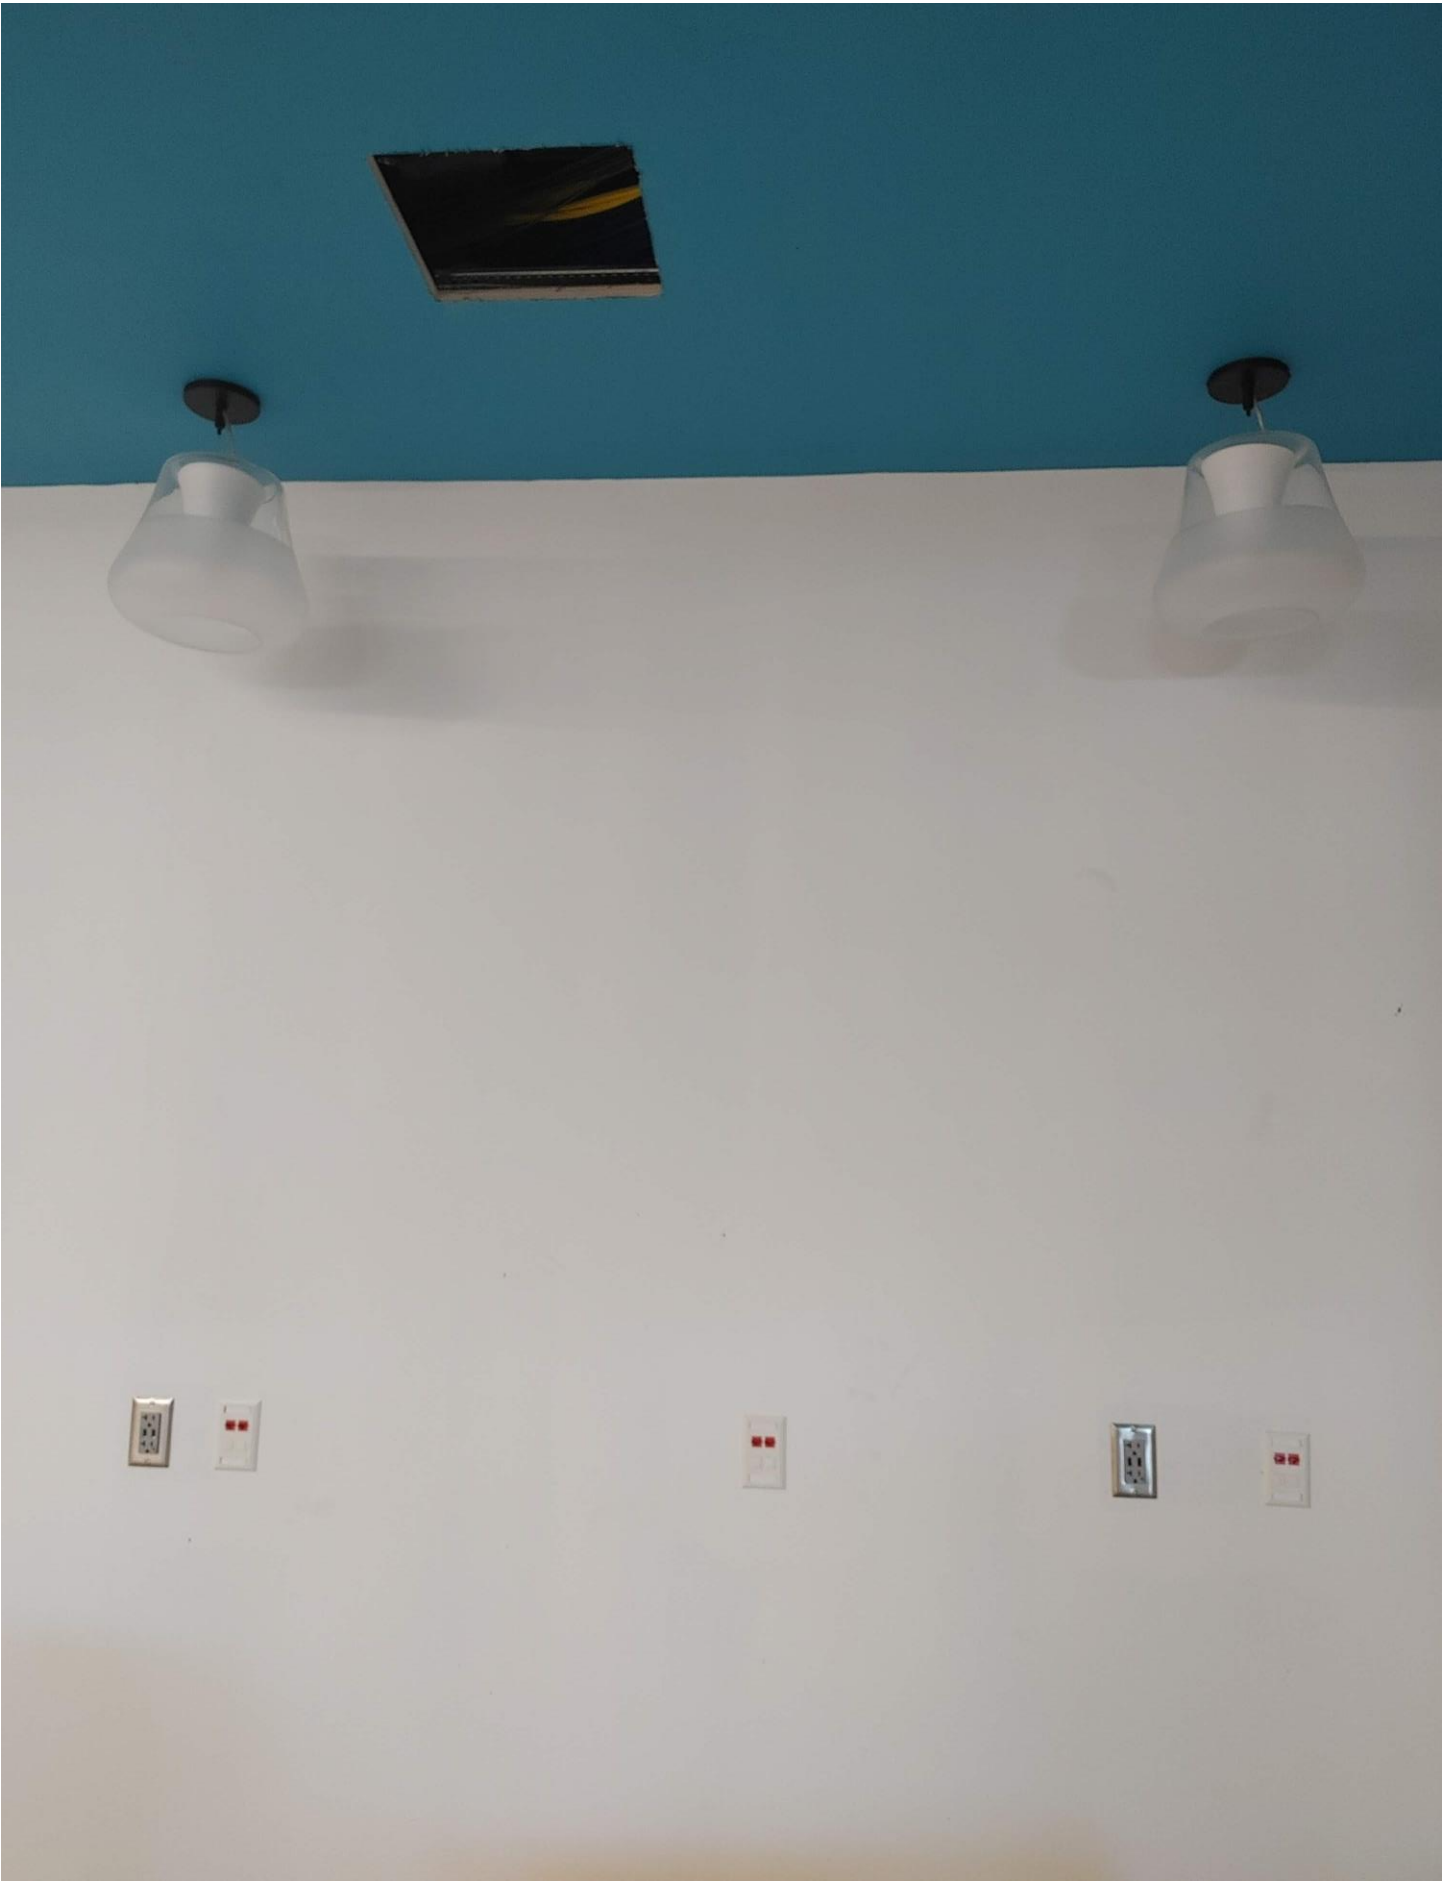


Photo 11 - Globe style lights are being installed in Area A



Photo 12 - LED Lights in Area A



Photo 13 - Excavation for the Sewage Tank has begun.
