



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 11/02/2021  
Weather: 52 degrees. Rain. High of 54 degrees today.  
Hours Worked: 10:30 – 13:30hrs (3hrs)

**Beuchert Excavation:** Five (5) men are on site today working on the West side of the School. Stone is also being delivered. Rain cause them to call it an early day.

**Industrial Concrete:** One (1) man is on site today grinding down Diamond that are sitting high.

**J.D. Long, Masons:** I did not observe anyone on site during my visit.

**Hazzard Electric:** Twelve (12) men are on site. They are running conduit out to the Student Parking area and setting light fixtures and Emergency Egress signage in Area A. They hope to energize the fixtures in the Administrative Office area later this week.

**Colonial Webb:** I observed two men on site today. I advised there site Superintendent that there was one of their ladders sticking out of the Water Meter Vault on the East side of the Site. I had the ladder removed and the lid shut because it was raining and the Vault does not have a Sump Pump. He indicated that someone must of borrowed the ladder because they have no reason to be in the pit. I told him he may want to get his ladder so that it doesn't walk away.

**Weldon Steel:** I did not observe anyone on site.

**JP Construction:** No one is on site today.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is here today.

**FG & M:** Four (4) men were on site today. They continue to set frames and glass in various locations and continue to work on SF5A in Area E.

**United Sprinkler:** One (1) man on site both days working on the Sprinkler System in Area E.

**CTSI:** Three (3) men are on site and are pulling low voltage wiring in Area E.

**M. L. Straight:** Five (5) men are on site Painting in Area A & C..

**K-Plus:** No one is on site.

**AAM:** Five (5) were on site but the rain caused them to leave.

**Hodgemen:** Four (4) men are working leveling floor in Area B.

**Deleware Elevator:** No one was on site during either visit.

**S&S Concrete Cutting Company:** No one was on site yesterday or today.

**TJ Distributers, INC:** No one was on site yesterday or today.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe anyone on site during my visits.

**Conversations with Branch Builds:** I met with John and Jake this morning. I asked them if Brian had relayed to them the County's request to have the Sign on the Corner of County Park Drive repainted. The lettering had faded that said Construction Entrance with an Arrow pointing traffic to the Construction Entrance of the site. Some delivery traffic was observed using County Park Drive. They indicated that Brian had relayed the info and they would have it addressed. I also asked if Brian had relayed my inquiry into the different mounting heights of the Mitsubishi Head units in the Room behind the Stage. Jake said he was looking into the matter. I also asked about the Concrete that has yet to be poured in the North East corner of the Administrative area on Area A. John said that they working on get their Sub (industrial Concrete) out to address that and several other areas around the site.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. DEQ has scheduled a visit for November 15, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report - 10/29/2021, 11/01/2021**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel)**

**Hillis-Carnes Bio Retention Pond Reports –**

**Submittals –**

**RFIs – #337, #343**

**Patrick Byrne –**

**Change Order/PCOs/Pay App – Change Order #12**

**Weekly Submittal Status Report:**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**

**PCO Log –**



Photo 1 - They have begun to pour Light Poles Bases in front of the School.



Photo 2 - The Mow Strip has been poured on the North side of Area A.



Photo 3 - Concrete has yet to be poured in the North East corner of the Administrative Office Area.

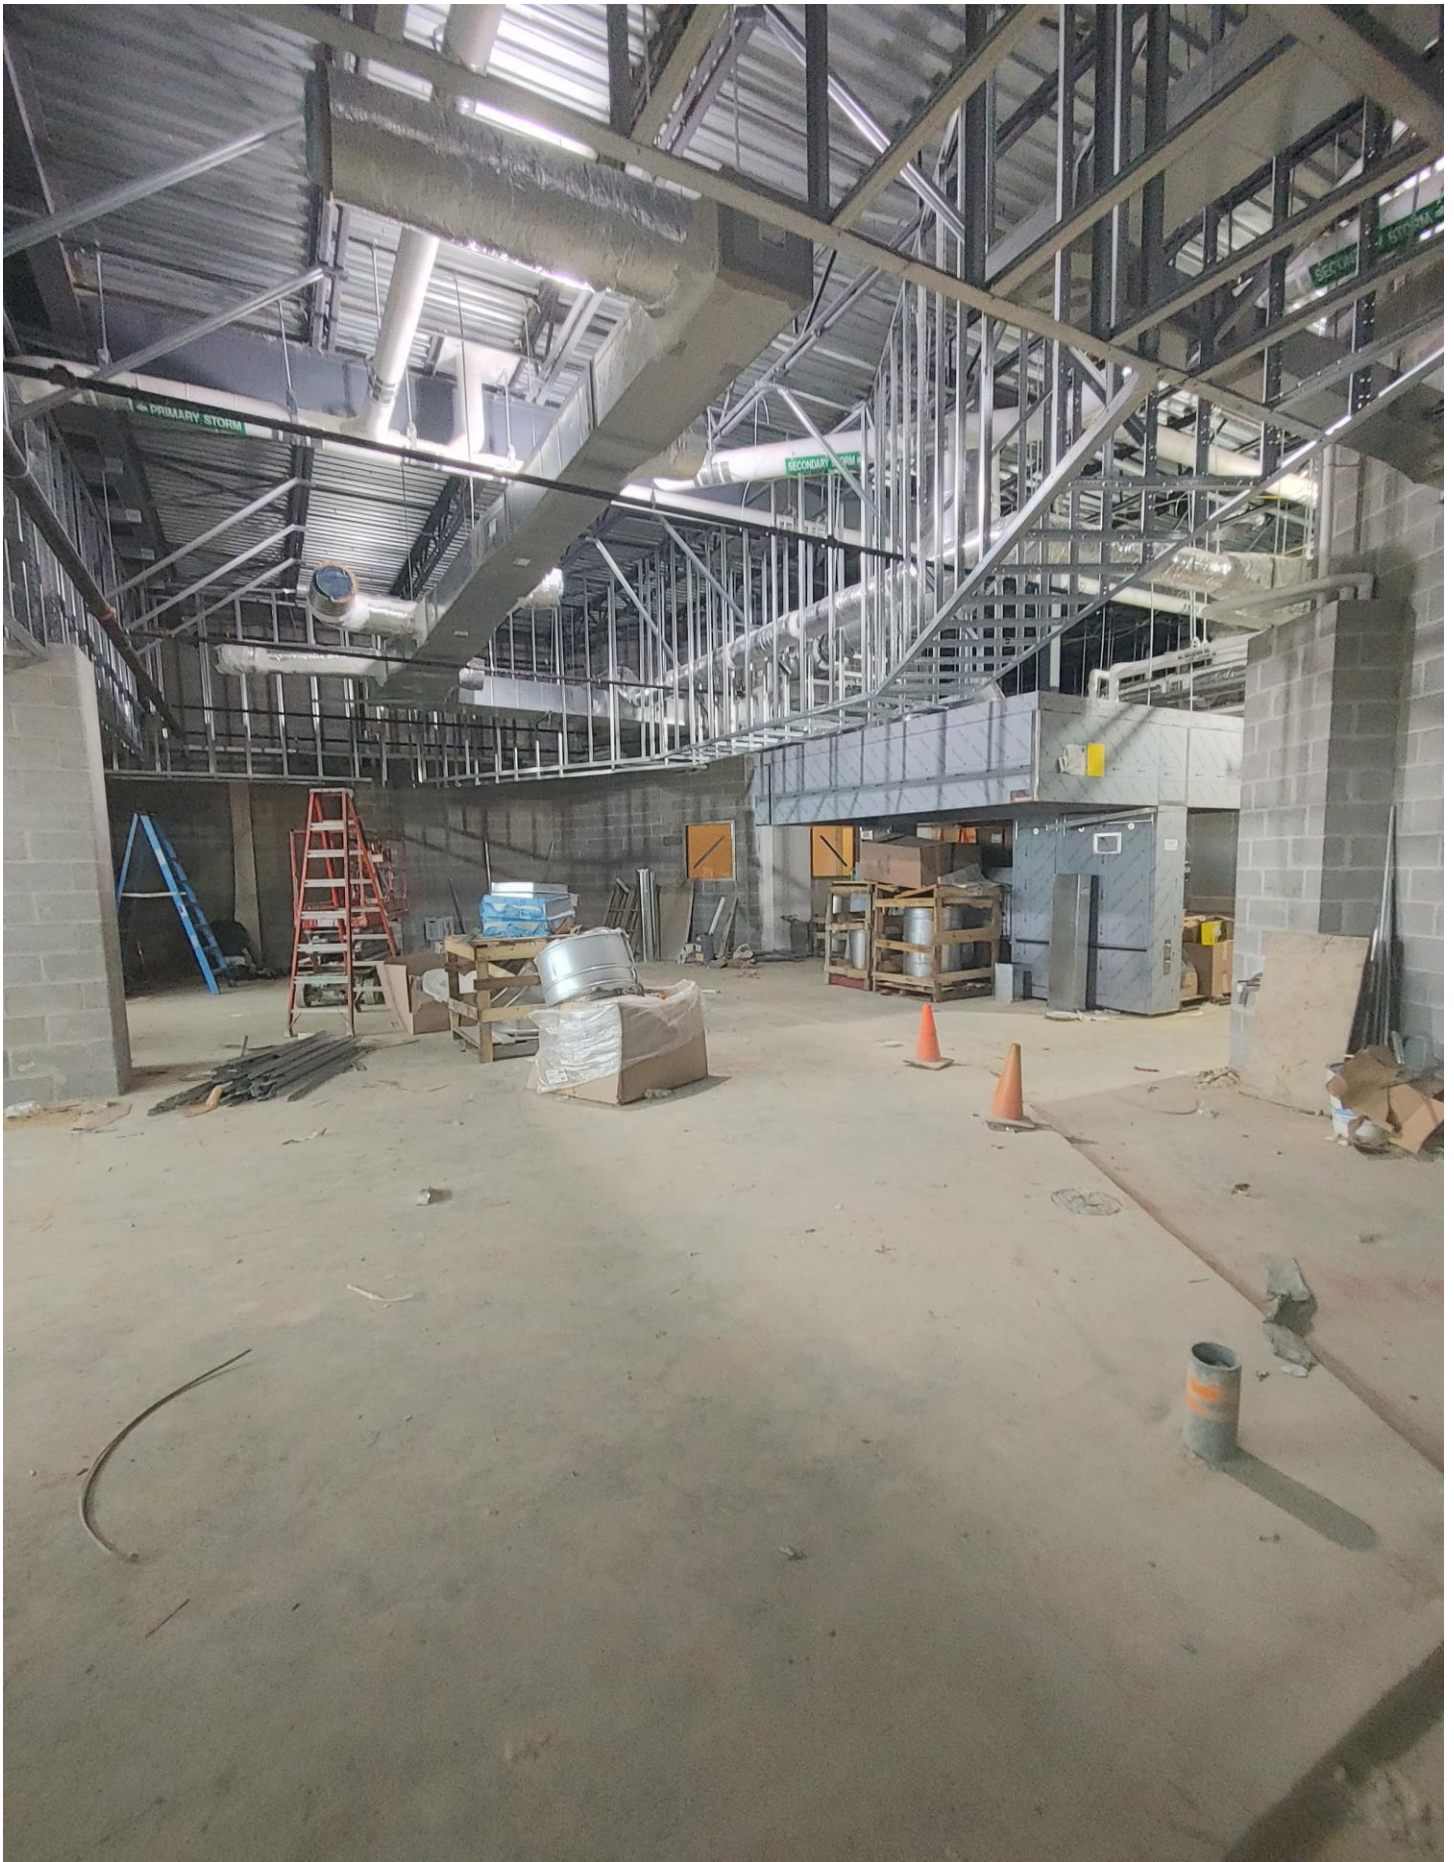


Photo 4 - Bulk Head Framing continues in the Kitchen Area.

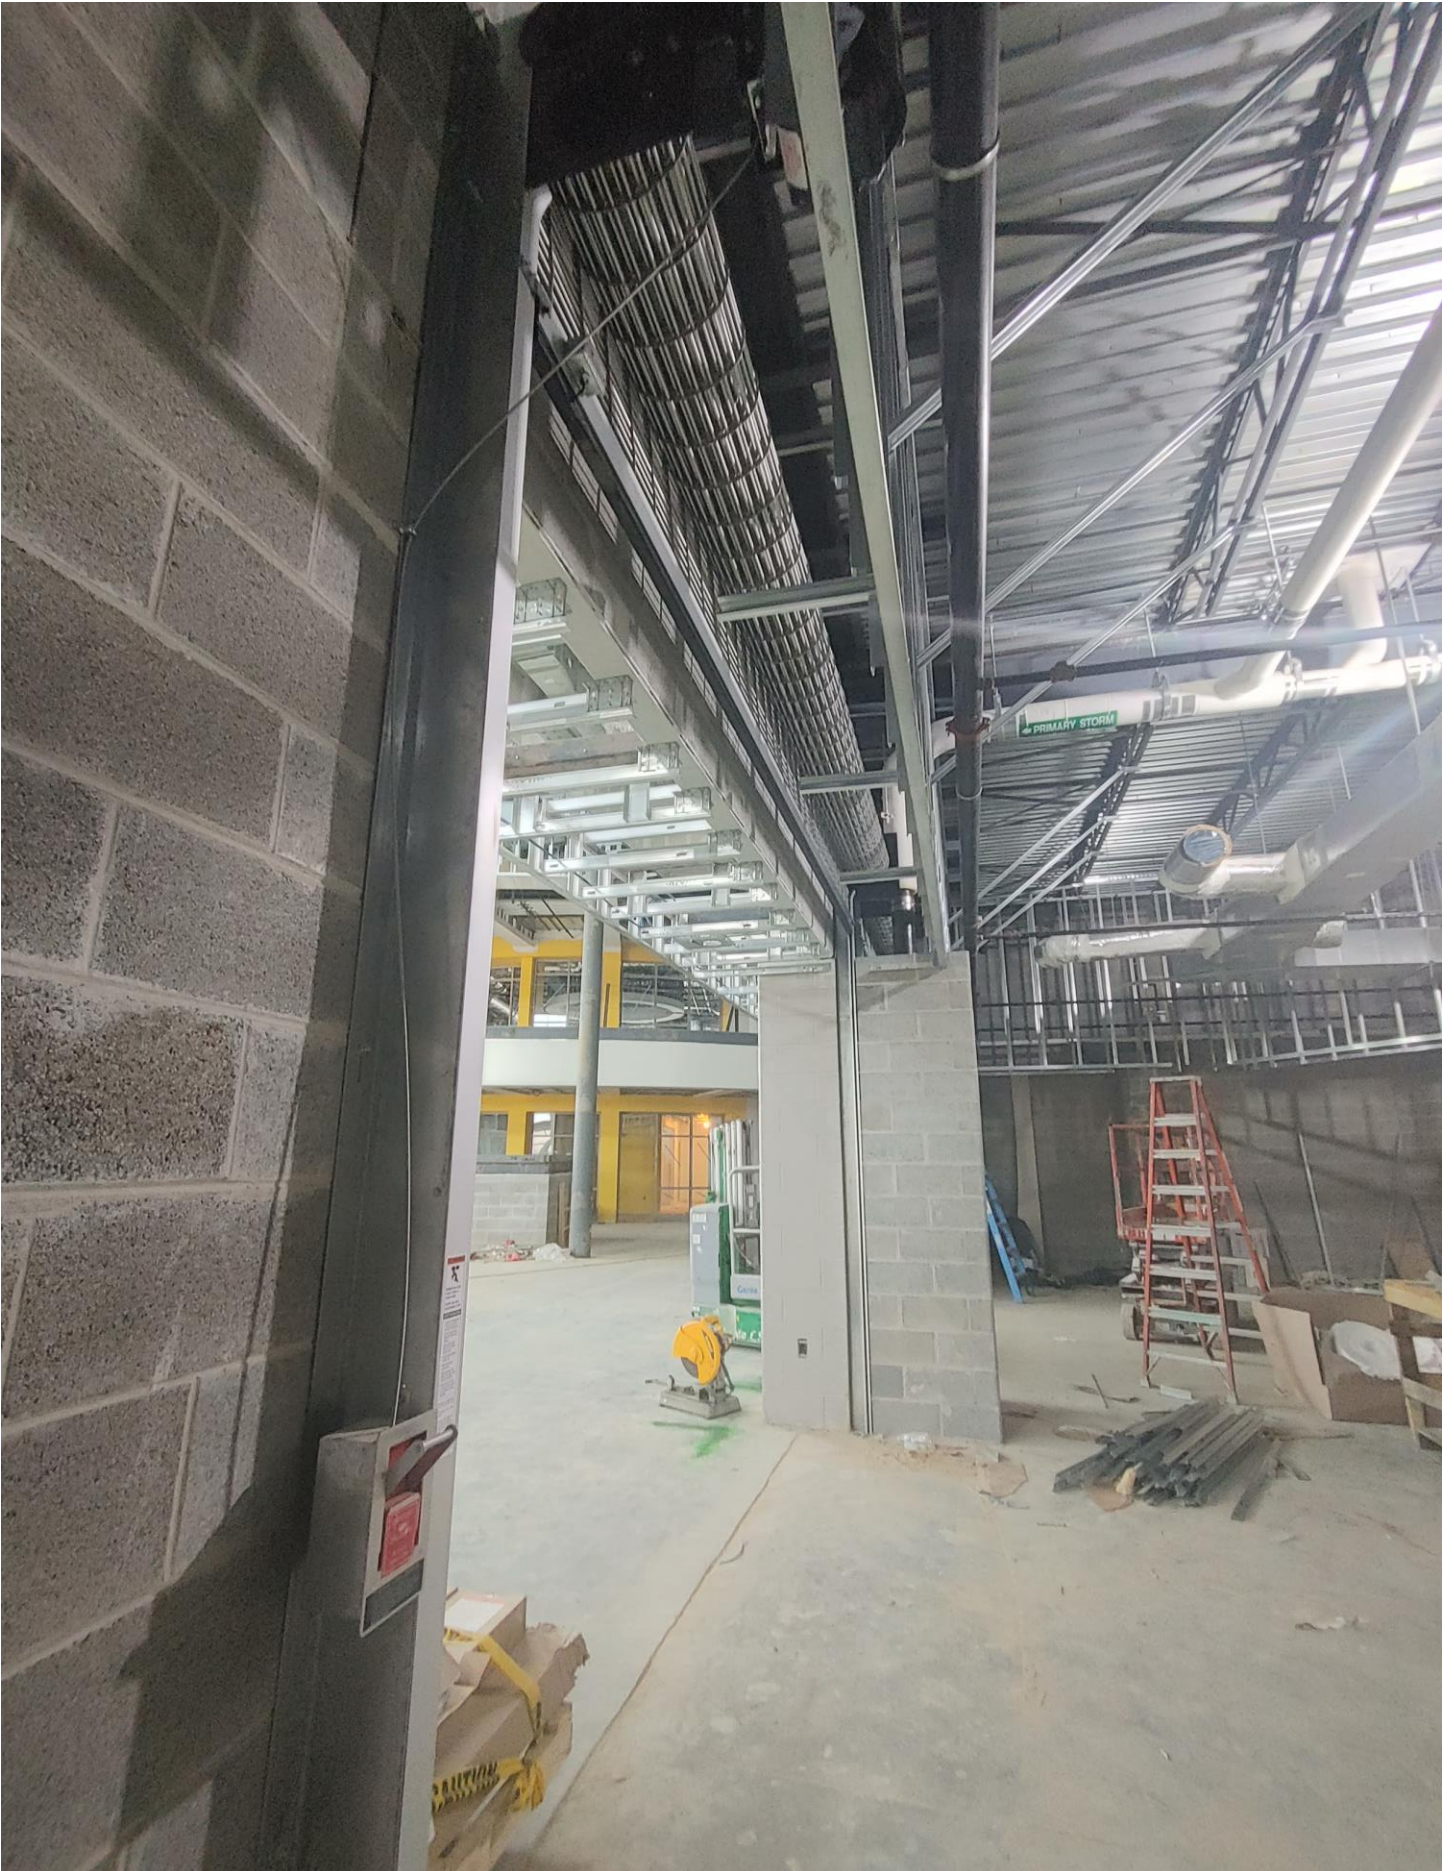
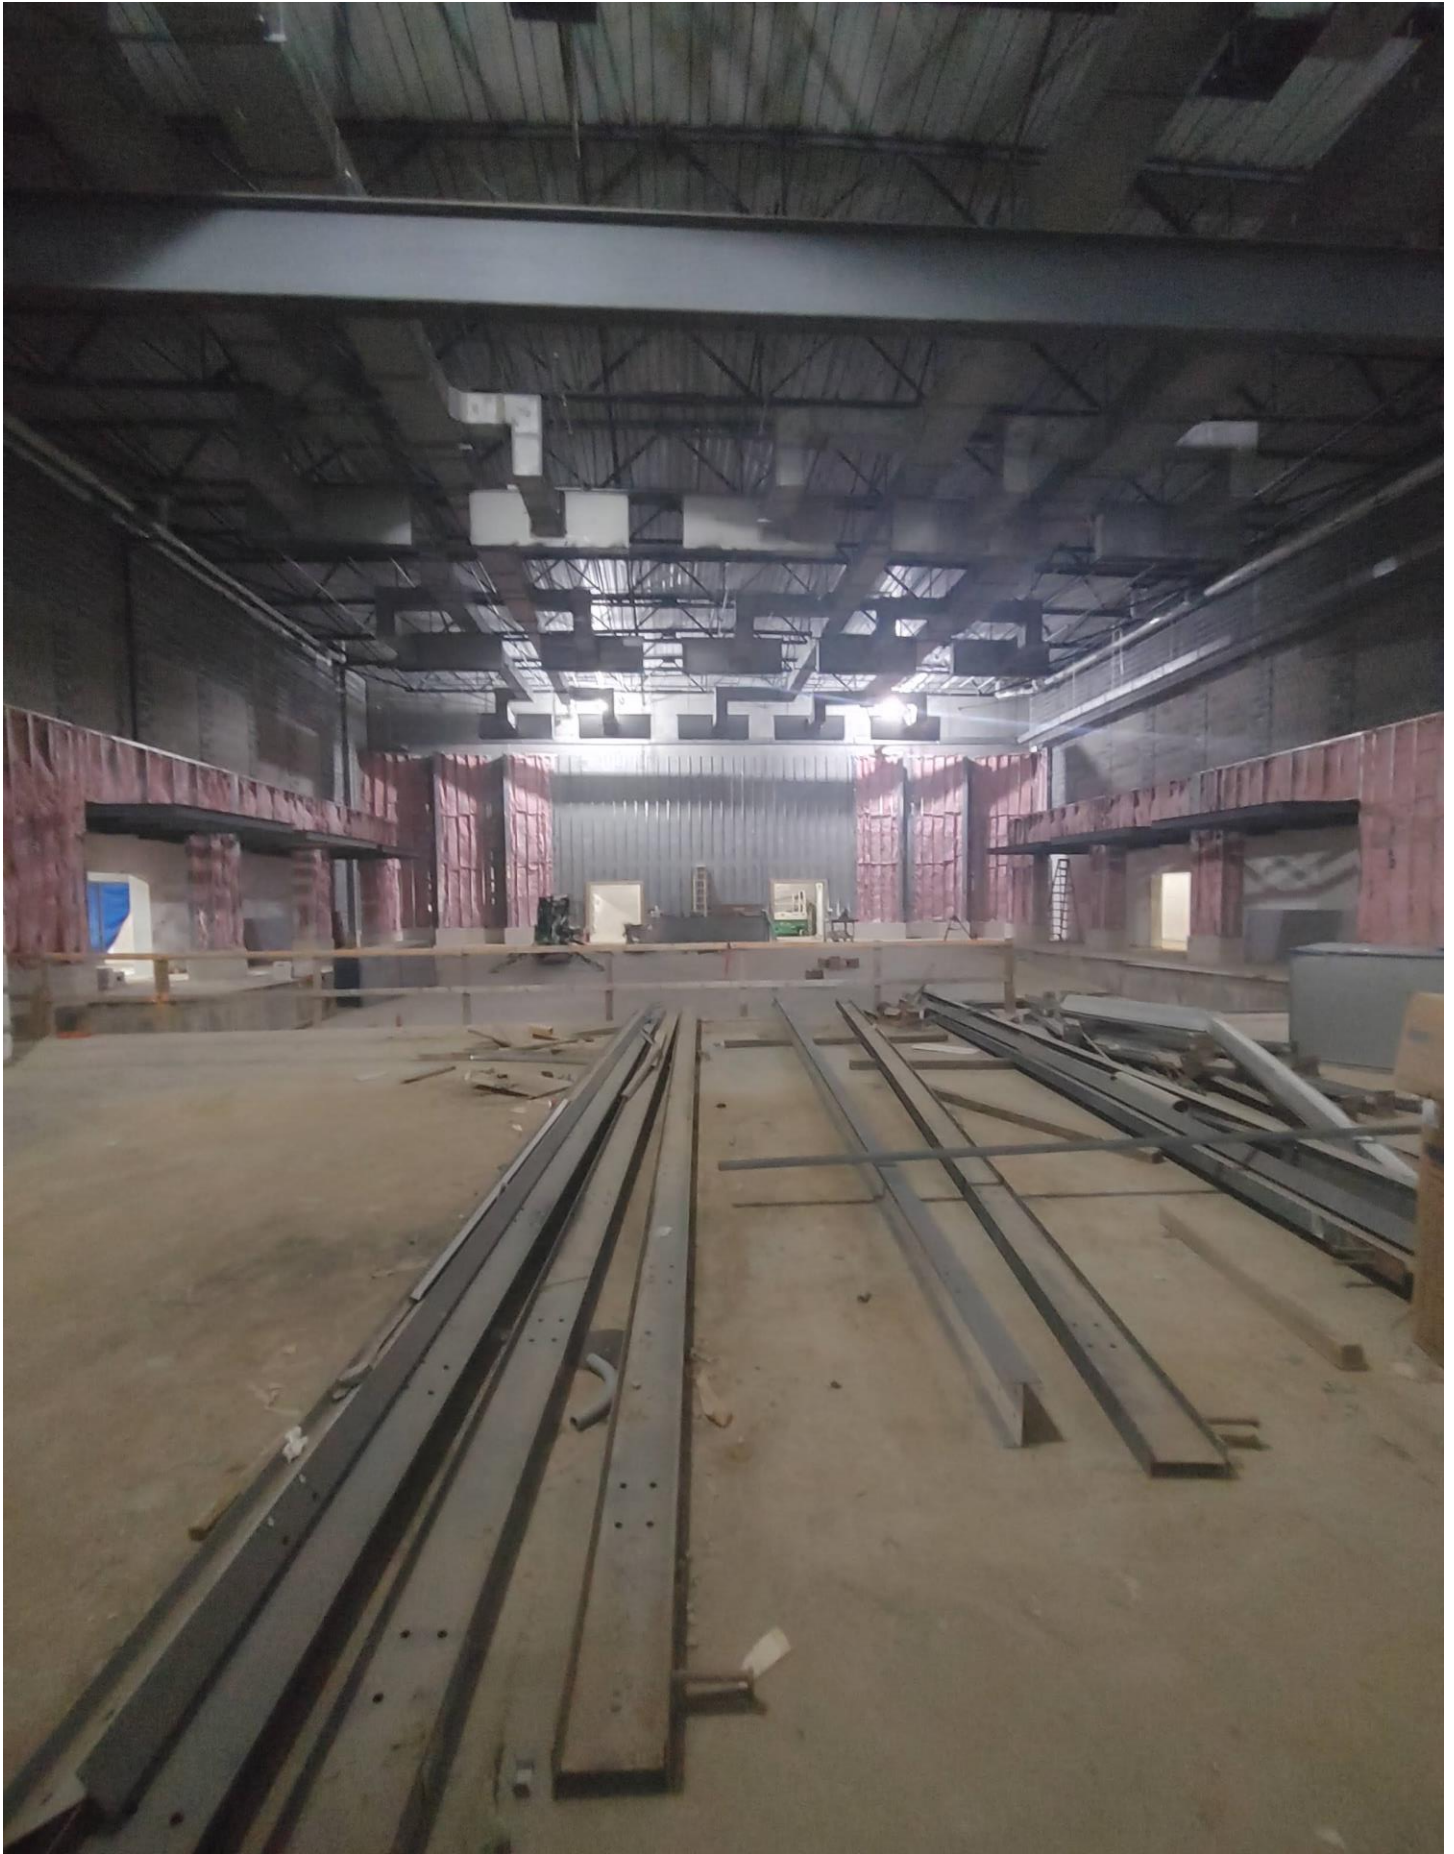


Photo 5 - Overhead Doors have been installed in the Kitchen.



*Photo 6 - Unprotected Drop Inlet in the Loading Dock Area allowing silt into the Storm Water Management System.*





*Photo 7 - They have begun to install Insulation in the Auditorium.*



Photo 8 - Insulation has been installed in Area D

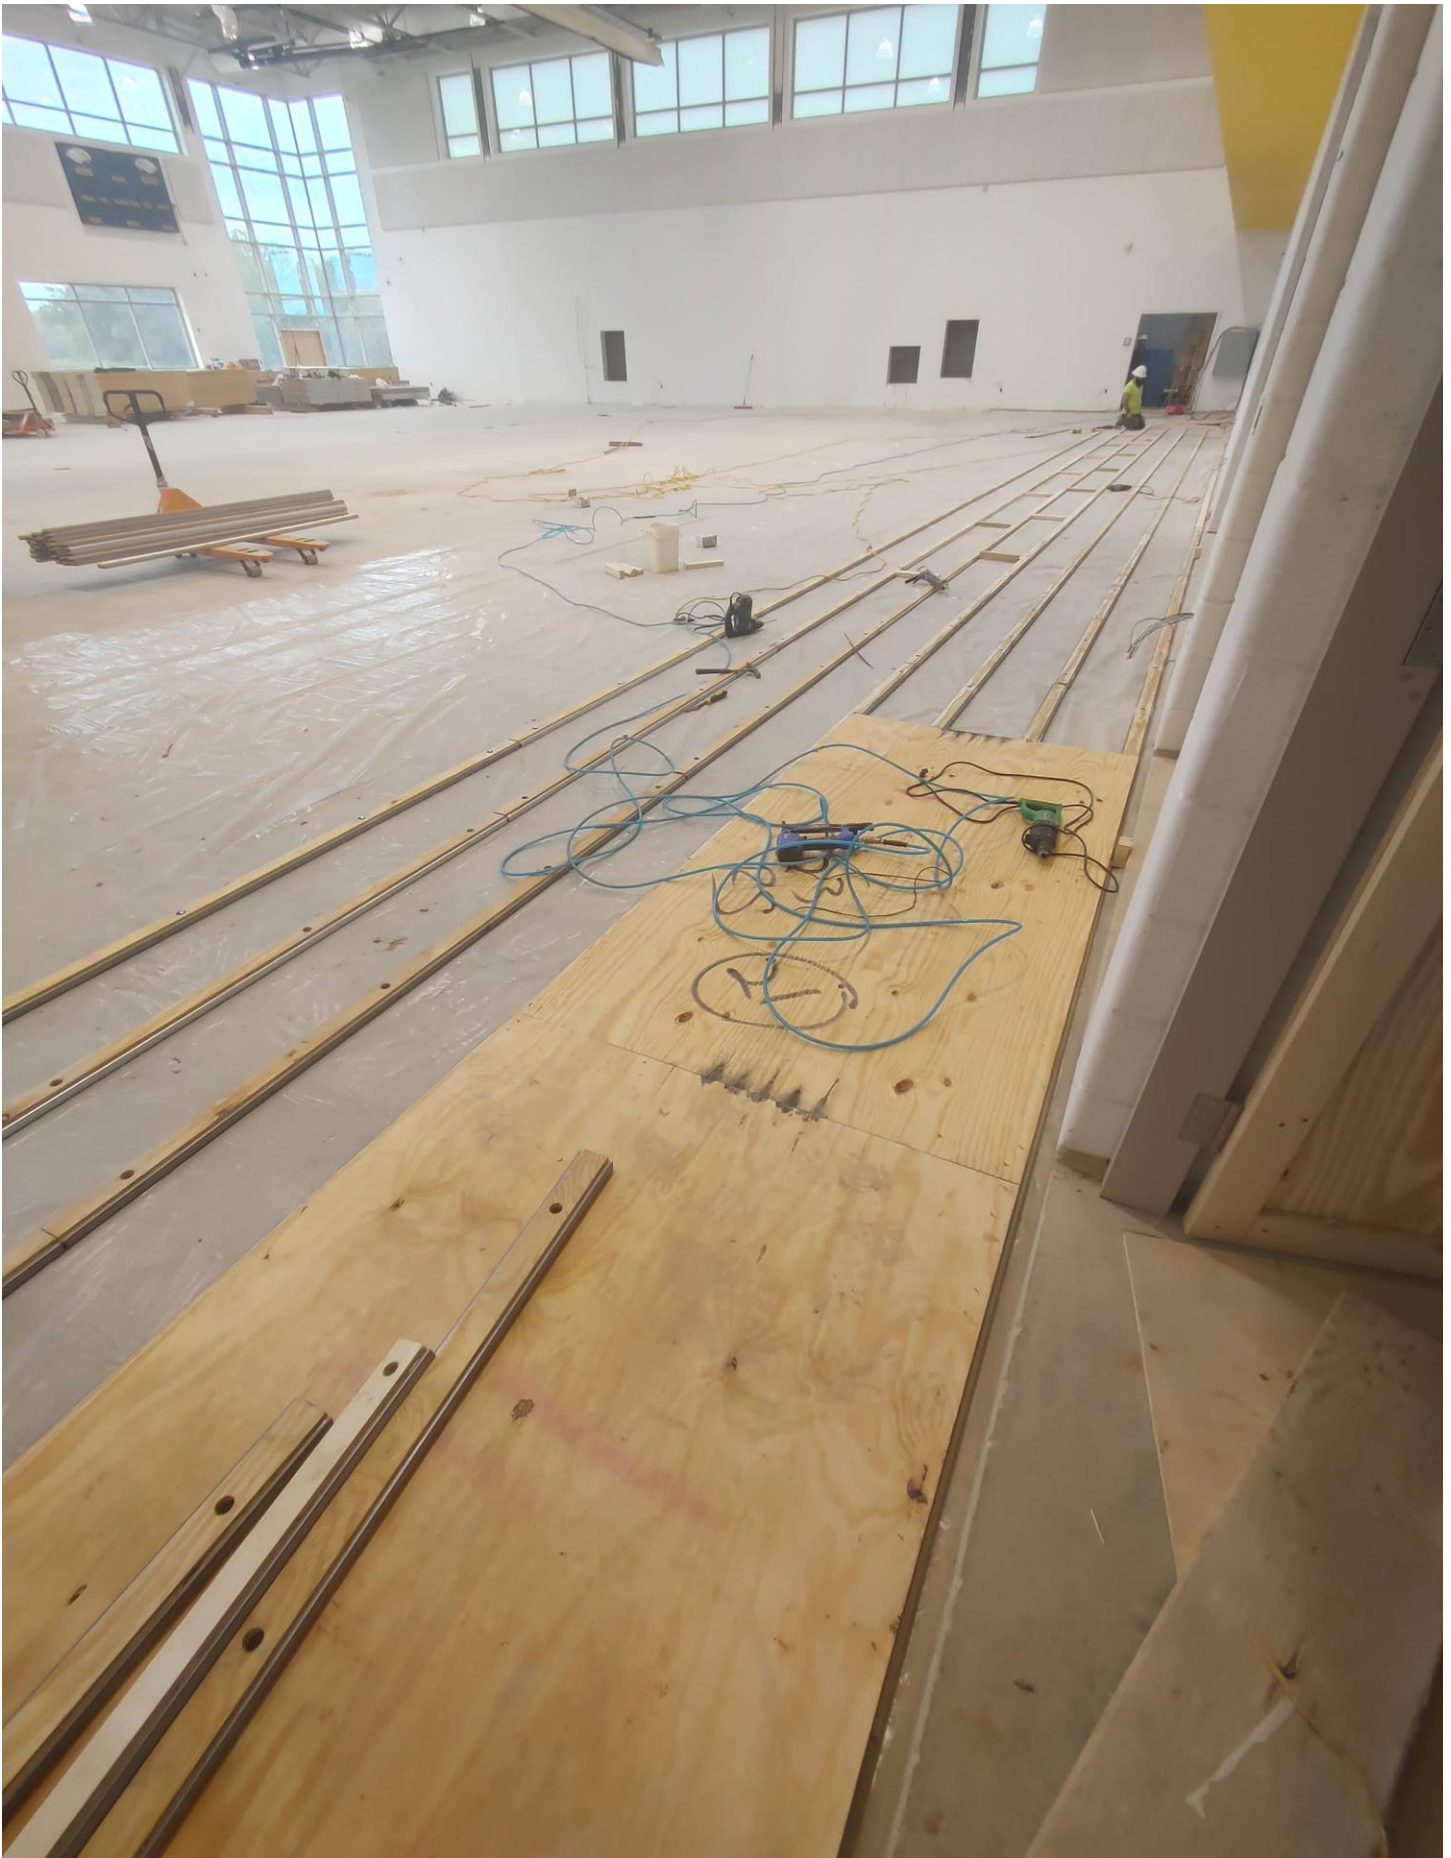


Photo 9 - They have begun to lay the floor in the Gymnasium.



Photo 10 - FG&M continue to work on SF5A in Area E.



Photo 11 - Cabinetry has been installed throughout Area B



*Photo 12 - Stone is being delivered on the West side of the site.*



*Photo 13 - View from the roof of the South West side of the site.*



Photo 14 - Stone has been laid between Area B & E.
