



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 01/05/2022

Weather: 44 degrees. Cloudy. High of 46 degrees today. Snow still on ground from storm Monday Morning. The area received approximately 6" of snow and ice.

Hours Worked: 11:00 – 12:30hrs (1.5hrs) Progress Meeting  
12:30 – 15:30hrs (3hrs) Site Visit.

**Beuchert Excavation:** Is not on site today.

**Industrial Concrete:** I did not observe them on site during my visit.

**J.D. Long, Masons:** No one is on site today.

**Hazzard Electric:** They are on site working in various areas around the site.

**Colonial Webb:** They are on site working in various areas.

**Talley & Armstrong (Sub-Contractor of Beuchert):** I did not onserve anyone on site today.

**Weldon Steel:** I did not observe anyone on site.

**JP Construction:** They have a crew on site today running ceiling grid in Area C and setting acoustical tile in Area A.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is here today.

**FG & M:** I did not observe anyone on site today.

**United Sprinkler:** I did not observe anyone on site today.

**CTSI:** They are on site and are pulling low voltage wiring.

**M. L. Straight:** They are currently painting in Area B.

**K-Plus:** I did not note anyone on site during my visit.

**AAM:** Metal Panel Sub. I did not see anyone on site during my visit.

**Hodgemen:** They have a crew on site laying VCT in Area B.

**Deleware Elevator:** Two men are on site today working in the Elevator Equipment room and Elevator Pit.

**S&S Concrete Cutting Company:** No one is on site today.

**DES:** They have a few men on site assembling Cabinetry in Area A.

**Smith:** Epoxy Floor Sub. No one is on site to my knowledge.

**TJ Distributers, INC:** A crew is on site working on the Gymnasium Bleachers.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe a Tech on site during my visit.

**Conversations with Branch Builds:** During the Progress Meeting today I inquired as to the status of the outstanding items identified in the Email Hillis-Carnes sent out in mid-November. After the meeting I met with Todd, Copper, Lee and John and we discussed the outstanding items. Branch indicated that most of the items that we flagged by Hillis-Carnes have been addressed and resolved. Branch is going to reach back out to Hillis-Carnes and request an updated list.

During my visit today I noted that the Sprinkler Pipe and Heads under the Grand Staircase are readily accessible. I understand the need and requirement for these heads. However, I just point out their accessibility and the potential to be damaged or vandalized by students. Furthermore, I noted that the hanging lights adjacent to the Grand Staircase are accessible from the Staircase. Again I only point this out as something that may or may not be of concern to school faculty. I have attached pictures below of the Sprinkler head and lights I am referring to above.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports –**

**Hillis-Carnes Bio Retention Pond Reports –**

**Submittals –**#07 84 46-2.1, #08 80 00-2.2, #08 80 00-4.0, #11 31 00-5.0, #25 32 13-5.0, #26 50 00-5.4, #27 53 00-1.0, #27 53 00-2.0

**RFIs –** #328, #346, #356, #357, #359, #360,

**Patrick Byrne –**

**Alexes Lee –**

**Tara Delaney –**

**Change Order/PCOs/Pay App –**

**Weekly Submittal Status Report: 12/31/2021**

**Weekly RFI Status Update – 12/31/2021**

**Weekly Daily Log Summary – 12/31/2021**

**PCO Log – 12/31/2021**



Photo 1 - Lights have been installed in Corridor A13 near the main entrance.




Photo 2 - Acoustical Ceiling Grid and HVAC Duct is being installed.




Photo 3 - Acoustical Tile being installed in Area A.



Photo 4 - White Boards being stored in Area D.

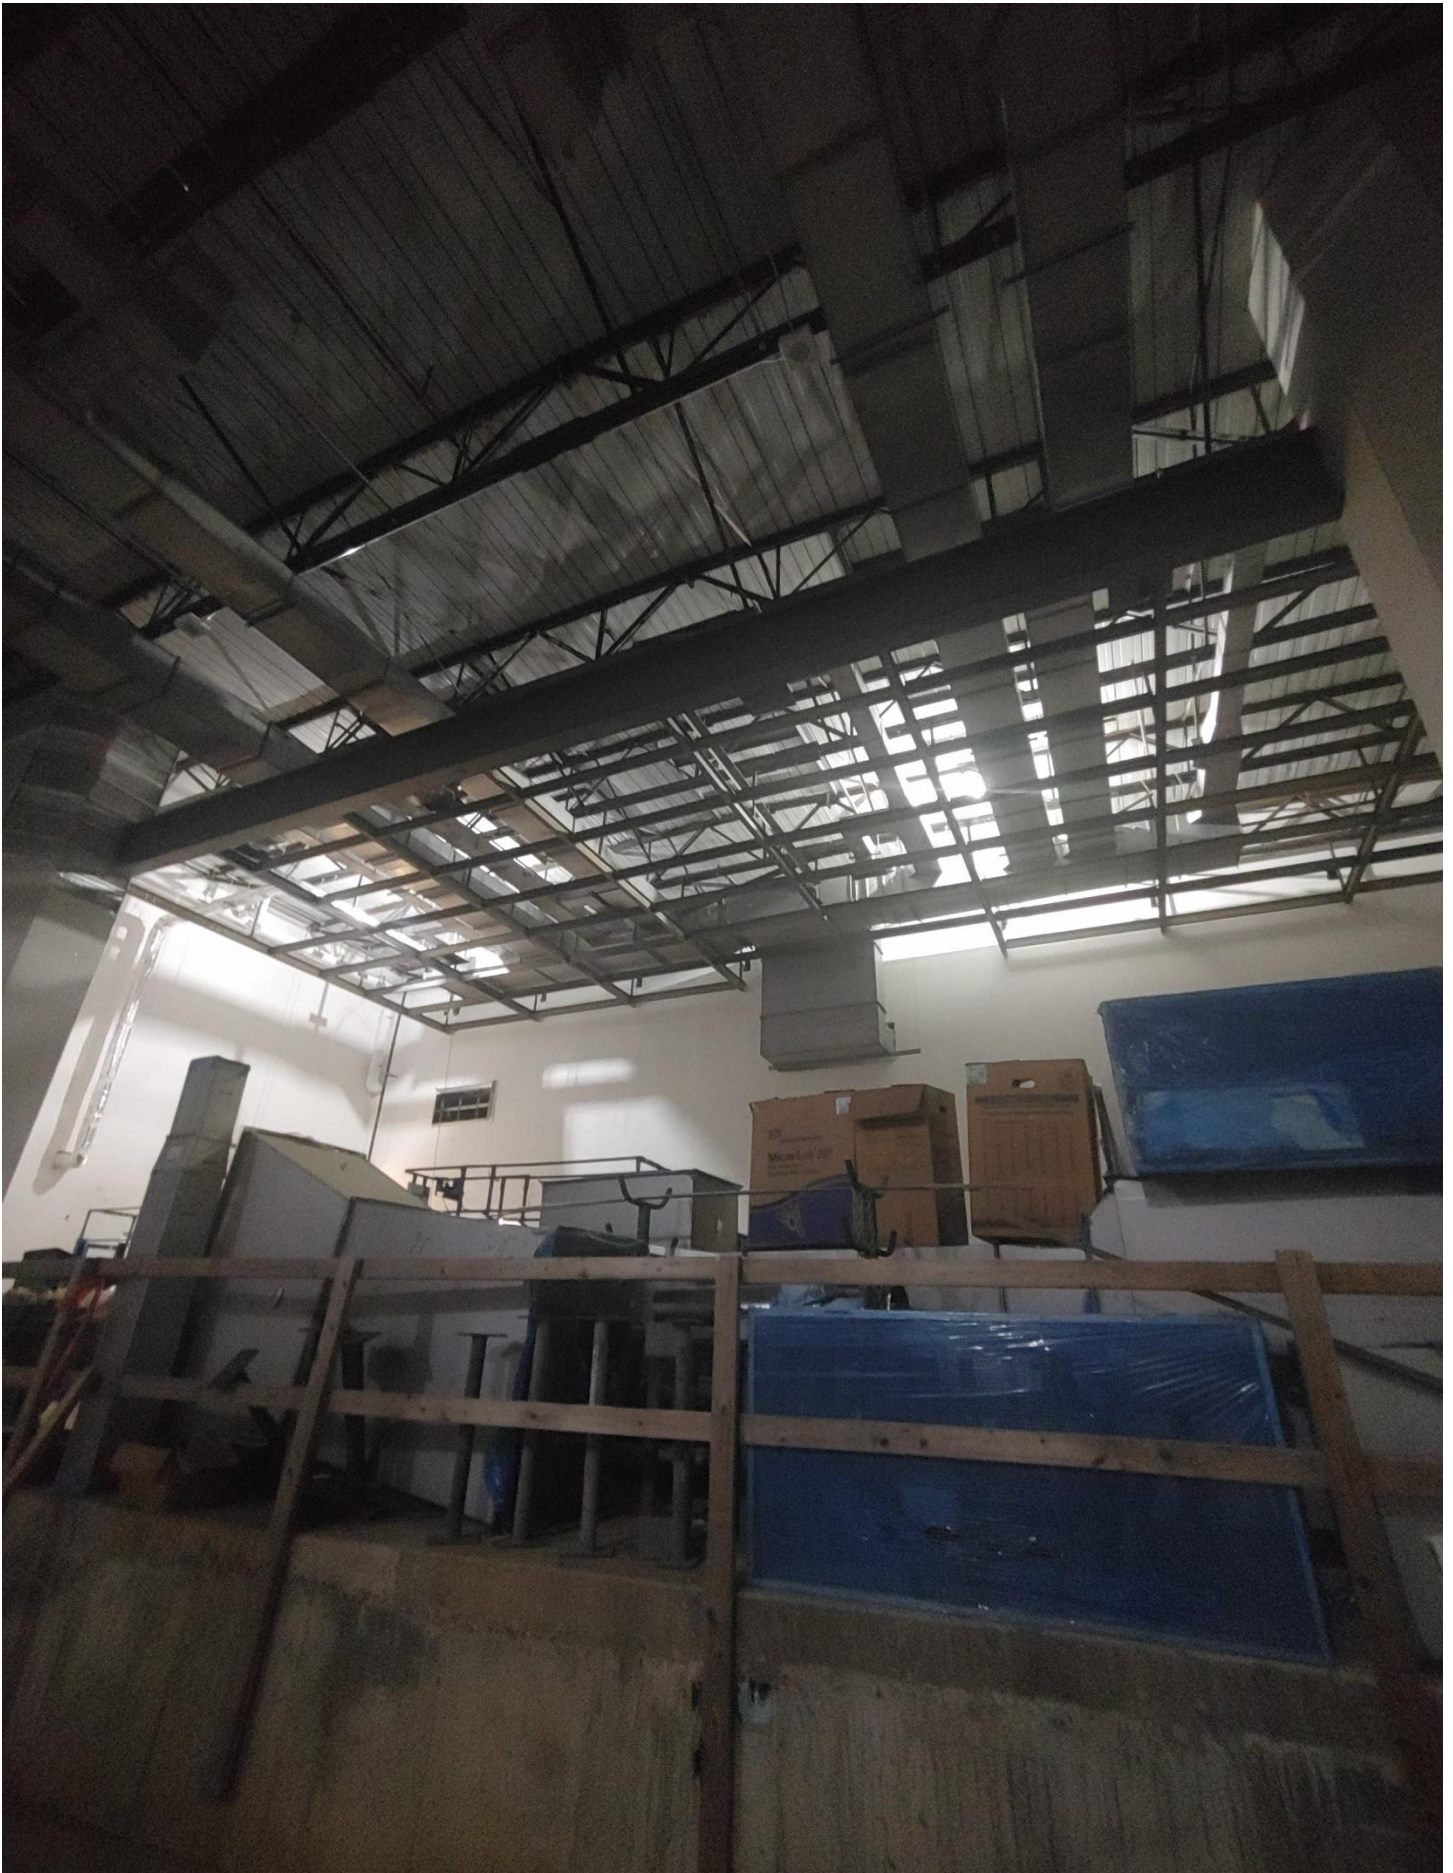


*Photo 5 - Ceiling substructure of Auditorium Stage is being installed.*

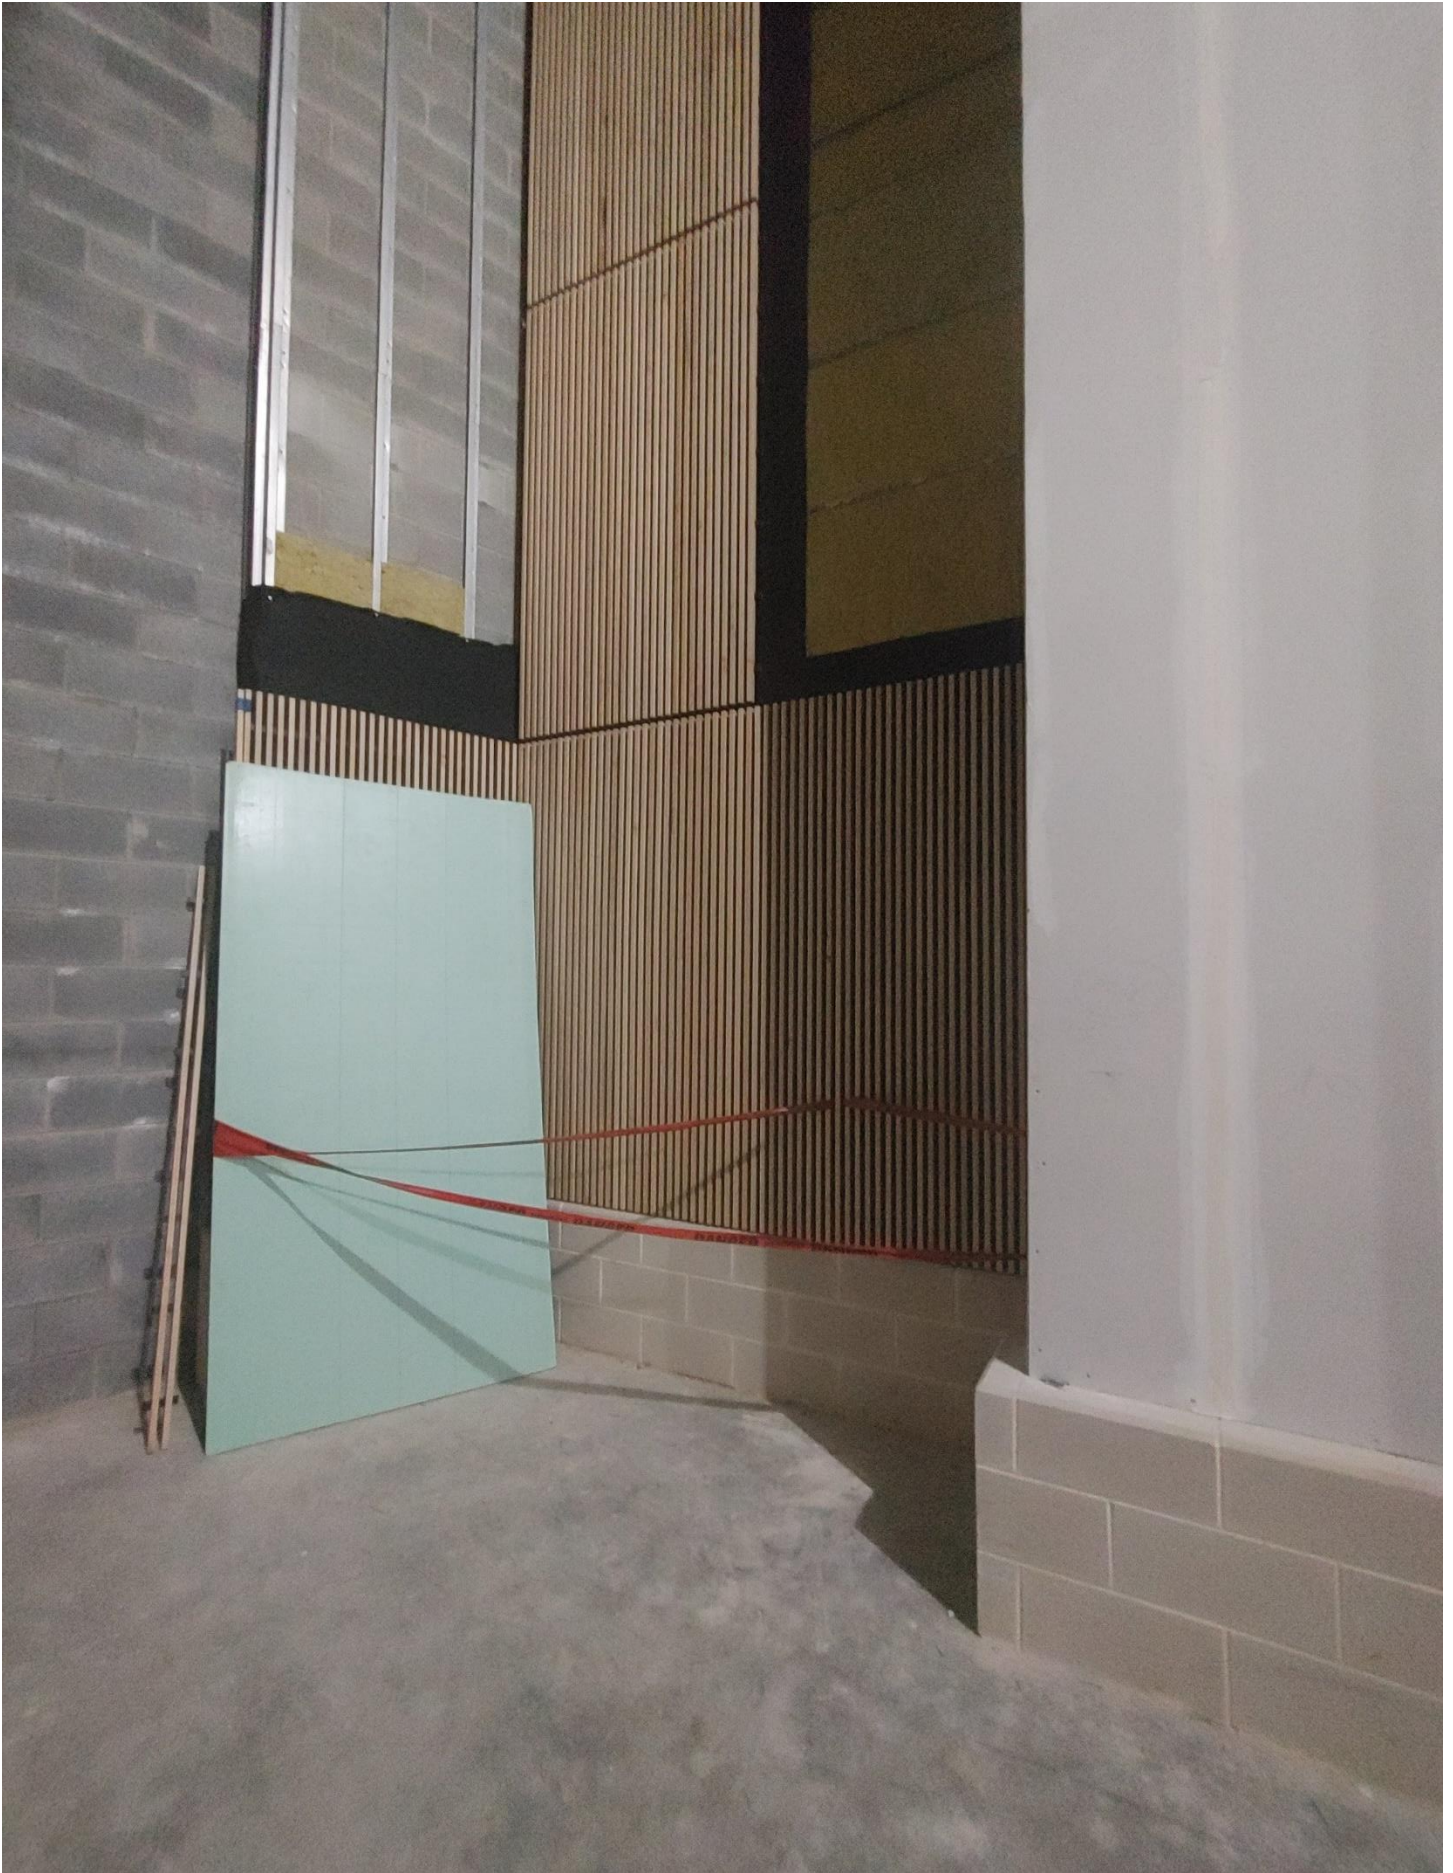

*Photo 6 - Acoustical Sound absorption panels are being installed in Auditorium.*



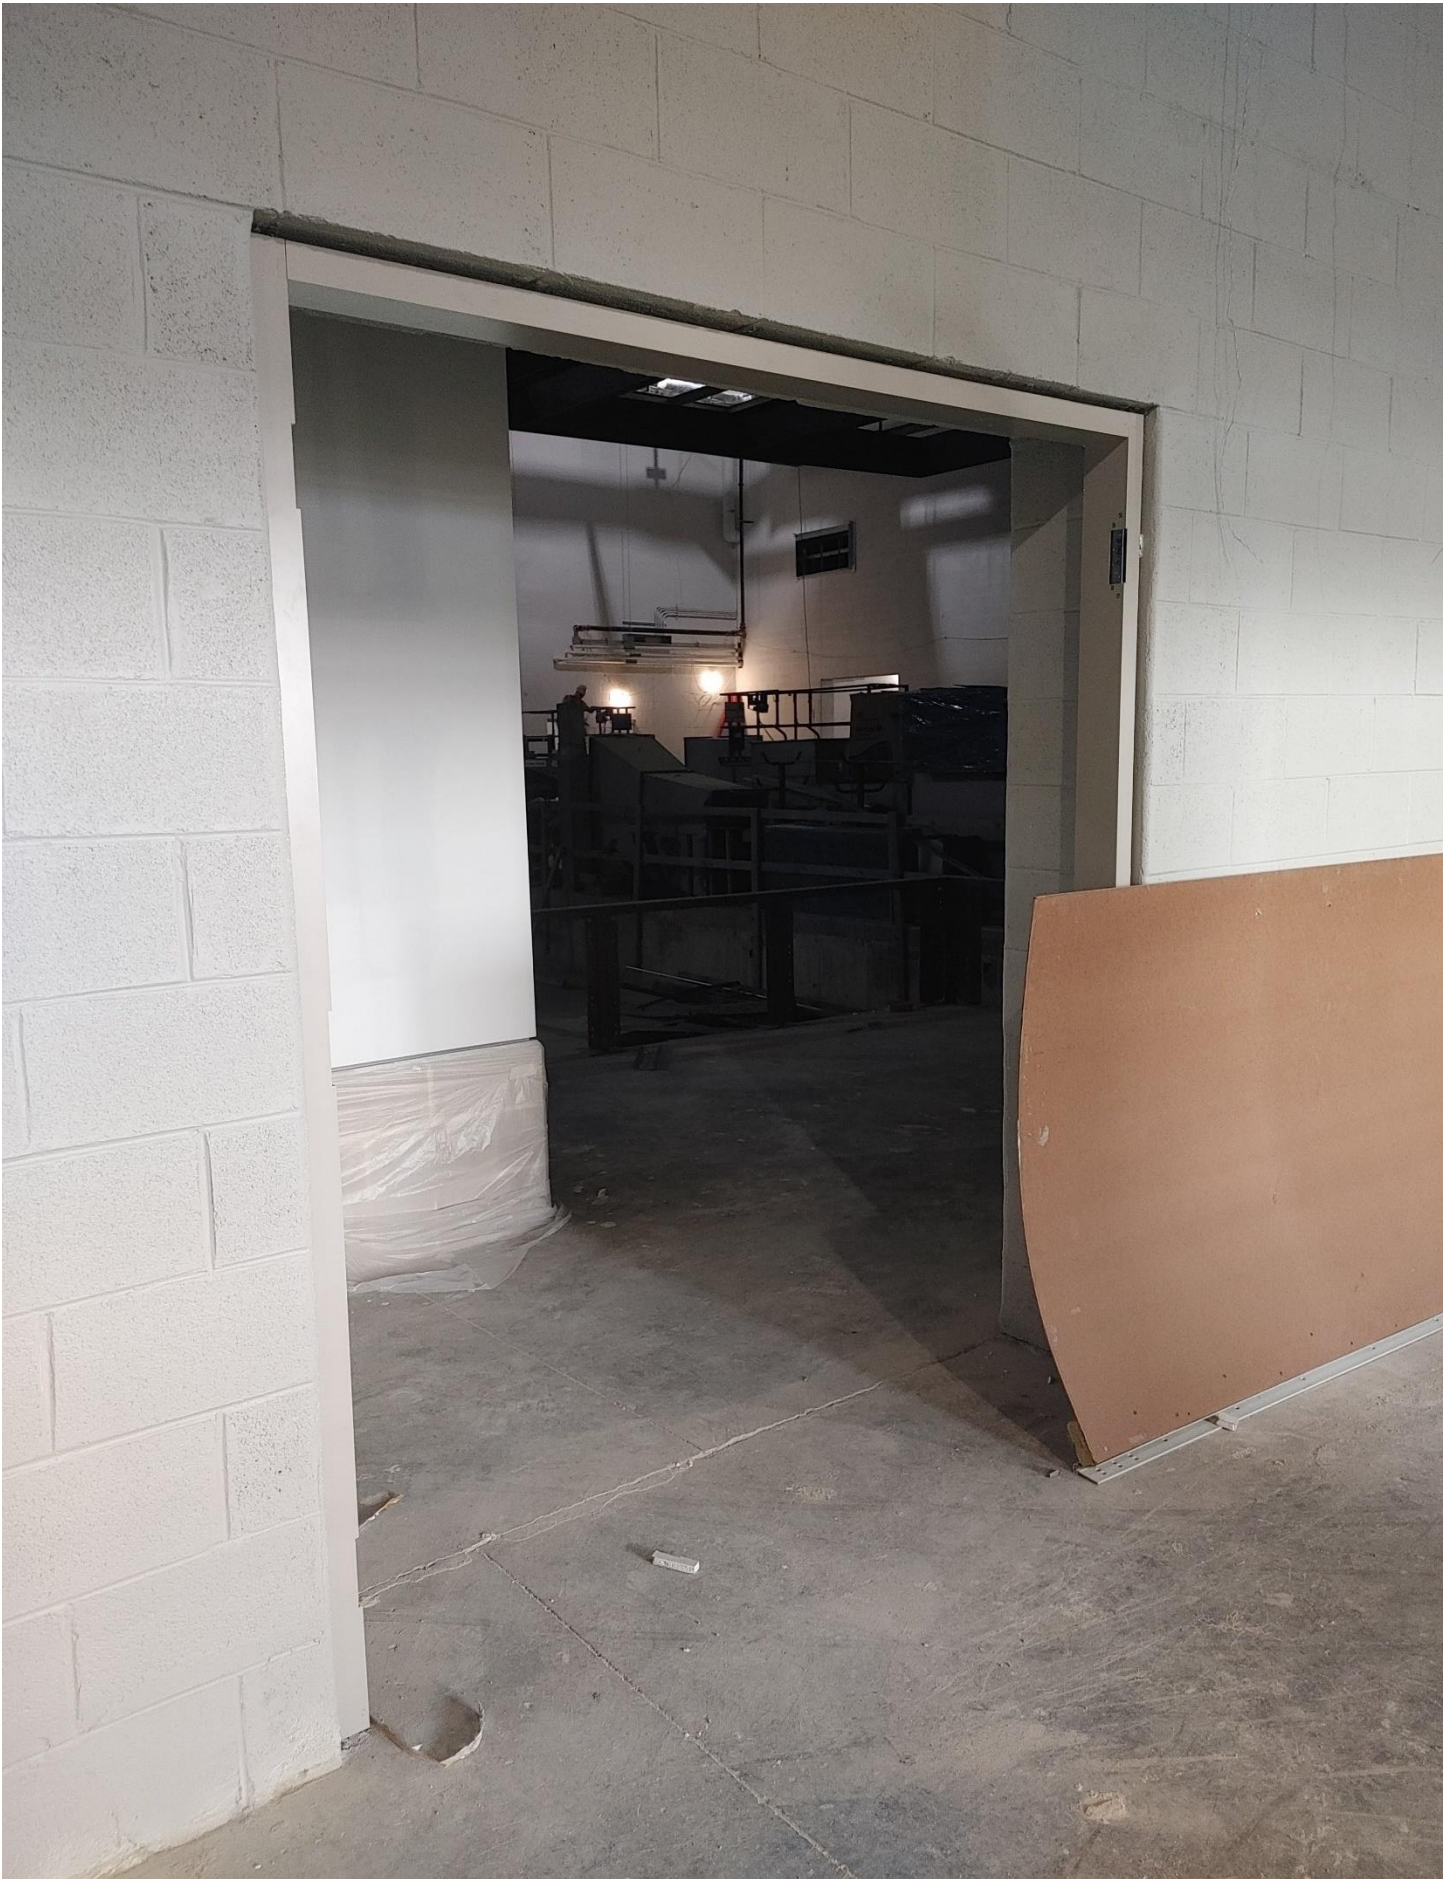

*Photo 7 - Door Frames have been installed in Area D*



Photo 8 - Frame D12 has been installed.



Photo 9 - Rear Canopy and columns of Area C have been painted.



Photo 10 - Wall tile has been set in Vestibule E105. Still needs to be grouted.



Photo 11 - Wall tile has been set in Boys Toilet E103.



Photo 12 - Bleachers are being constructed in Gym.

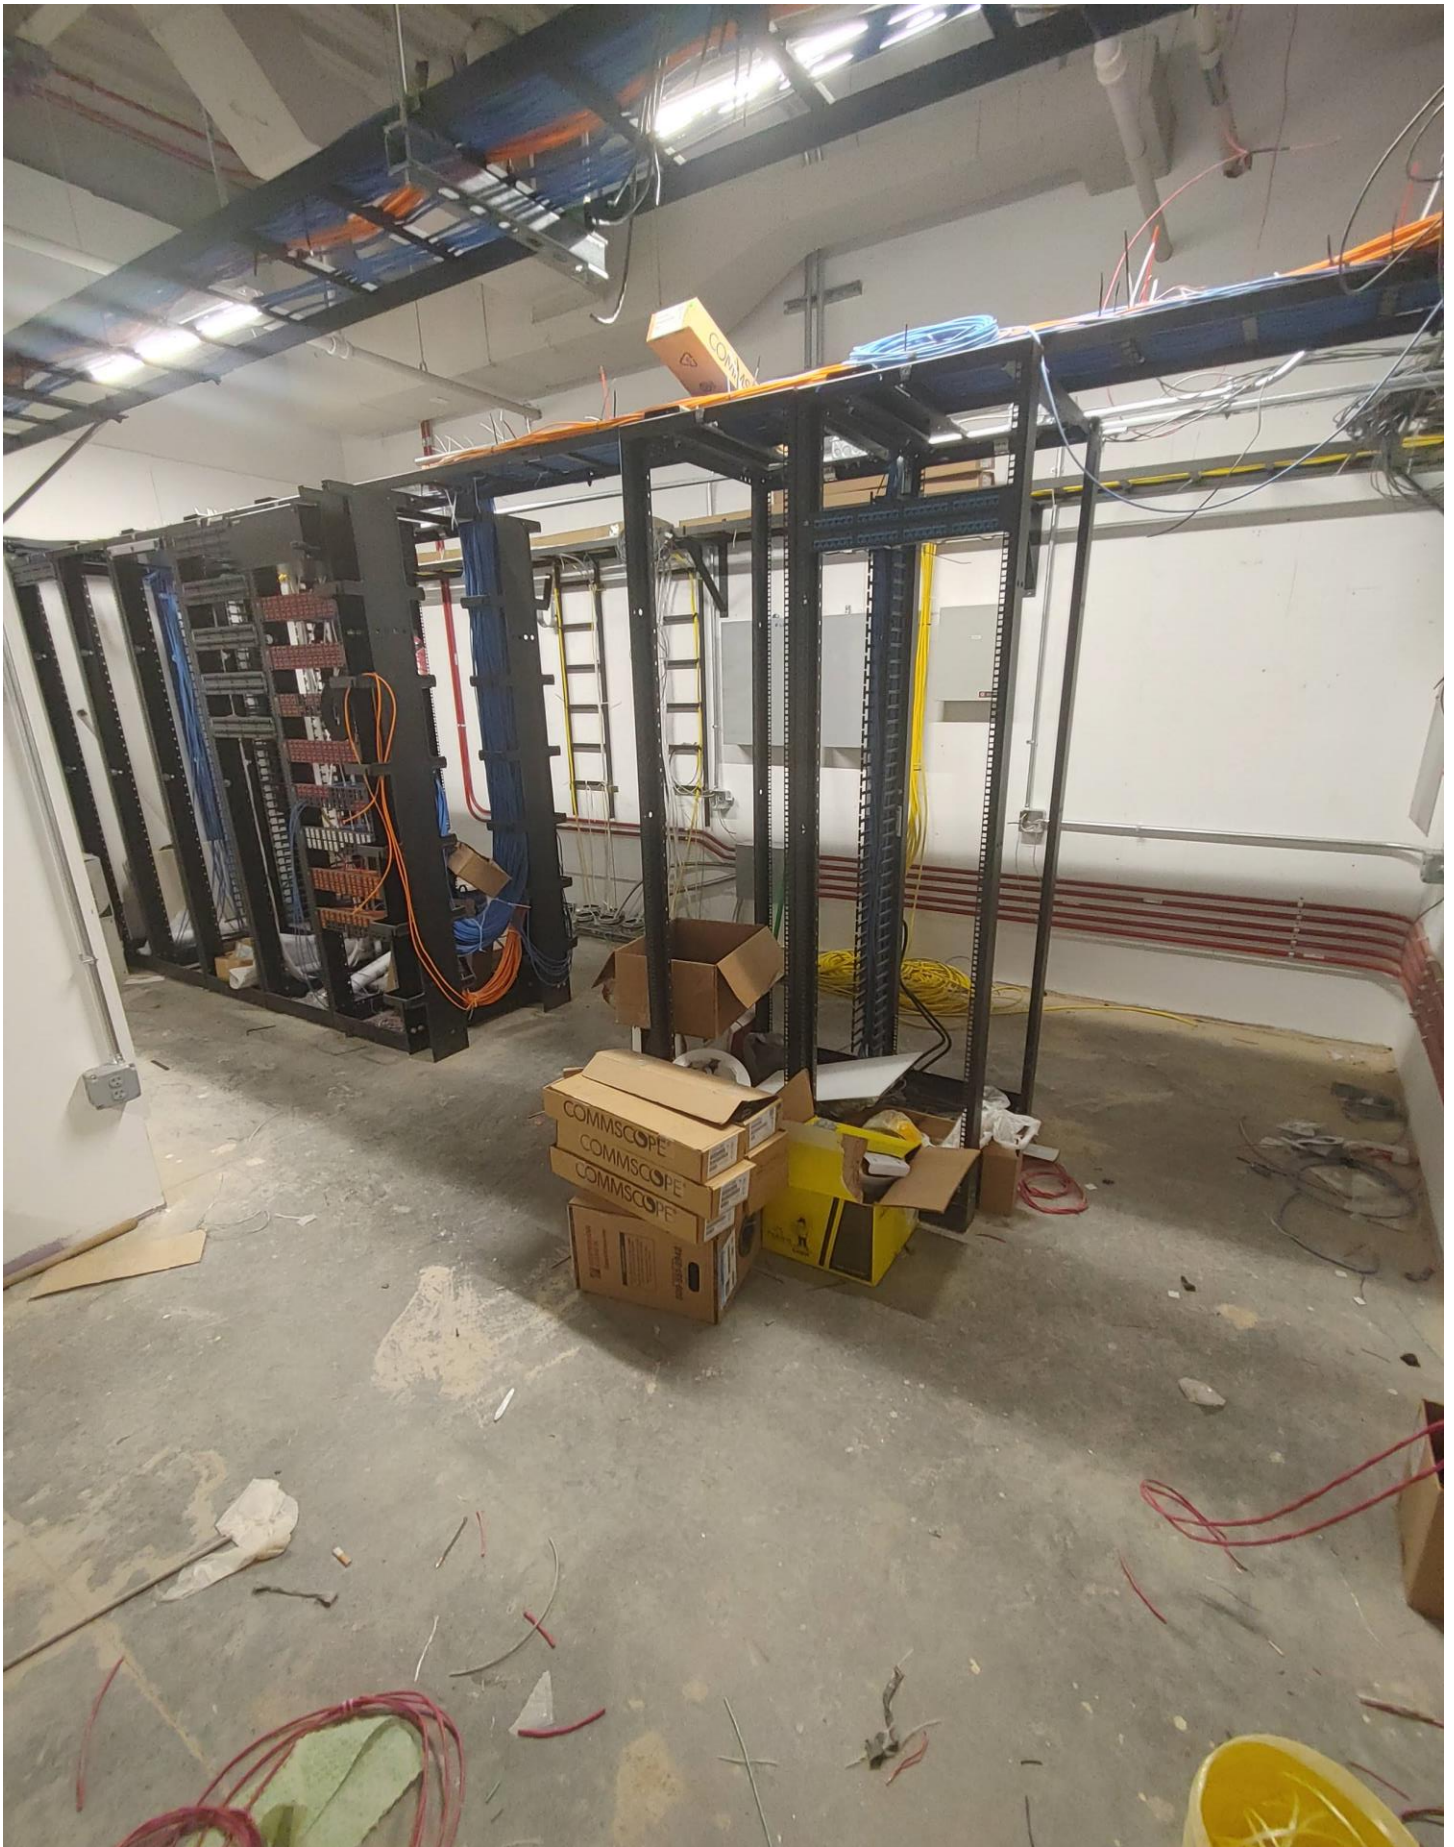


Photo 13 - A114



Photo 14 - Digital Temperature & Humidity Monitor on the 2nd floor of Area A





Photo 15 - VCT is being laid in Area B



Photo 16 - Retention Pond on Northside of Bus Loop.



*Photo 17 - Retention Pond on Westside of Bus loop.*

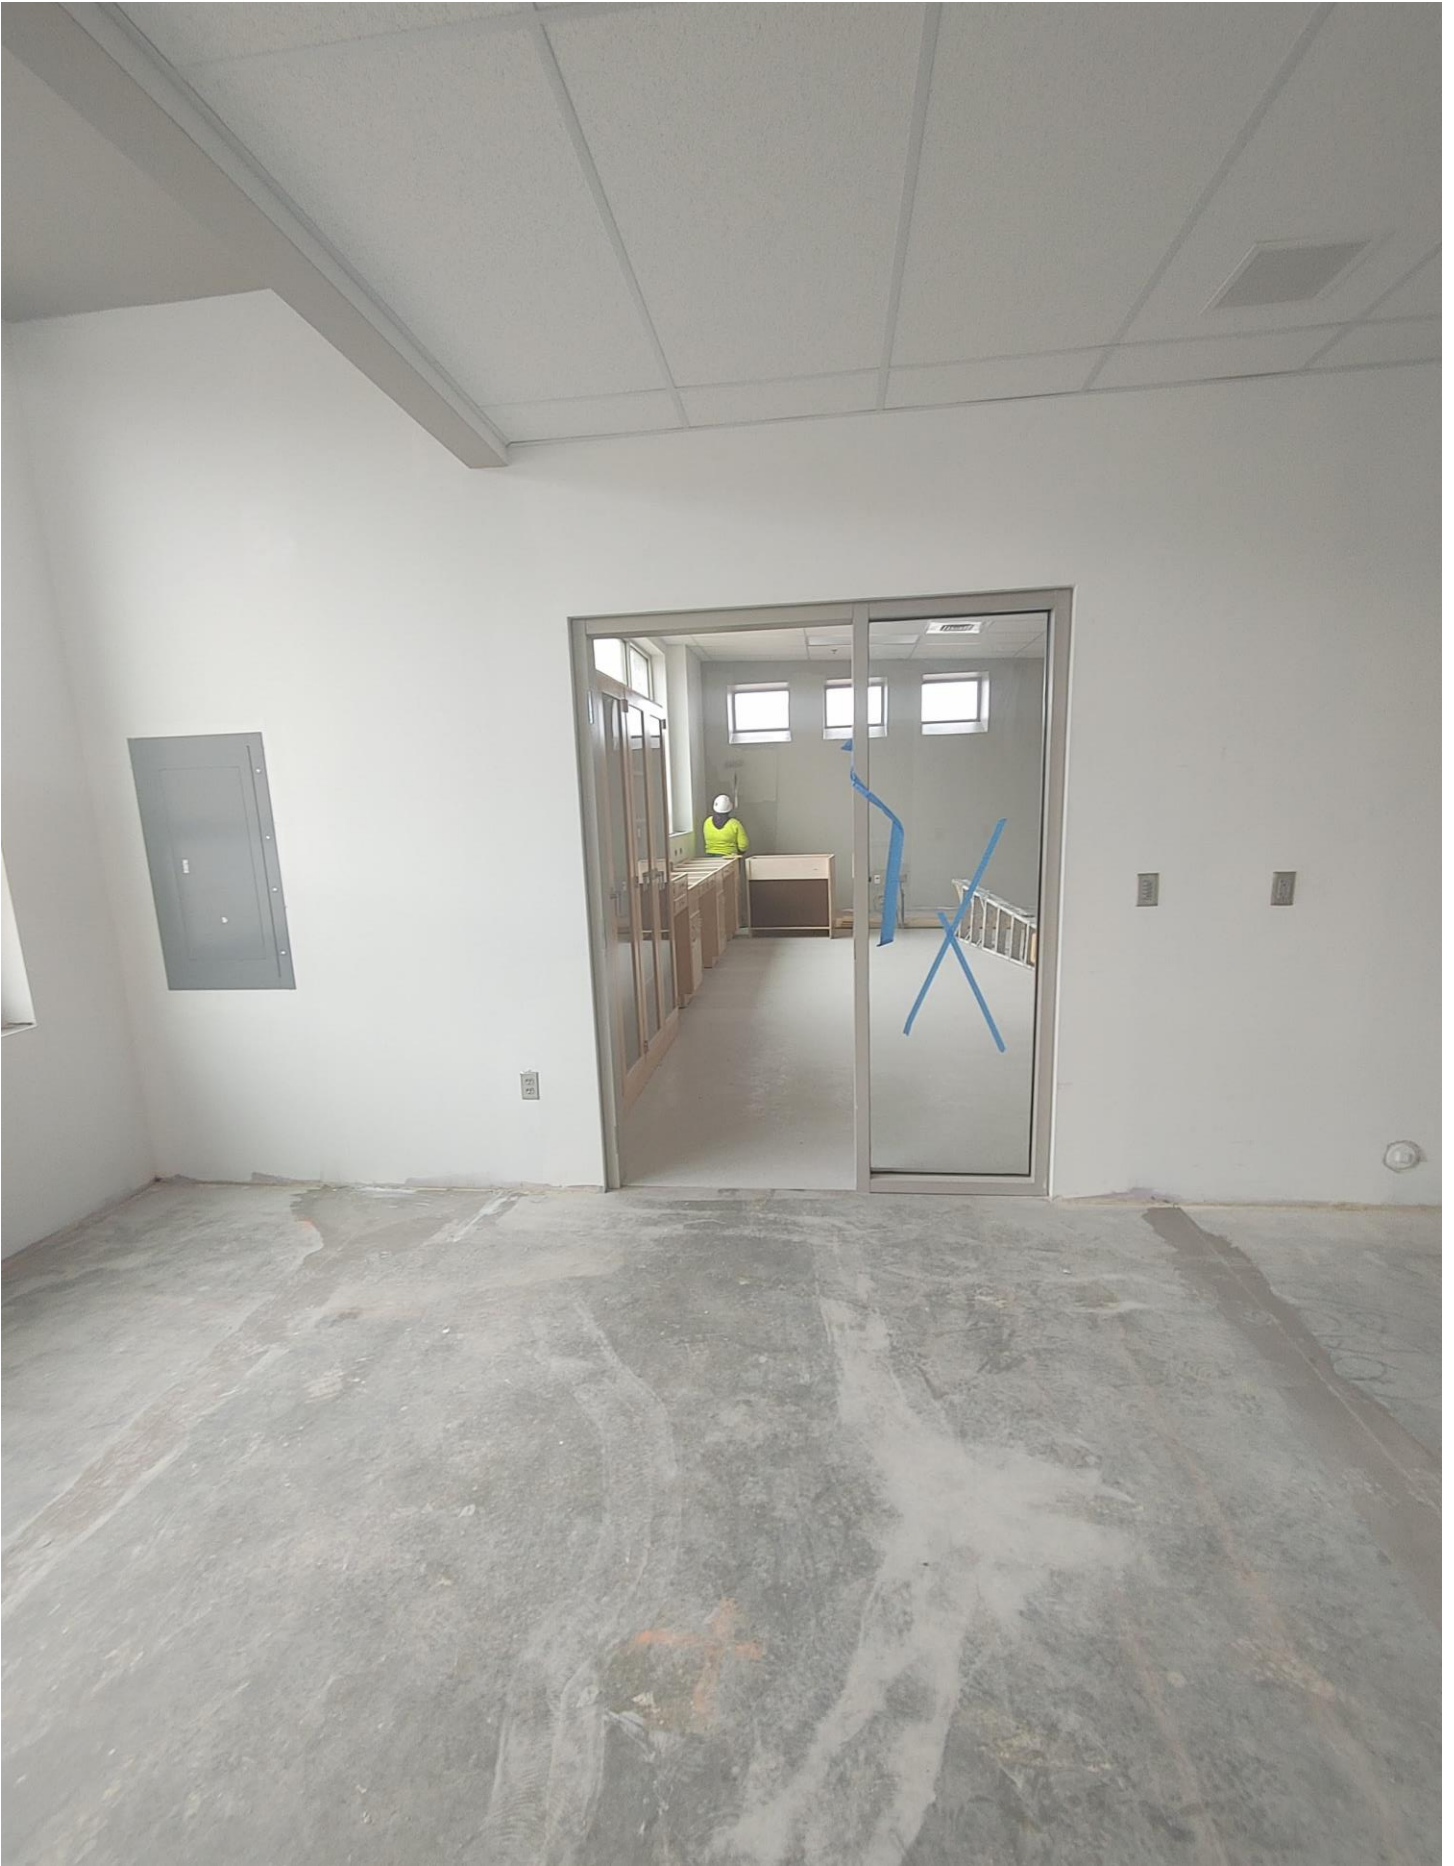


Photo 18 - Painters are painting in Area B



Photo 19 - Sprinkler pipe and head under Grand Staircase.



Photo 20 - Lights accessible from Grand Staircase Landing.
