



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 01/19/2022
Weather: 43 degrees. Sunny. High of 54 degrees today. Rain/Snow in the forecast for tomorrow, Friday and Saturday.
Hours Worked: 09:00 – 14:00hrs (5hrs) Site Visit, Progress Meeting, Camera Meeting with School Staff.

The Site was shut down last week from Tuesday, January 11th to Friday, January 14, 2022 because of several cases of Covid. The Site guys and Concrete crew were the only Subs working and it was all outside work.

Beuchert Excavation: Six men are on site working on the ditch line of Bus Entrance.

Industrial Concrete: I did not observe them on site during my visit.

J.D. Long, Masons: No one is on site today.

Hazzard Electric: Eleven men on site. They are working in ones #1, #2, #3.

Colonial Webb: Seven Men on site today. They are working in Zones #1, #4, & #5.

Talley & Armstrong (Sub-Contractor of Beuchert): I did not observe anyone on site today.

Weldon Steel: I did not observe anyone on site.

JP Construction: Fifteen men are on site. They are working in Zones #1, & #2 doing ceiling work.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: No one is on site today.

United Sprinkler: Two men are on site today. They are working in Zone #1.

CTSI: Five men are on site. They are working in Zones #1, #2, & #3

M. L. Straight: Four guys are here today.

K-Plus: I observed One guy caulking in the Boys Locker Room, E126.

AAM: Metal Panel Sub. Five guys are on site installing metal panels outside of the Ticket Booth area.

Hodgemen: They have a crew on site laying VCT in Area B, 2nd floor and prepping the 2nd floor of Area A for VCT.

Deleware Elevator: Two men are on site today working in the Elevator Equipment room and Elevator Pit.

S&S Concrete Cutting Company: No one is on site today.

DES: Three men are here today assembling Cabinetry in Zone #4.

Smith: Epoxy Floor Sub. No one is on site to my knowledge.

TJ Distributers, INC: No one is here today.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site during my visit.

Conversations with Branch Builds: I met with John and also Todd today during my visit. John and I spoke about when Franklin Mechanical would be energizing the Sewage Pump Station. I told I had spoke with them this morning and they would get back to me later today. This meeting was scheduled for Thursday of last week but it was canceled when the Job Site was shut down dur to Covid. We also spoke about the Pole Cameras. I told John I would bring it up today at the Progress meeting so that a meeting could be set up with the School's IT/Security Personnel and Branch Builds. Meeting was set to occur at 13:30 hours today.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports – 01/10/2022

Hillis-Carnes Bio Retention Pond Reports –

Submittals: #06 20 00-6.0, #09 51 00-6.0, #09 52 50-8.0, #11 53 13-4.1, #11 51 23-2.2, #10 00 05-9.0

RFIs – #342, #335, #364

Patrick Byrne –

Alexes Lee –

Tara Delaney –

Change Order/PCOs/Pay App –

Weekly Submittal Status Report: 01/07/2022, 01/14/2022

Weekly RFI Status Update – 01/07/2022, 01/14/2022

Weekly Daily Log Summary – 01/07/2022, 01/14/2022

PCO Log – 01/07/2022, 01/14/2022



Photo 1 - East side of School



Photo 2 - Grand Staircase Treads have been poured



Photo 3 - Metal Panels are being installed outside of Ticket Office.



Photo 4 - Painters are painting walls in Area C

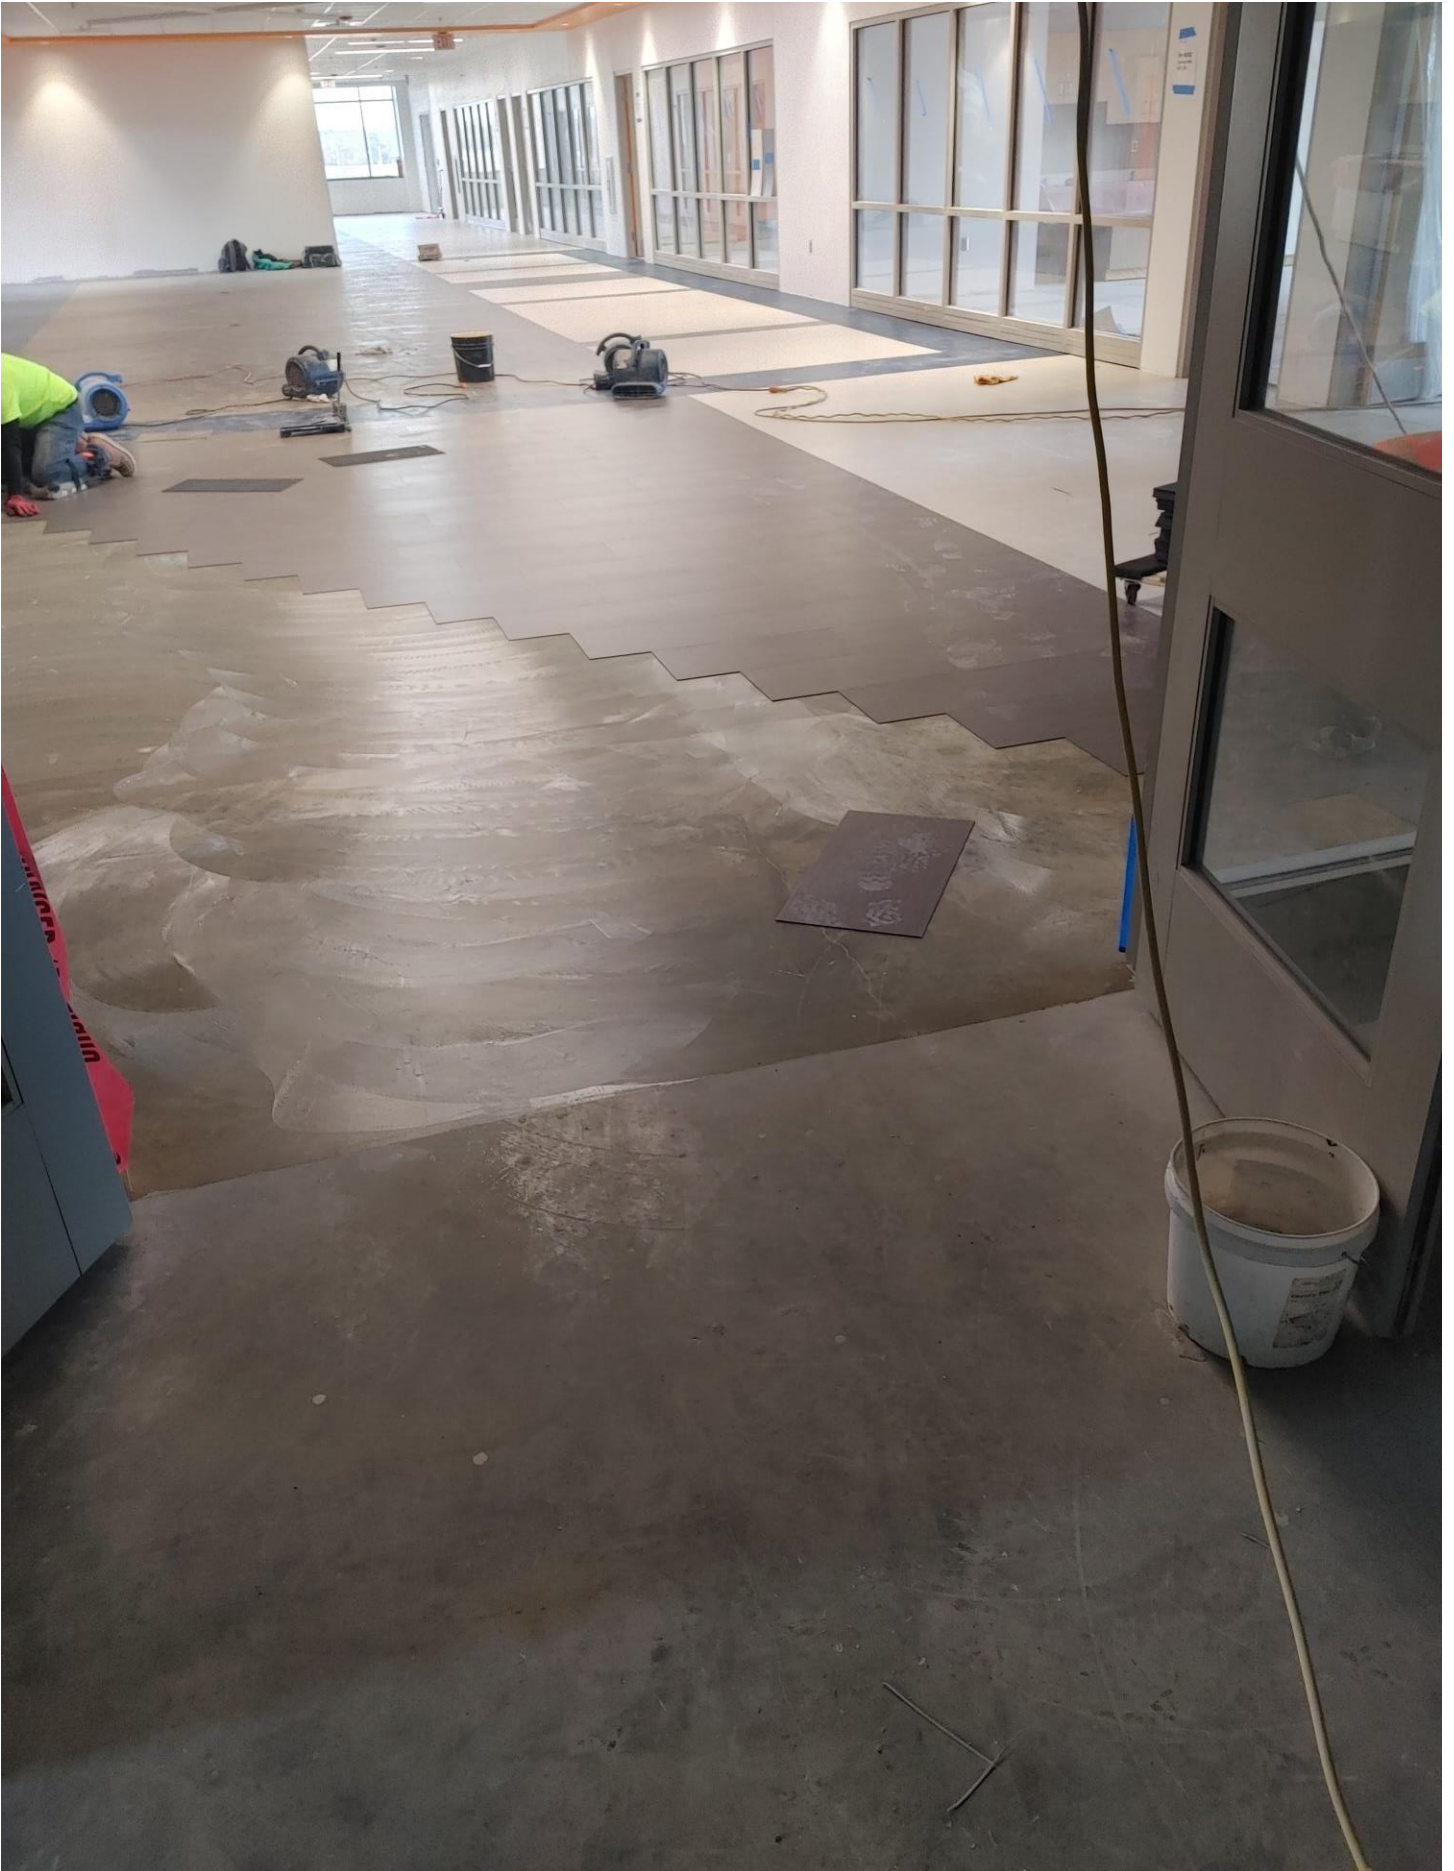


Photo 5 - VCT is being laid in Area B, 2nd floor.



Photo 6 - Acoustical Panels are being installed in Area A, A220

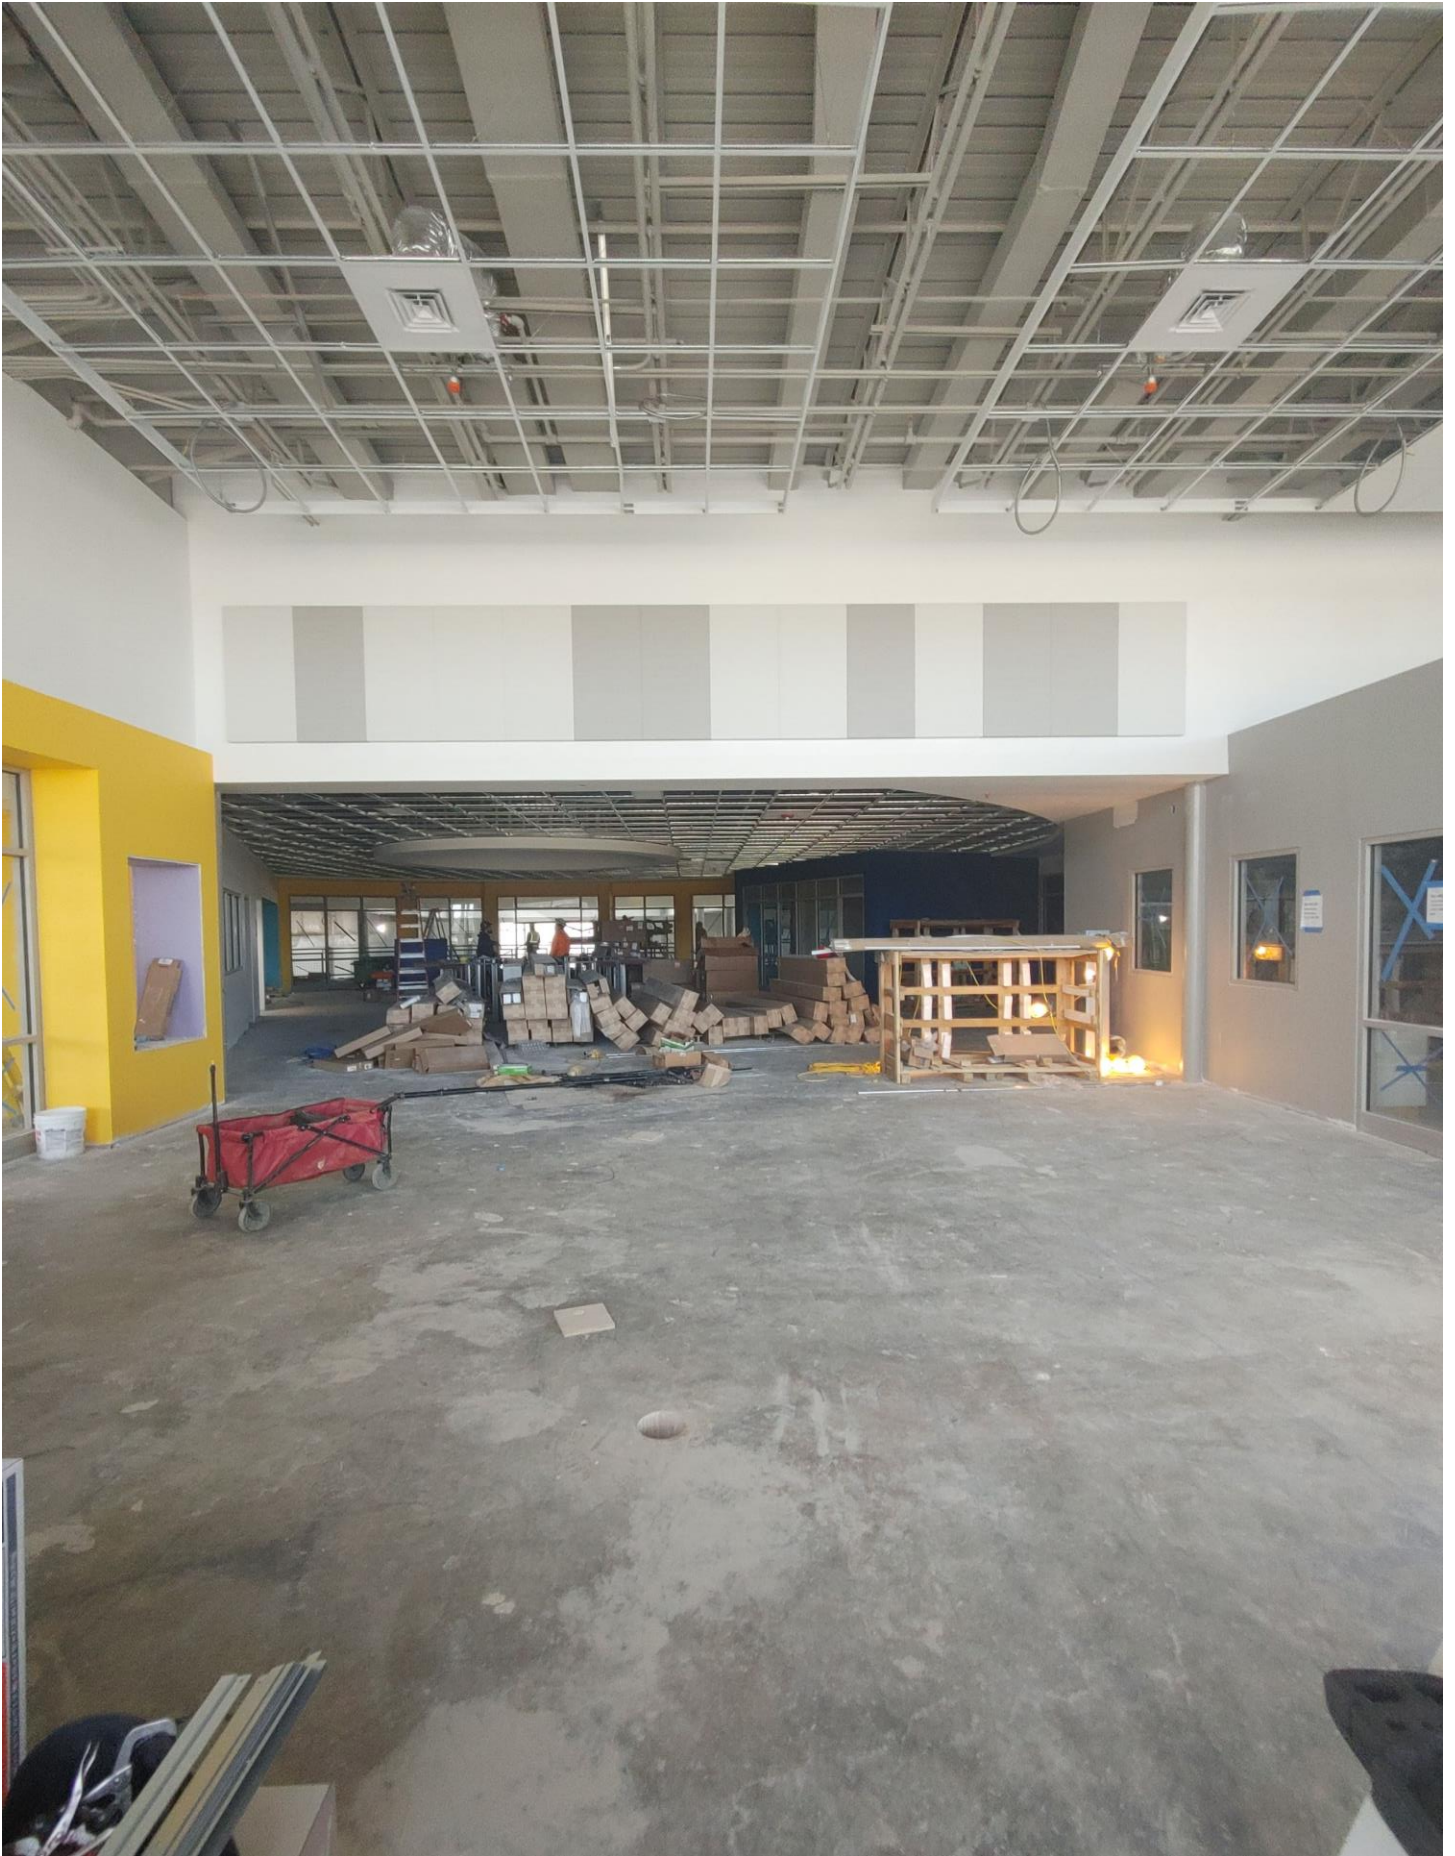


Photo 7 - Acoustical Panels installed in Area A, A220



Photo 8 - Work progressing in room A221, TV Studio/Video Production

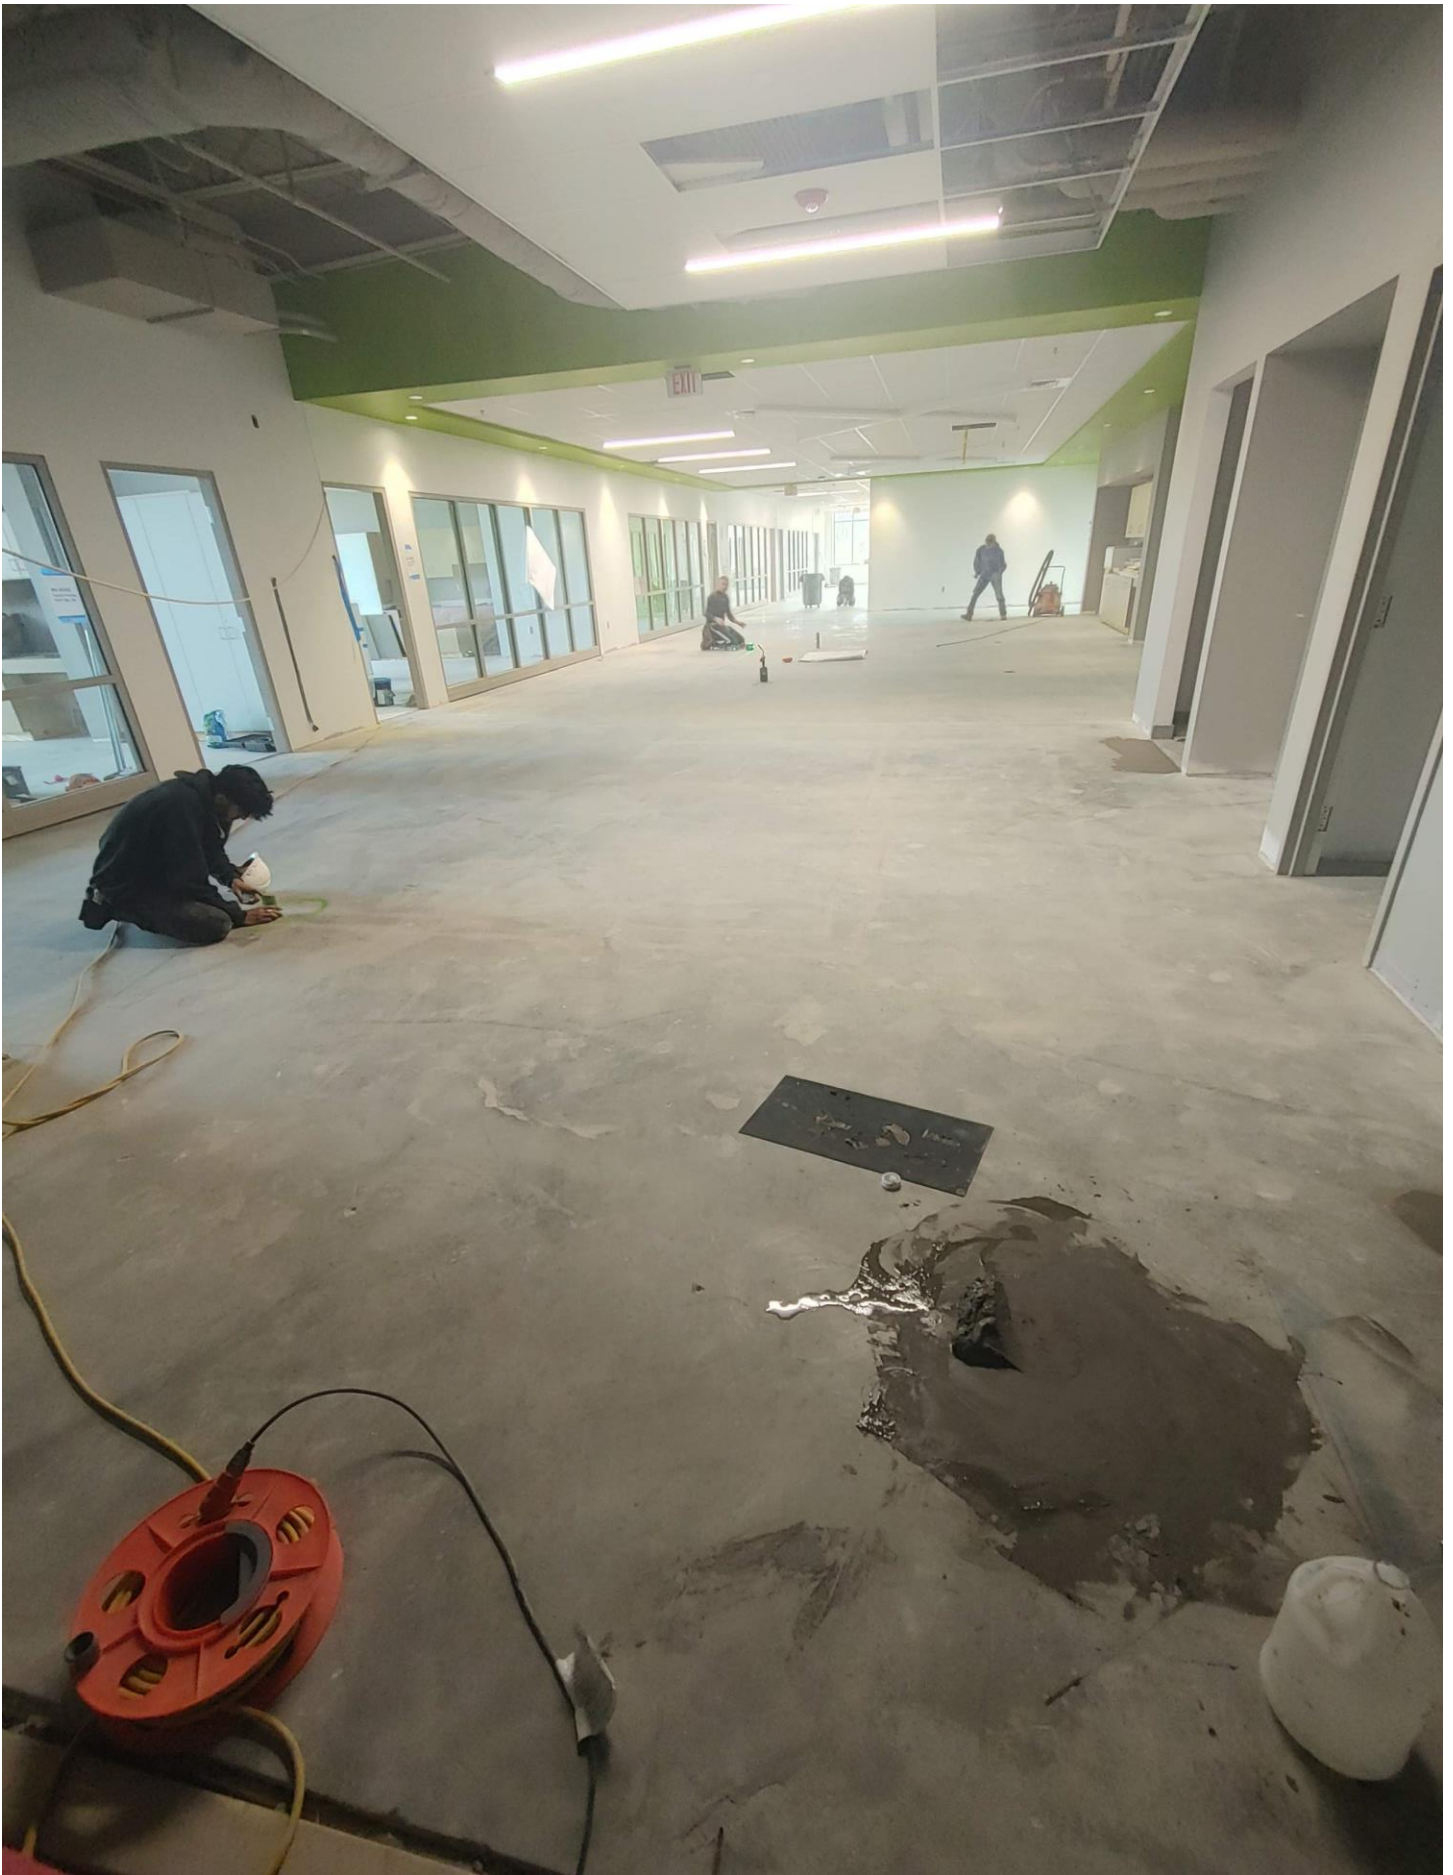


Photo 9 - 2nd floor, Area A being prepped for VCT.



Photo 10 - Doors have been hung in Area B, 1st floor.



Photo 11 - Room B110, Science Lab



Photo 12 - Northwest Corner of Site



Photo 13 - Bus Entrance shoulder work and ditch grading is ongoing.



Photo 14 - West side of School



Photo 15 - Ditch and Bank Grading is occurring on West side of site



Photo 16 - Bio-Retention Pond on West side of Site.
