



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 01/26/2022

Weather: 27 degrees. Sunny. High of 35 degrees today. Rain/Snow in the forecast for Friday and Saturday.

Hours Worked: 09:00 – 13:00hrs (4hrs) Meeting with Franklin Mechanical & Site Visit.

Meeting at 09:00hrs this morning with Franklin Mechanical, Ronnie Saunders, Lee with Branch Builds, Hazzard Electric and Factory Rep Chris White with Duhart Co. for the purpose of starting up and testing the Sewage Pump Station. The system was started and trailer loads of water was dumped into the tank to verify that the pumps were operating correctly. The High Water Float alarm was also tested. I verified that the separate Maintenance Electrical Circuit was installed. The wiring has been run but the receptacle has not been installed.

**Conversations with Branch Builds:** I met with John, Lee and Chandler. I told Lee that the silt fence on the last retention pond (BMP2B) that was completed had been pushed over and silt was now getting into the pond. Lee said that Beuchert was going to get super silt installed in multiple areas that were being stress by large stormwater runoff. Lee then called Beuchert and told them about the sit fence and told them they may want to correct the problem before the storm arrived this weekend. See Pictures below.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports – 01/25/2021**

**Hillis-Carnes Bio Retention Pond Reports –**

**Submittals - #08 80 00-2.2**

**RFIs – #363**

**Patrick Byrne – PR#24**

**Alexes Lee –**


**Tara Delaney –**  
**Change Order/PCOs/Pay App – #15**  
**Weekly Submittal Status Report – 01/21/2022**  
**Weekly RFI Status Update – 01/21/2022**  
**Weekly Daily Log Summary – 01/21/2022**  
**PCO Log – 01/21/2022**



*Photo 1 - BMP2B silt fence in need of repair.*



Photo 2 - BMP2B

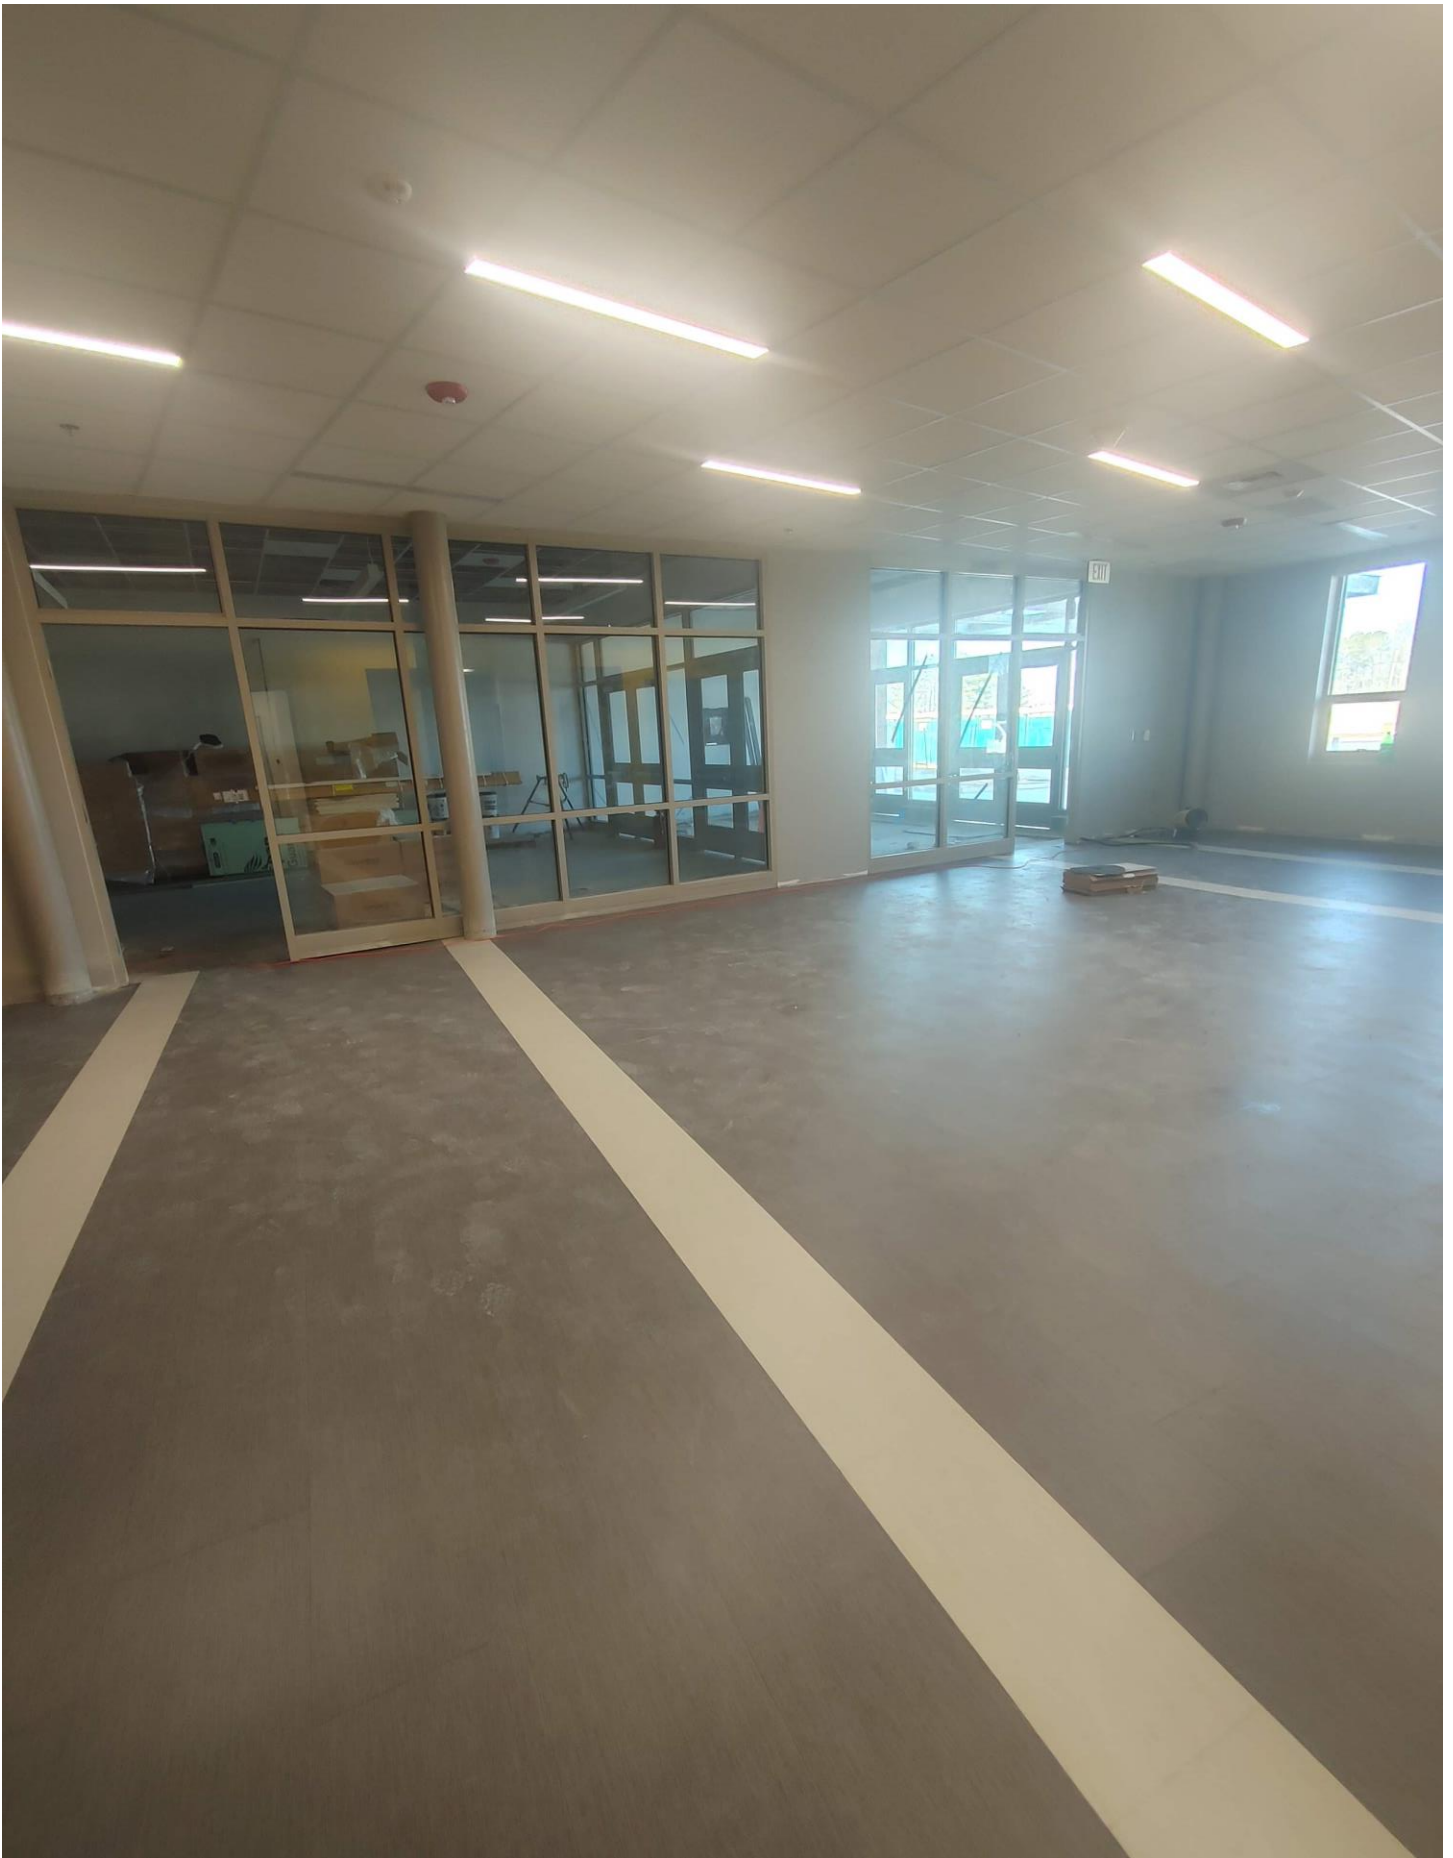

*Photo 3 - A120 tile has been completed*



Photo 4 - Metal wall has been completed in Area C



Photo 5 - Metal Wall completed outside of D104 and D117

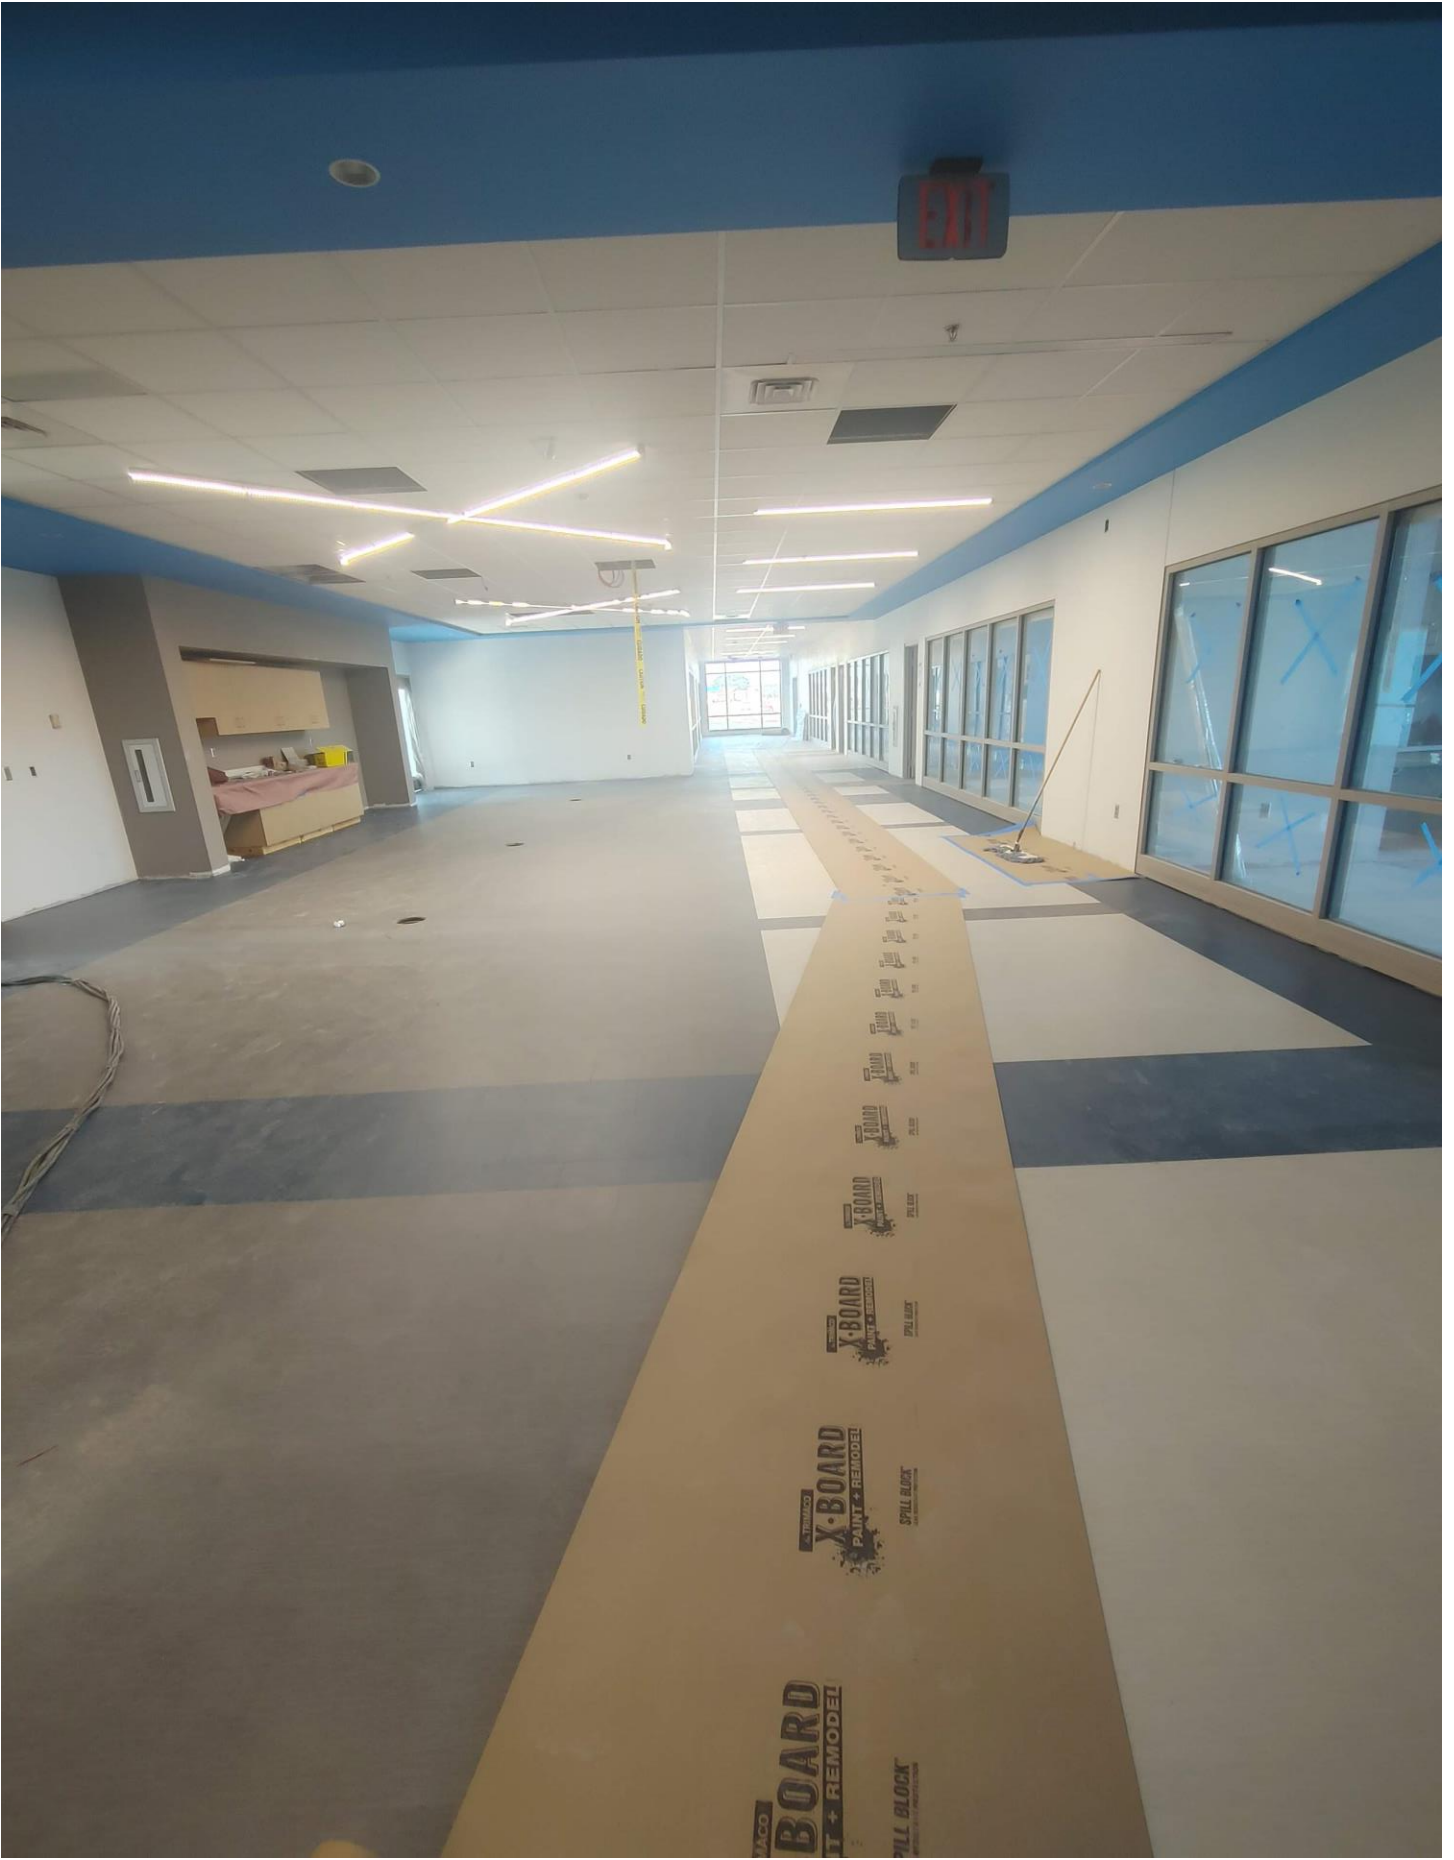


Photo 6 - VCT has been laid in area B10 & B12
