



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 01/31/2022

Weather: 27 degrees. Sunny. High of 35 degrees today. Rain/Snow in the forecast for Friday and Saturday.

Hours Worked: 13:00 – 15:30hrs (2.5hrs) – Site Visit

Walked the site today. The Sprinkler sub was working in Area C. We had a discussion about the Sprinkler heads under the Grand Stair Case. I noted that the track for the Continuous glass draft stop in Corridor A13 was being installed. Hodgeman was laying VCT in A10 Design Commons.

The Painters were painting in various areas on the 2<sup>nd</sup> floor of Area B. DES was installing Cabinetry in room B206. Room B209 concrete has been prepped for the installation of the epoxy floor (note: Concrete had numerous, larger than hairline, cracks). A cleanup Crew is vacuuming and mopping various rooms in Area B.

The Acoustic Cloud Ceiling was being installed in around the perimeter of Area C. A painter was also painting the Roof deck in this area. Metal Panels are also being installed around vestibule C110.

Storage Cages have been installed in E130 and the flooring guys was laying tile in E134A.

They have begun to frame the wall above the stage in Area D.

Silt fence continues to be erected around the site.

**Conversations with Branch Builds:** I met with John, Lee, Cooper and Chandler. We discussed the possibility of when Branch may begin to lock down the building when no one is on site working. John and I also discussed the cracked concrete floor in Room B209.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**  
**Hillis-Carnes Grout Inspection/Compression Strength Test –**  
**Hillis-Carnes Field Reports –**  
**Hillis-Carnes Bio Retention Pond Reports –**  
**Submittals -**  
**RFIs – #363, #366, #367, #368**  
**Patrick Byrne –**  
**Alexes Lee –**  
**Tara Delaney –**  
**Change Order/PCOs/Pay App –**  
**Weekly Submittal Status Report – 01/28/2022**  
**Weekly RFI Status Update – 01/28/2022**  
**Weekly Daily Log Summary – 01/28/ 2022**  
**PCO Log – 01/28/2022**



Photo 1 - Acoustical Cloud Ceiling is being installed in Area C



Photo 2 - 1st Floor, Area B, Room B10 - Design Commons



Photo 3 - Painter is painting in Area B



Photo 4 - Roof Deck is being painted in Area C.



Photo 5 - Equipment Cages have been installed in Room E130



Photo 6 - Metal Panels are being installed in Area C.



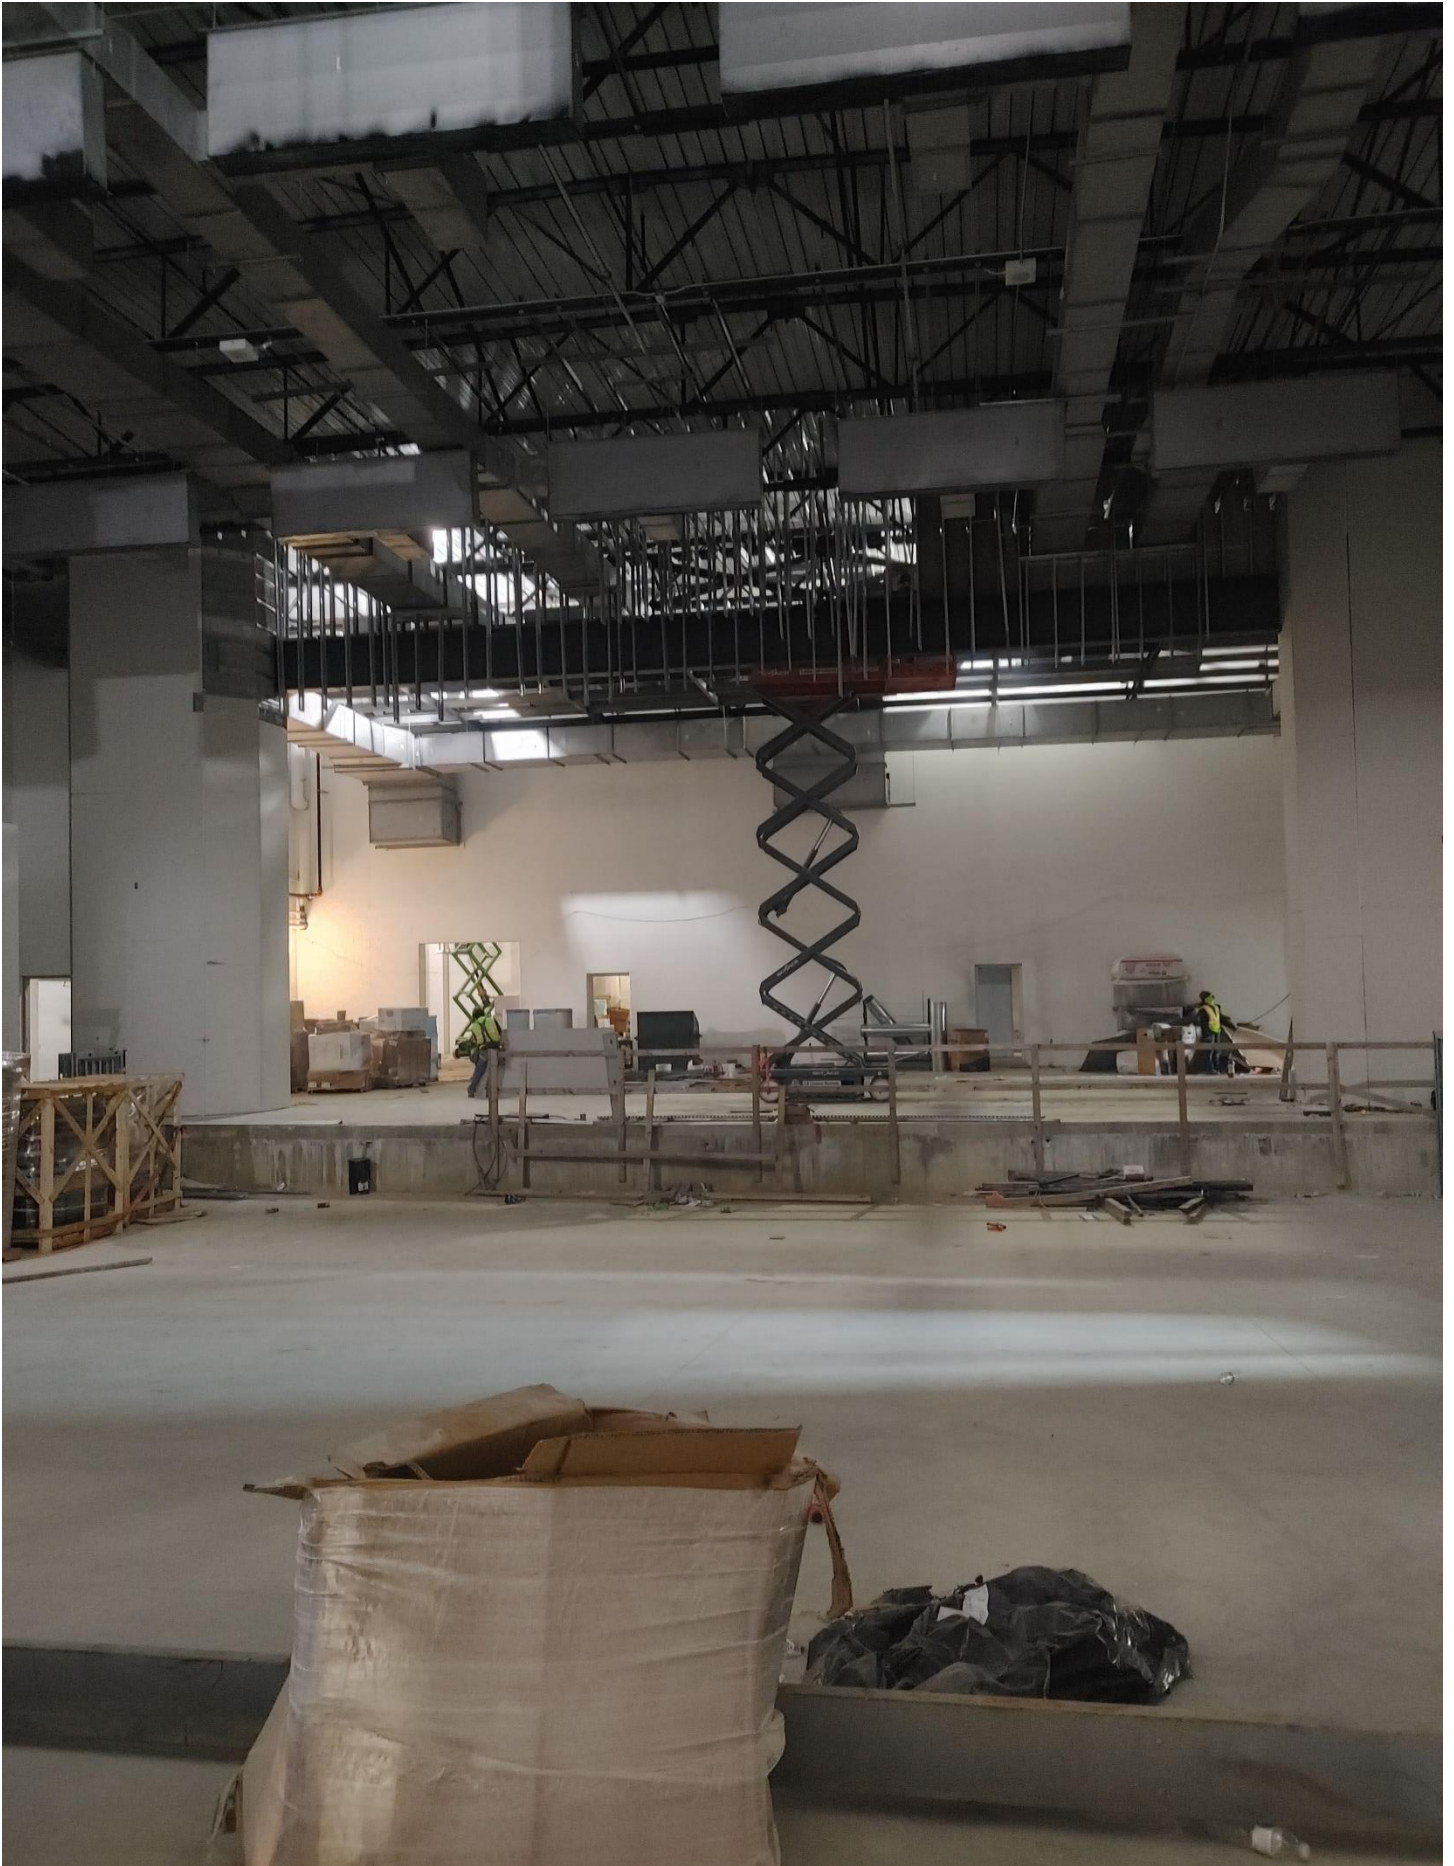


Photo 7 - Wall above Auditorium Stage is being constructed.

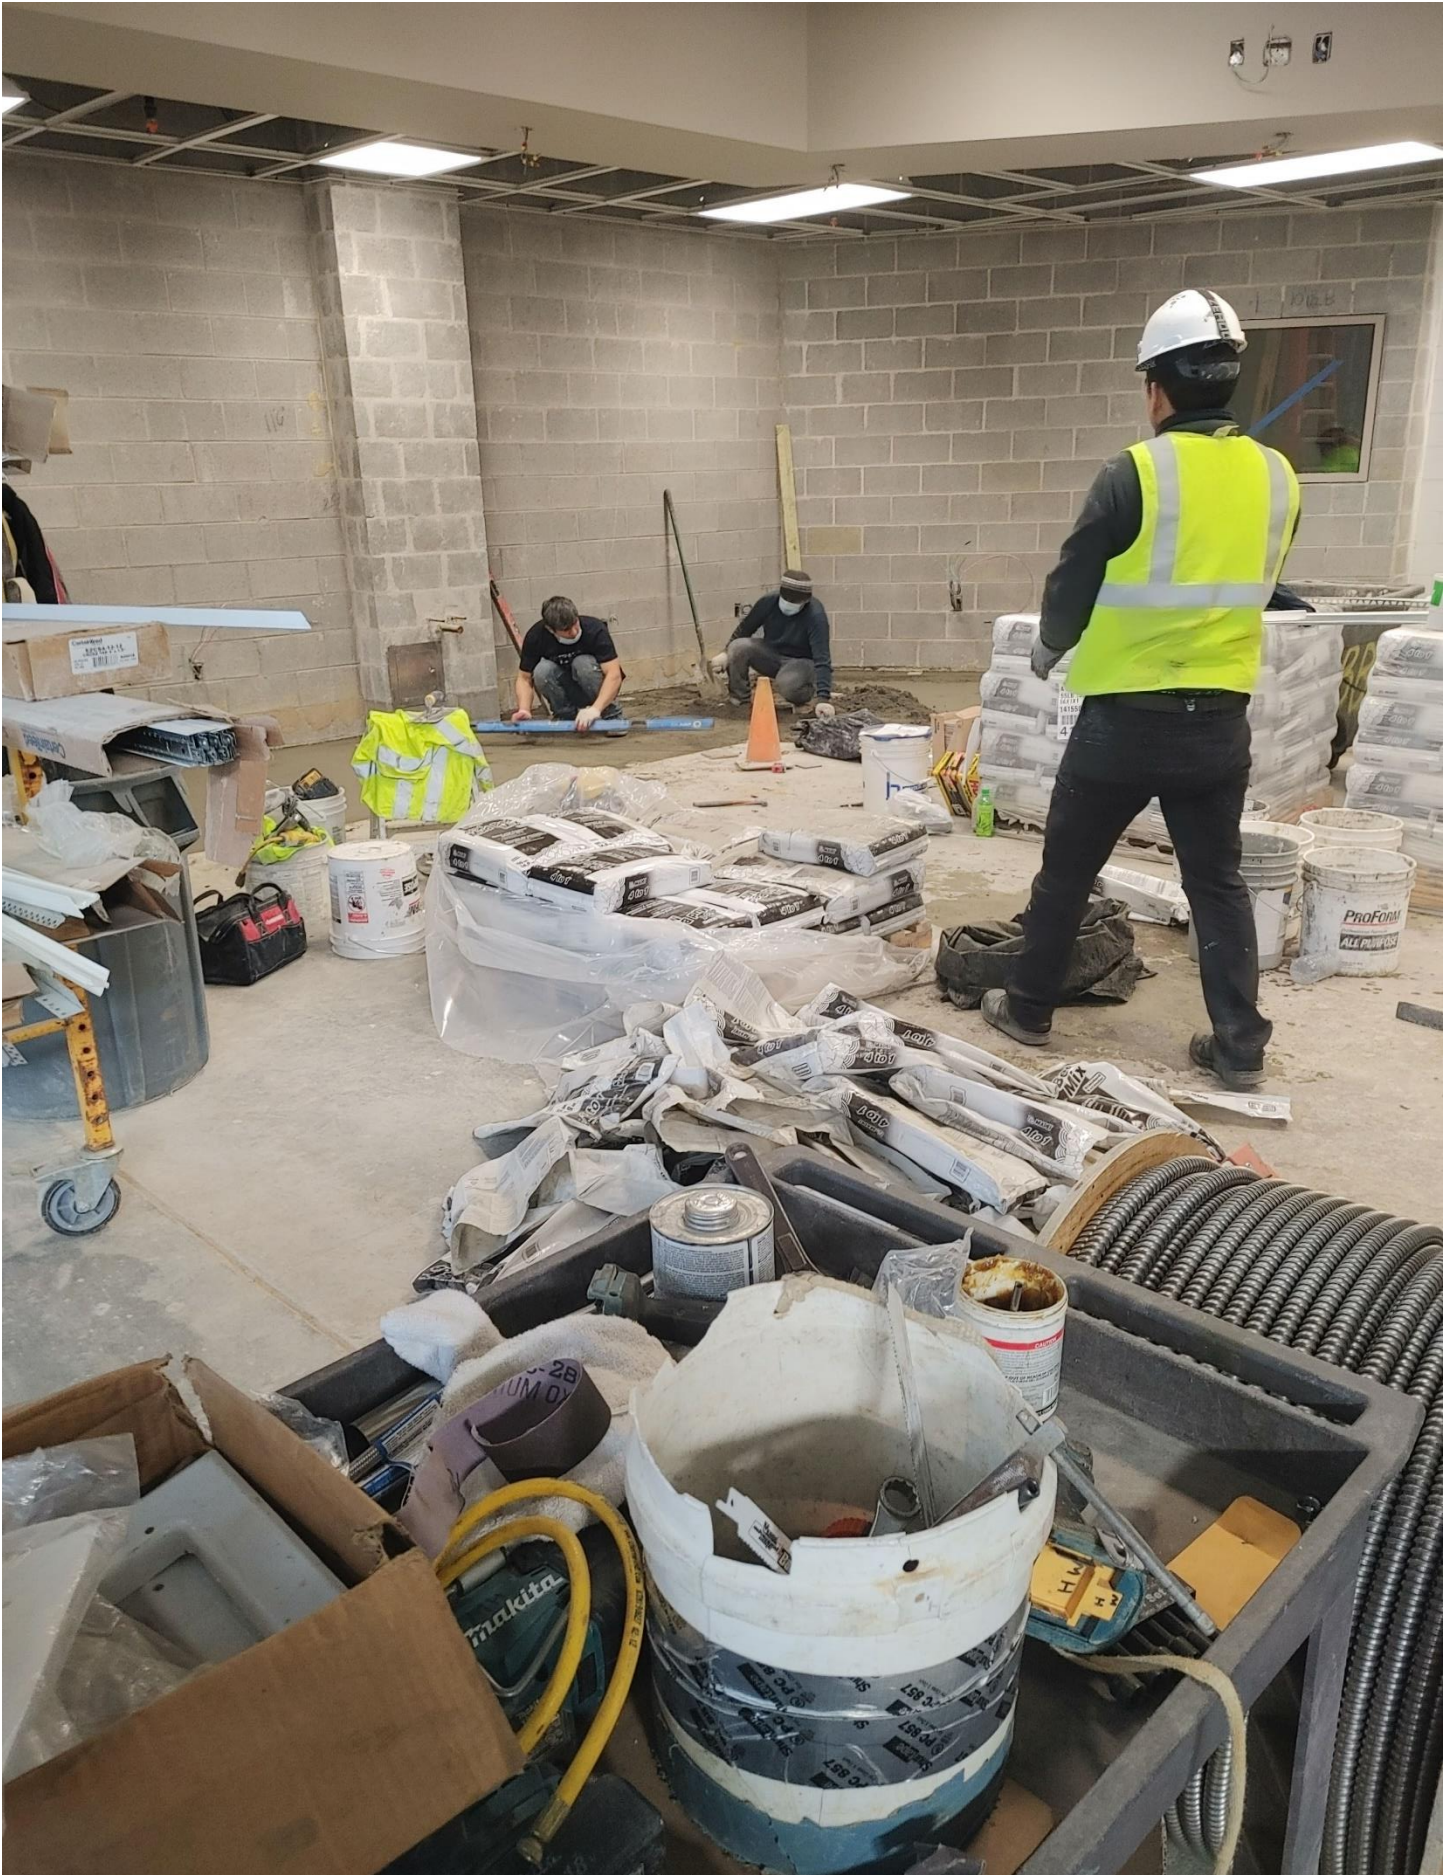


Photo 8 - Flooring crew working in the Kitchen



Photo 9 - VCT is being laid in A10 Design Commons



Photo 10 - Silt Fence is being erected around the site.
