



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 02/14/2022
Weather: 34 degrees - High of 36 degrees today.
Hours Worked: 12:00 – 15:00hrs (3hrs) – Site Visit

Heat has been turned on in the building.

Area A - Electricians are working on the second floor in A220. Door hardware is also being installed on door A20.

Area B

The Painters were painting in various areas on the 1st & 2nd floor of Area B.

Area C

The Sprinkler sub is working in Area D. The Painters are painting the Grand Staircase. The large Ceiling Fans are being installed in C100. Flooring crew is grouting tile in the Kitchen.

Area D - Bose Speakers have been installed in rooms D122 & D127. Door hardware is being installed on XD05.

Area E – They have begun to install the flooring in Vestibule E10. Electricians are running wire in Corridor E14. Flooring crew is laying tile in Room E121.

Site – I did not observe Beuchert on site today.

Conversations with Branch Builds: I met with John Farthro . I advised him that Chris Evans was having a Promethean Board delivered this week. John said that Branch was going to start Punching down the 2nd Floor of Area B this week. Branch has assigned a QR Code to each room and this is tied into Procore. Items noted will be logged into the System and any sub will be able to Scan the QR Code and see what work needs to be completed in each room.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report -
Hillis-Carnes Grout Inspection/Compression Strength Test –
Hillis-Carnes Field Reports – Bio Retention Pond – 02/11/2022
Hillis-Carnes Bio Retention Pond Reports –
Submittals - #26 36 00-4.0, #26 50 00-5.5
RFIs – #379, #384
Patrick Byrne –
Alexes Lee –
Tara Delaney –
Change Order/PCOs/Pay App –
Weekly Submittal Status Report – 02/11/2022
Weekly RFI Status Update – 02/11/2022
Weekly Daily Log Summary – 02/11/ 2022
PCO Log – 02/11/2022



Photo 1 - Room B206



Photo 2 - Room B209

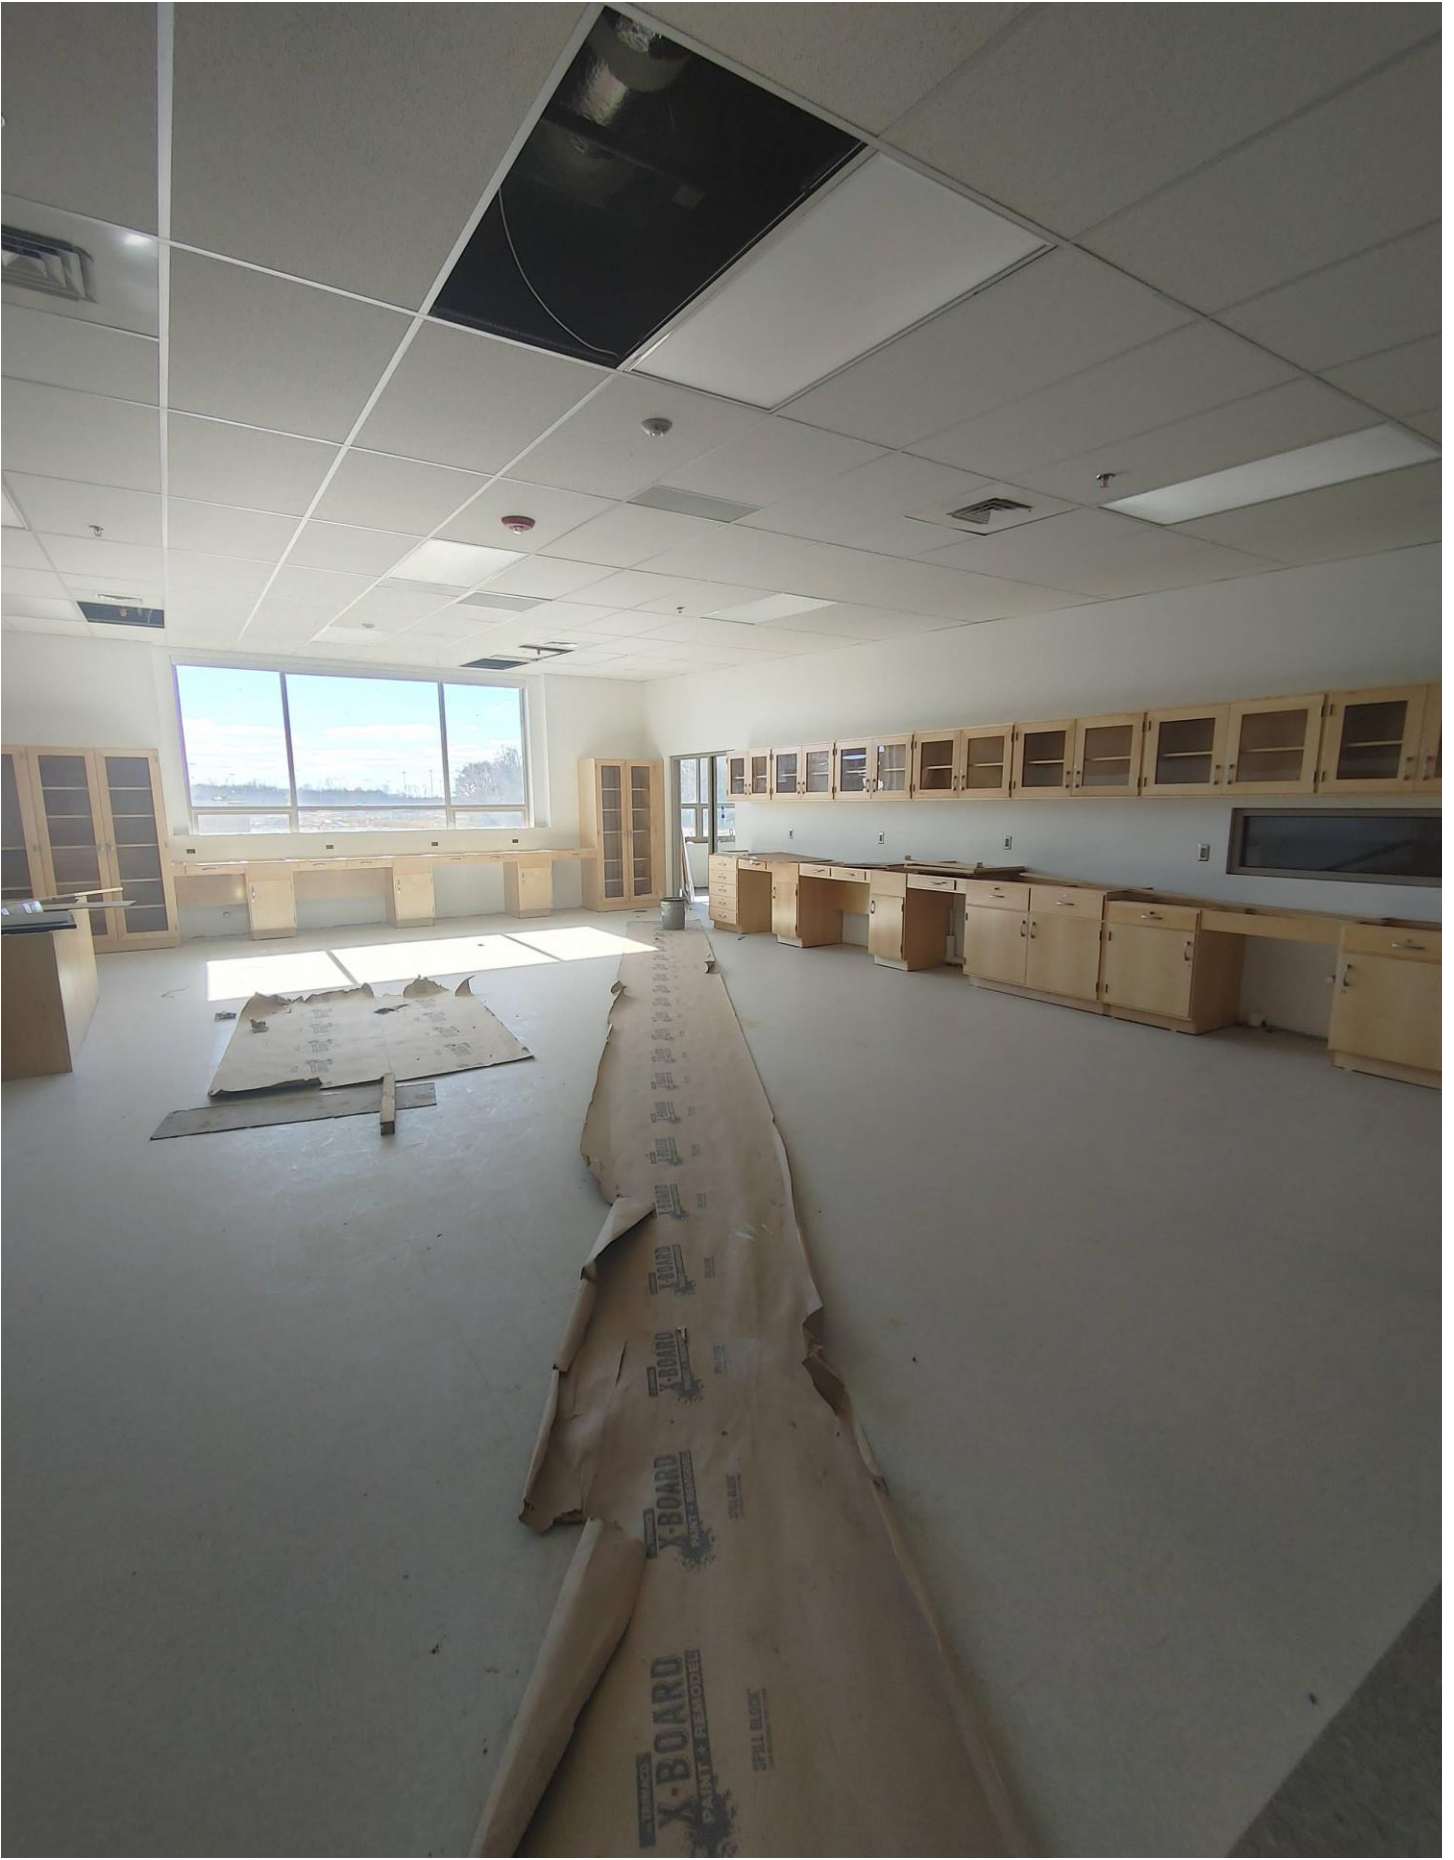


Photo 3 - Room B210



Photo 4 - Design Commons B10

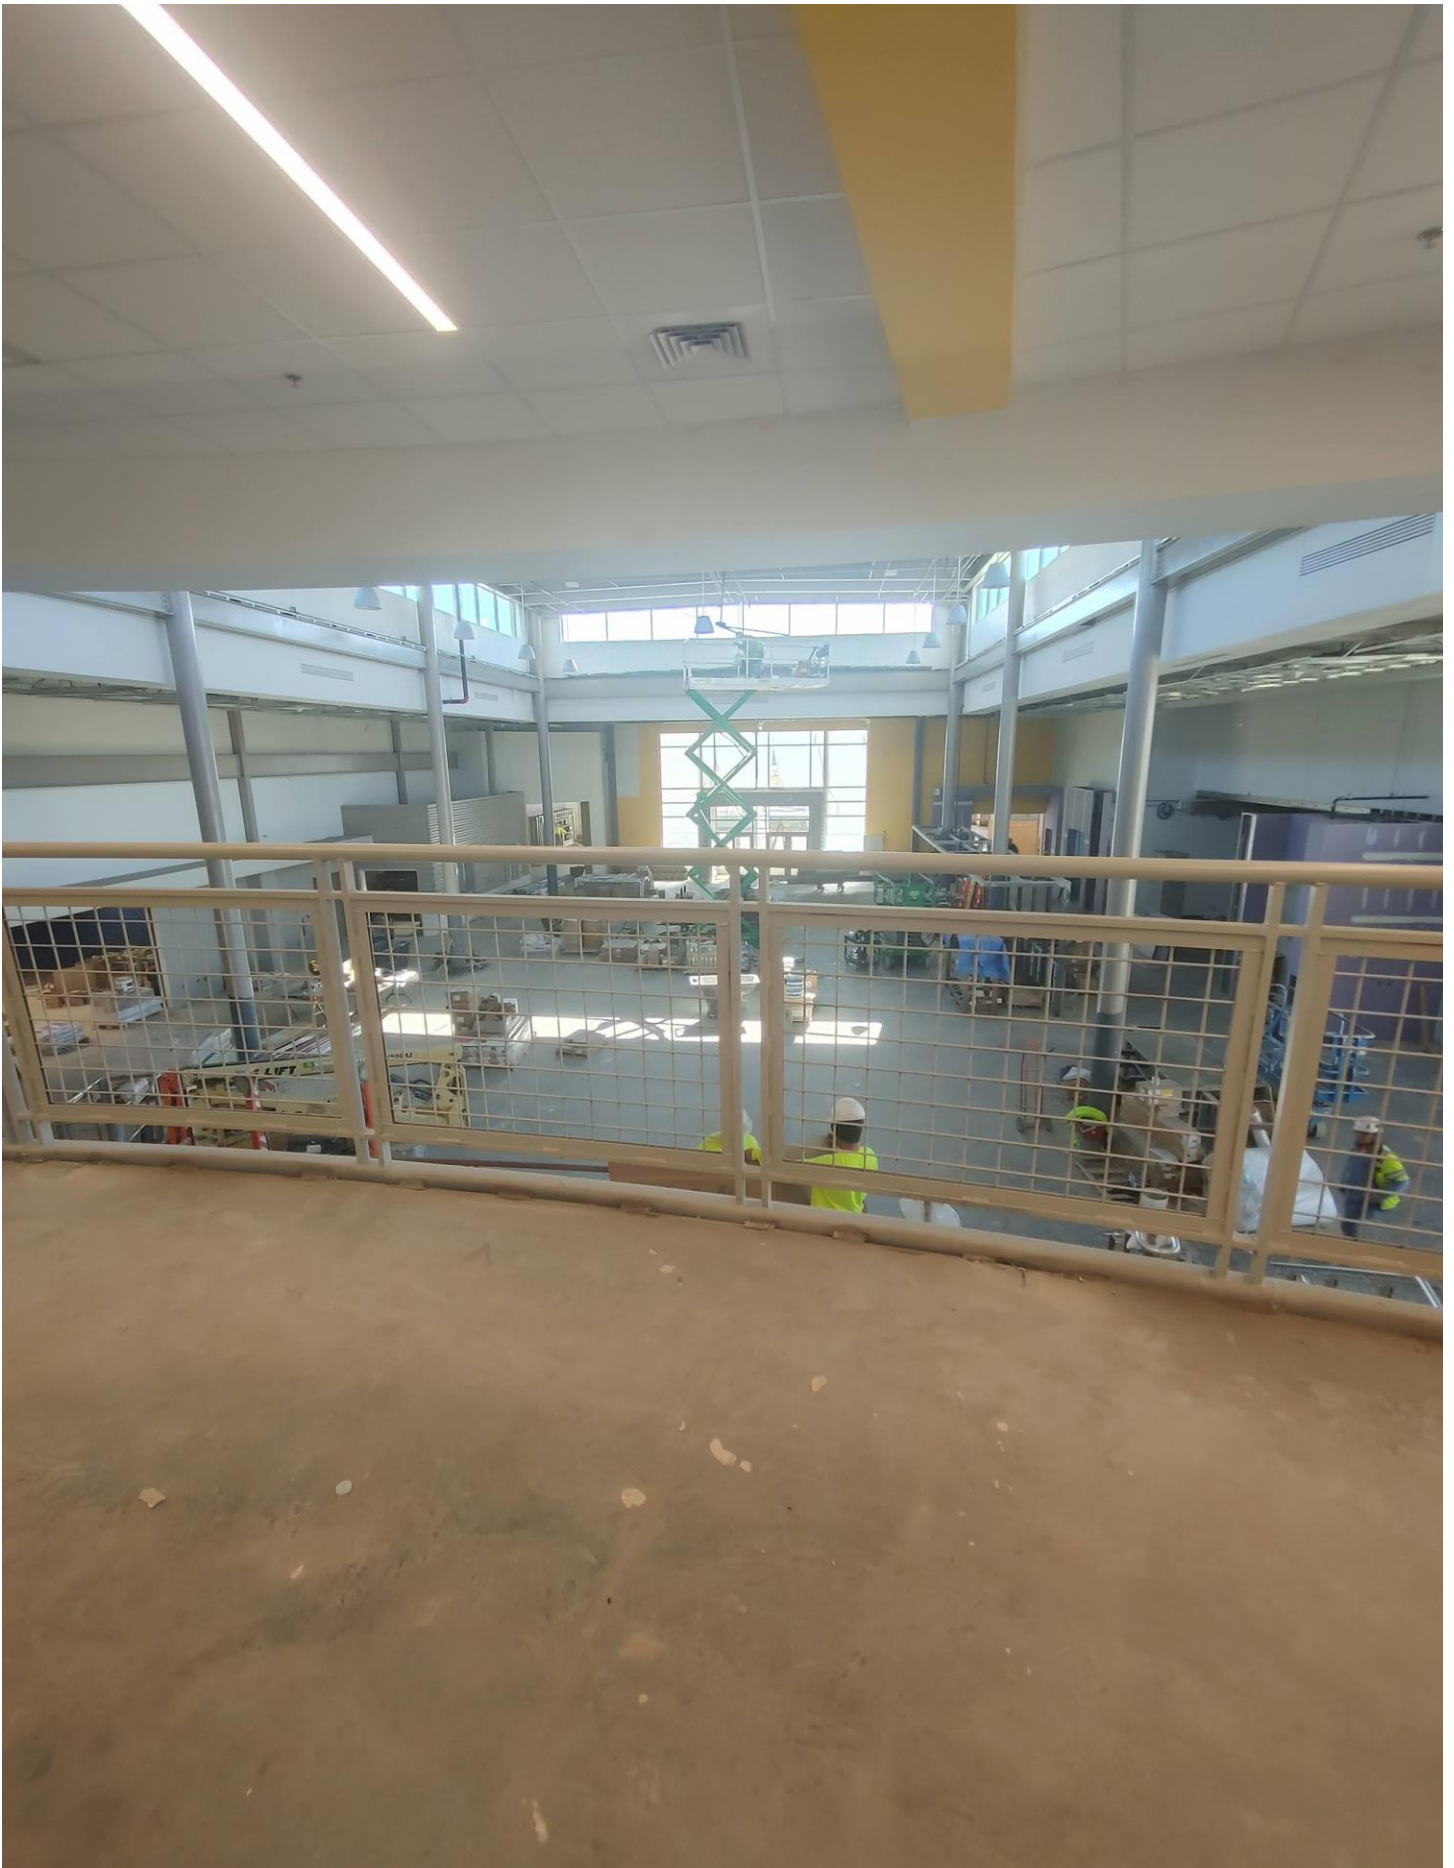


Photo 5 - Area C, Student Commons



Photo 6 - Grand Staircase is being painted



Photo 7 - Wall tile has been laid in the Kitchen



Photo 8 - Floor tile is being grouted in the Kitchen



Photo 9 - Bose Speakers have been hung in D122 & D127.

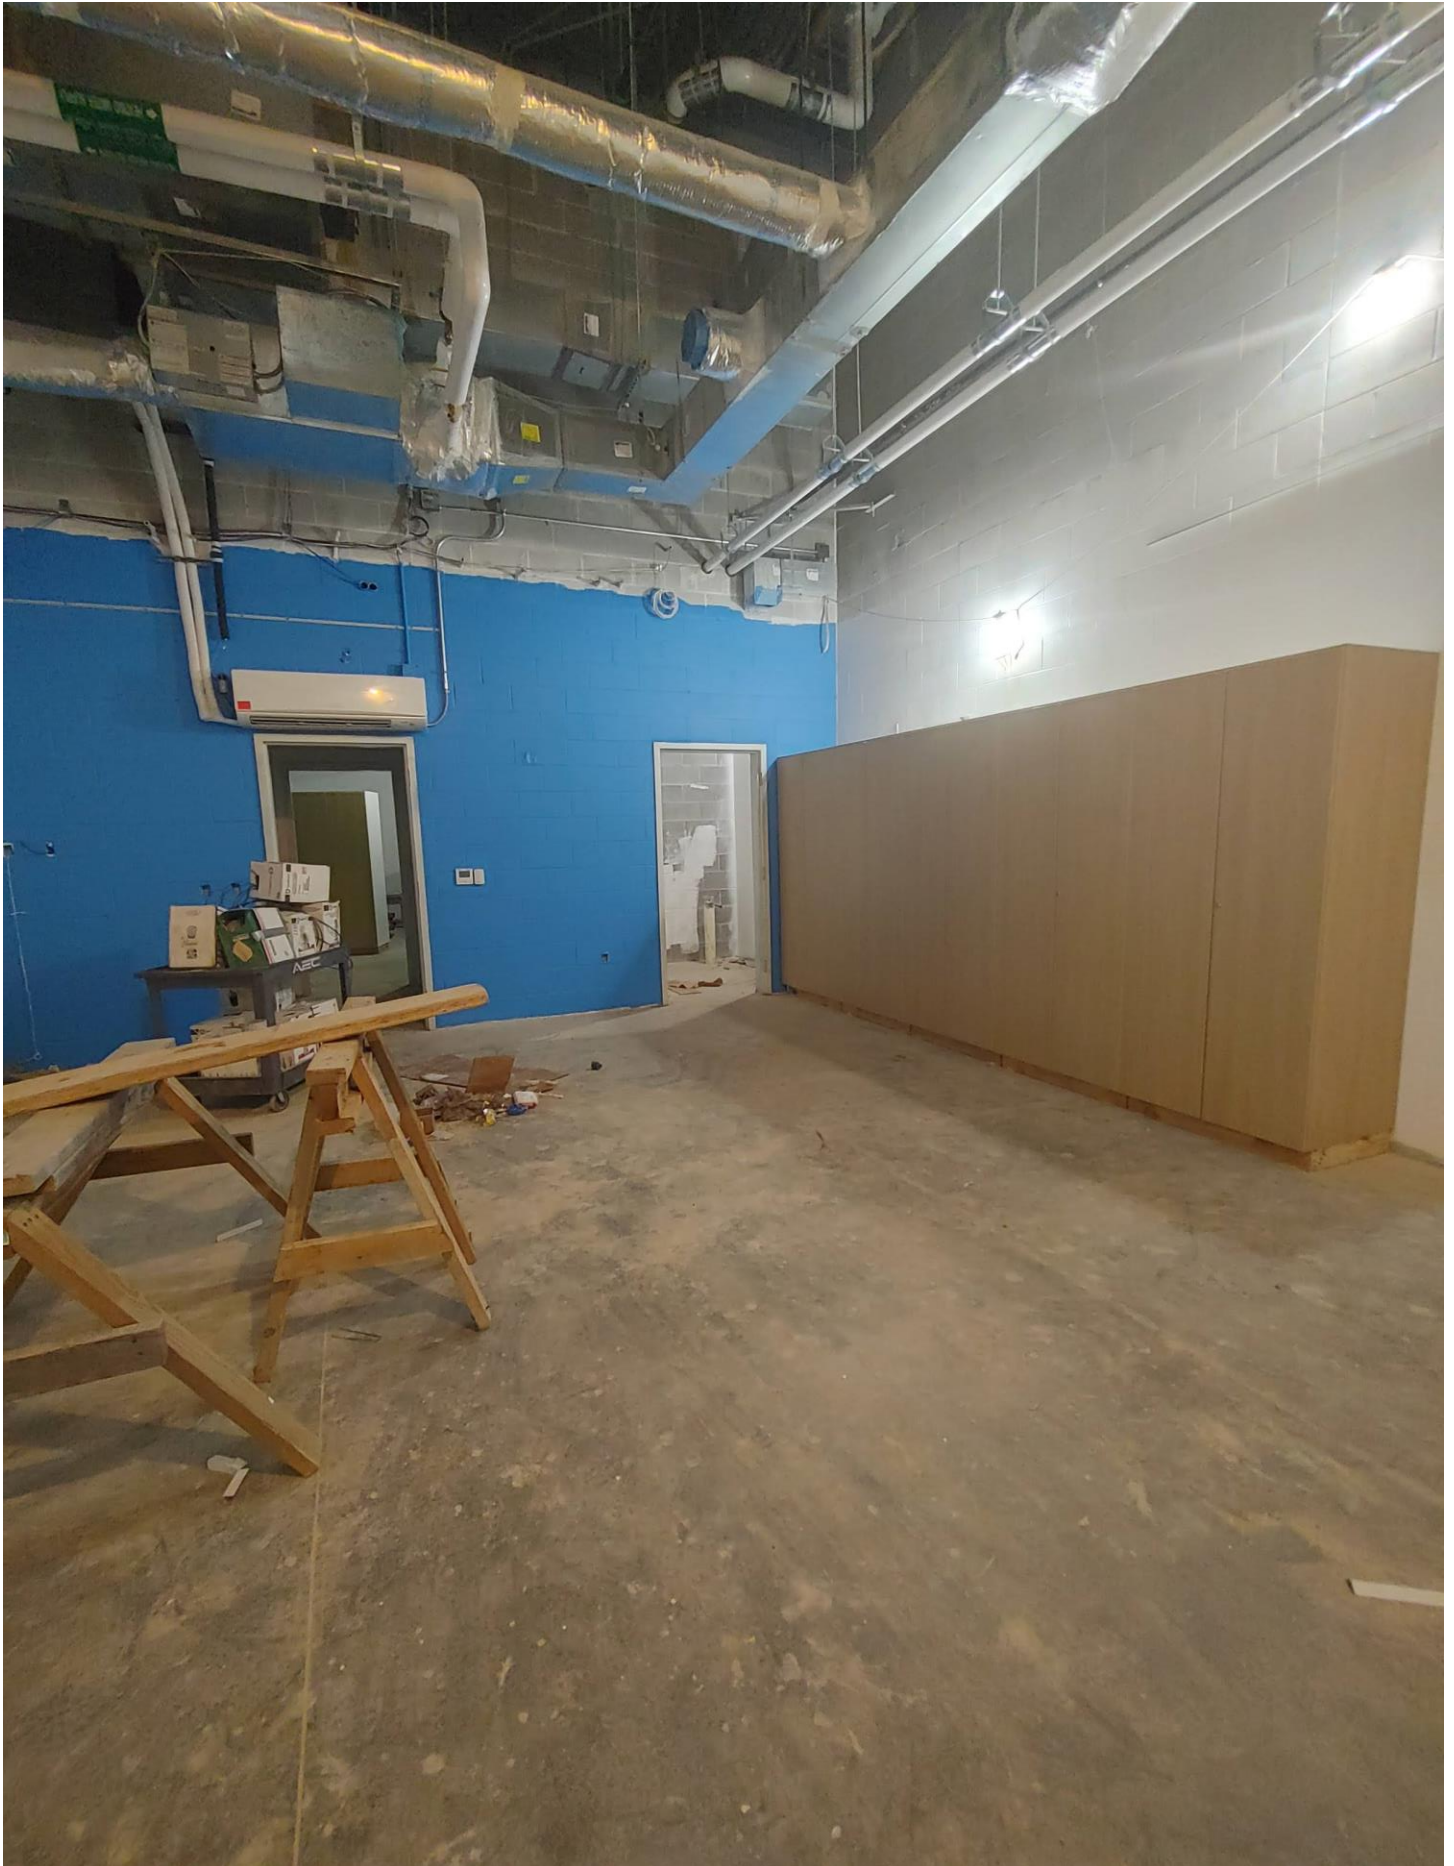


Photo 10 - Cabinetry is being installed in Rooms D131 & D132



Photo 11 - XD09 is out of Plumb and will not latch.

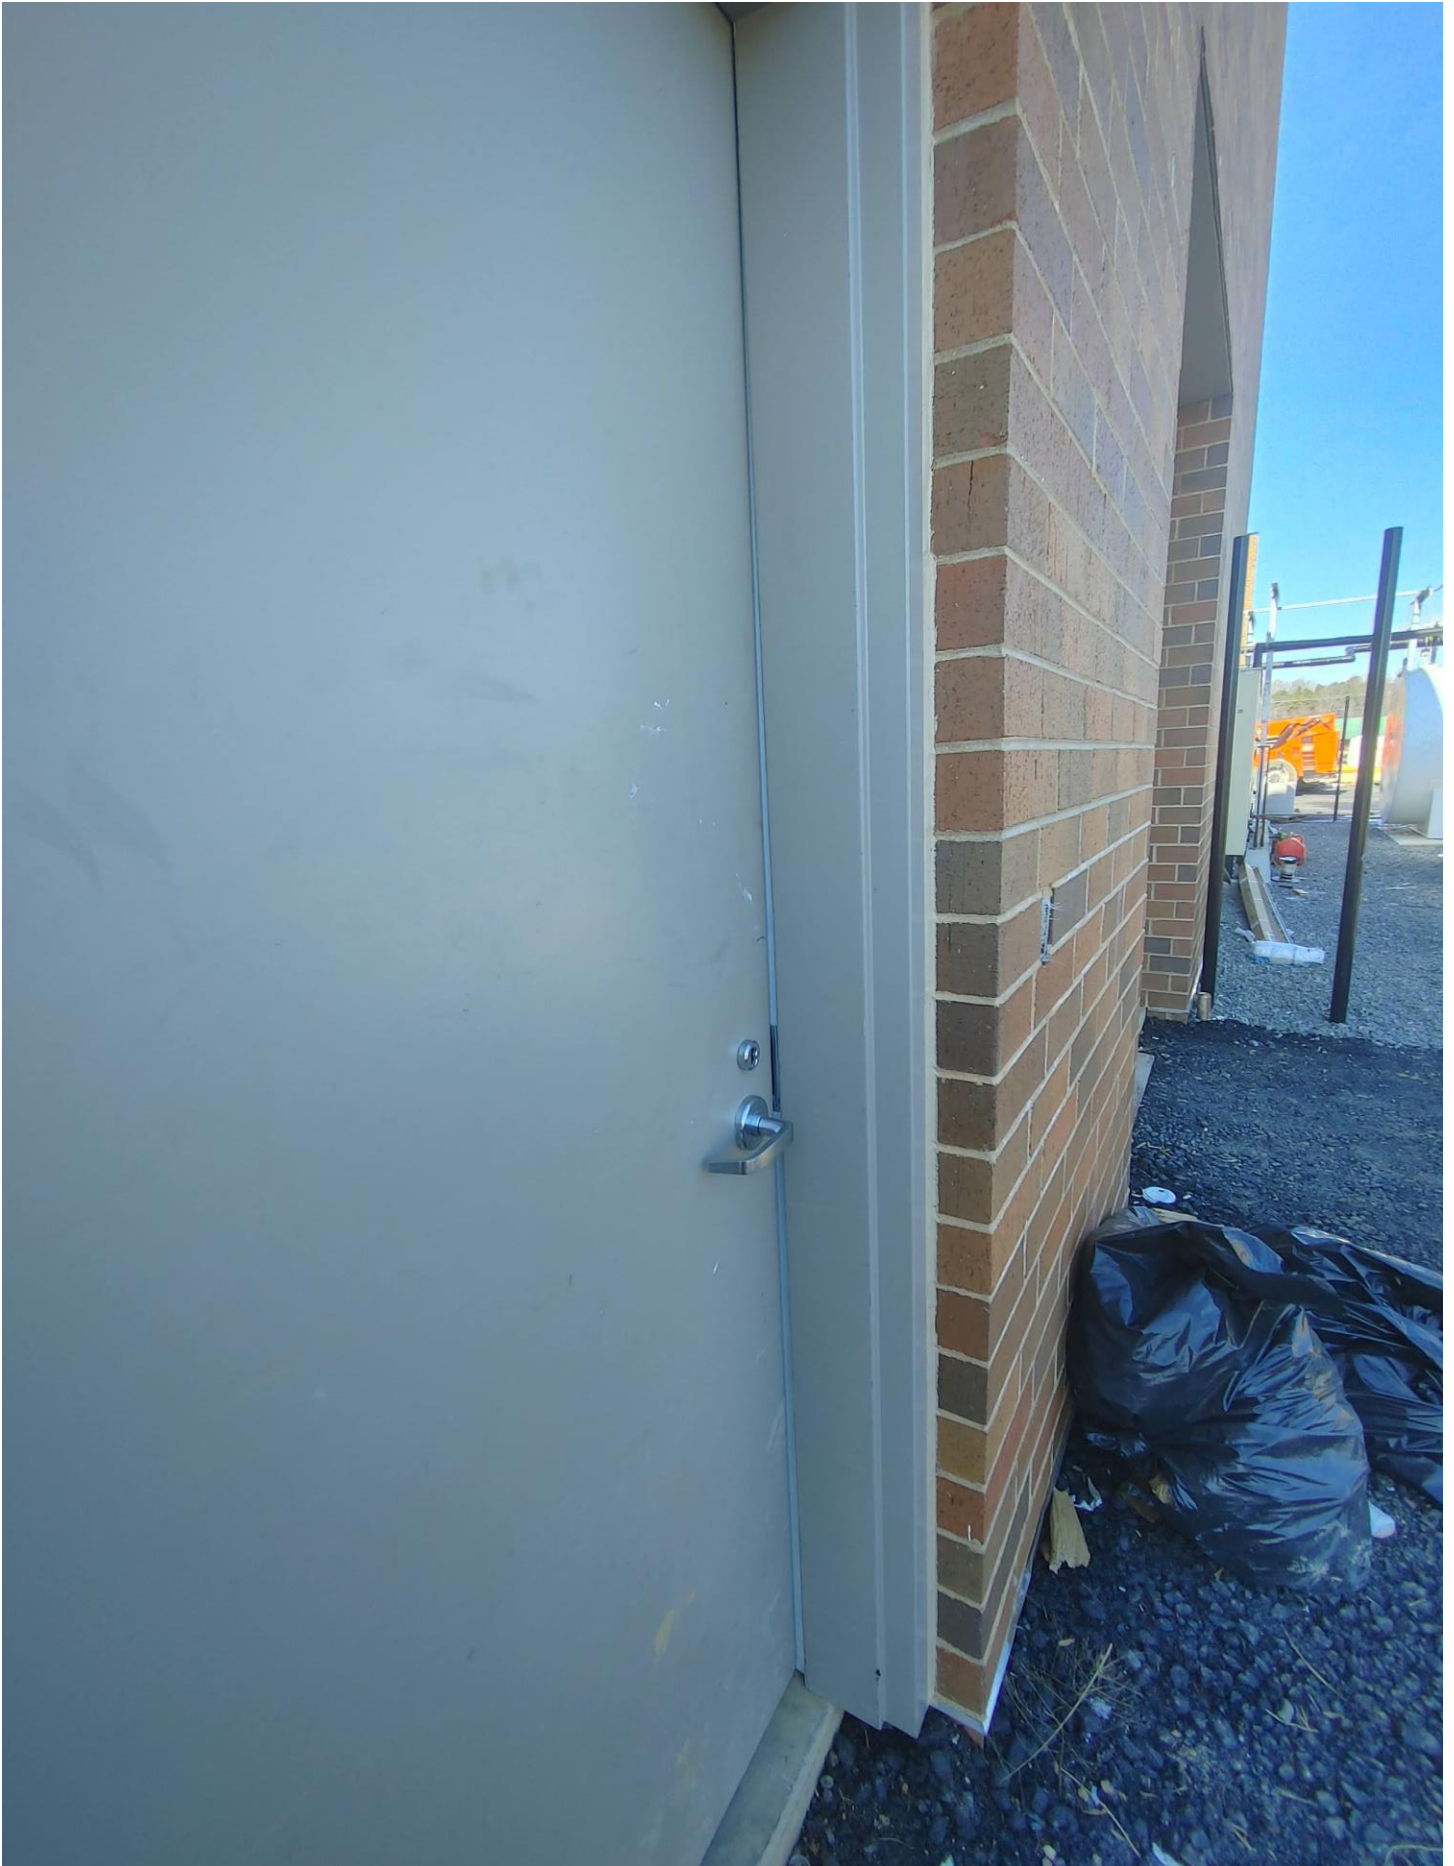


Photo 12 - Door XD09

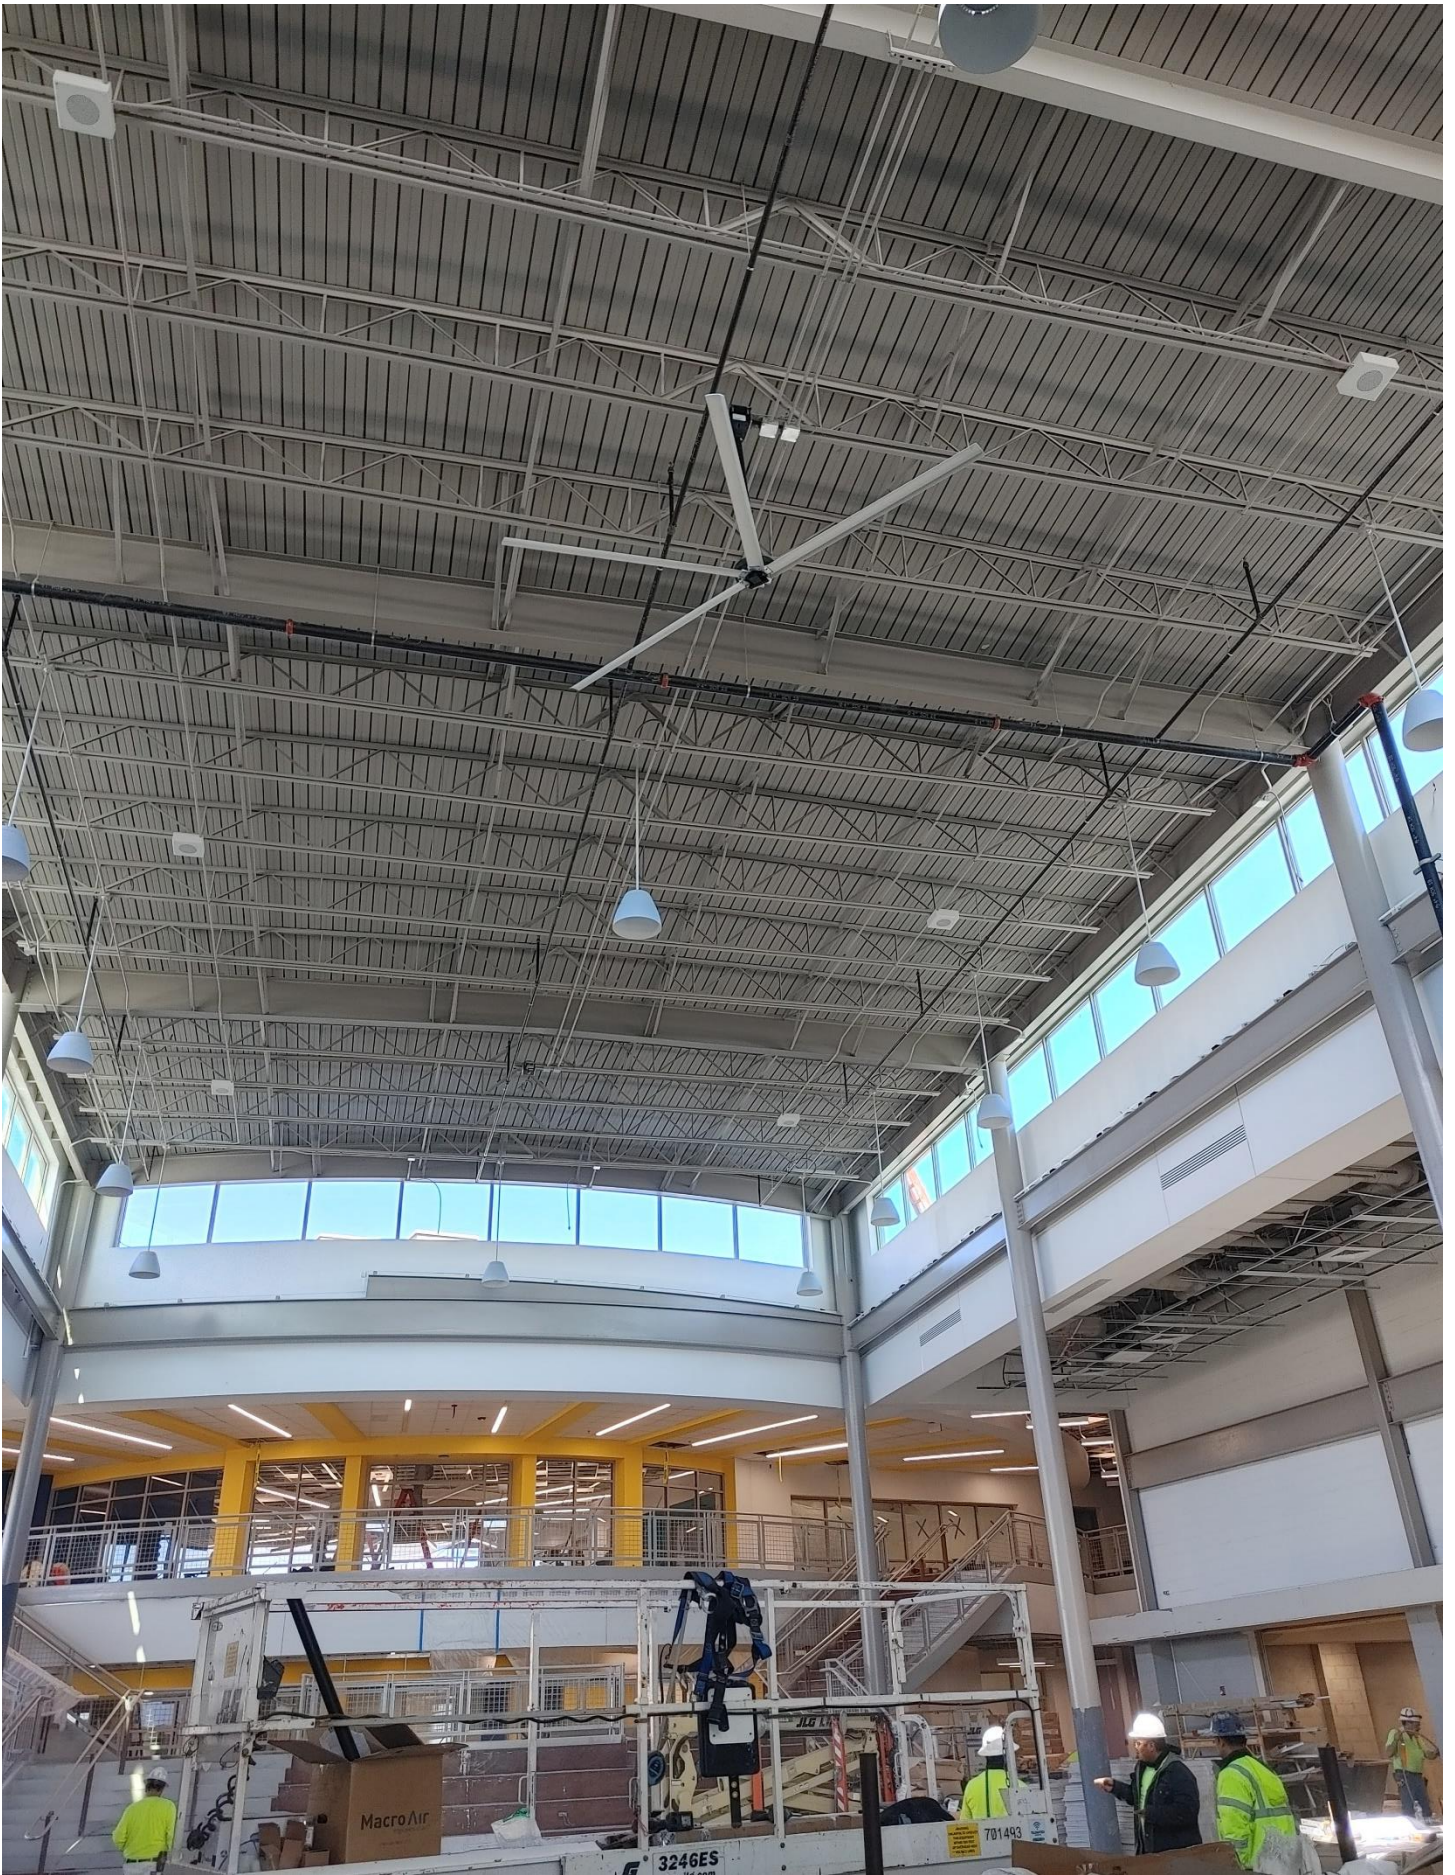


Photo 13 - Large 12' Ceiling Fans are being installed in the Student Comms Area, C100

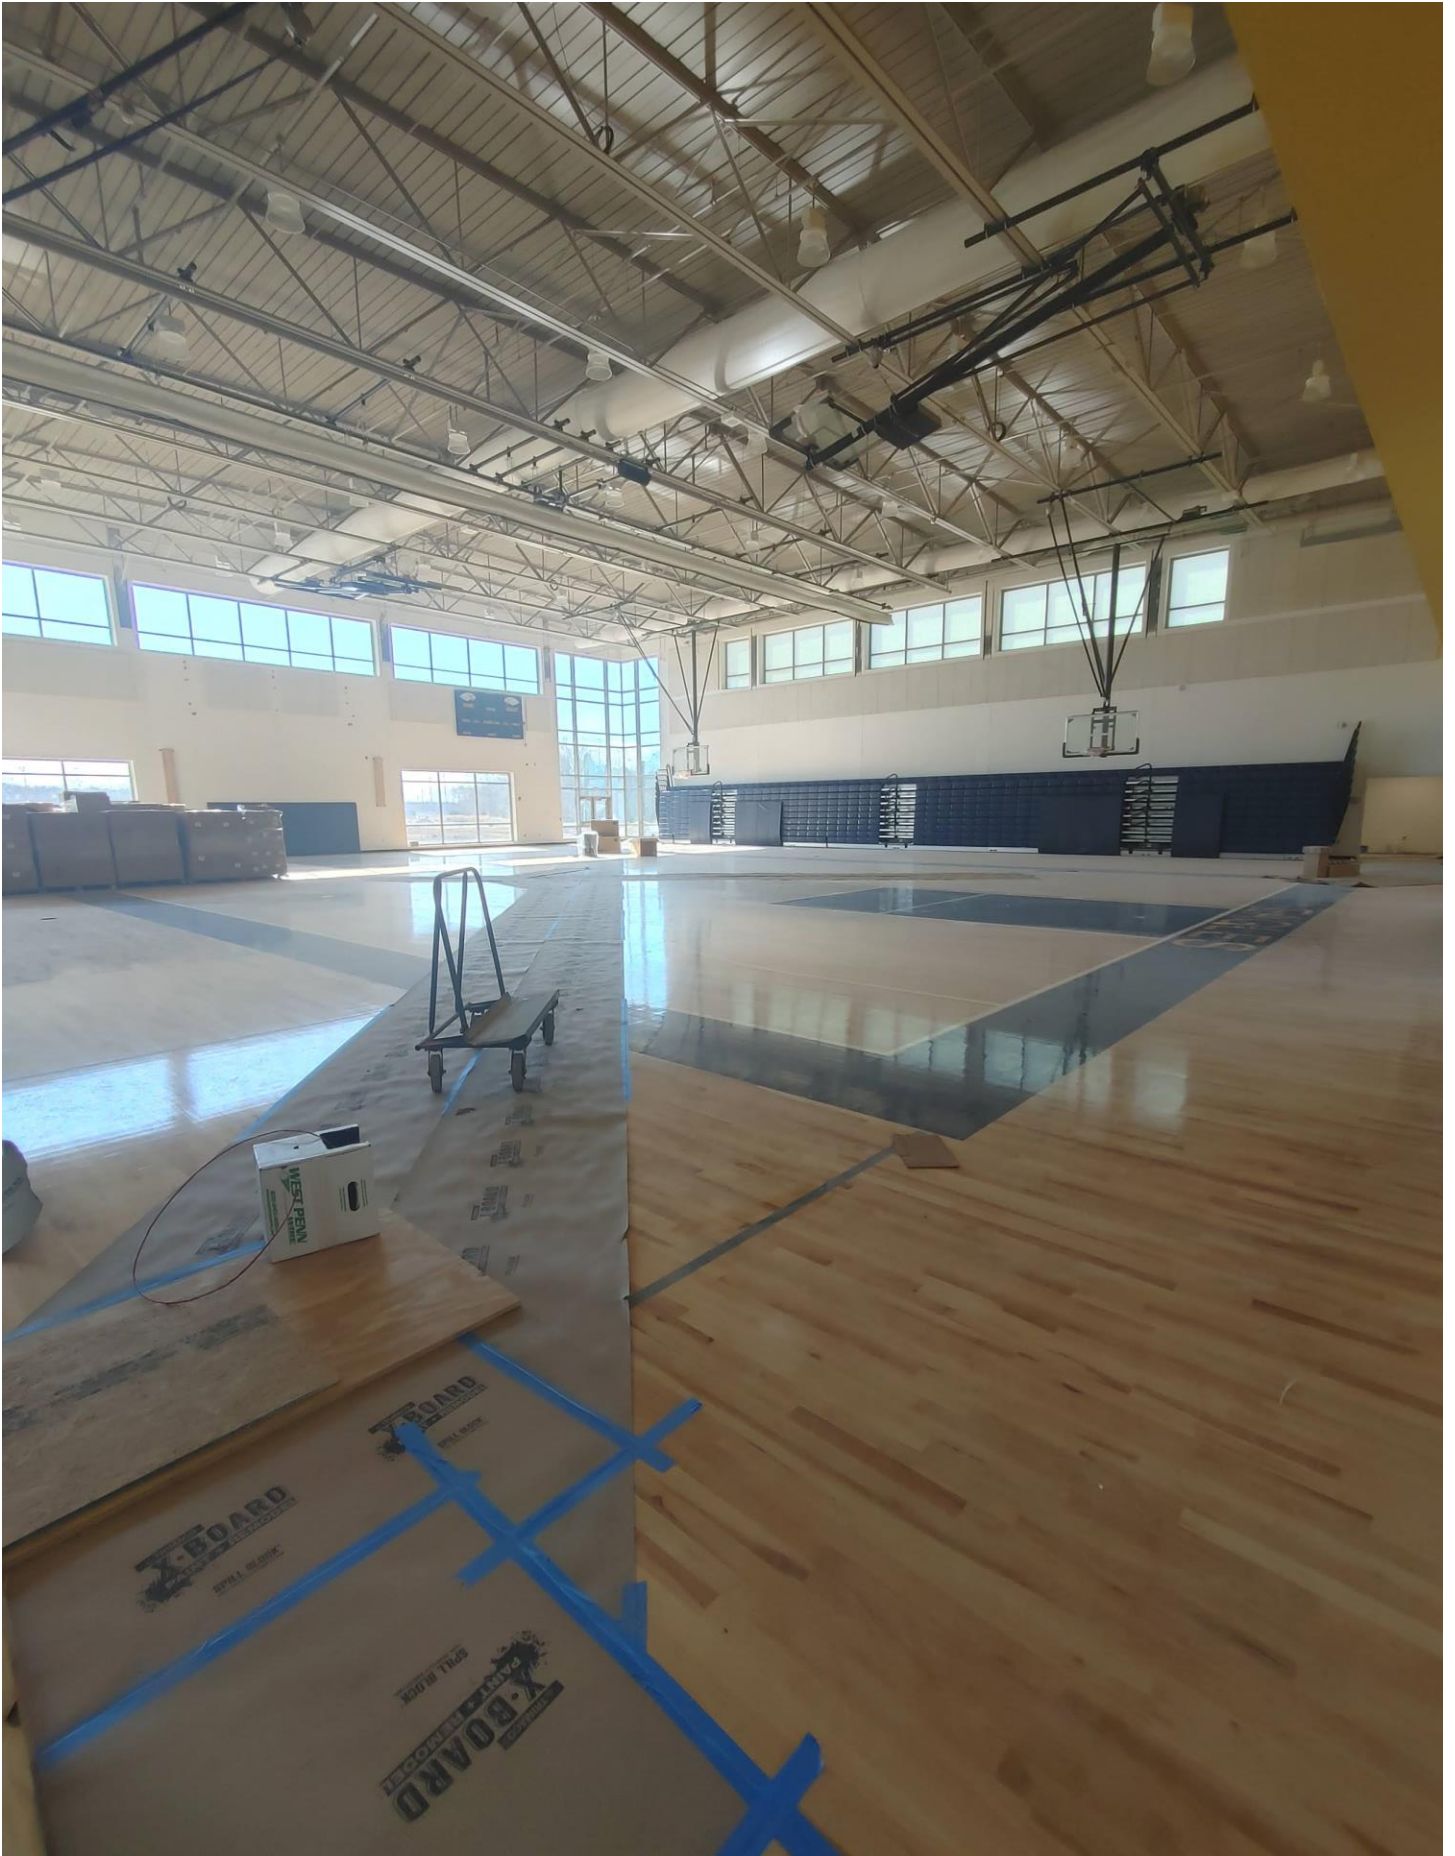


Photo 14 - Gymnasium



Photo 15 - Cabinetry has been installed in the Couch's Office E131

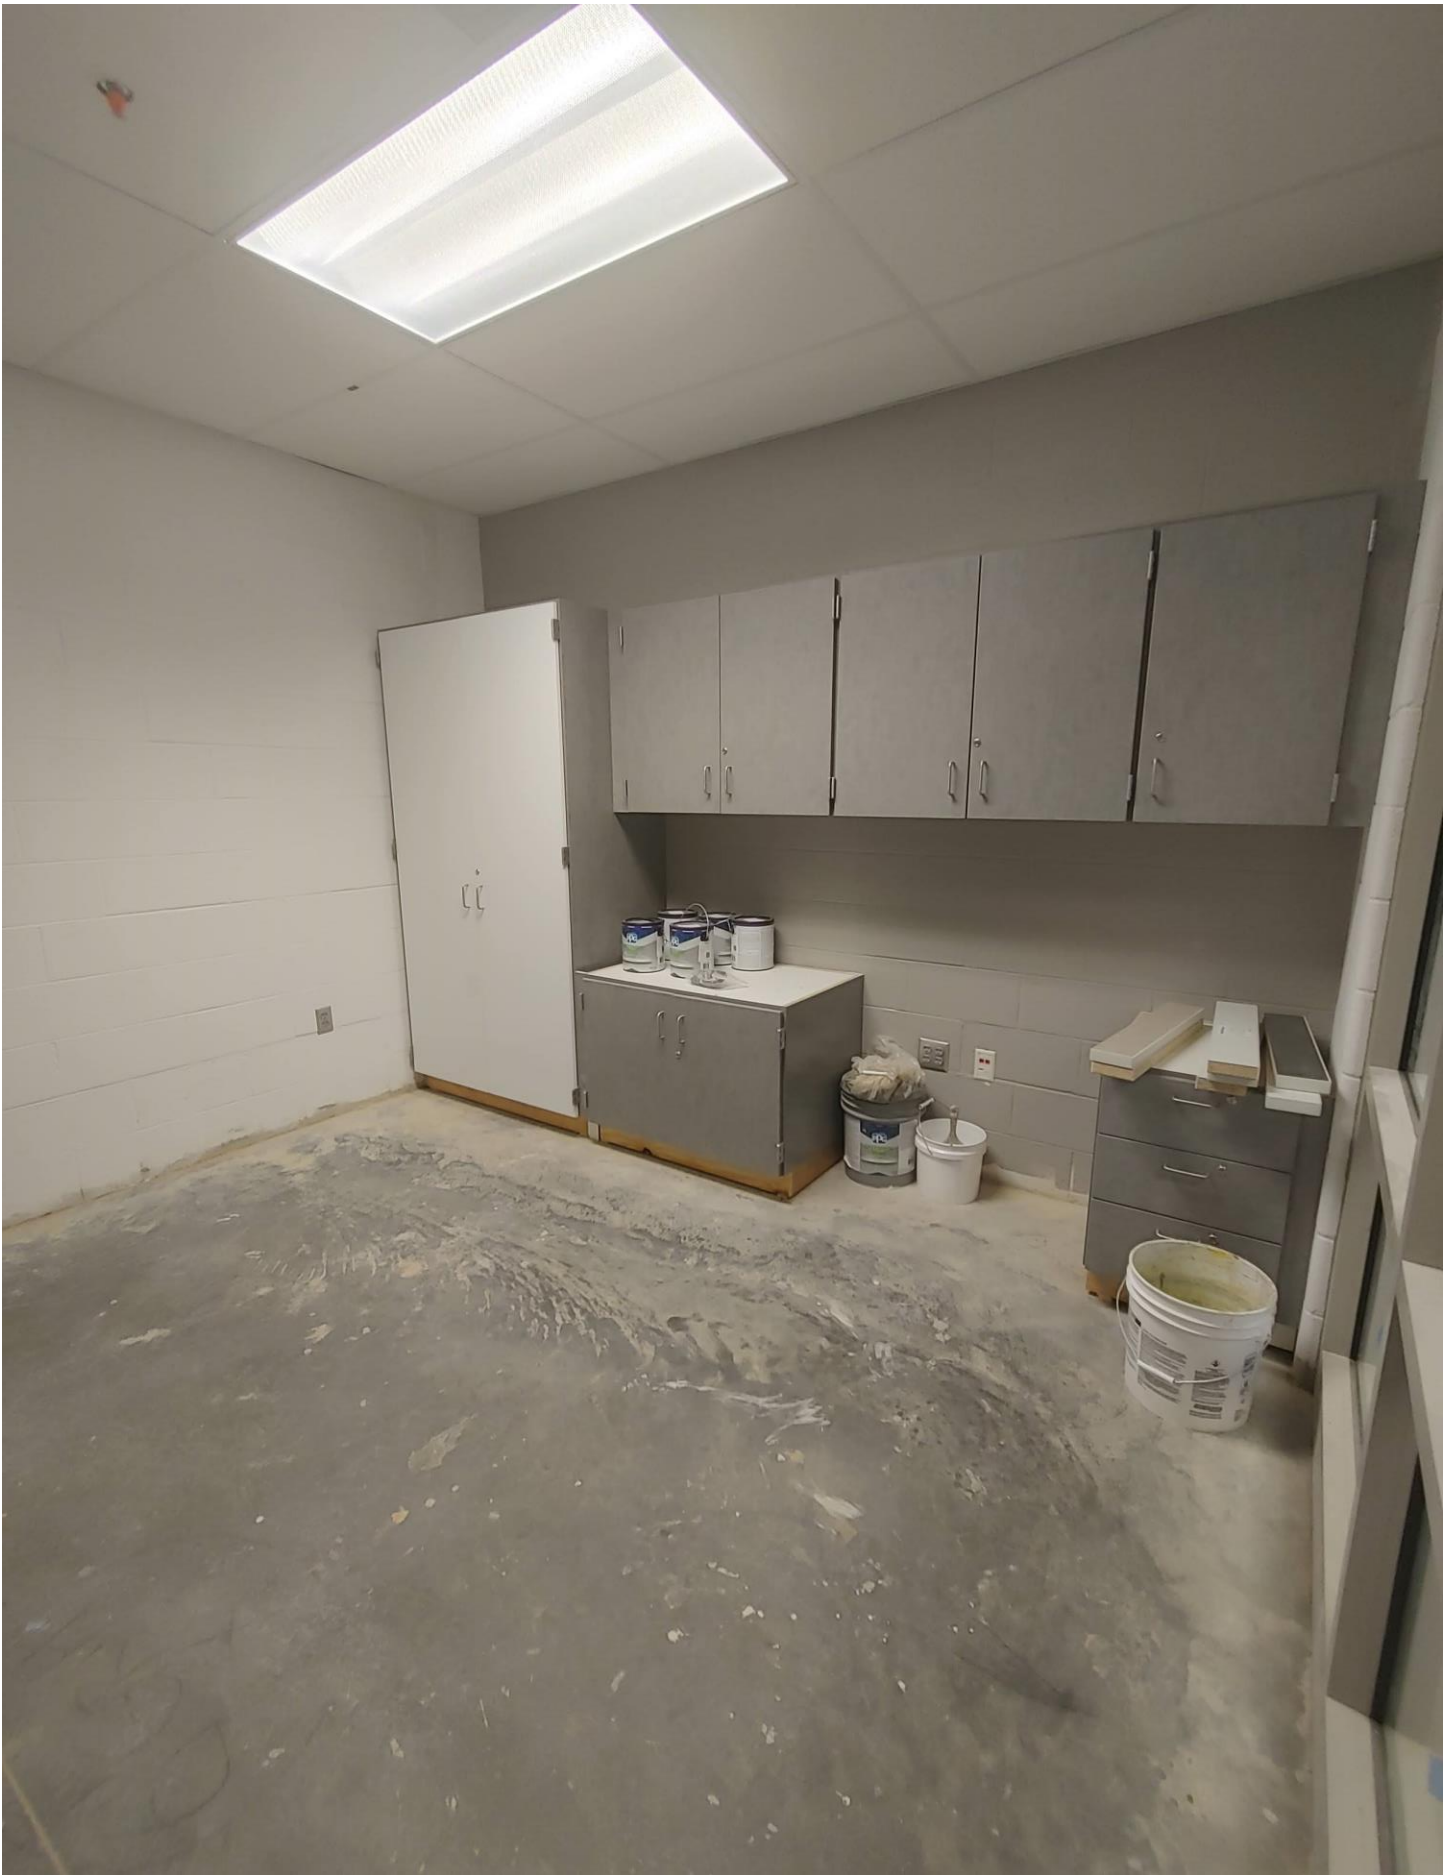


Photo 16 - Cabinetry has been installed in the Athletic Director's Office E121

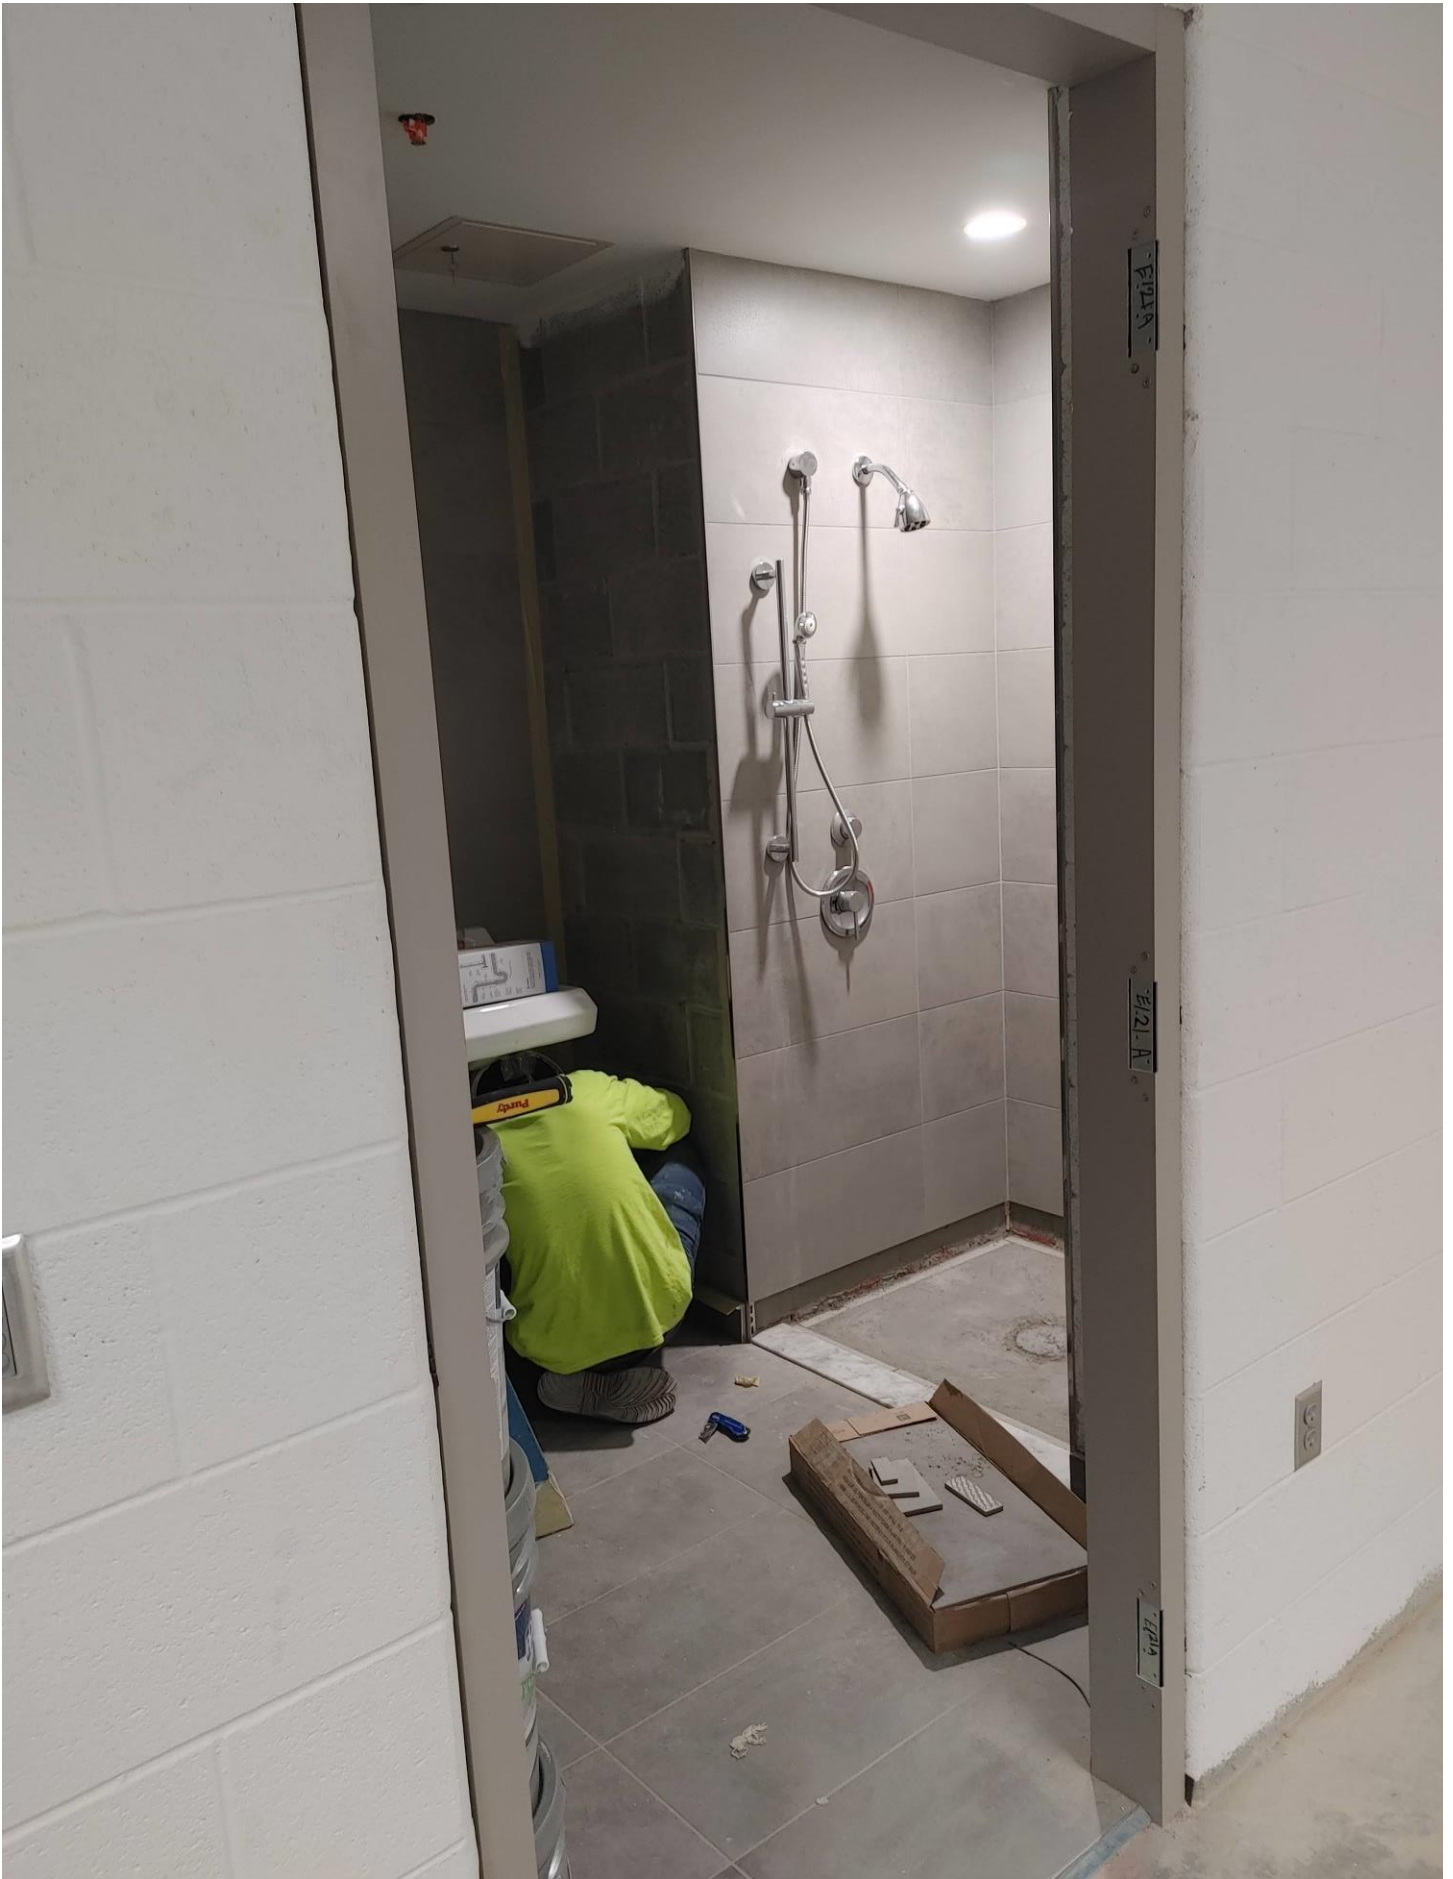


Photo 17 - Tile being laid in the Athletic Director Bathroom E121
