



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 03/17/2022

er: 57 degrees - High of 59 degrees today. Light rain.

Hours Worked: 11:30 – 15:00hrs (3.5hrs) – Site Visit

I attended the Progress Meeting yesterday in Norm’s Risavi’s Conference Room. Landscaper has planted numerous shrubs and trees since my last visit on Wednesday of last week.

**Area A** – Painters are painting in various areas throughout Area A.

**Area B** – Touch up and punch list items are being addressed.

**Area C** – Sheetrock is being finished and Plumbers are setting fixtures.

**Area D** – Sheetrock is being finished, flooring installed, Sprinkler pipe/Heads being installed and electricians running wire/making electrical connections.

**Area E** – Electricians are working in various areas.

**Site** – Beuchert is not on site today.

**Conversations with Branch Builds:** I met with Chandler, Lee and Jake during my visit. We discussed the Culvert Pipe (AKA Bridge) located on the Northeast corner of the property and also the visit later this evening with the Local Volunteer Fire Department. Chandler told me that the Cleaners are scheduled to begin a thorough cleaning of Area B prior to Patrick coming out to begin his punch.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports –**

**Hillis-Carnes Bio Retention Pond Reports –**

**Submittals -**

**RFIs –#372, #376, #391, #396, #399, #400, #402, #408, #409, #411, #414, #415, #418**

**Patrick Byrne –**

**Alexes Lee –**

**Tara Delaney –**

**Change Order/PCOs/Pay App –**

**Weekly Submittal Status Report – 02/11/2022**

**Weekly RFI Status Update – 02/11/2022**

**Weekly Daily Log Summary – 02/11/2022**

**PCO Log – 02/11/2022**



*Photo 1 - Galvanized Panel installed - Student Entrance area.*



Photo 2 - Equipment continues to be installed in the Kitchen





*Photo 3 - Carpet has been installed in the Administrative Office area.*

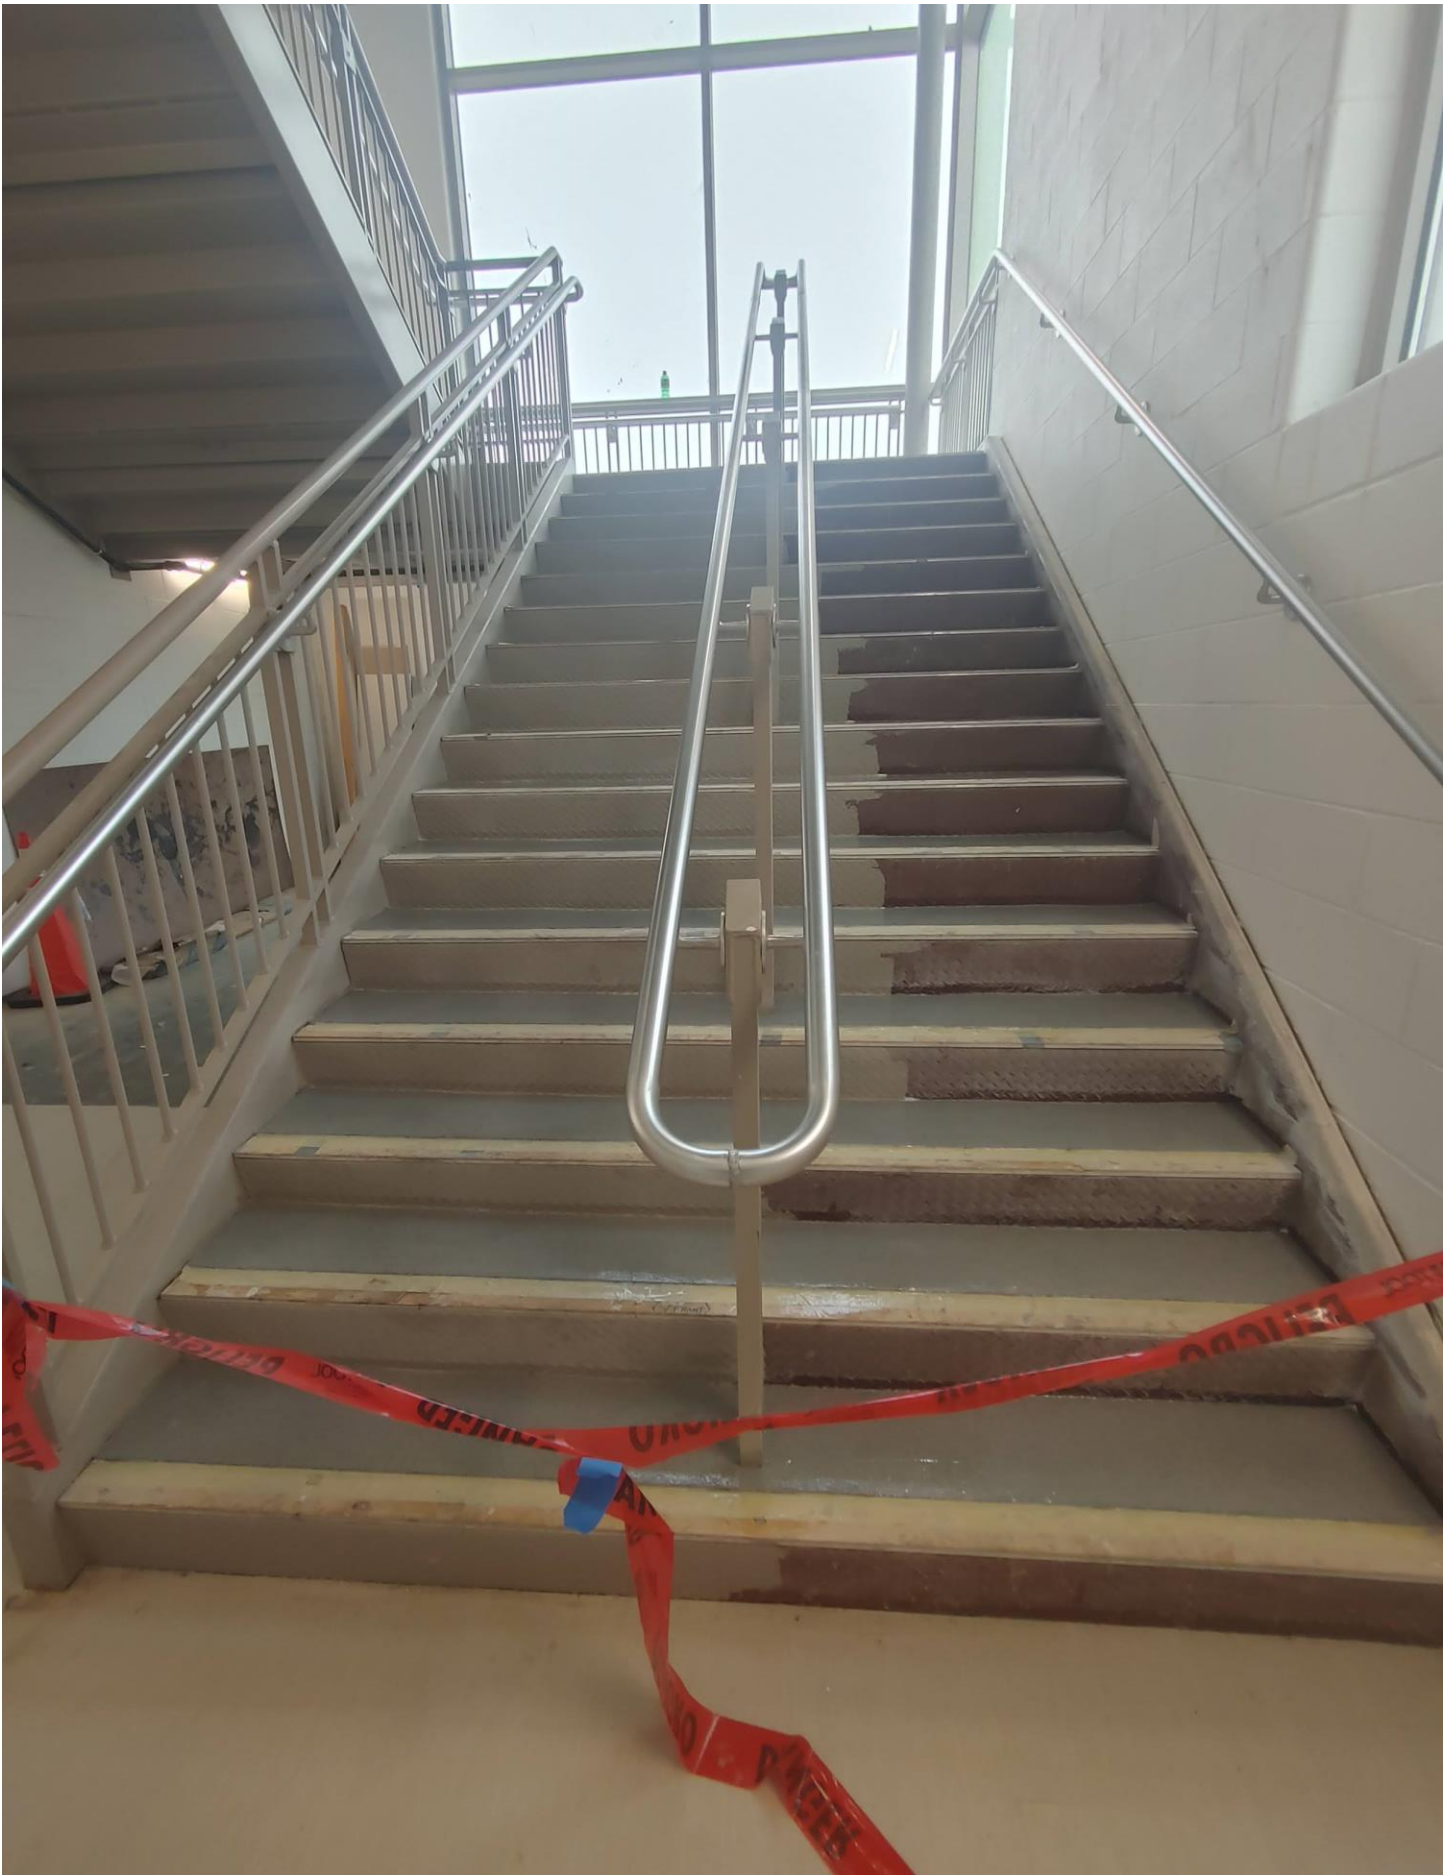


Photo 4 - Stair #1 is being painted





*Photo 5 - Promethean Board has been mounted.*



Photo 6 - Promethean Board



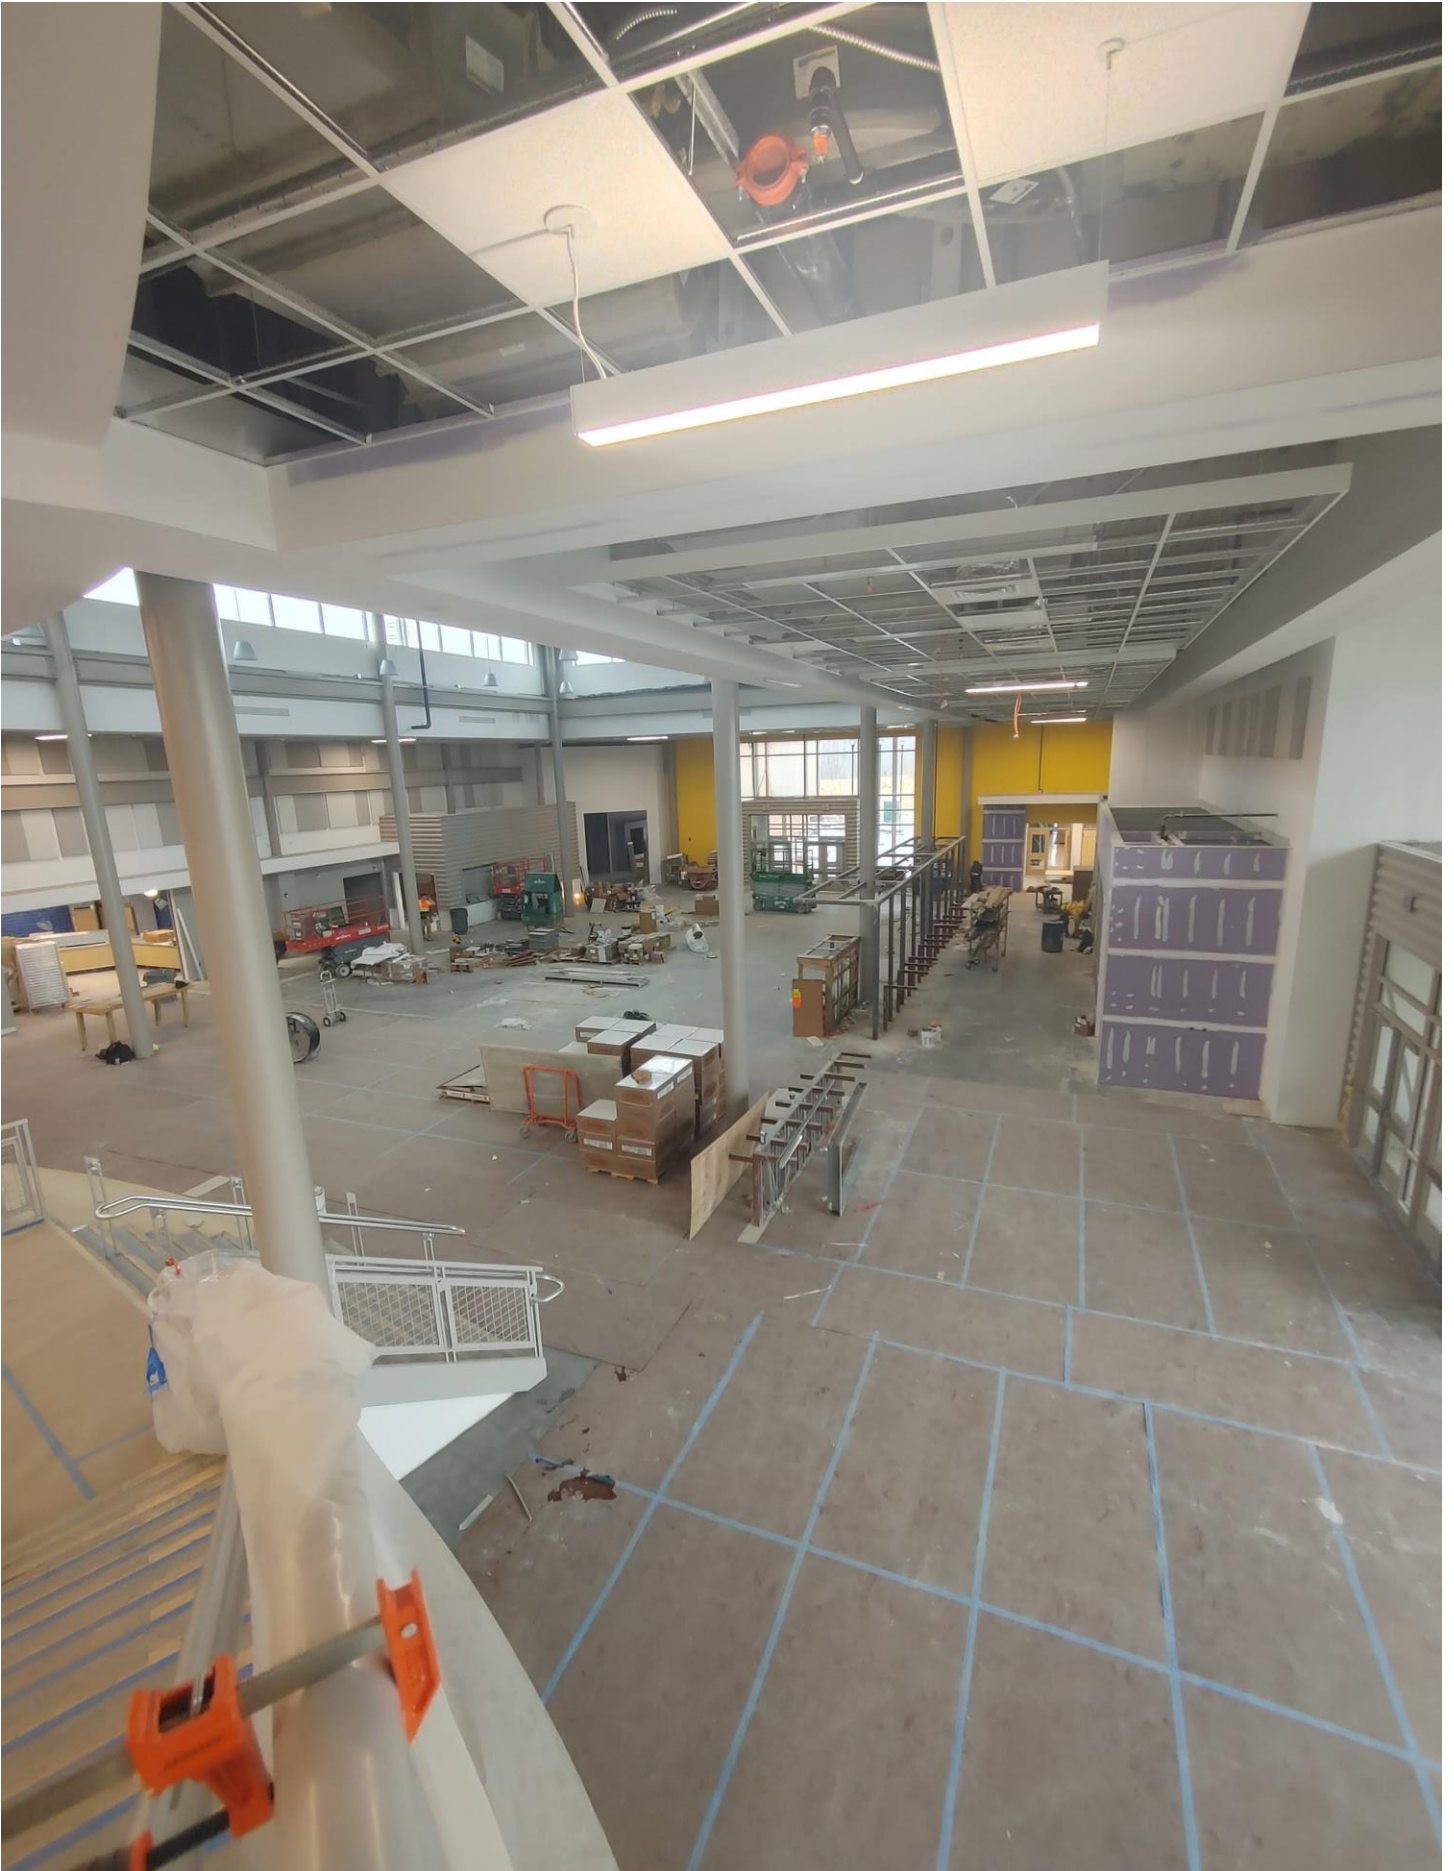


Photo 7 - Area C





Photo 8 - Acoustical Panels hung in Area C





Photo 9 - Entrance to Auditorium





Photo 10 - Shetrock is being finished in Auditorium

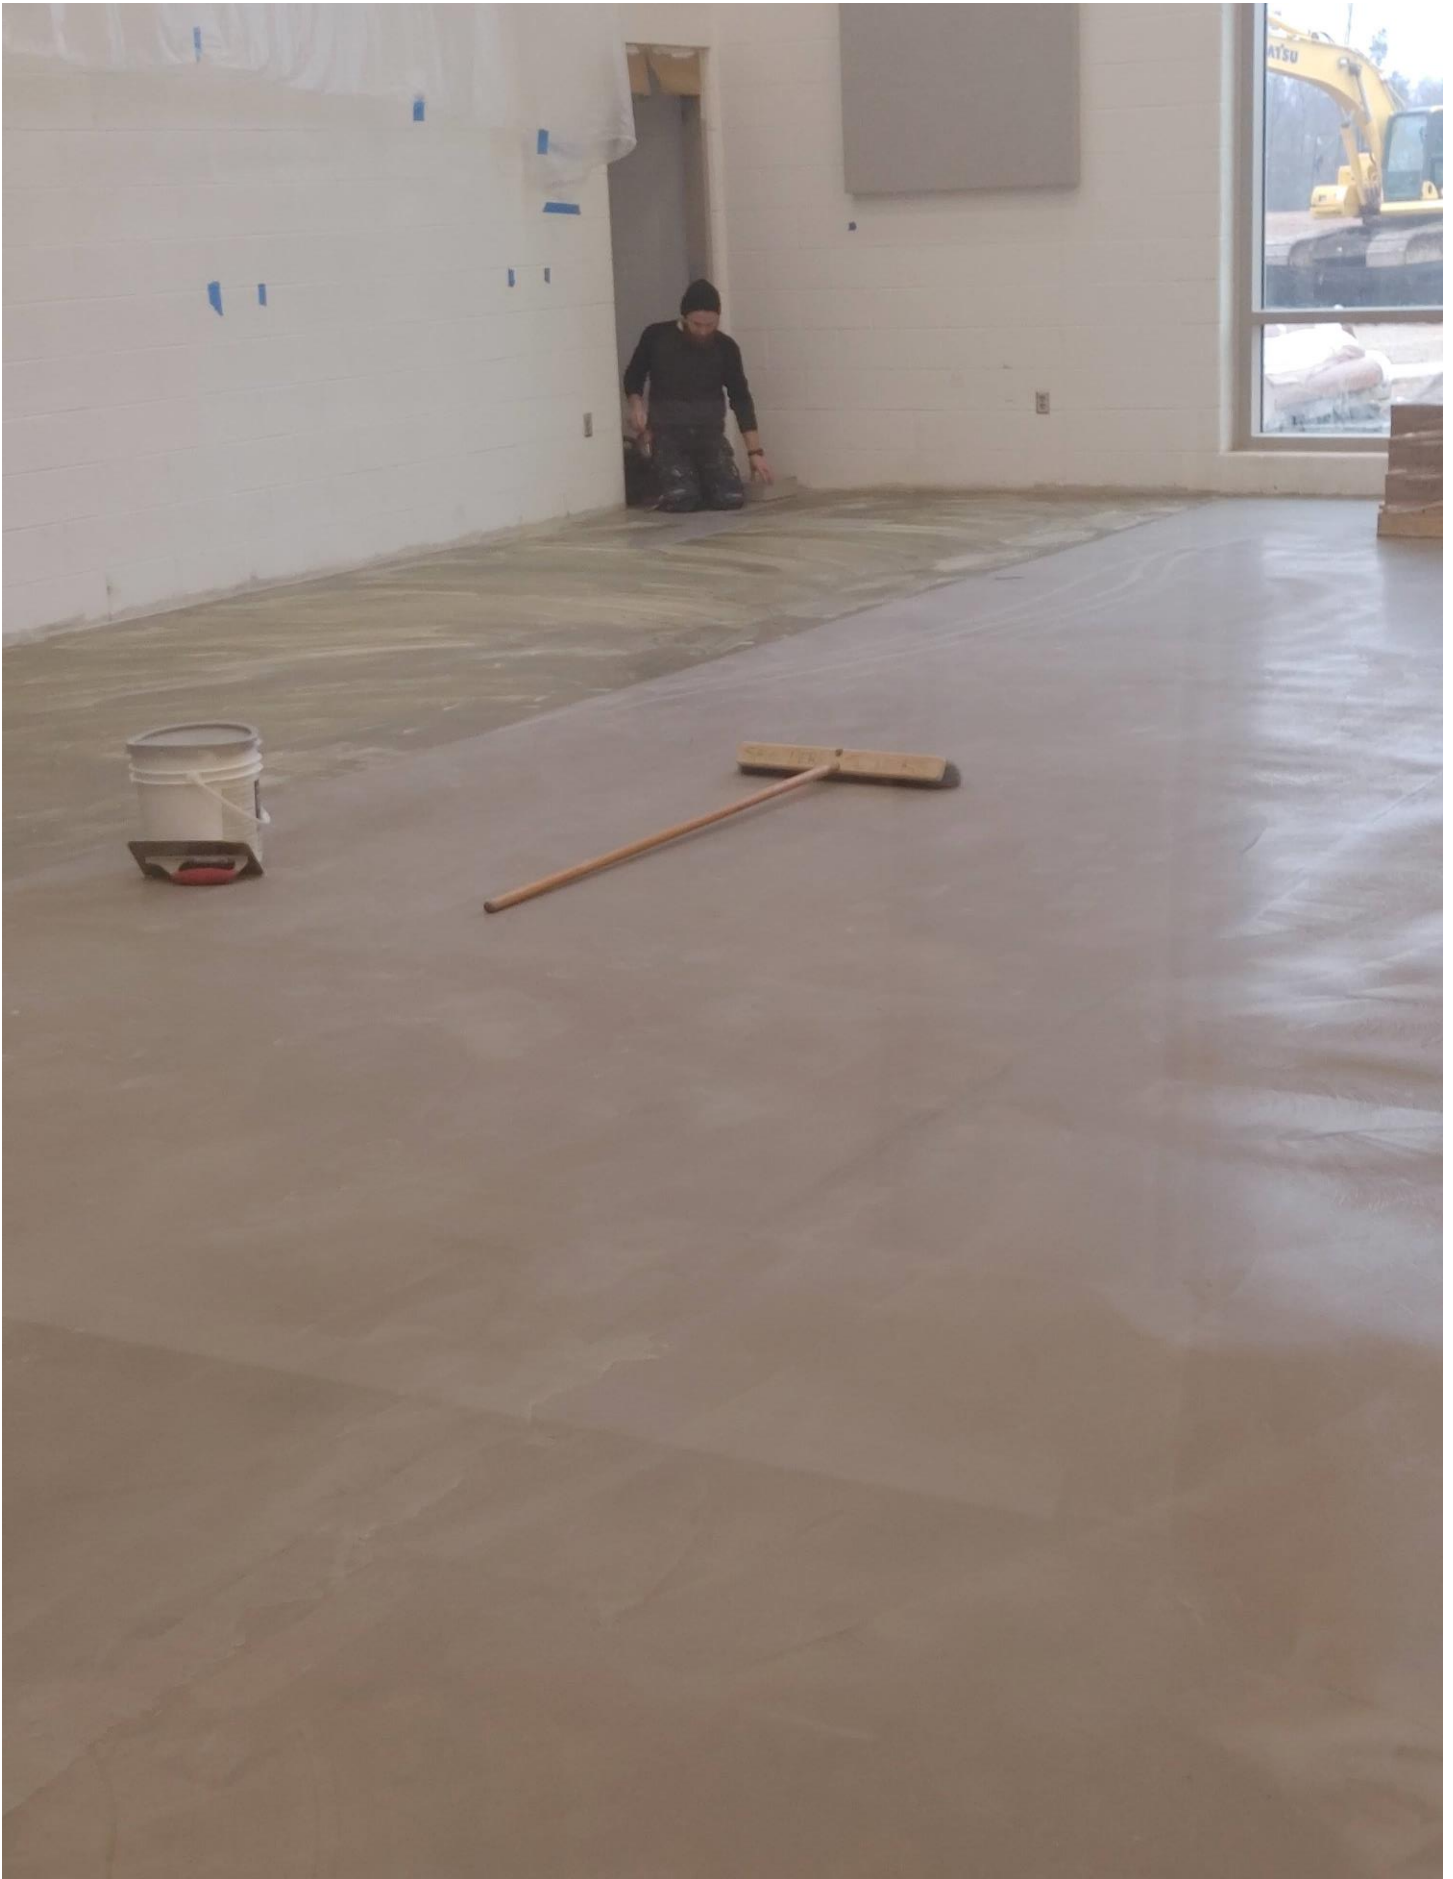


Photo 11 - VCT is being laid in Area D





Photo 12 - Piping from Fuel Tank to Mechanical Room appears to be sagging. Is additional bracing needed?





Photo 13 - Shrubs planted along Student Entrance





Photo 14 - Outdoor Benches & Trash receptacles delivered





*Photo 15 - Light poles installed and trees planted on South Entrance*





*Photo 16 - Shrubs planted along Loading Dock*





Photo 17 - Retention Pond on east side of Site.





Photo 18 - Northeast view of site
