



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/07/2022

er: 61 degrees - High of 63 degrees today. Light rain earlier today. Currently mostly Cloudy.

Hours Worked: 09:30 – 12:00hrs (2.5hrs) – Site Visit & BAS Controls Coordination Meeting

I attended the BAS Controls Coordination meeting with Branch Builds. Tom with Westmoreland County Schools was in attendance. After the meeting I told Tom that the Fire Department wants to meet with him after the key cylinders have been installed to go over the Keys that will need to be placed in the Knox Box.

I reviewed the Pay App for March and met up with Todd. Todd is going to review the pay app and remove the \$7,481.47 for the Dishwasher Counter Door. It has not been installed and it is not on site.

Conversations with Branch Builds: I met with Todd, Chandler, Lee and Lisa Bateman during my visit. We discussed the Project's timeline and material delays.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports –

Hillis-Carnes Bio Retention Pond Reports –

Submittals - #11 31 00-5.1, #12 35 53-9.0

RFIs – #373, #376, #386, #408, #410, #415, #418, #419, #420

Patrick Byrne – PCO #61, PCO #71, PCO #72, PCO #74-#77, PCO #78, #79, PCO #85

Alexes Lee –

Tara Delaney –

Change Order/PCOs/Pay App – PCO #88, PCO # 89 – Additional time for Material delays. PCO #92 – Football Field

Weekly Submittal Status Report – 03/18/2022, 03/25/2022, 04/01/2022

Weekly RFI Status Update – 03/18/2022, 03/25/2022, 04/01/2022

Weekly Daily Log Summary – 03/18/2022, 03/25/2022, 04/01/2022

PCO Log – 03/18/2022, 03/25/2022, 04/01/2022

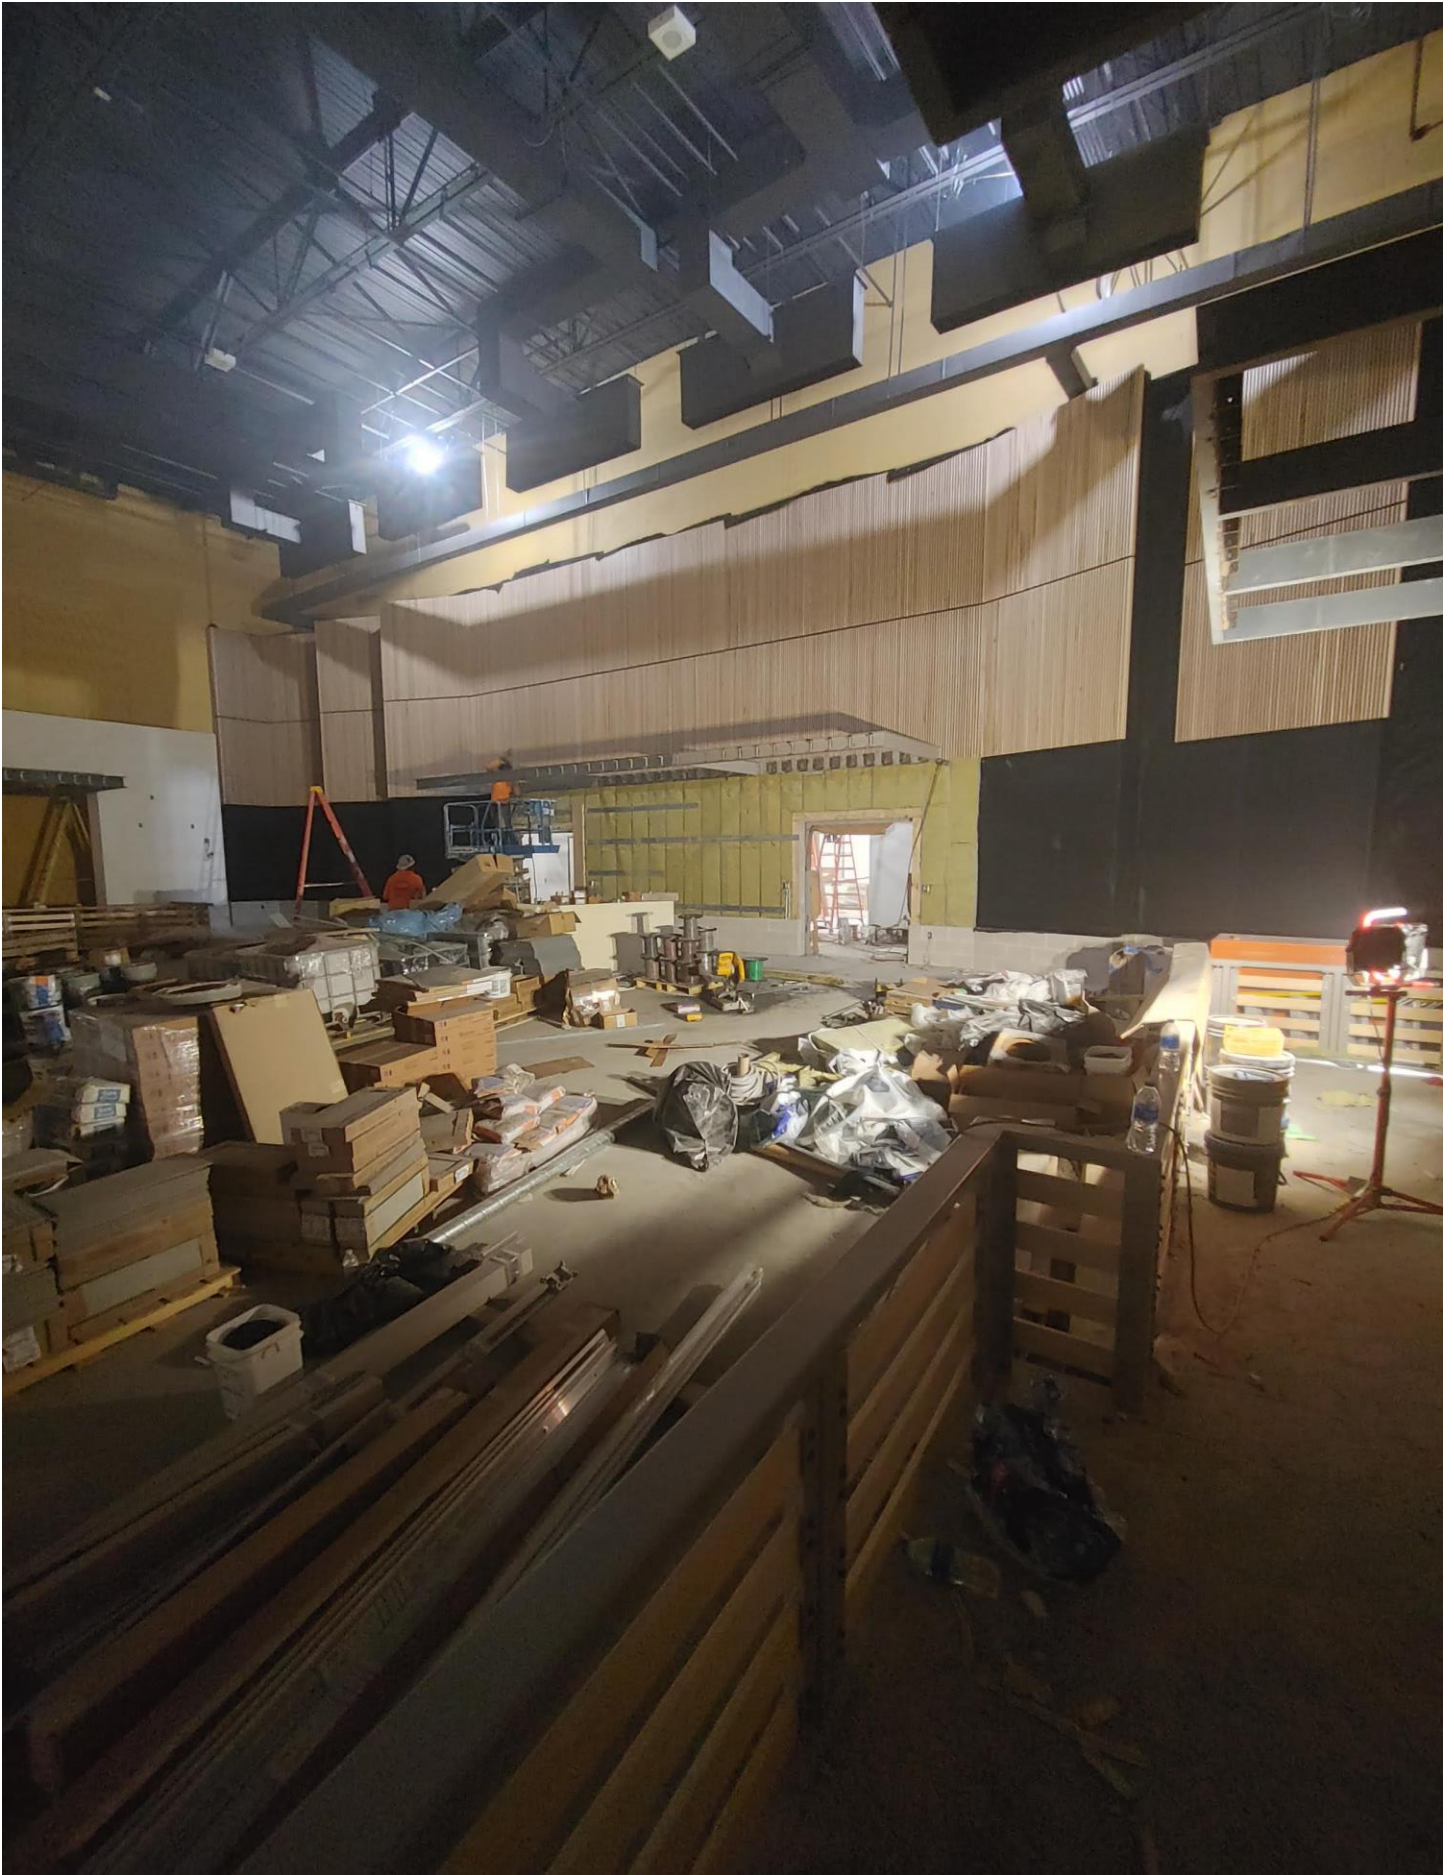


Photo 1 – Auditorium Panelized Linear Wood Wall System



Photo 2 - Kitchen



Photo 3 - Kitchen Dry Storage



Photo 4 - Dishwasher Area



Photo 5 - Kitchen Serving Line



Photo 6 - Antenna Wire (Equipment scheduled to arrive in early June. Wire to be curled up in ceiling until equipment arrives).



Photo 7 - Diamonds in Bathrooms. Brach says their Sub will fill Diamonds and skim coat entire floor so everything matches.



Photo 8 - Floors are being cleaned and waxed.



Photo 9 - Area B - 2nd floor

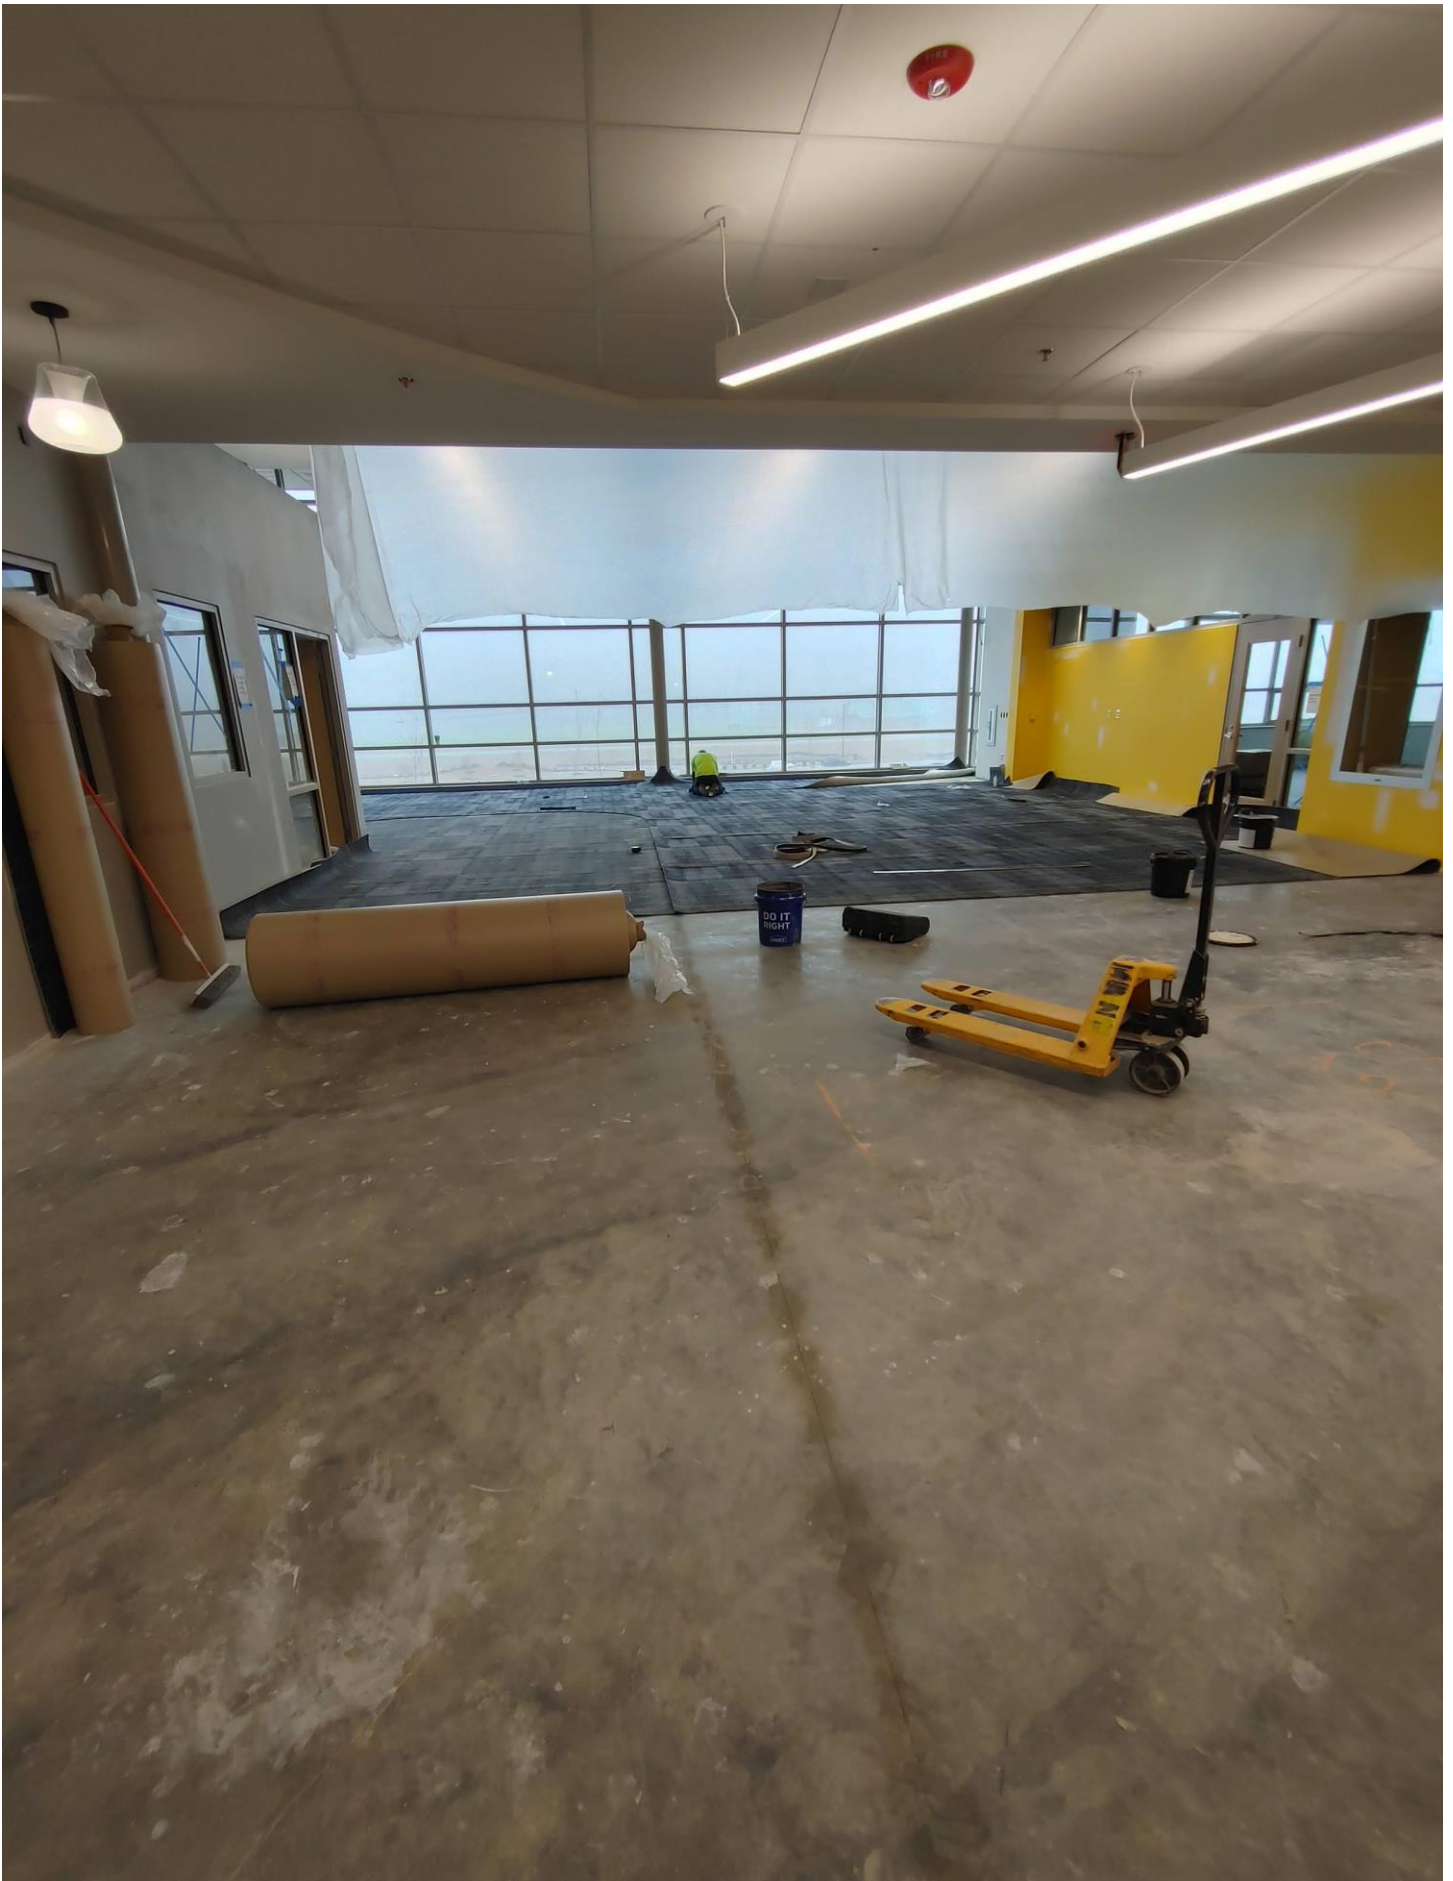


Photo 10 - Carpet is being installed in Area A - 2nd floor.



Photo 11 - Area A - 2nd Floor

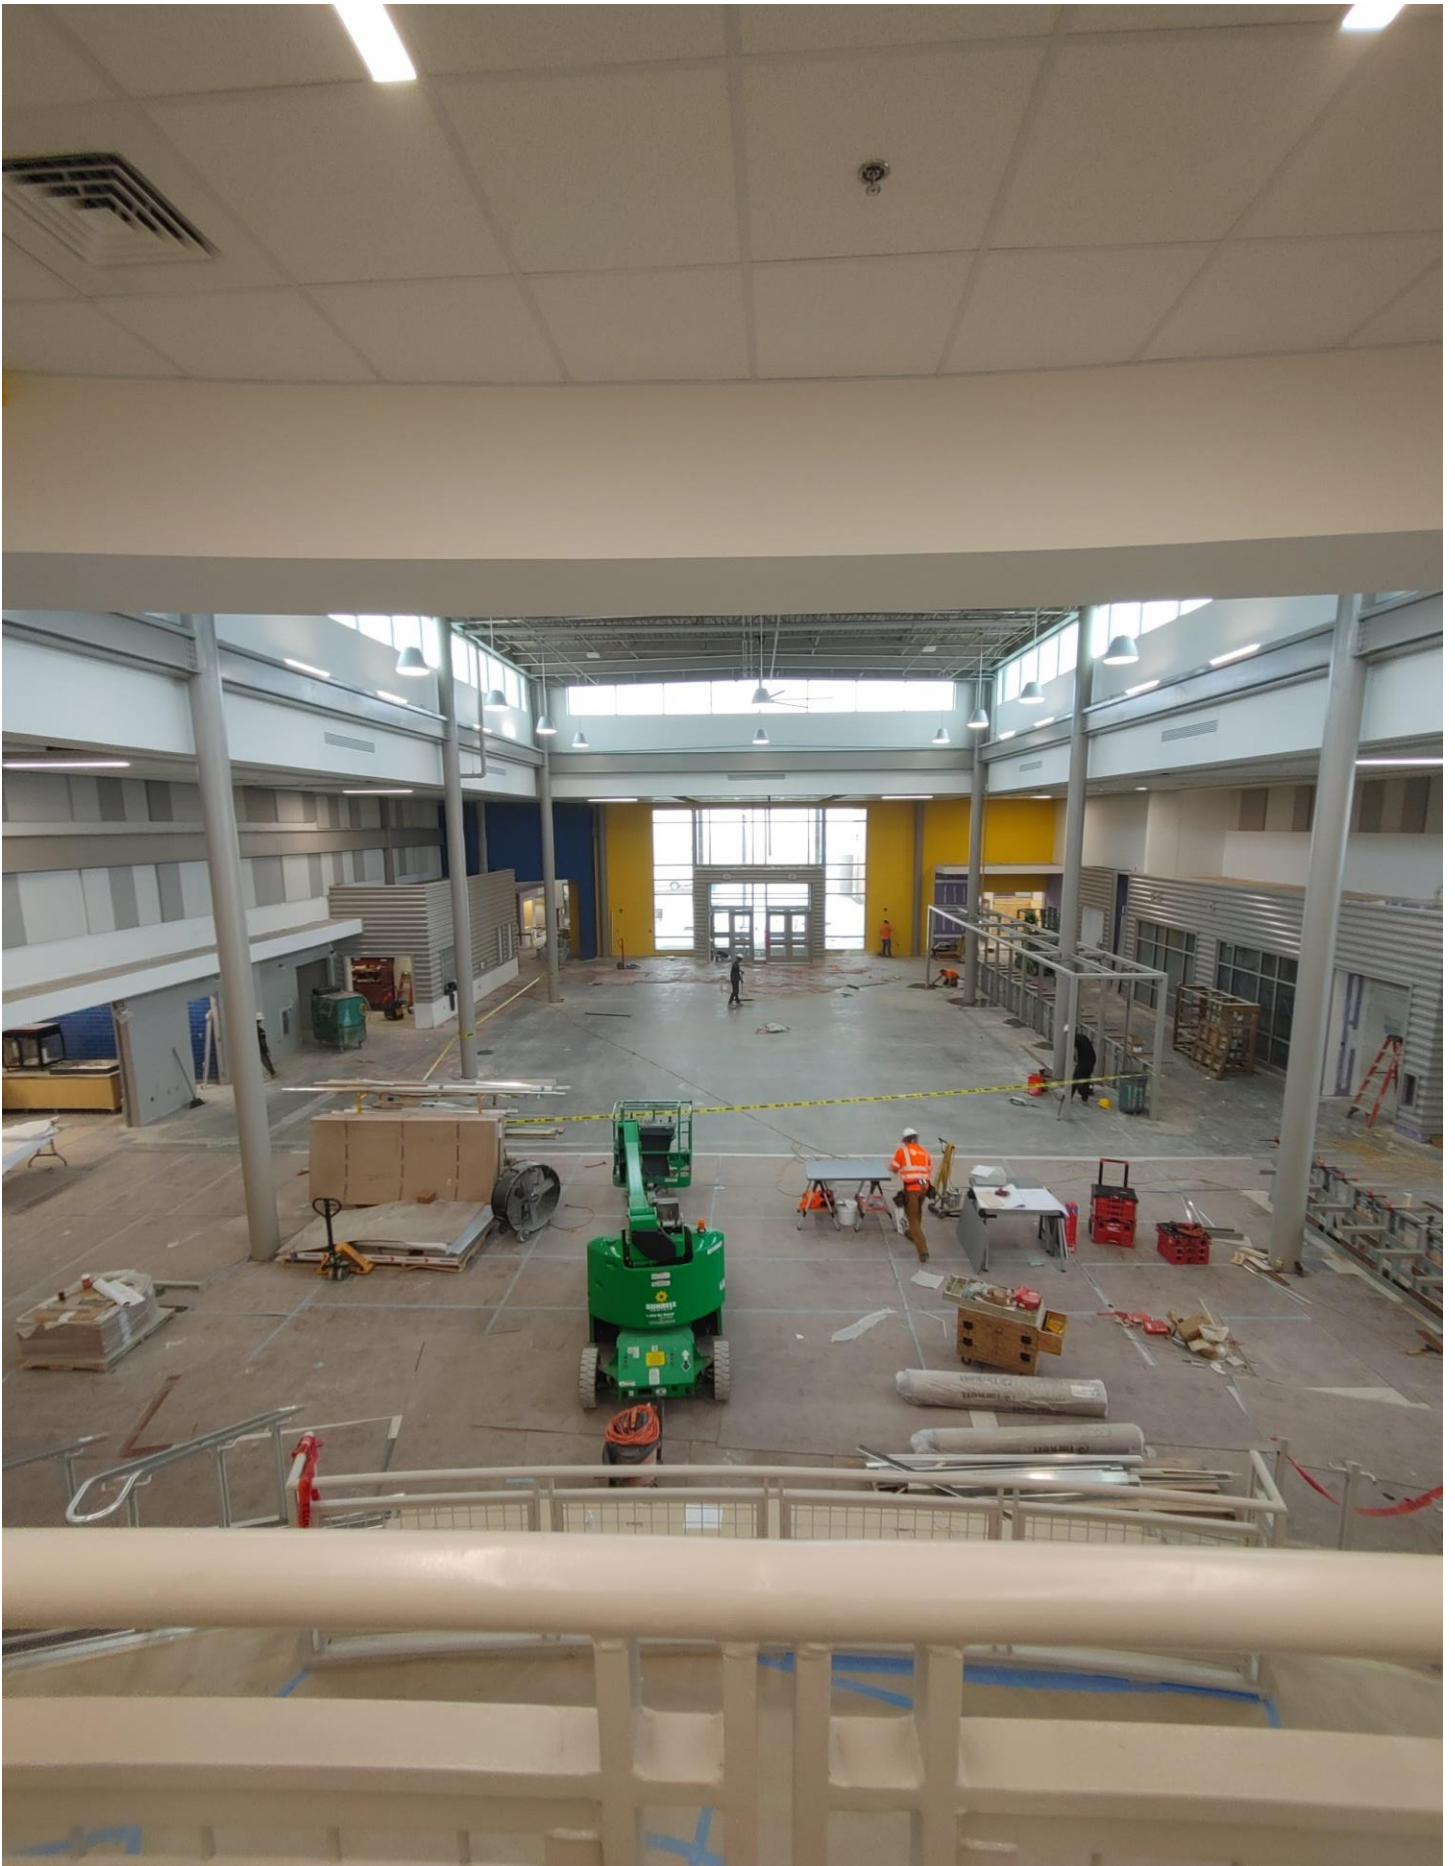


Photo 12 - Area C



Photo 13 - East side of site



Photo 14 - Front of site

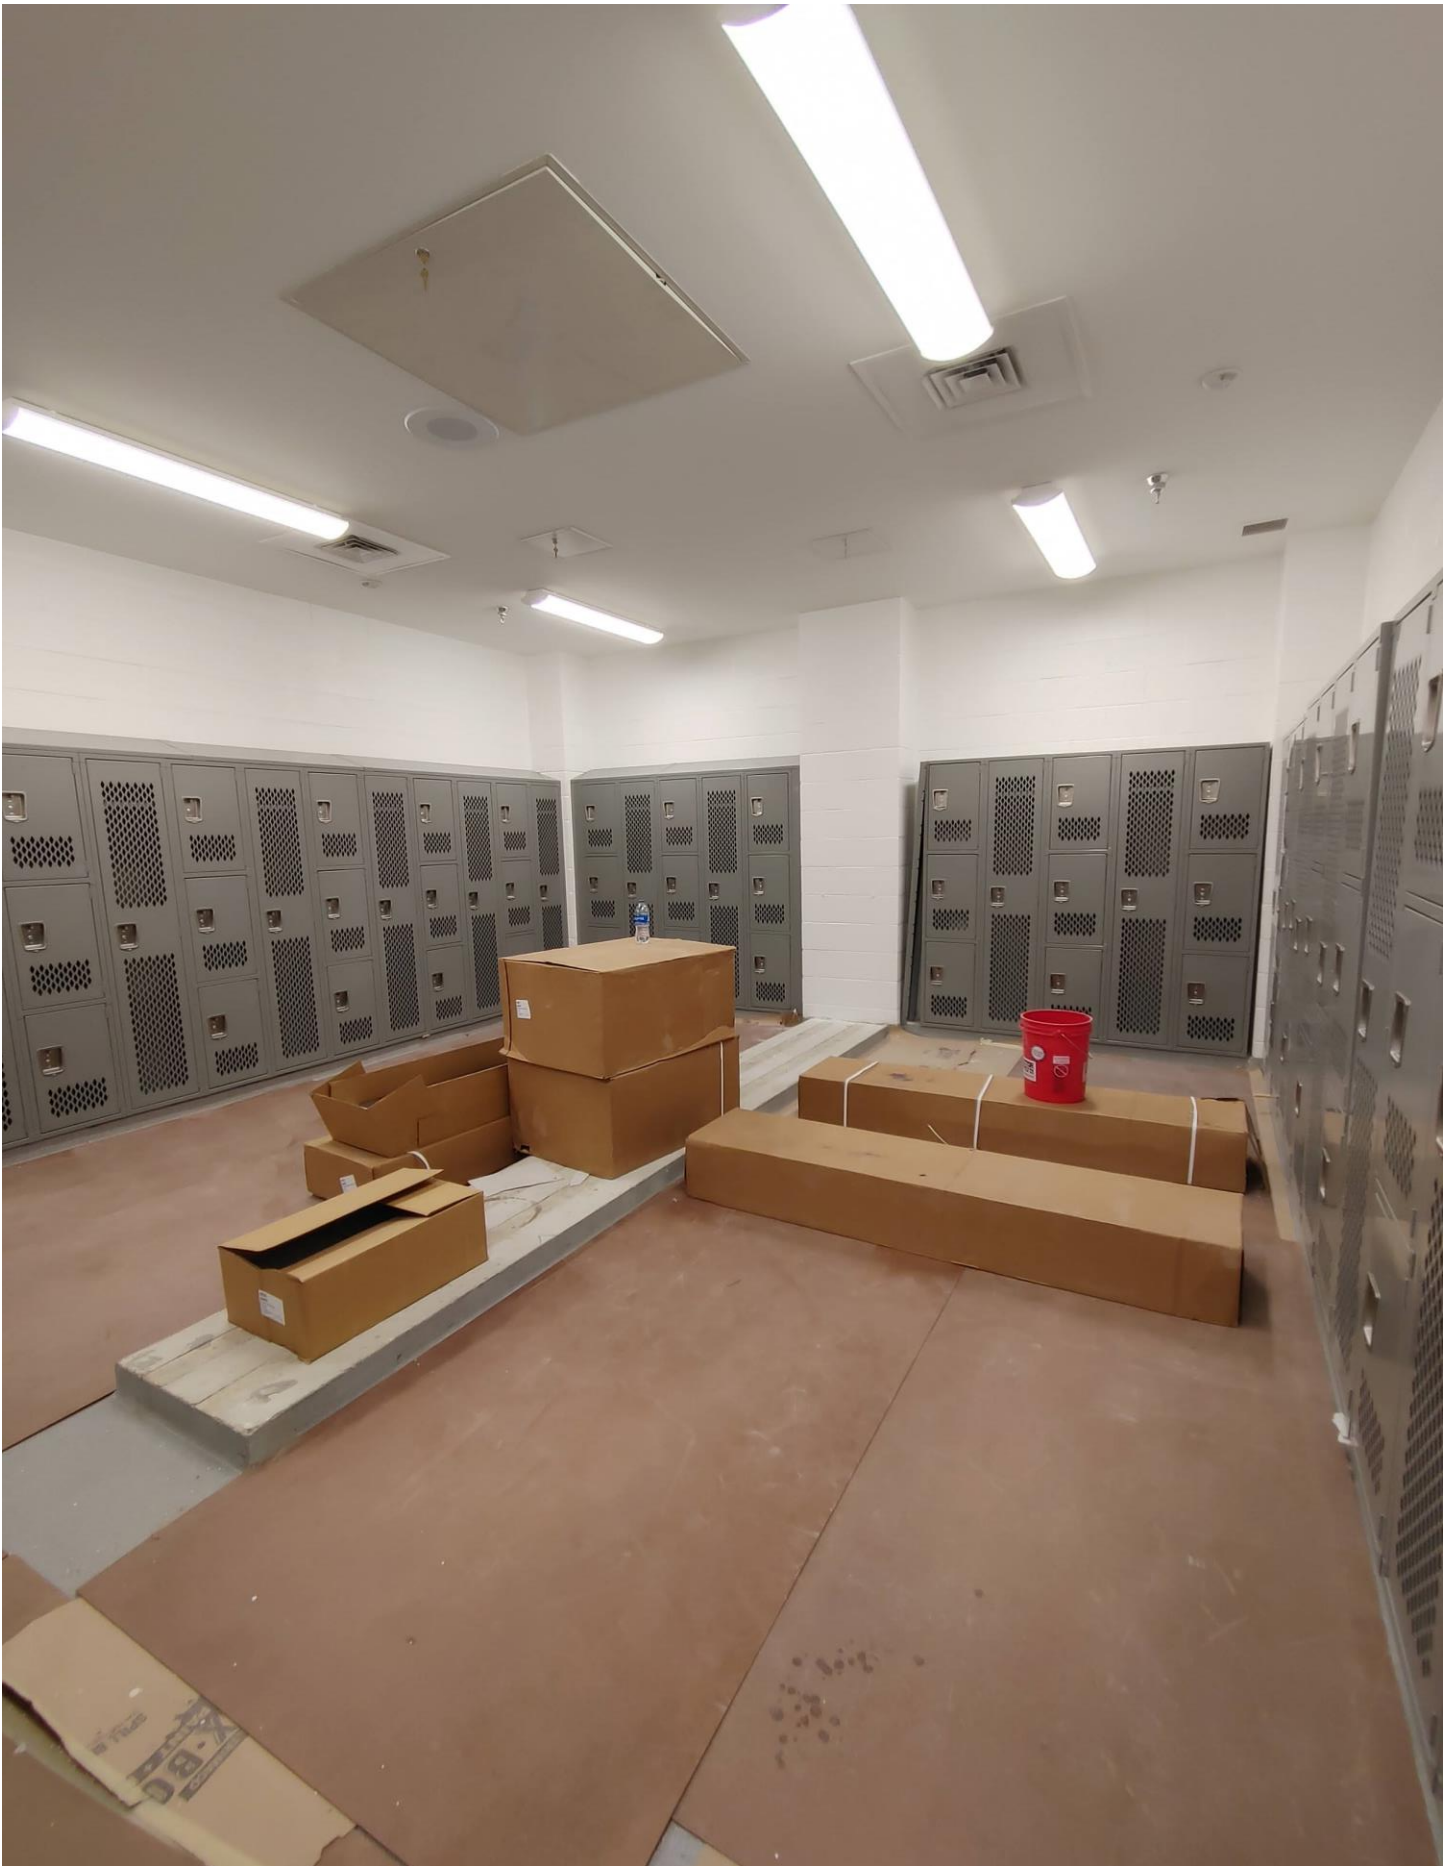


Photo 15 - Locker are being installed

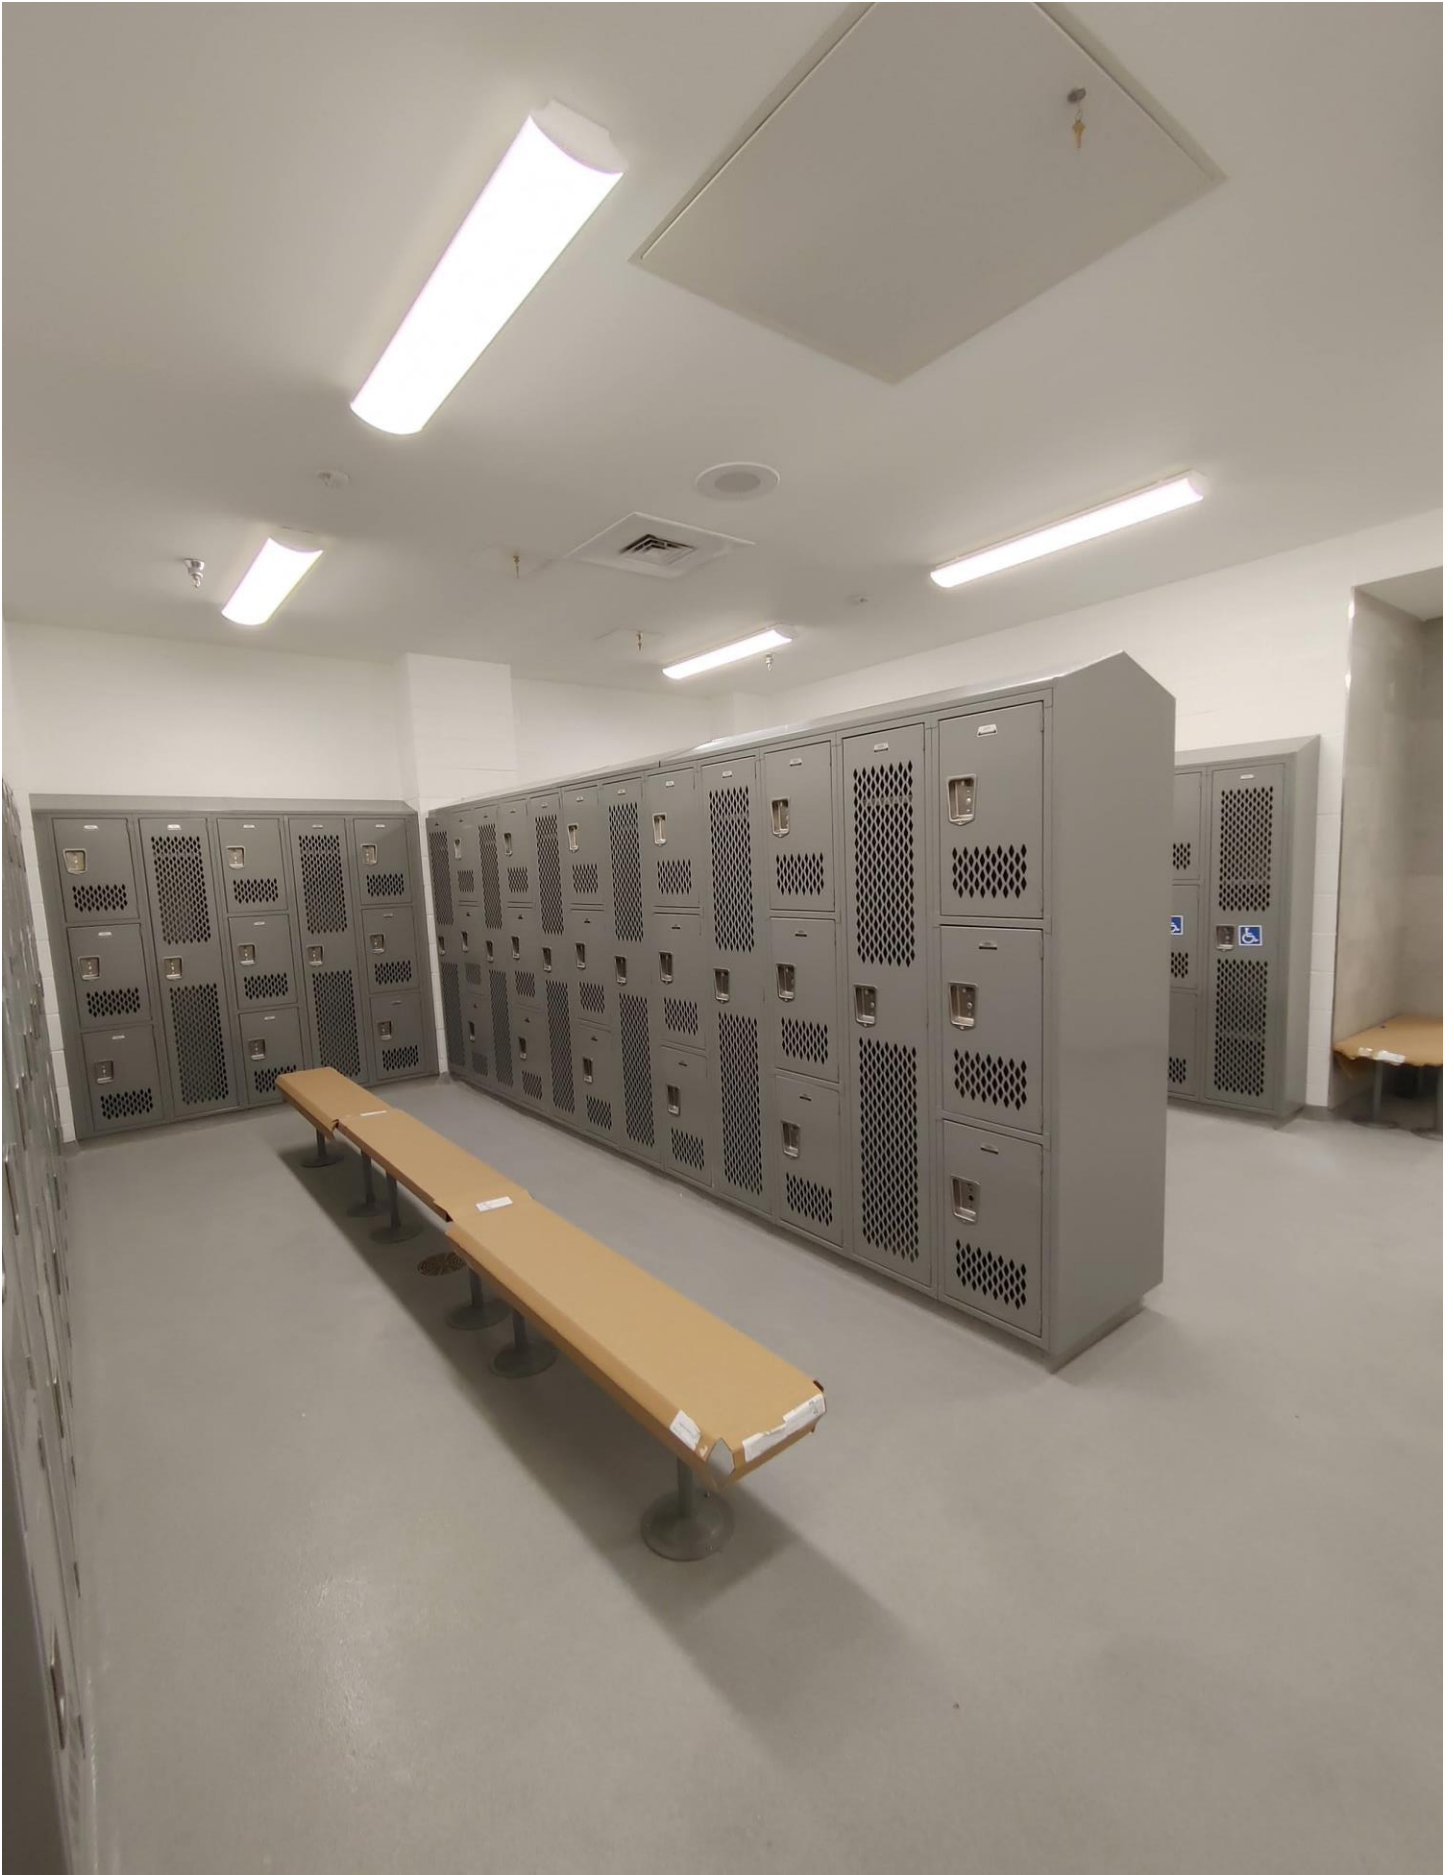


Photo 16 – Lockers and benches installed



Photo 17 - Locker and Benches have been installed
