



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/09/2021

Weather: 74 degrees at 12:00hrs. Mostly Cloudy. High 68 degrees today.

Hours Worked: 12:00hrs – 14:30hrs (2.5hrs) Site Visit.

I walked the site and observed the work being performed.

Beuchert Excavation: Four (4) men on site today. They continue to work on the Eastside of the site reshaping the Retention ponds along County Park Drive.

Industrial Concrete: Four (4) men are on site today. They are pouring concrete in the diamonds around columns and preparing other diamonds to be poured in Area C.

J.D. Long, Masons: Twenty-seven (27) men are on site. A crew is laying brick on the Northside of Area A and also on the Northside of Area E. A crew is breaking down scaffolding on the low roof of Area D and a crew is laying block in Room D 131.

Hazzard Electric: Eleven (11) men are on site today. They continue to work in Area A & B & D running conduit.

Colonial Webb: Five men (5) men are on site today. A crew is running sanitary pipe in Area B and another crew is preparing to set the Grease Trap outside of Area D.

Weldon Steel: No men are on site today.

JP Construction: Fourteen (14) men are on site today. They continue to erect interior walls in Area A, 2nd floor and they are also hanging sheet rock on the 1st floor of Area A.

AAR Roofing: Four (4) men are on site today. They are working on the roof of Area B.

Tailored Foam: No men are on site today.

FG & M: Two (2) men are on site. They continue to work on the large Storefront on the eastside of Area A. I observed them leave the site at 13:00hrs.

United Sprinkler: Two (2) men are on site today running Sprinkler pipe on the 2nd floor of Area B. I observed them leave the site at approximately 13:30hrs.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: I met with Brian, Cooper and Jake upon arriving on site. We spoke about what was going on today and the plans for next week. Brian left the site after our meeting at approximately 12:30hrs. I asked Cooper if he knew when Beuchert was going to have the Hydro-seed crew back out on site and he did not know. My concern, as previously expressed is the area along the Rec Park Rod that has been disturbed that is part of Westmoreland County's DEQ Permit. The County will be held responsible for something they have not done.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was yesterday on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report – 04/09/2021

Weekly RFI Status Update – 04/09/2021

Weekly Daily Log Summary – 04/09/2021



Photo 1 - Brick being laid on the Northside of Area A



Photo 2 - Masons are breaking down Scaffolding on the low roof of Area A



Photo 3 - HVAC Units set on the roof of Area A



Photo 4 - Sheetrock being hung in Area A

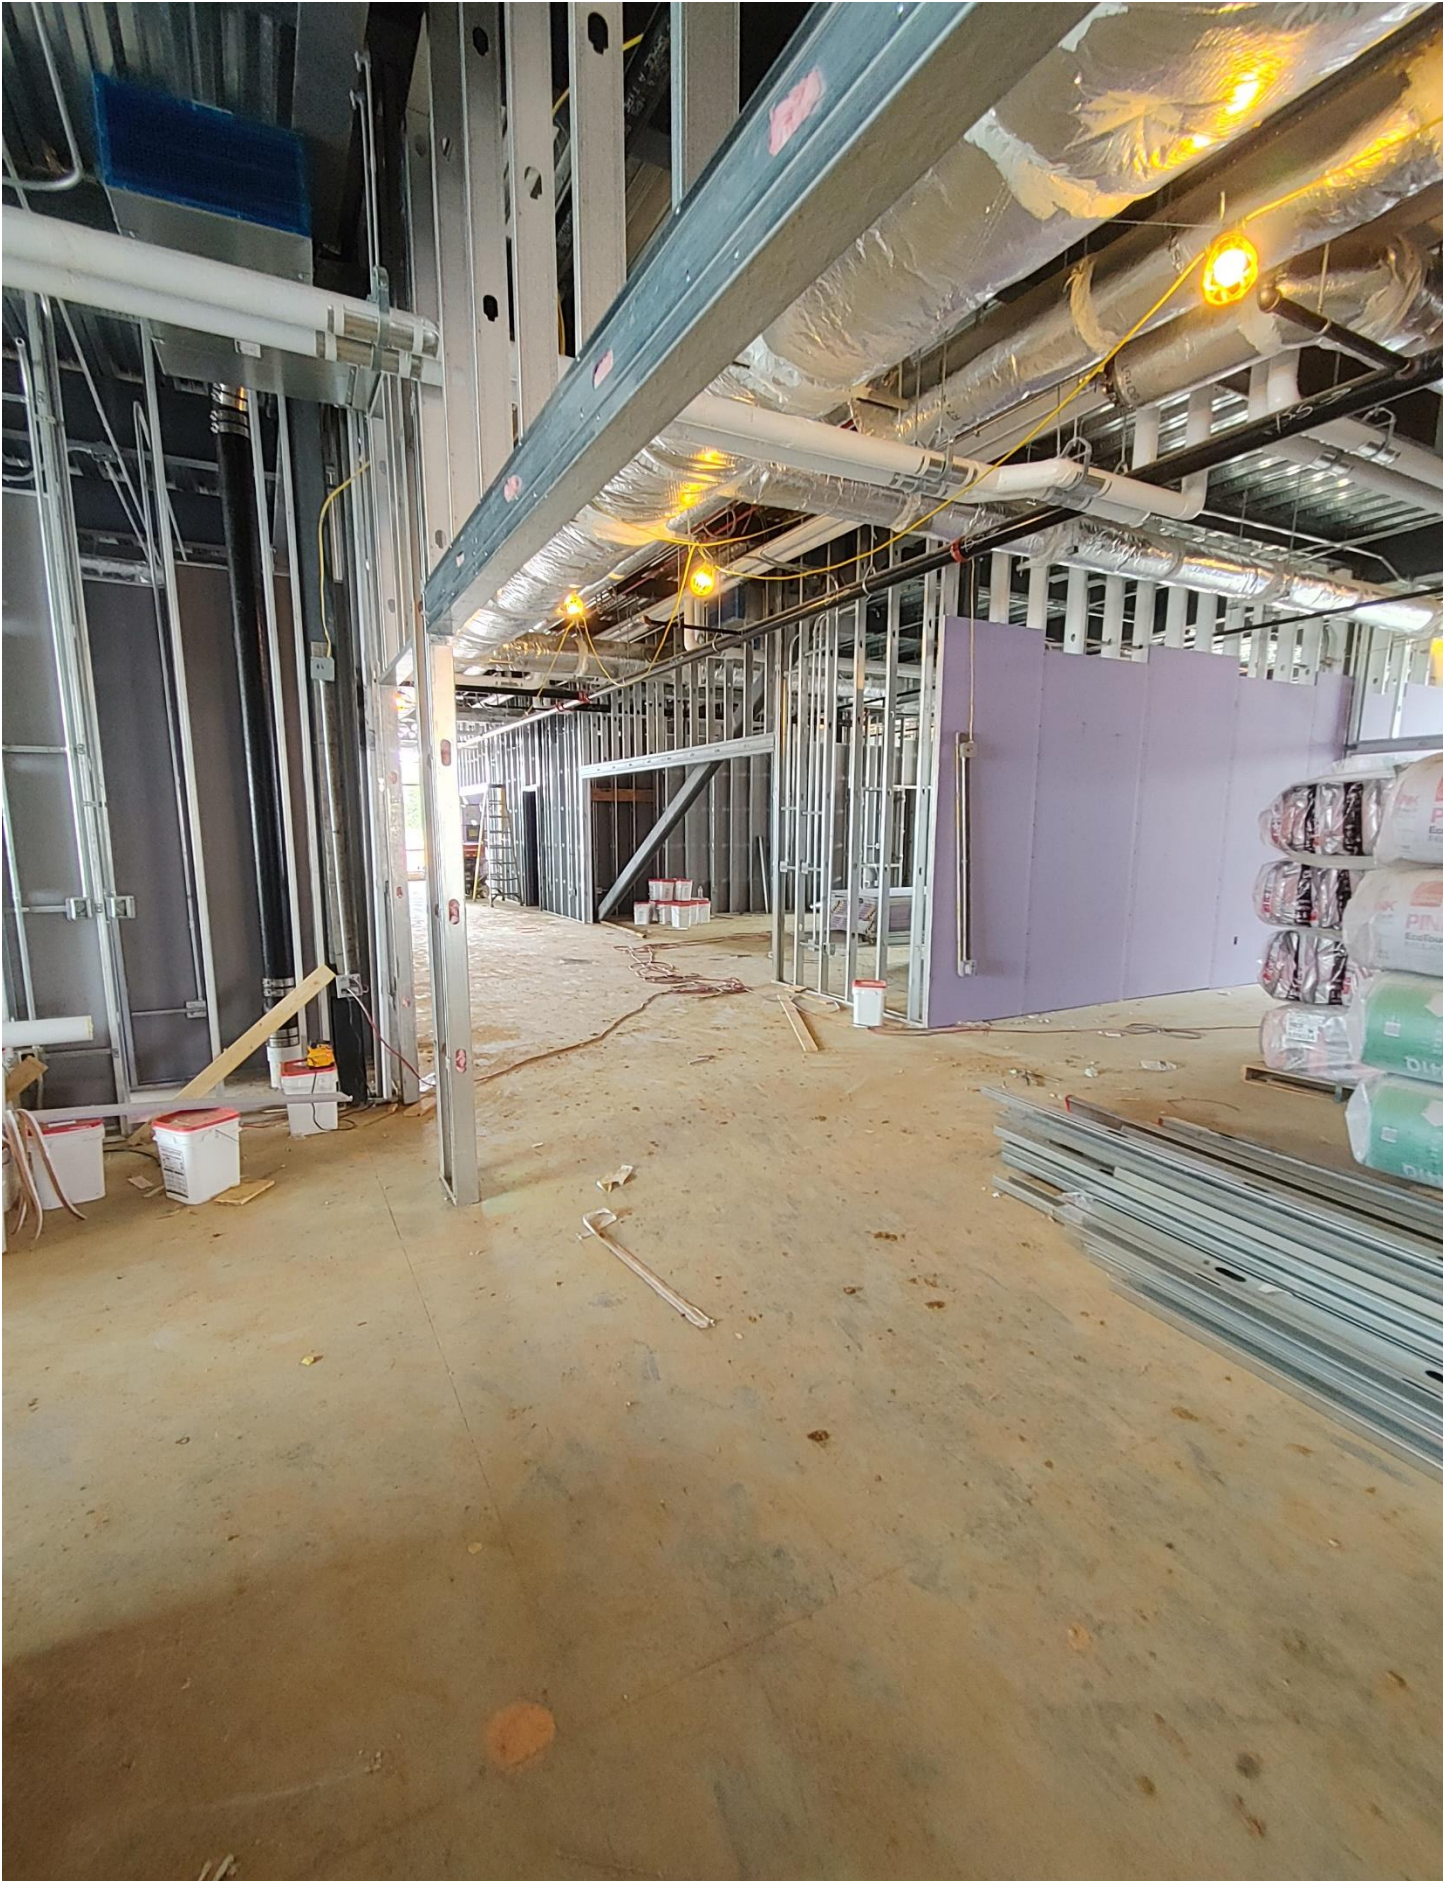


Photo 5 - Sheetrock is being hung throughout the 1st floor of Area A



Photo 6 - Diamonds be poured and finished in Area C



Photo 7 - Block being grouted on the Southside of Area C



Photo 8 - Walls are being framed on the 2nd floor of Area A



Photo 9 - Masons are laying Brick on the Northside of Area E



Photo 10 - Roofers continue to work on the Rook of Area B



Photo 11 - Colonial is preparing to set the Grease Trap (in the back ground) into the pit on the Northside of Area D.
