



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 04/12/2021

Weather: 64 degrees at 10:00hrs. Mostly Sunny. High 69 degrees today.

Hours Worked: 10:00hrs – 13:00hrs (3hrs) Site Visit.

I received an Easement request from Dominion Power that I forwarded to Dr. Perry so that the School Board can give Dominion an easement to run their cable from the Transformer on School Property to Rec Park Road so that it can then be taken back to the Ball Fields.

I walked the site and observed the work being performed.

**Beuchert Excavation:** Six (6) men on site today. They continue to work on the Eastside of the site reshaping the Retention ponds along County Park Drive.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Twenty-seven (27) men are on site. Crews continue to lay brick on the Northside of Area A and also on the Northside of Area E. A crew is also breaking down scaffolding in Area D.

**Hazzard Electric:** Eleven (11) men are on site today. They continue to work in Area A & B & D running conduit.

**Colonial Webb:** Five men (5) men are on site today. A crew is running sanitary pipe in Area B and another crew is working on the Grease Trap that was set on Friday outside of Area D.

**Weldon Steel:** Six (6) men are on site today. They continue to set and weld steel in Area C.

**JP Construction:** Fourteen (14) men are on site today. They continue to erect interior walls in Area A, 2<sup>nd</sup> floor and hang sheet rock on the 1<sup>st</sup> floor of Area A.

**AAR Roofing:** Four (4) men are on site today. They are working on the roof of Area B.

**Tailored Foam:** Two (2) men are on site today but I did not observe where they are working.

**FG & M:** Two (2) men are on site. They continue to work on the large Storefront on the eastside of Area A.

**United Sprinkler:** One (1) man are on site today running Sprinkler pipe on the 2<sup>nd</sup> floor of Area B.

**S&S Concrete Cutting Company:** I did not observe anyone on site during my visit today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** I did not observe anyone on site during my visit.

**Questions to or from Branch Builds:** Brian Topper is off today. I met with Cooper in the Trailer this morning and we discussed what was happening on site today. I told Cooper that I had met earlier with Beuchert's Superintendent this morning to determine if he was going to seed the area between to two entrances to the School from County Park Road. DEQ requires it to be seeded within seven days after work has been completed. Beuchert's Superintendent said he didn't know when he was going to get it seeded. After some discussion, we agreed that I would seed the area and he would apply strawing matting to the area so that it can be stabilized.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** Last Inspection was yesterday on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) – 04/08/2021**
- Submittals –**
- RFIs –**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**



Photo 1 – Flashing being installed on the Northside of Area A



Photo 2 - Adhesive being applied prior to the second part of the flashing is installed on the Northside of Area A



Photo 3 - Fredericksburg Mirror and Glass working on the Storefront on the Eastside of Area A



Photo 4 - Brick continues to be laid on the Eastside of Area A



Photo 5 - Grease Trap has been set



*Photo 6 - Colonial Webb is setting Vent hoods and preparing to set rooftop units.*





Photo 7 - Roofer continue to work on the roof of Area A

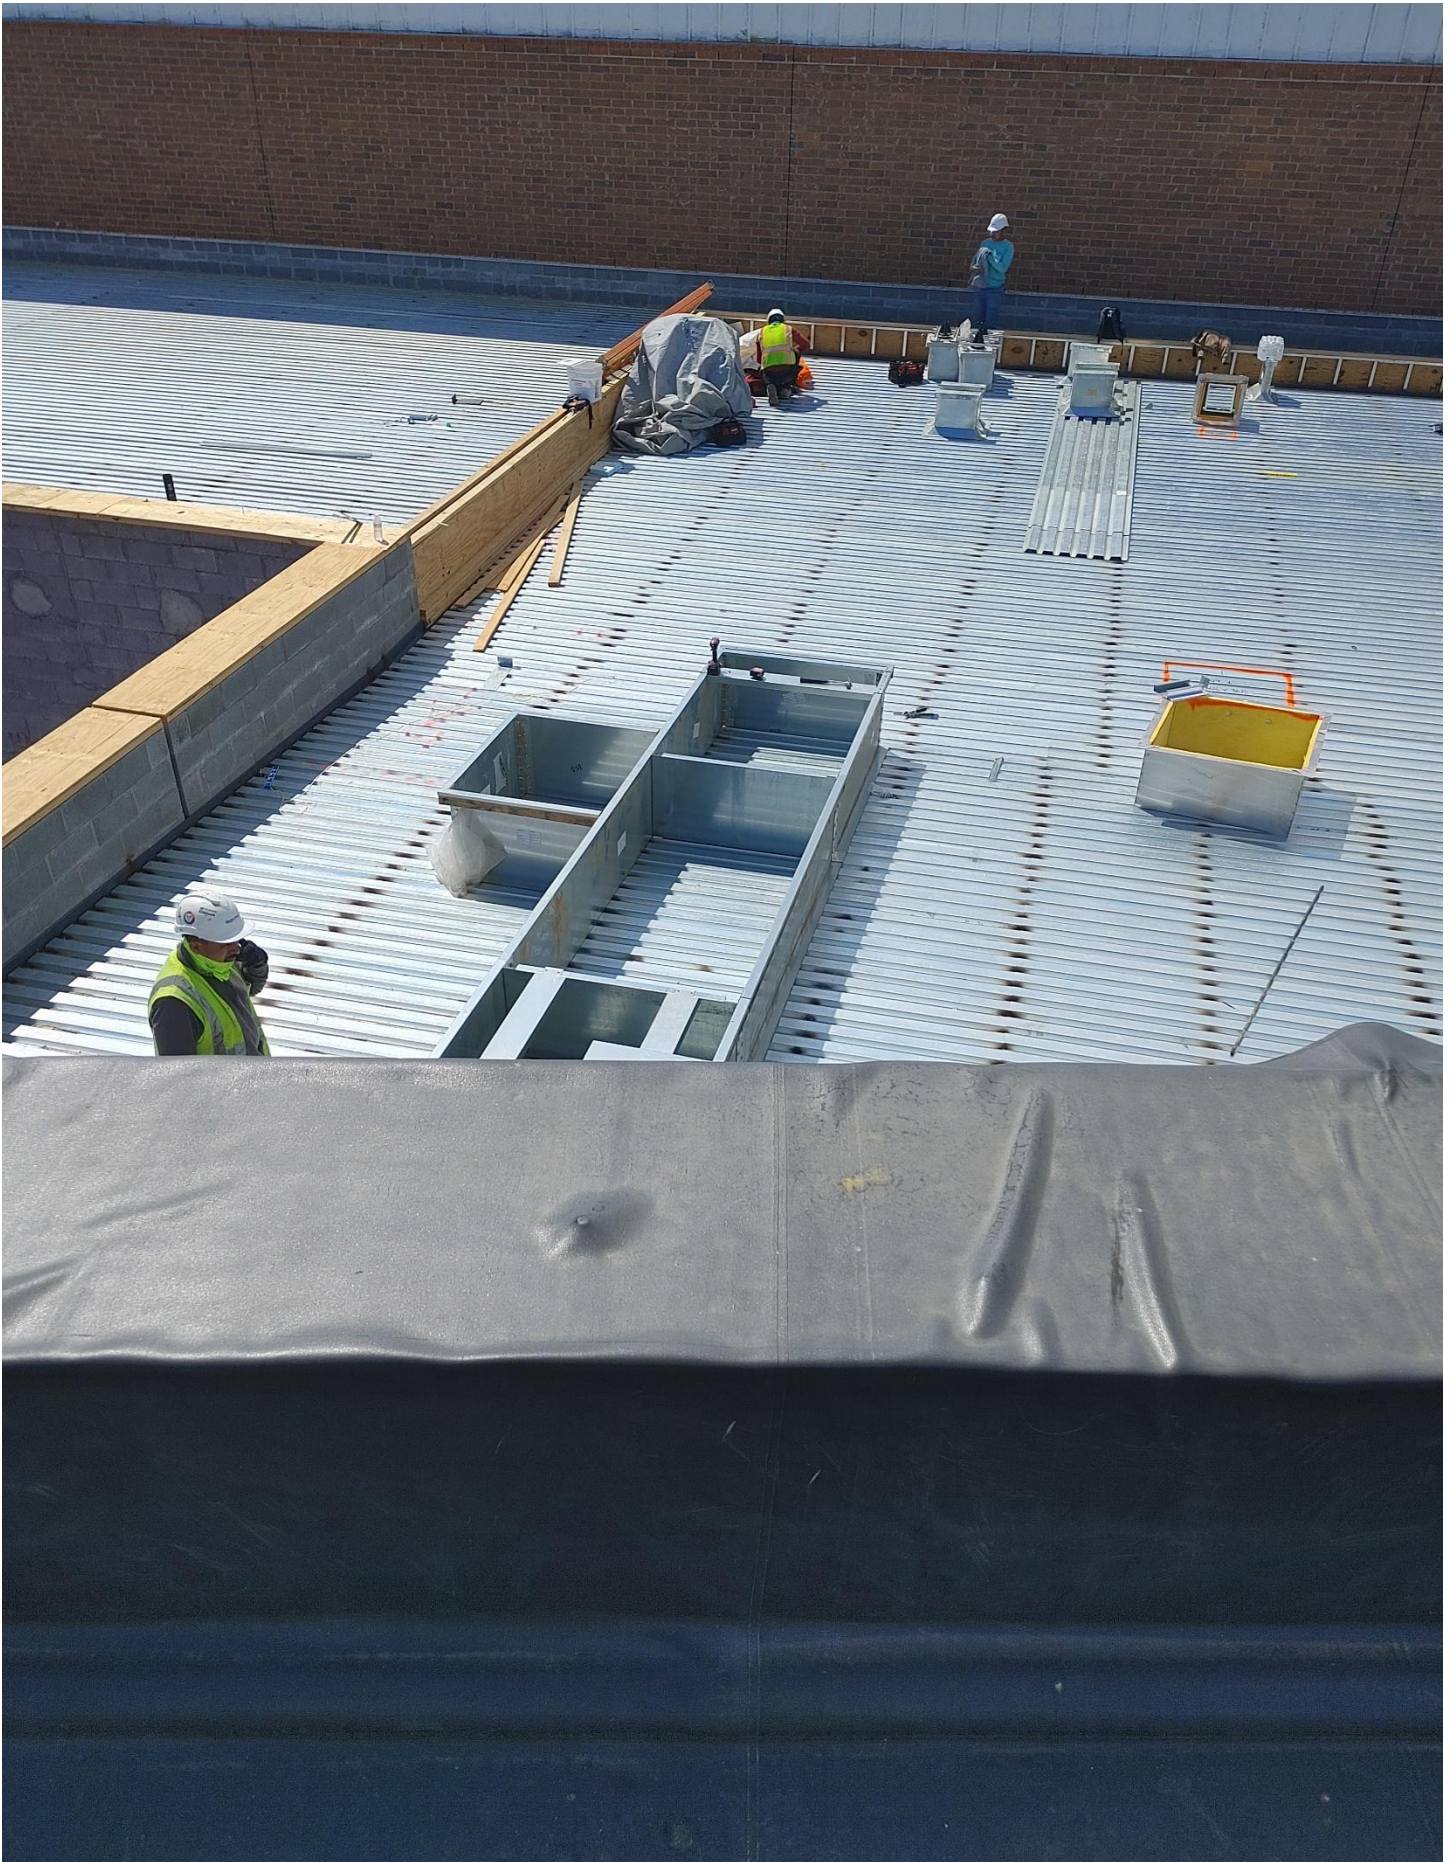


Photo 8 - Colonial Webb working on the low roof of Area D preparing to make penetrations for rooftop units



Photo 9 - Hi-Abuse Fire Shield Rock is being hung on the 1st floor of Area A



Photo 10 - Brick continues to be laid on the Northside of Area E
