



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/21/2022
Weather: 62 degrees - High of 70 degrees today. Sunny
Hours Worked: 10:00 – 13:30hrs (3.5hrs) – Site Visit & Meeting

Walked the site. Met with Chandler and Cooper. We discussed the need for dedicated telephone lines for the Elevator and Fire Alarm System. I had given Chandler Chris Evans phone number earlier this week and Chandler said that Chris is working on the matter. Two lines will be need for the Fire Alarm system and at a minimum one line for the Elevator. Chris is also working on the clocks that the Owner is supposed to supply and the Contractor is to install. Chris said the clocks are to ship at the end of this month and arrive at during the first week of May.

I also met with Todd, Lee, Chandler and Cooper and we walked out to the Farmer's Road to inspect and evaluate what is happening and what can be done to alleviate problems in the future. Buechert was not on site for the meeting. However, Beuchert had recommended a cost effective solution and Todd will put that recommendation forward hopefully tomorrow. Basically the recommendation is to remove the unsuitable soil to a solid base and add #3 stone and possibly follow up with some 21 or 57 stone and open up the area that has been blocked by the property owner with discarded concrete. Pictures below. They are also going to install the stone spreader at the outlet pipe and stabilize the soil in the areas to the left and right of the outlet pipe.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports – 4/20/2022**
- Hillis-Carnes Bio Retention Pond Reports –**
- Submittals -**

RFIs – #424

Patrick Byrne –

Alexes Lee –

Tara Delaney –

Change Order/PCOs/Pay App – PCO #92

Weekly Submittal Status Report – 4/15/2022

Weekly RFI Status Update – 04/15/2022

Weekly Daily Log Summary – 04/15/2022

PCO Log – 04/15/2022



Photo 1 - Farmers Road taken on 4/19/2022



Photo 2 - Super Silt Fence Failed - Taken 4/19/2022

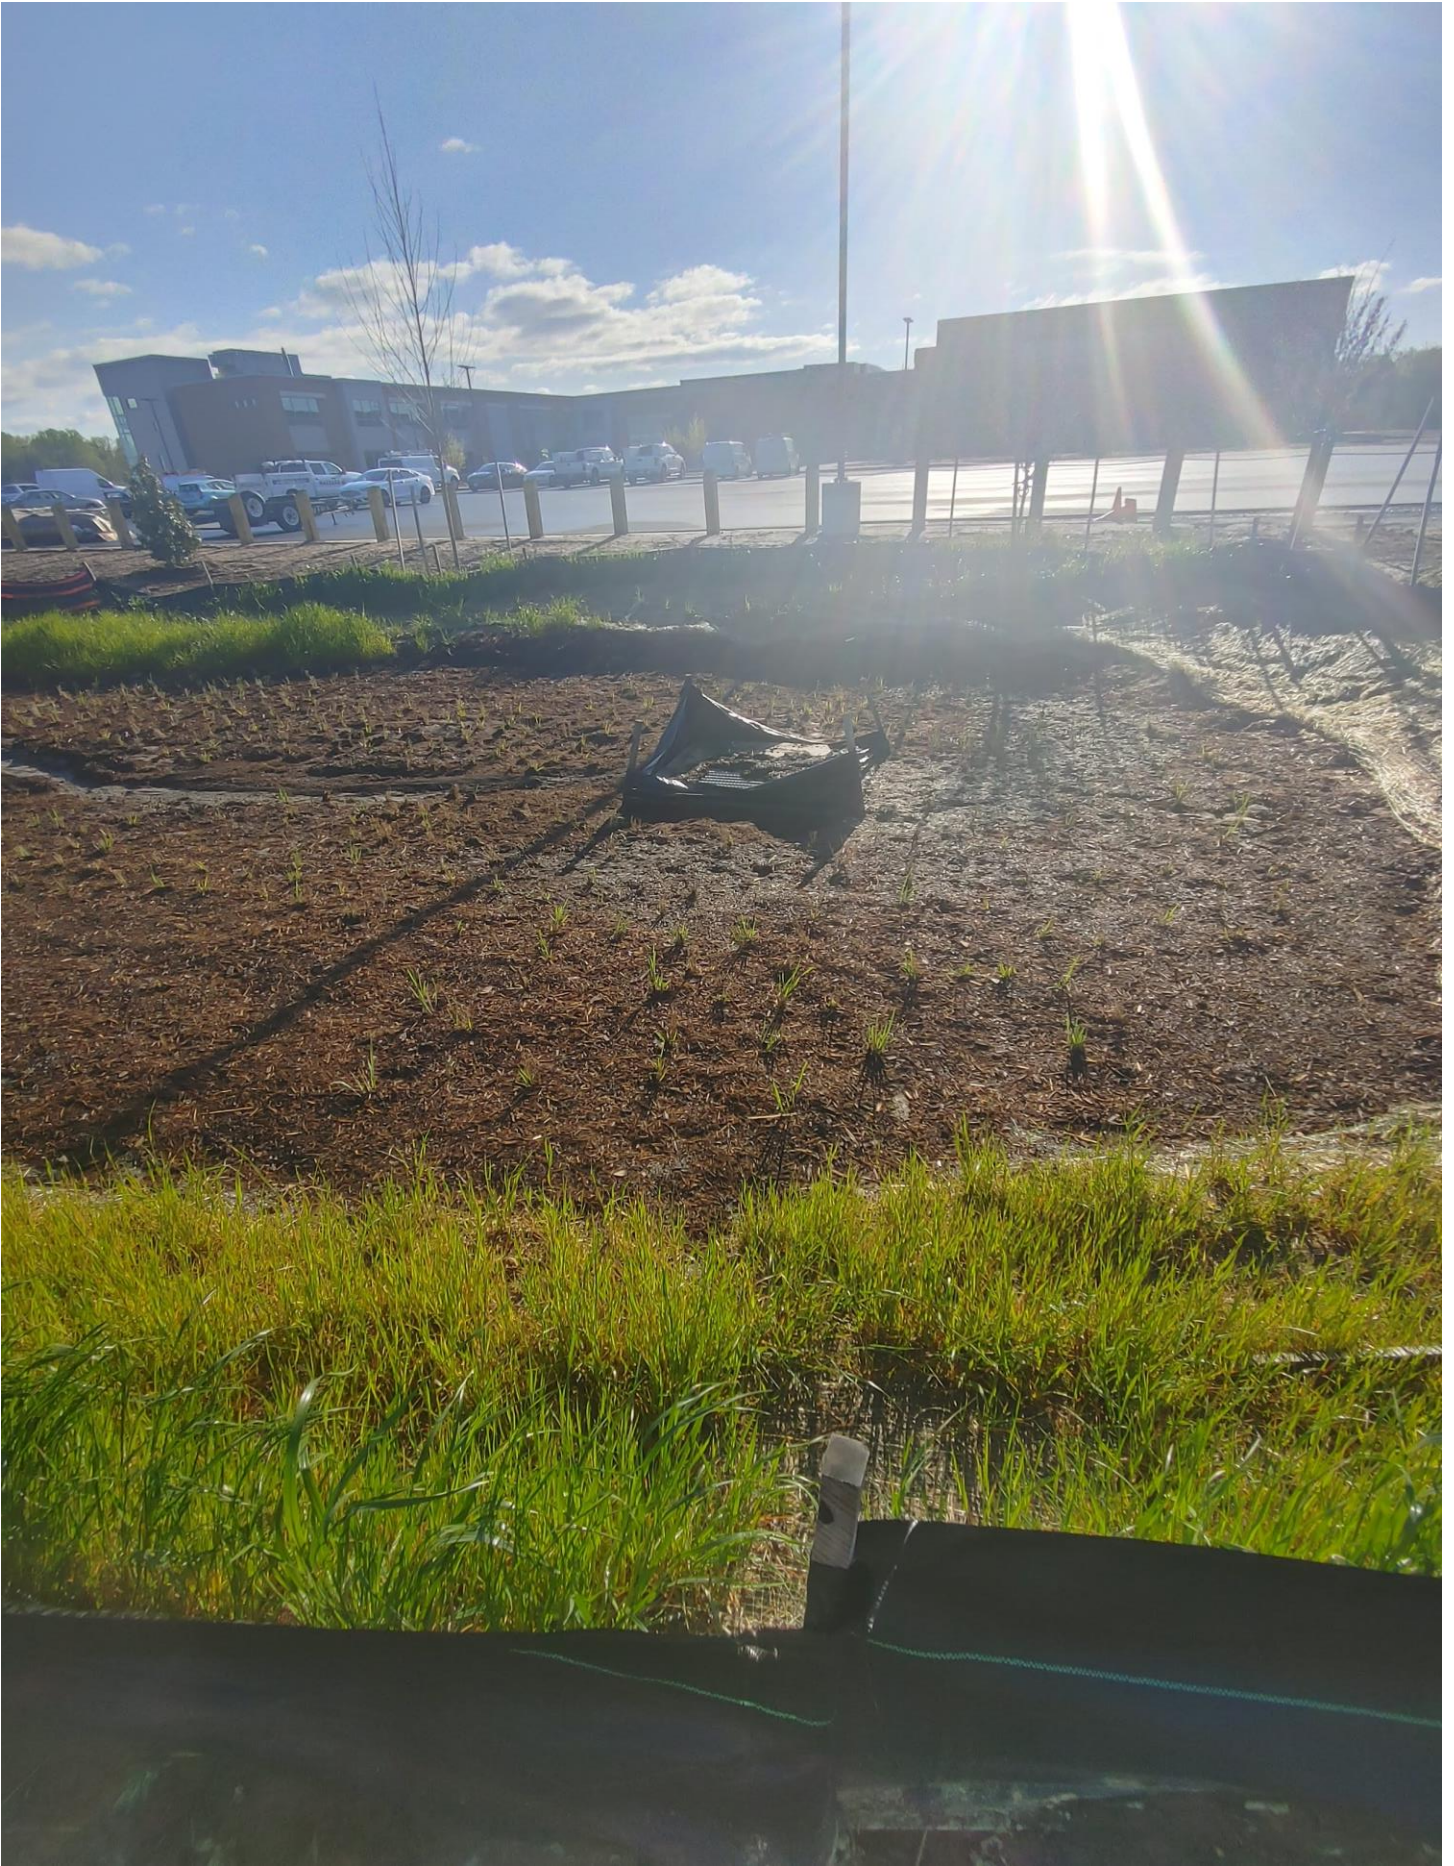


Photo 3 - Inlet Protection Failed - taken 4/19/2022



Photo 4 - Taken 4/19/2022 - Inlet Protection Failed.



Photo 5 - Wood Slats are being installed in the Student Commons Area - Area C

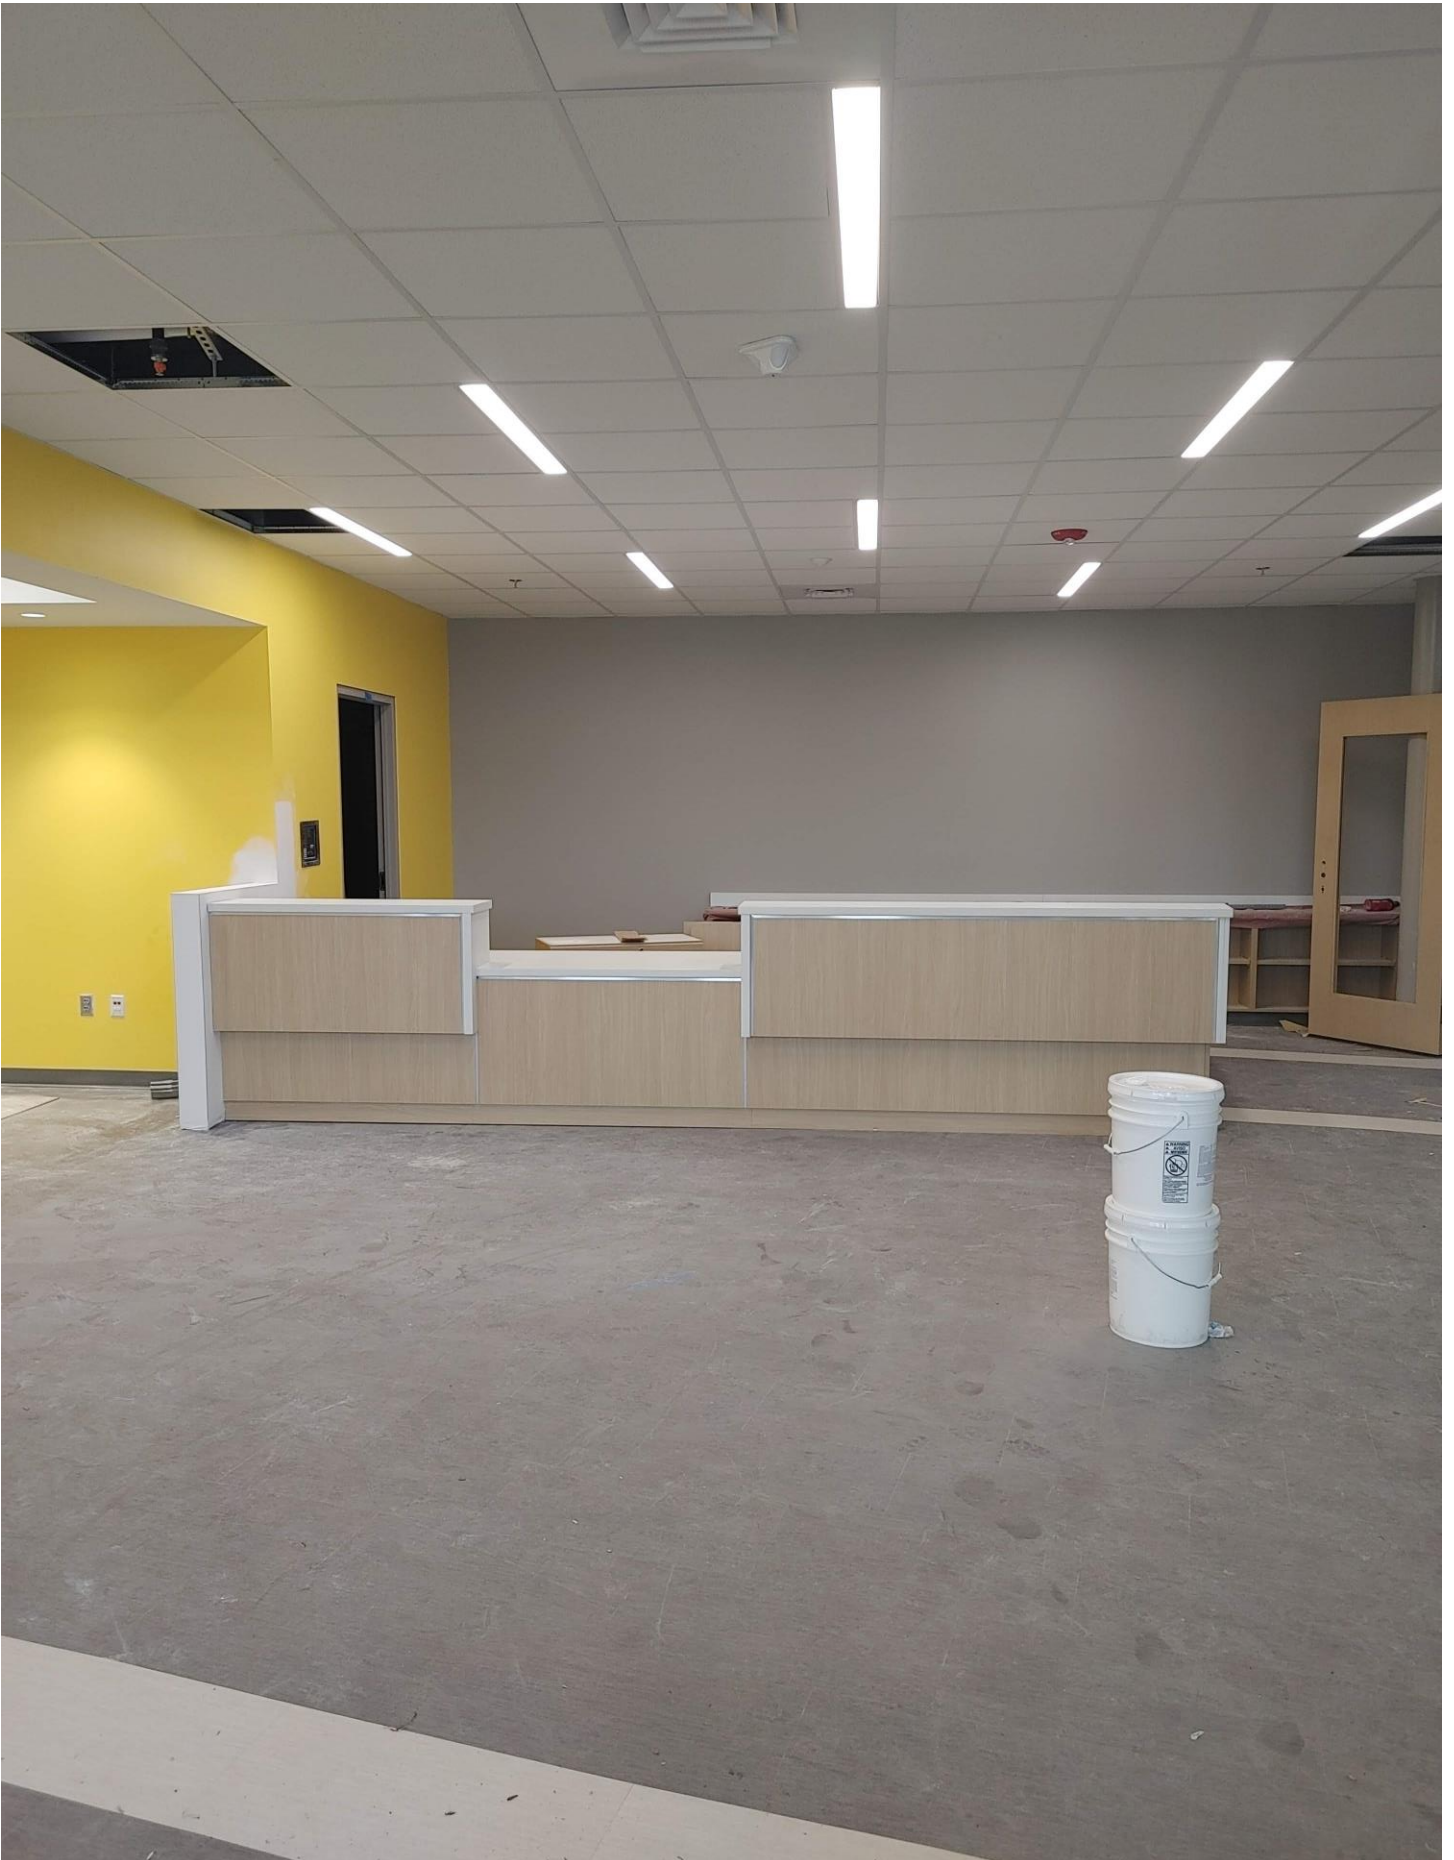


Photo 6 - Work Station and Counter Tops have been installed at the Administrative Reception Area in Area A



Photo 7 - Curtain Wall Glass is being installed in Area C



Photo 8 - Concrete blocking Spillway on Farmers Property



Photo 9 - Concrete is piled up in Spillway of Farmer's Property



Photo 10 - Another view of the concrete that is piled up.



Photo 11 - Concrete is cracked on Student Entranceway from Bus Loop.



Photo 12 - Sub Floor has been laid in the Stage Area of the Auditorium.



Photo 13 - Asphalt continues to be laid in the front of the School.
