



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 04/27/2022
Weather: 57 degrees - High of 63 degrees today. Sunny
Hours Worked: 12:00 – 15:00hrs (3hrs) – Site Visit & Progress Meeting (13:30 – 14:45)

I walked the site to observe what is and has transpired since my last visit. A crew continues to work on the Decorative wood slats in Area C – Student Commons area (picture below). The Sprinkler guy is on site and continues to wrap up small details with his system. The electrician are on site pulling wire, setting lights, and wiring devices. I also observed a cleaning crew cleaning the Administrative Area in Area A.

I met with Chandler, Lee and Cooper. Lee advised that Branch was finished with the Back Flow Meter Device that they borrowed from Westmoreland County and therefore turned it over to me to deliver to the County. I gave the device to Ronnie Saunders, Maintenance Supervisor for Westmoreland County. We also discussed the grass that has begun to sprout up throughout the site and the Furniture that was delivered and stored in various locations in Areas A, B and E.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report -
Hillis-Carnes Grout Inspection/Compression Strength Test –
Hillis-Carnes Field Reports – 04/21/2022, 04/22/2022
Hillis-Carnes Bio Retention Pond Reports –
Submittals -
RFIs – #410, #414, #421, #423, #425, #426
Patrick Byrne –
Alexes Lee –
Tara Delaney –
Change Order/PCOs/Pay App – PCO 094, CO# 17&18

Weekly Submittal Status Report – 4/22/2022

Weekly RFI Status Update – 04/22/2022

Weekly Daily Log Summary – 04/22/2022

PCO Log – 04/22/2022



Photo 1 - Decorative Wood wall is being constructed in Area C

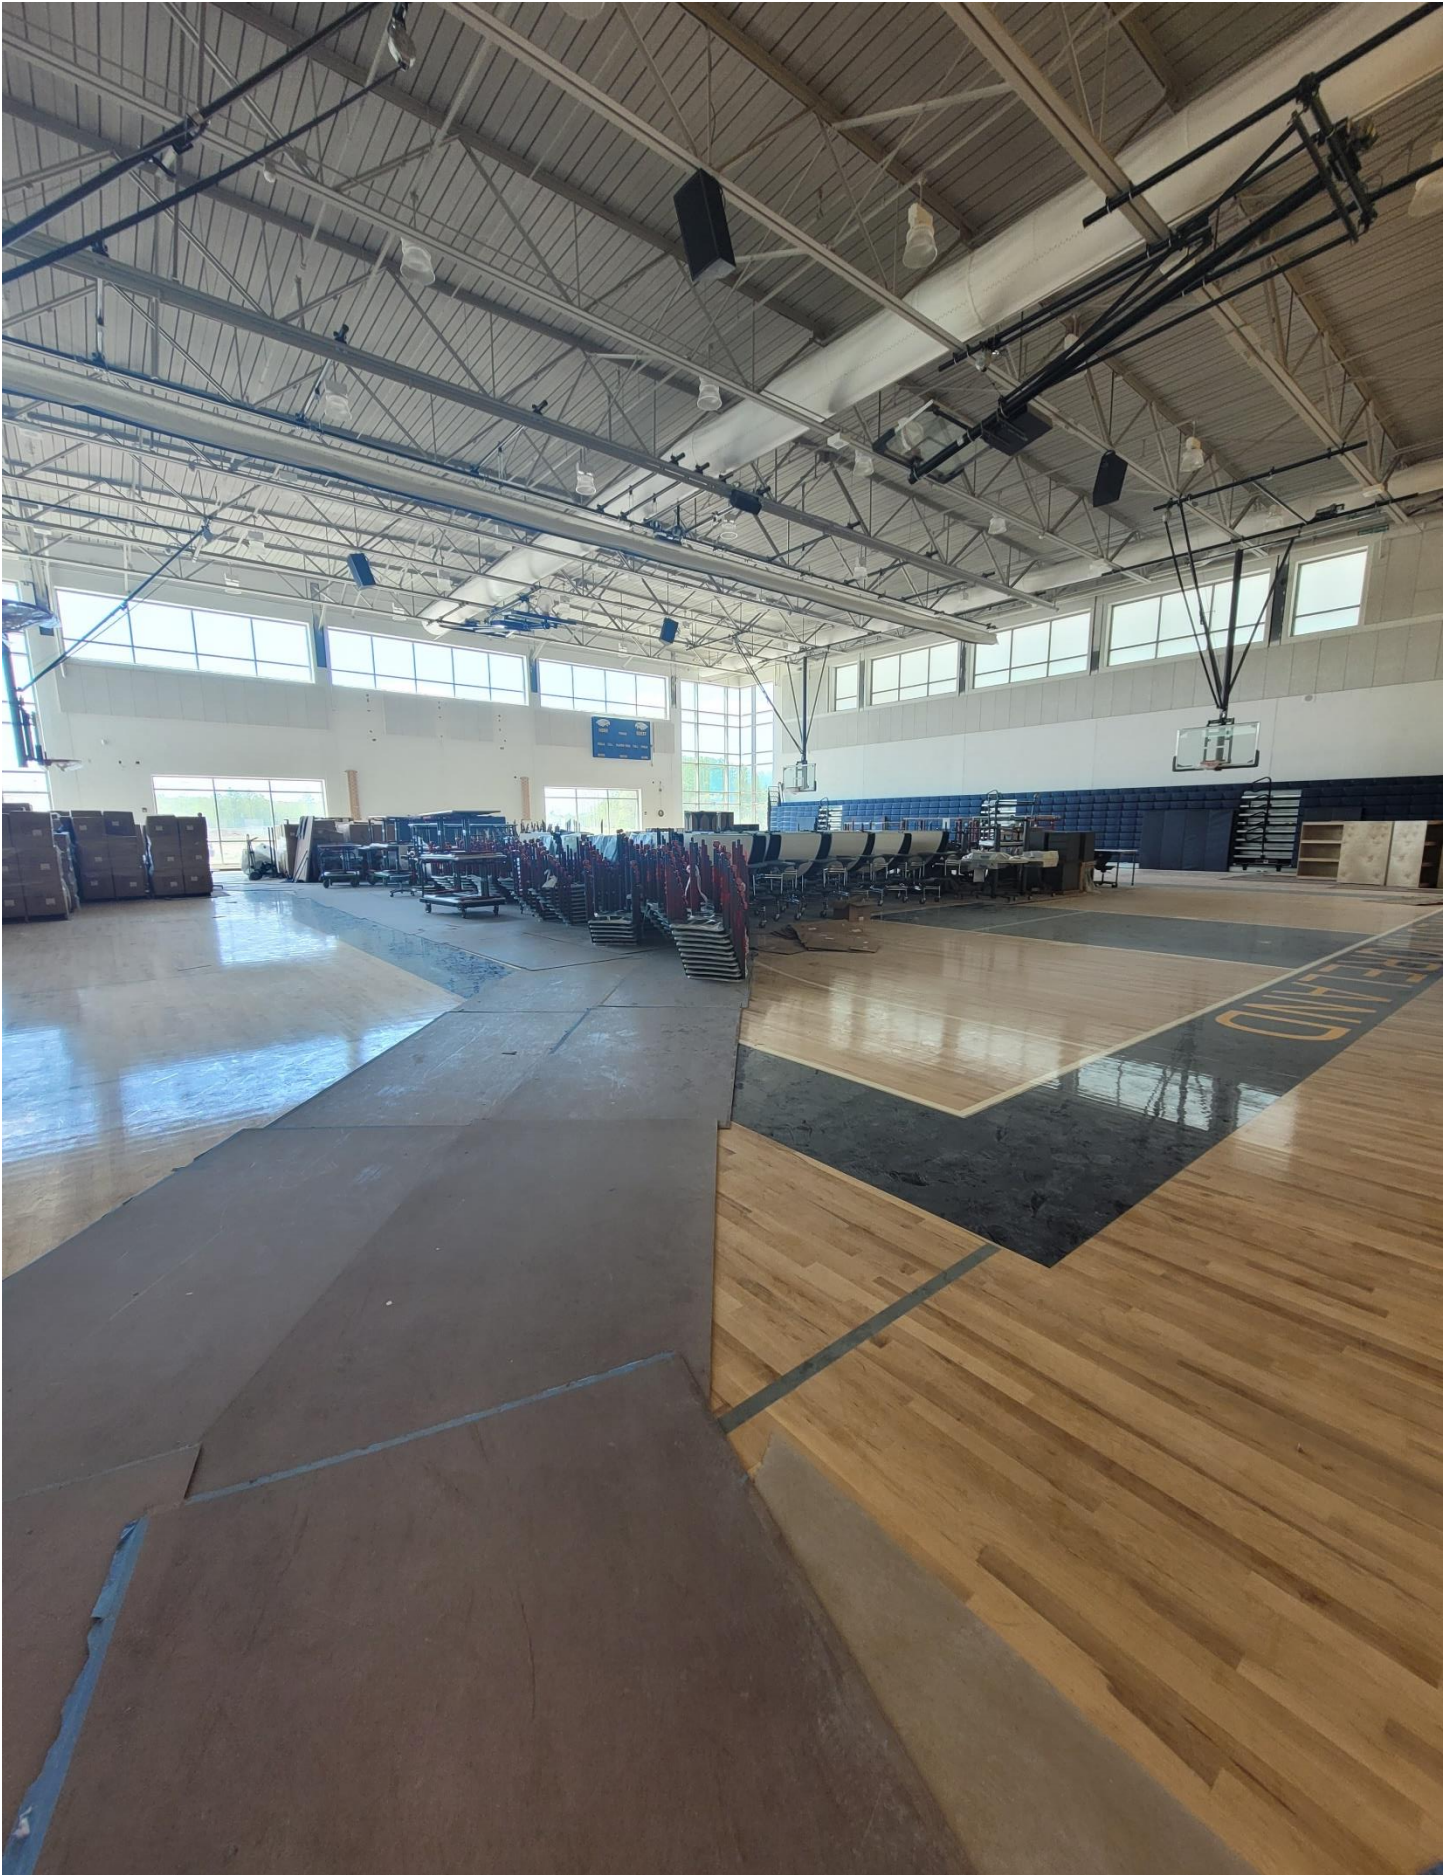


Photo 2 - Furniture is being stored in the Gym



Photo 3 - Entrance to Auditorium



Photo 4 - Acoustical Ceiling is being installed outside of the Auditorium



Photo 5 - Side wall lighting has been installed in Auditorium



Photo 6 - Furniture stored in Area A



Photo 7 - B106 - Area B



Photo 8 - B110 - Area B



Photo 9 - Furniture is being stored in the Learning Labs of Area A & B, 1st floor



Photo 10 - Furniture is being stored in Area B



Photo 11 - Grass is starting to come up in Various areas
