



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 05/12/2022
Weather: 63 degrees - High of 66 degrees today. Light Rain
Hours Worked: 10:00 – 13:00hrs (3hrs)

Upon arriving on Site I ran into the Hillis-Carnes Tech who was there to perform a Structural Steel Inspection in Area D. He advised that they were not ready for him to Inspect and advised them what needed to occur prior to him coming back and also what he wanted to see when the Anchor Bolts were epoxied in place.

I walked the site to observe what is and has transpired since my last visit. A crew continues to work on the Decorative wood slats in Area C – Student Commons area (picture below). The electrician are on site pulling wire, setting lights, and wiring devices. Flooring crew is on site laying tile in Area D.

I met with Chandler and we discussed the damaged furniture. Chandler said that the Company noted the damaged furniture when it was delivered and that replacements had been ordered. He said no meeting was necessary since the damage had been recorded.

I received a phone call from Dr. Perry and he asked me to attend a meeting that was being set up with the adjacent property owner, Mr. Chandler to discuss the repair of his road. I reached out to Todd and asked him to let me know when that meeting was going to occur so that I could attend.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report -
Hillis-Carnes Grout Inspection/Compression Strength Test –
Hillis-Carnes Field Reports –
Hillis-Carnes Bio Retention Pond Reports –
Submittals - #26 32 13-3.0

RFIs – #425, #428

Patrick Byrne –

Alexes Lee –

Tara Delaney –

Change Order/PCOs/Pay App – April Pay App, Change Order #17 & #18

Weekly Submittal Status Report – 04/29/2022, 05/06/2022

Weekly RFI Status Update – 04/29/2022, 05/06/2022

Weekly Daily Log Summary – 04/29/2022, 05/06/2022

PCO Log – 04/29/2022, 05/06/2022



Photo 1 - Kitchen Overhead Roll Up Security Grills have been installed.

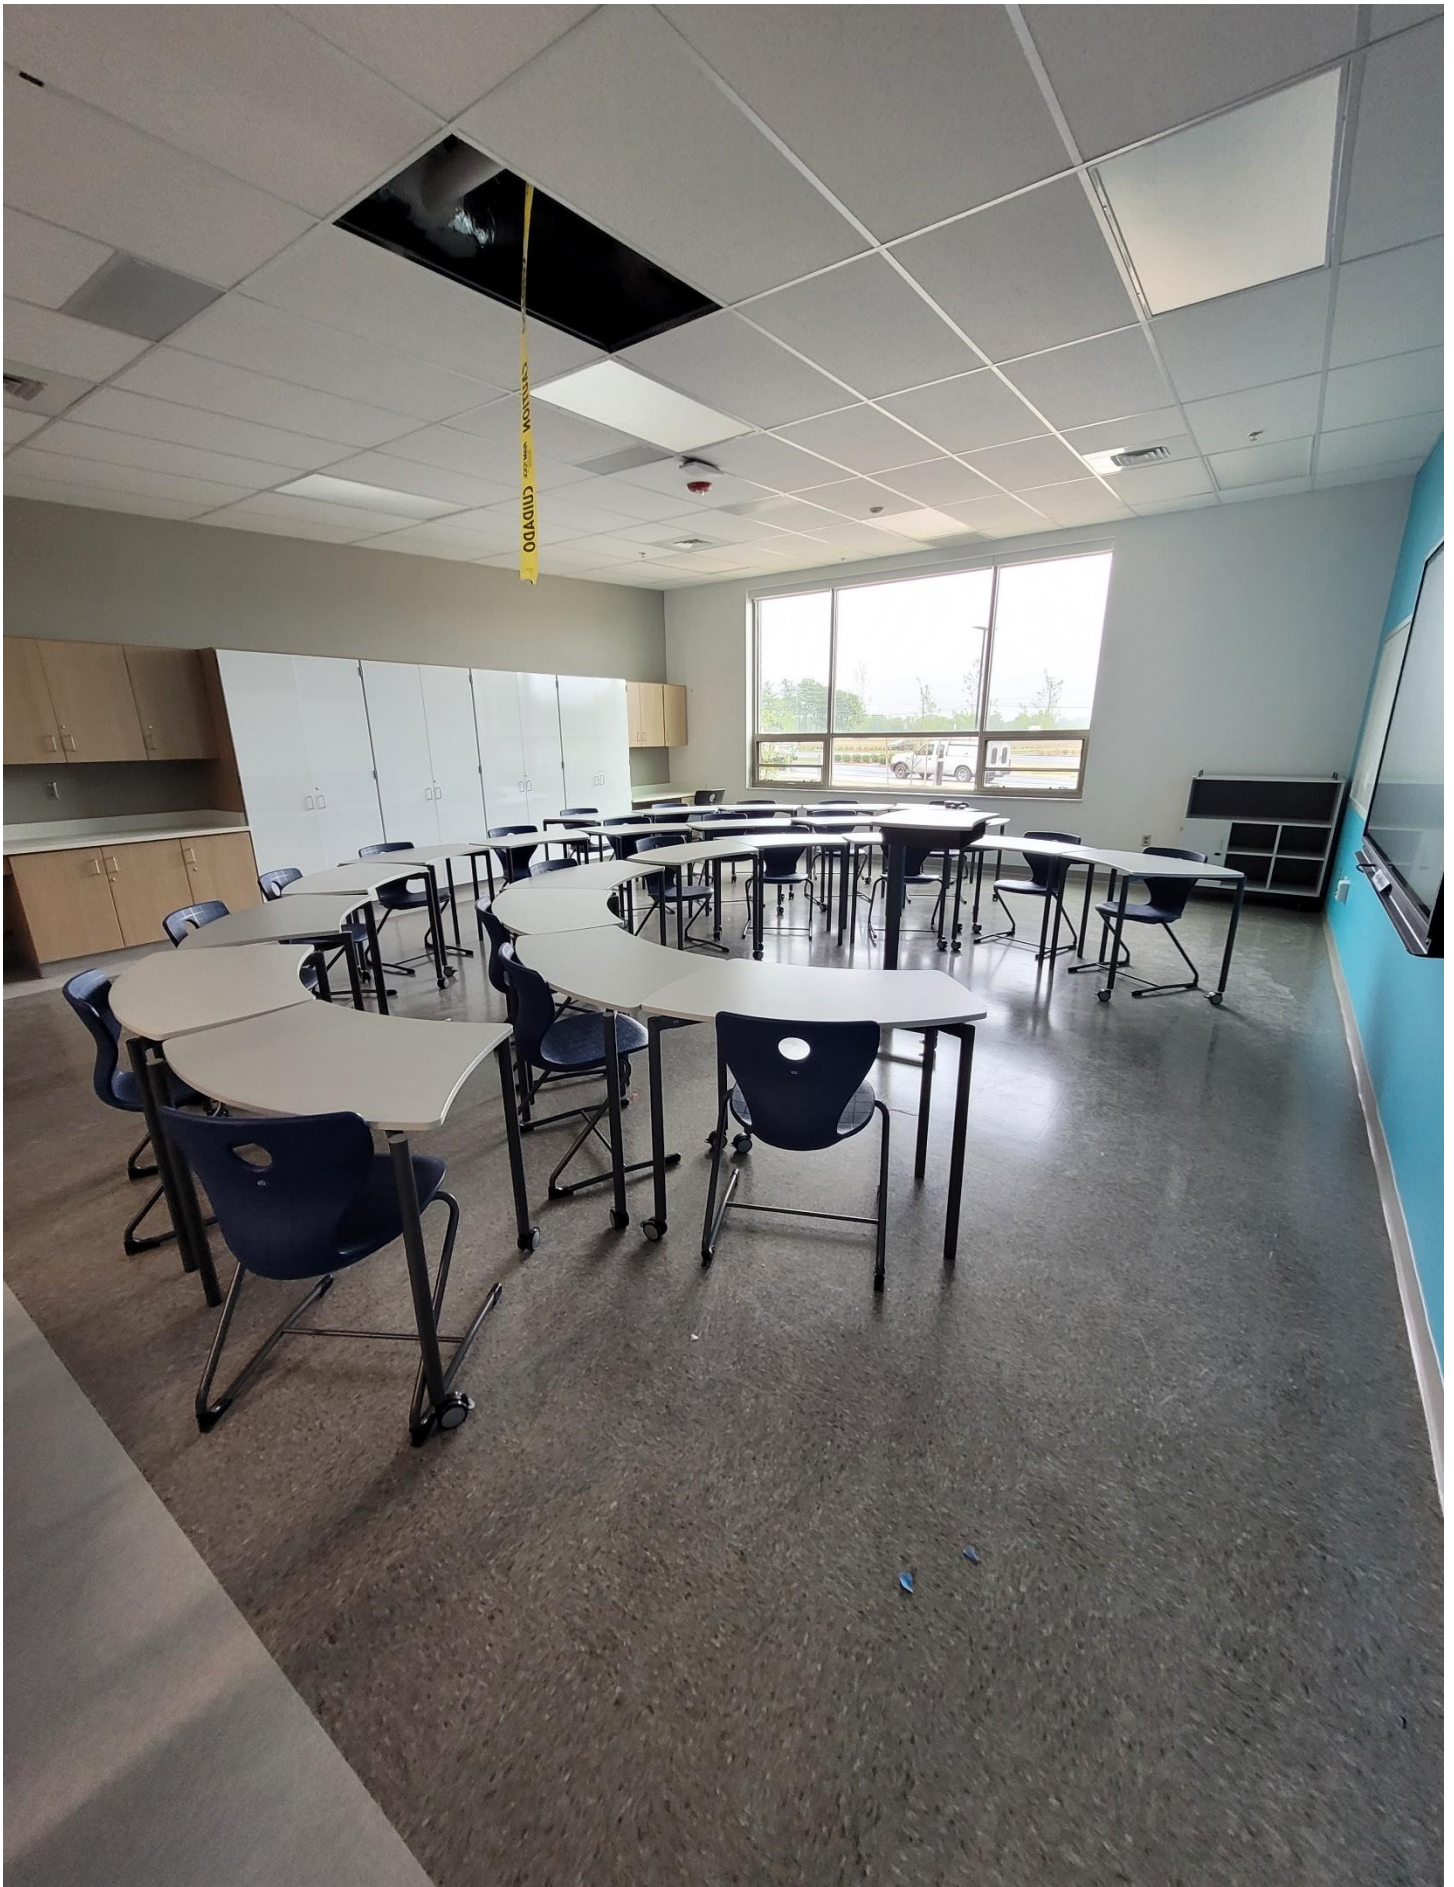


Photo 2 - Furniture is being set up in various learning Studios



Photo 3 - Diamonds in Restroom are being filled and blended to match existing floor



Photo 4 - Work continues in Area C - Commons Area - Wood Slats



Photo 5 - Tile is being laid in Corridor D#14 & #15



Photo 6 - Marquee Boards and door to Auditorium have been installed



Photo 7 - Stage Curtains have been installed



Photo 8 - Dressing Room D132



Photo 9 - Tile has been laid and doors are being installed in Corridor D12



Photo 10 - Court Yard - Southside of Area C



Photo 11 - Corridor E15



Photo 12 - Fitness E122 Floor has been installed



Photo 13 - Court Yard between Areas B & E



Photo 14 - Area C Mezzanine view



Photo 15 - Innovation Commons A220



Photo 16 - Innovation Commons A220



Photo 17 - Innovation Commons A220



Photo 18 - Furniture has been set up in one of the Learning Studios
