



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 05/19/2021
Weather: 74 degrees. High of 77 degrees today.
Hours Worked: 11:30hrs – 14:00hrs (2.5hrs) On Site.

Yesterday my Report incorrectly indicated that there was going to be a Site Tour conducted today by Grimm & Parker for Stafford County Officials. However, I was advised yesterday evening by Paul Klee that the Tour is actually scheduled for tomorrow, Thursday at 15:00hrs.

Beuchert Excavation: They are on site today. They are currently excavating material from the East side of the site to be utilized elsewhere on site. They are also sifting and mixing soil to be used in the BMPs.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: There are Twenty-five (25) men are on site today. They continue to lay Brick on the East and West side of Area D and also on the West side of Area E.

Hazzard Electric: They have Fourteen (14) men on site. They continue to run Conduit and pull wire throughout the site.

Colonial Webb: There are Thirty-seven (37) men are on site today. Duct is being run and insulated in Area A & B. Crews also continue to work on Roof top units in Areas A & E.

Weldon Steel: Five (5) men are on site today. They are working on Joists and decking in Area C.

JP Construction: They have Seventeen (17) men here today. They are framing bulk heads in Area A and hanging and finishing sheetrock in Areas A & B.

AAR Roofing: One (1) man is on site today. He is handling administrative matters.

Tailored Foam: Two (2) men are on site today. They are installing Transition Membrane in Area D.

FG & M: There are Eight (8) men on site today and they continue there work in Area E on storefronts and curtain walls.

United Sprinkler: No one is on site today.

CTSI: No one is on site today.

S&S Concrete Cutting Company: I did not observe anyone on site during my visit today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes. I did not observe anyone on site during my visit.

Questions to or from Branch Builds: I spoke with Brian and Jake during my visit today and asked them what Weldon Steel and Beauchert were doing on site today. Brian also informed me that he has filed his response with DEQ over the recent DEQ Inspection Report identifying the corrective action taken by Branch to address the items noted as deficient. Brian also reminded me of the two meeting scheduled for tomorrow. Finally, he gave me an update on what was happening today. He said that a request has been made to add a security camera on the South side of Area E without using exposed conduit. He currently is looking into what can be done to accommodate this request.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. A DEQ Warning Letter was issued on April 30th, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations. I was advised on 05/19/2021 that a response has been sent by Branch Builds to DEQ.

Reviewed emails:

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs –**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



Photo 1 - Work continues in Area D Mechanical Room



Photo 2 - Bulk Heads being constructed in Area A

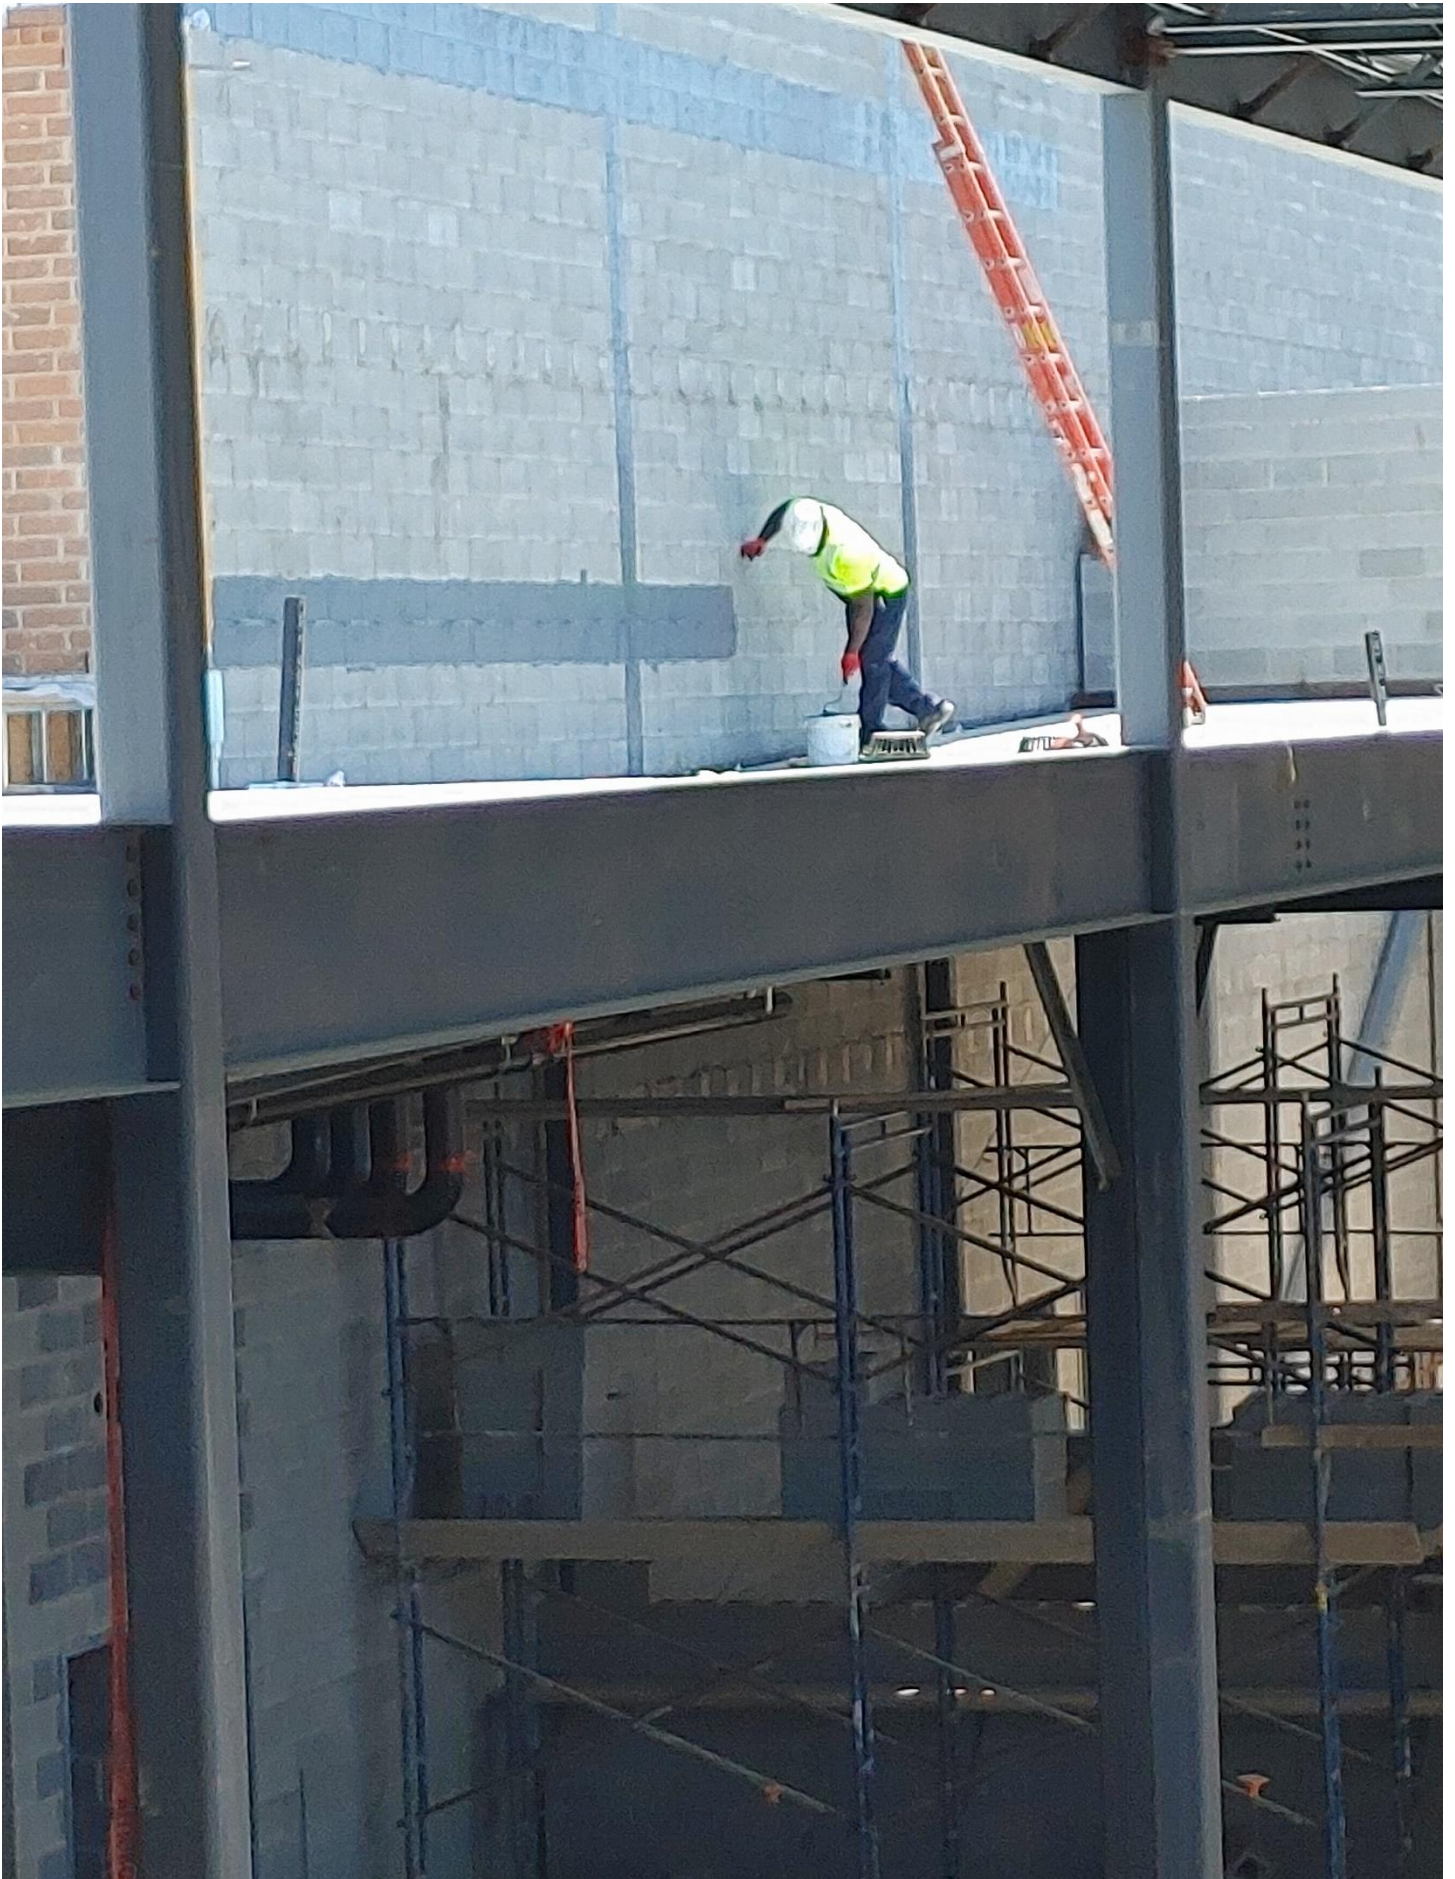


Photo 3 - Transition Membrane being installed on the West side of Area D



Photo 4 - Duct Banks being run in Area A



Photo 5 - Work continues on the roof top units in Area E

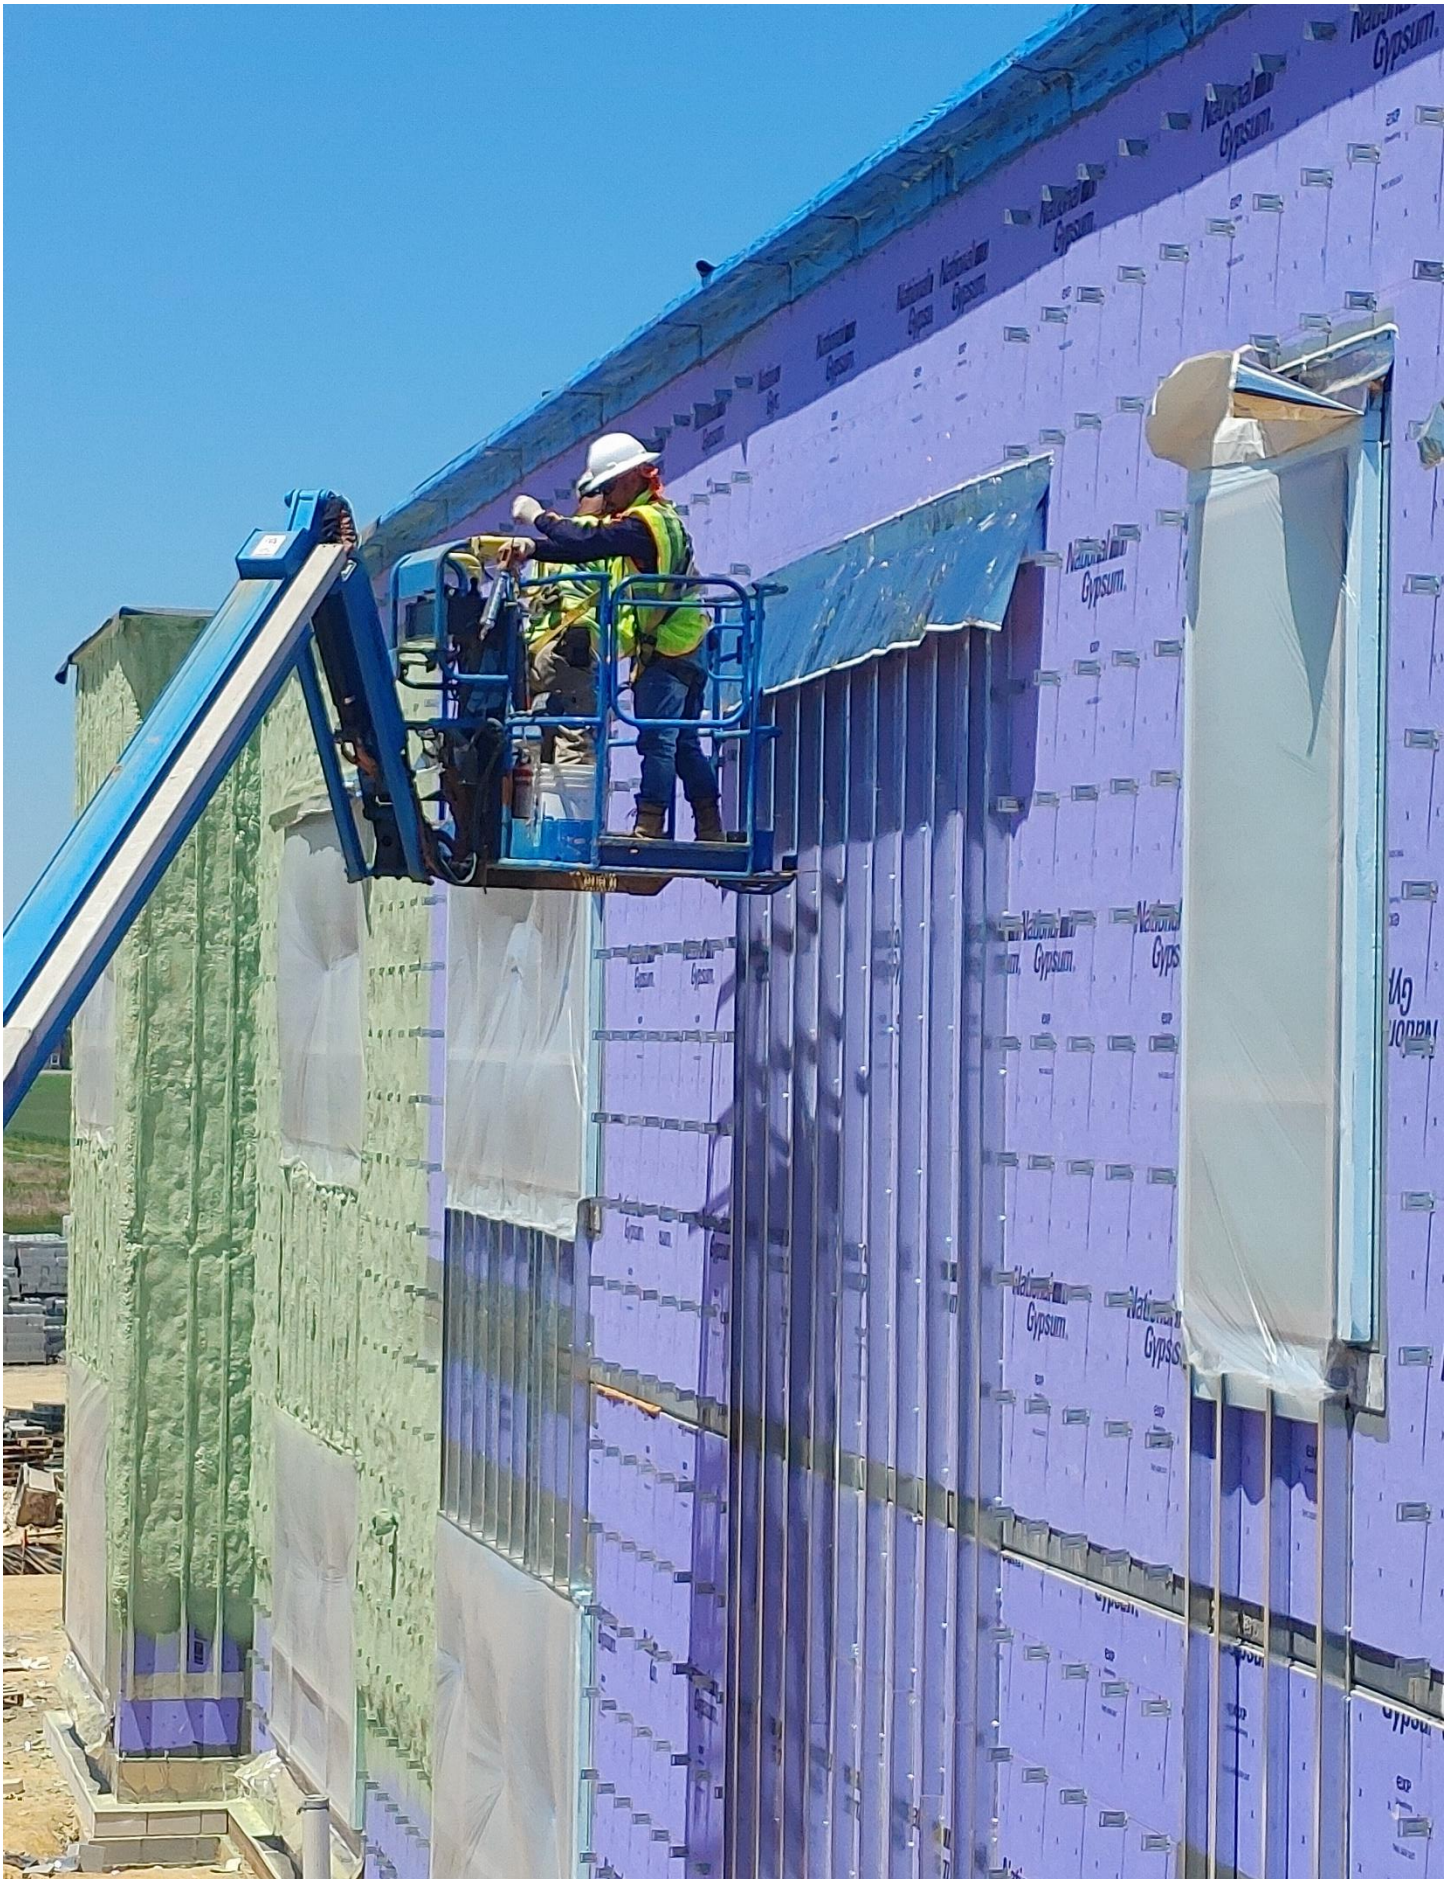


Photo 6 - Flashing being installed on the Southside of Area B



Photo 7 - Parapet walls being constructed on the roof of Area E



Photo 8 - Front elevation coming along
