



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 05/28/2021  
Weather: 74 degrees. Mostly Cloudy. High of 76 degrees today.  
Hours Worked: 09:00hrs – 12:00hrs (3hrs) On Site.

I did not visit the site on 05/26/2021 or on 05/27/2021. However, I did attend the virtual 05/26/2021 Progress Meeting in Norm Risavi's Conference Room and I also attended a meeting with Dr. Perry and Ralph Fallin on 05/27/2021 at the School Board's Meeting Room to discuss and explain the 12" water line tie-in and the installation of the Backflow device.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** No one is on site today. They did complete pour concrete in the Diamonds in Area C since my last visit.

**J.D. Long, Masons:** Twenty (20) men are here today. They are laying Brick on the North side of Area B and on the West side of Area D. A crew is also laying Block on the East Parapet wall in Area C. Two men are also washing and cleaning the brick on the South side of Area D.

**Hazzard Electric:** Twelve (12) men are on site. They continue to pull home runs from Area B to Area D. They are also pulling wire and running conduit on the 1st and 2<sup>nd</sup> floors of Area A.

**Colonial Webb:** No one is on site today.

**Weldon Steel:** No one is on site today.

**JP Construction:** No one is on site today.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is on site today.

**FG & M:** Six (6) men are here today. They are currently setting Storefront frames in Area B on the first floor.

**United Sprinkler:** No one is on site today.

**CTSI:** No one is on site today.

**S&S Concrete Cutting Company:** No one is on site today.

**Linear Surveyors:** I did not observe anyone on site today.

**Hillis-Carnes.** I did not observe a Tech on site during my visit.

**Questions to or from Branch Builds:** I met with Brian and Cooper first thing this morning. I brought Brian up to date on the meeting yesterday with Resource International and Enviroscapes to discuss and plan the installation on the 12" water line and Backflow device to the High School. I told Brian that when the install occurs they will have to shut off water to the High School site to make the Tap. I have advised Enviroscapes to provide me with an ample amount of notice so that Branch can take the necessary steps to allow for the loss of water on that day. I also advised Brian that the DEQ Inspector will be on site on June 7, 2021 at 09:00hrs to conduct a re-inspection of the High School site, Recreation Park Road & the Recreation Park.

Brian and I also discussed Branch's plan of when we will have to vacate our current Office location so that Beuchert can perform the necessary work required where our offices are located. This will most likely occur during late Summer.

Brian asked me to speak with the Sheriff's Office and let them know that the site will be shut down on Monday for Memorial Day and request that the Sheriff's office keep an eye on the site. I spoke with Chris Hawkins and he said that the Sheriff's Office would patrol the area several times a day over the weekend.

Yesterday Ralph Fallin asked me during my meeting if I had noticed the cracked concrete in the slab along the West Curtain wall in Area C. The crack extends approximately 10' or so through the top and side of the slab. I told Ralph I had noted the crack and had also mentioned it several times in my reports. Ralph requested that I say something to Branch again. So, I mentioned it to Brian and he said he would take a look at it today.

Finally, Brian said that they would be knocking off early today. Probably around 1PM or 2PM.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** Last Inspection was on 03/09/2021. The Report has been distributed and DEQ turned over the Inspection results to the DEQ Enforcement Division. A DEQ Warning Letter was issued on April 30<sup>th</sup>, 2021 to Branch Builds. The letter gives Branch Builds 30 days to arrange a meeting with DEQ Staff or provide a written response detailing actions they have taken or will take ensure compliance with state law and DEQ regulations. I was advised on 05/19/2021 that a response has been sent by Branch Builds to DEQ.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report - 05/25/2021**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals – #11 00 05-1.0, #28 13 00-1.1**
- RFIs – #267**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procure –**
- Weekly Submittal Status Report – 05/28/2021**
- Weekly RFI Status Update – 05/28/2021**

**Weekly Daily Log Summary – 05/28/2021**  
**PCO Log – 05/28/2021**





Photo 1 - Brick is being laid on the North side of Area B.



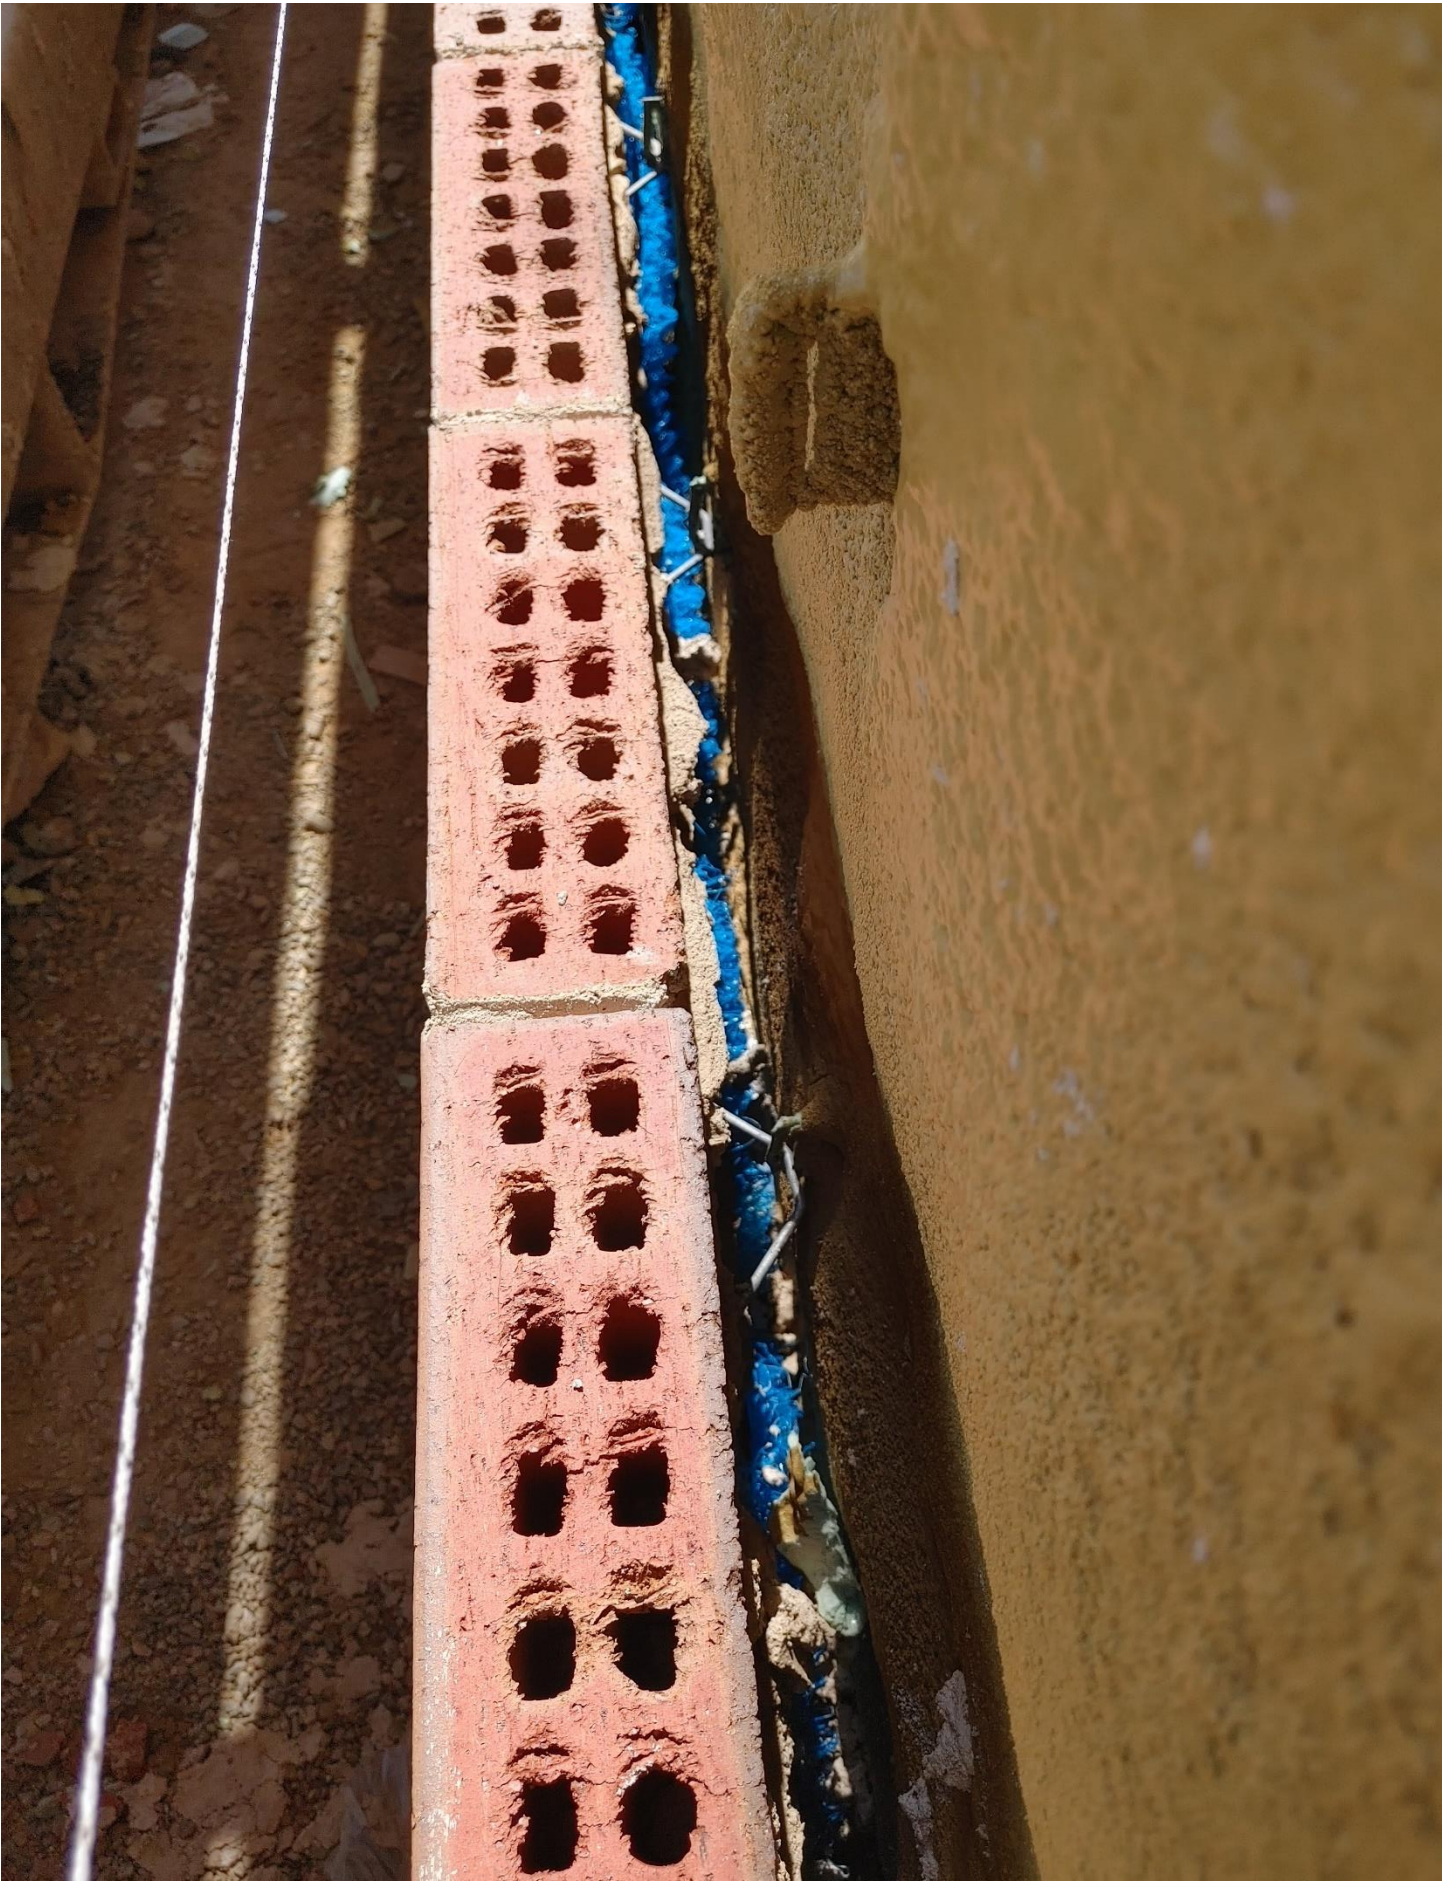


Photo 2 - Verification that Brick ties are being installed on the North side of Area B.





Photo 3 - Flashing installed on the North side of Area B.



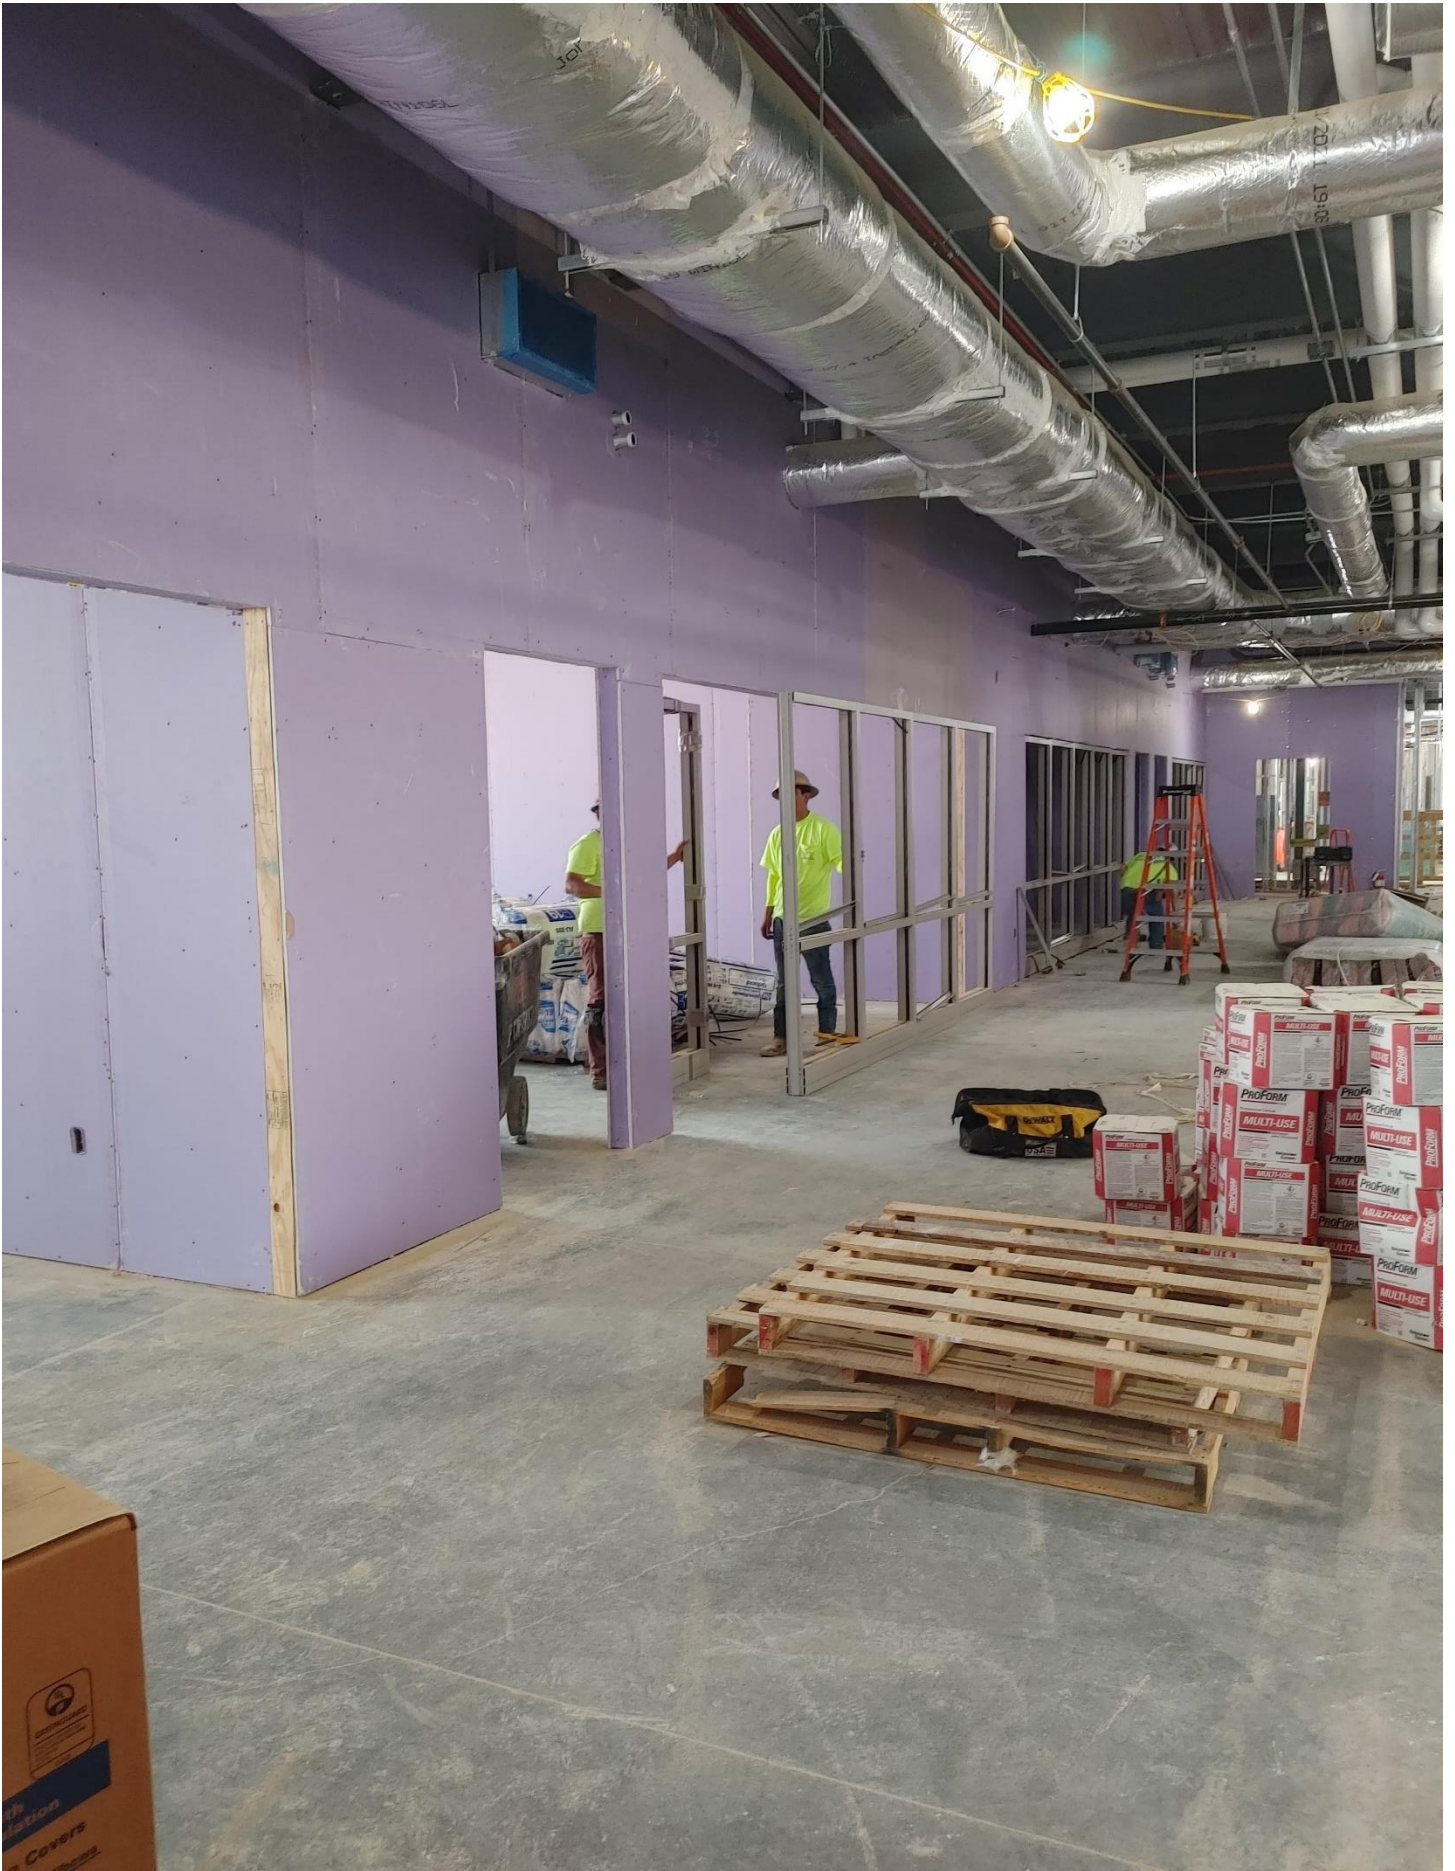


Photo 4 - Storefronts are being installed in Area B, 1st Floor.





*Photo 5 - Electrical Panels have been installed on the 1st Floor of Area A, A113.*



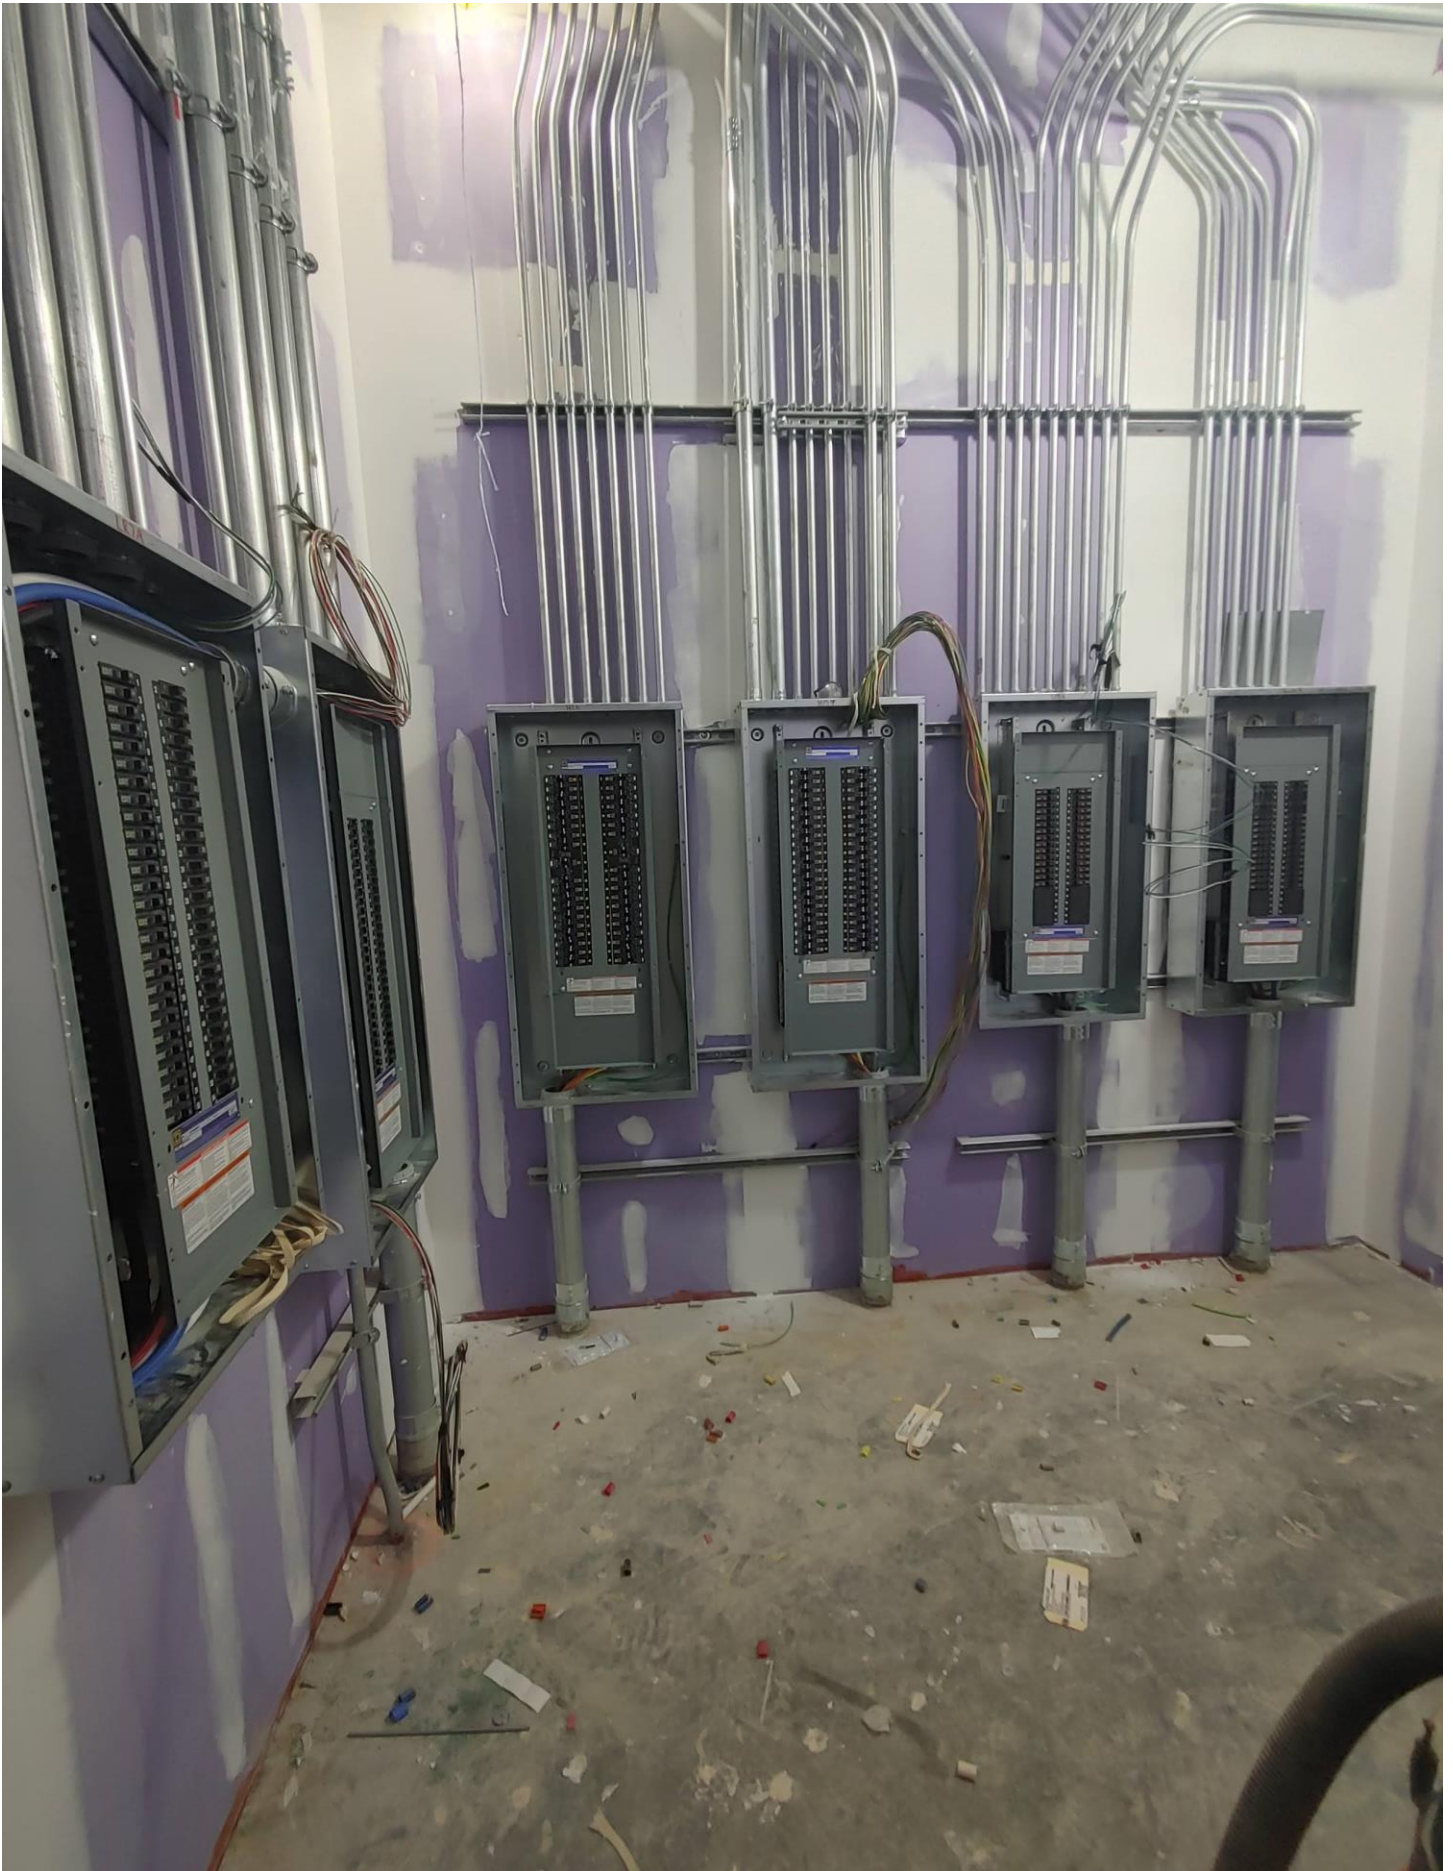


Photo 6 - Electrical Panels install in Area A, 2nd Floor A213.





Photo 7 - Block being laid on the Parapet wall in Area C.





Photo 8 - Brick is being washed on the South side of Area D.





Photo 9 - Brick is being laid on the West side of Area D.
