



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 06/08/2021
Weather: 81 degrees. Mostly Cloudy. High of 85 degrees today.
Hours Worked: 10:30hrs – 13:00hrs (2.5hrs) On Site.

I did not visit the site yesterday, nor was I able to attend the scheduled Progress Meeting.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one site today.

J.D. Long, Masons: Twenty-one (21) men are here today. They are laying Brick on the North side of Area D in the loading dock area. Brick is also being laid on the West side of Area D and the South side of Area C. They have also begun to break down the Fraco Scaffolding on the North side of Area B.

Hazzard Electric: Fourteen (14) men are on site. They continue to pull wire in Area A, B, C & D.

Colonial Webb: Twenty-nine (29) men are on site today. They continue to insulate pipe and run HVAC Duct in Area D. They are also running and insulating copper pipe in Area A and B. Line set are also being run to roof top units in Area A.

Weldon Steel: Three (3) men are site today welding steel in Area C.

JP Construction: Twenty-four (24) men are on site today. They continue to work in in Area A, B & C framing walls, bulkheads, and hanging and finishing Sheetrock. Two men continue to frame parapet walls on the roof of Area C.

AAR Roofing: Three (3) men are on site today working on the roof of Area C.

Tailored Foam: No one is on site today.

FG & M: No one is on site today.

United Sprinkler: Two (2) men are on site today. They continue to run pipe in Areas A & B.

CTSI: No one is on site today.

M. L. Straight: Two (2) men are on site today spraying and back rolling Block sealer in Area E.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: I did not observe anyone on site today.

Hillis-Carnes: A Tech was on site earlier today conducting inspections.

Questions to or from Branch Builds: I advised Brian that my inspection of the Drop Inlet (noted in 06/08/2021) revealed that Beuchert had filled in the hole they had made in the manhole. However, it also revealed that there was a 4" factory cut hole in the manhole that was causing the erosion around the manhole. I cemented the hole up to fix the problem.

Yesterday, late afternoon, I received a call from Brian & Todd. They indicated that the BMP process requires that the Owner's provide a third party Representative to verify, document and sign off on the BMPs as they are constructed. I told them I thought from our last meeting on the subject that HG was going to do that. They said that this was different. I told them I would meet with them today to review the documents and we could discuss the matter further.

This morning I received a call from Hillis-Carnes stating that they had been contacted by Branch about representing the Owner during the BMP Process. I told Hillis-Carnes to not do anything unless they here from me.

I spoke with Todd about our conversation yesterday. I asked him to show me in writing where is states that the owner needs a Representative to document the BMP process by Branch Builds. He said that there is no documentation, but typically the Owner hires a third party to document the process. I told him that I don't totally understand why the Owner needs to document Branch Build process. I told him that Branch has to build it according to the plans and I was under the impression that HG was going to inspect/monitor the process. I told Todd that I would speak with Dr. Perry about the matter and get back to him.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 06/07/2021

Submittals – #10 21 23-5.1, #11 52 13-5.0, #23 80 00-15.0, #26 50 00-5.0

RFIs –

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procure –

Weekly Submittal Status Report –

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - Manhole along Rec Park Road that was patched by Beuchert.

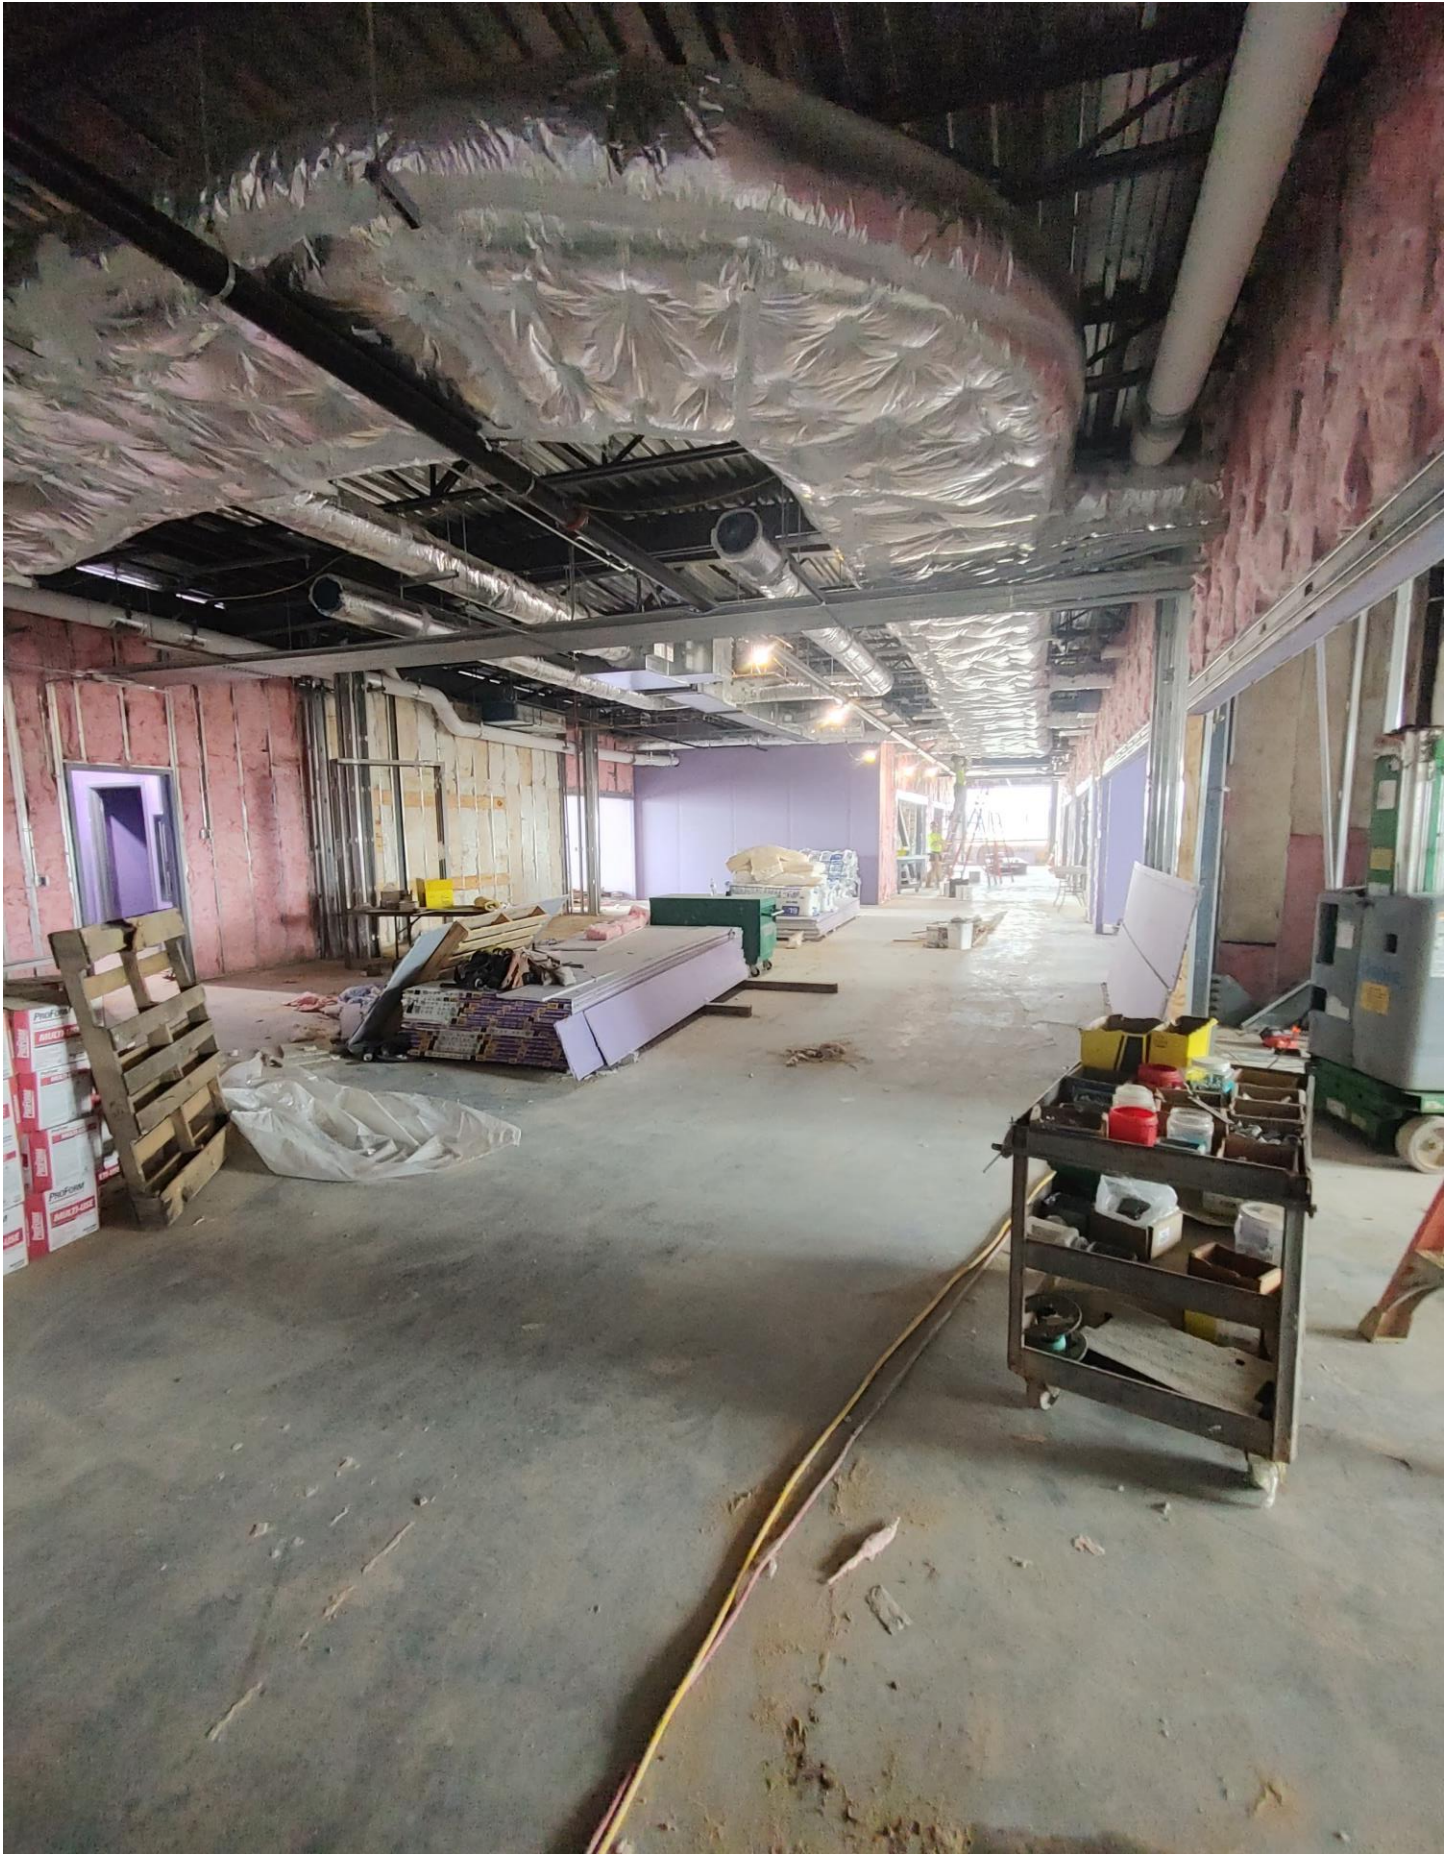


Photo 2 - Insulation being installed on the 2nd floor of Area B.



Photo 3 - Brick is being laid on the West side of Area D.



Photo 4 - Block sealer is being sprayed and back rolled in Area E.



Photo 5 - Brick is being laid on the North side of Area D.



Photo 6 - Parapet walls are being framed in Area C.

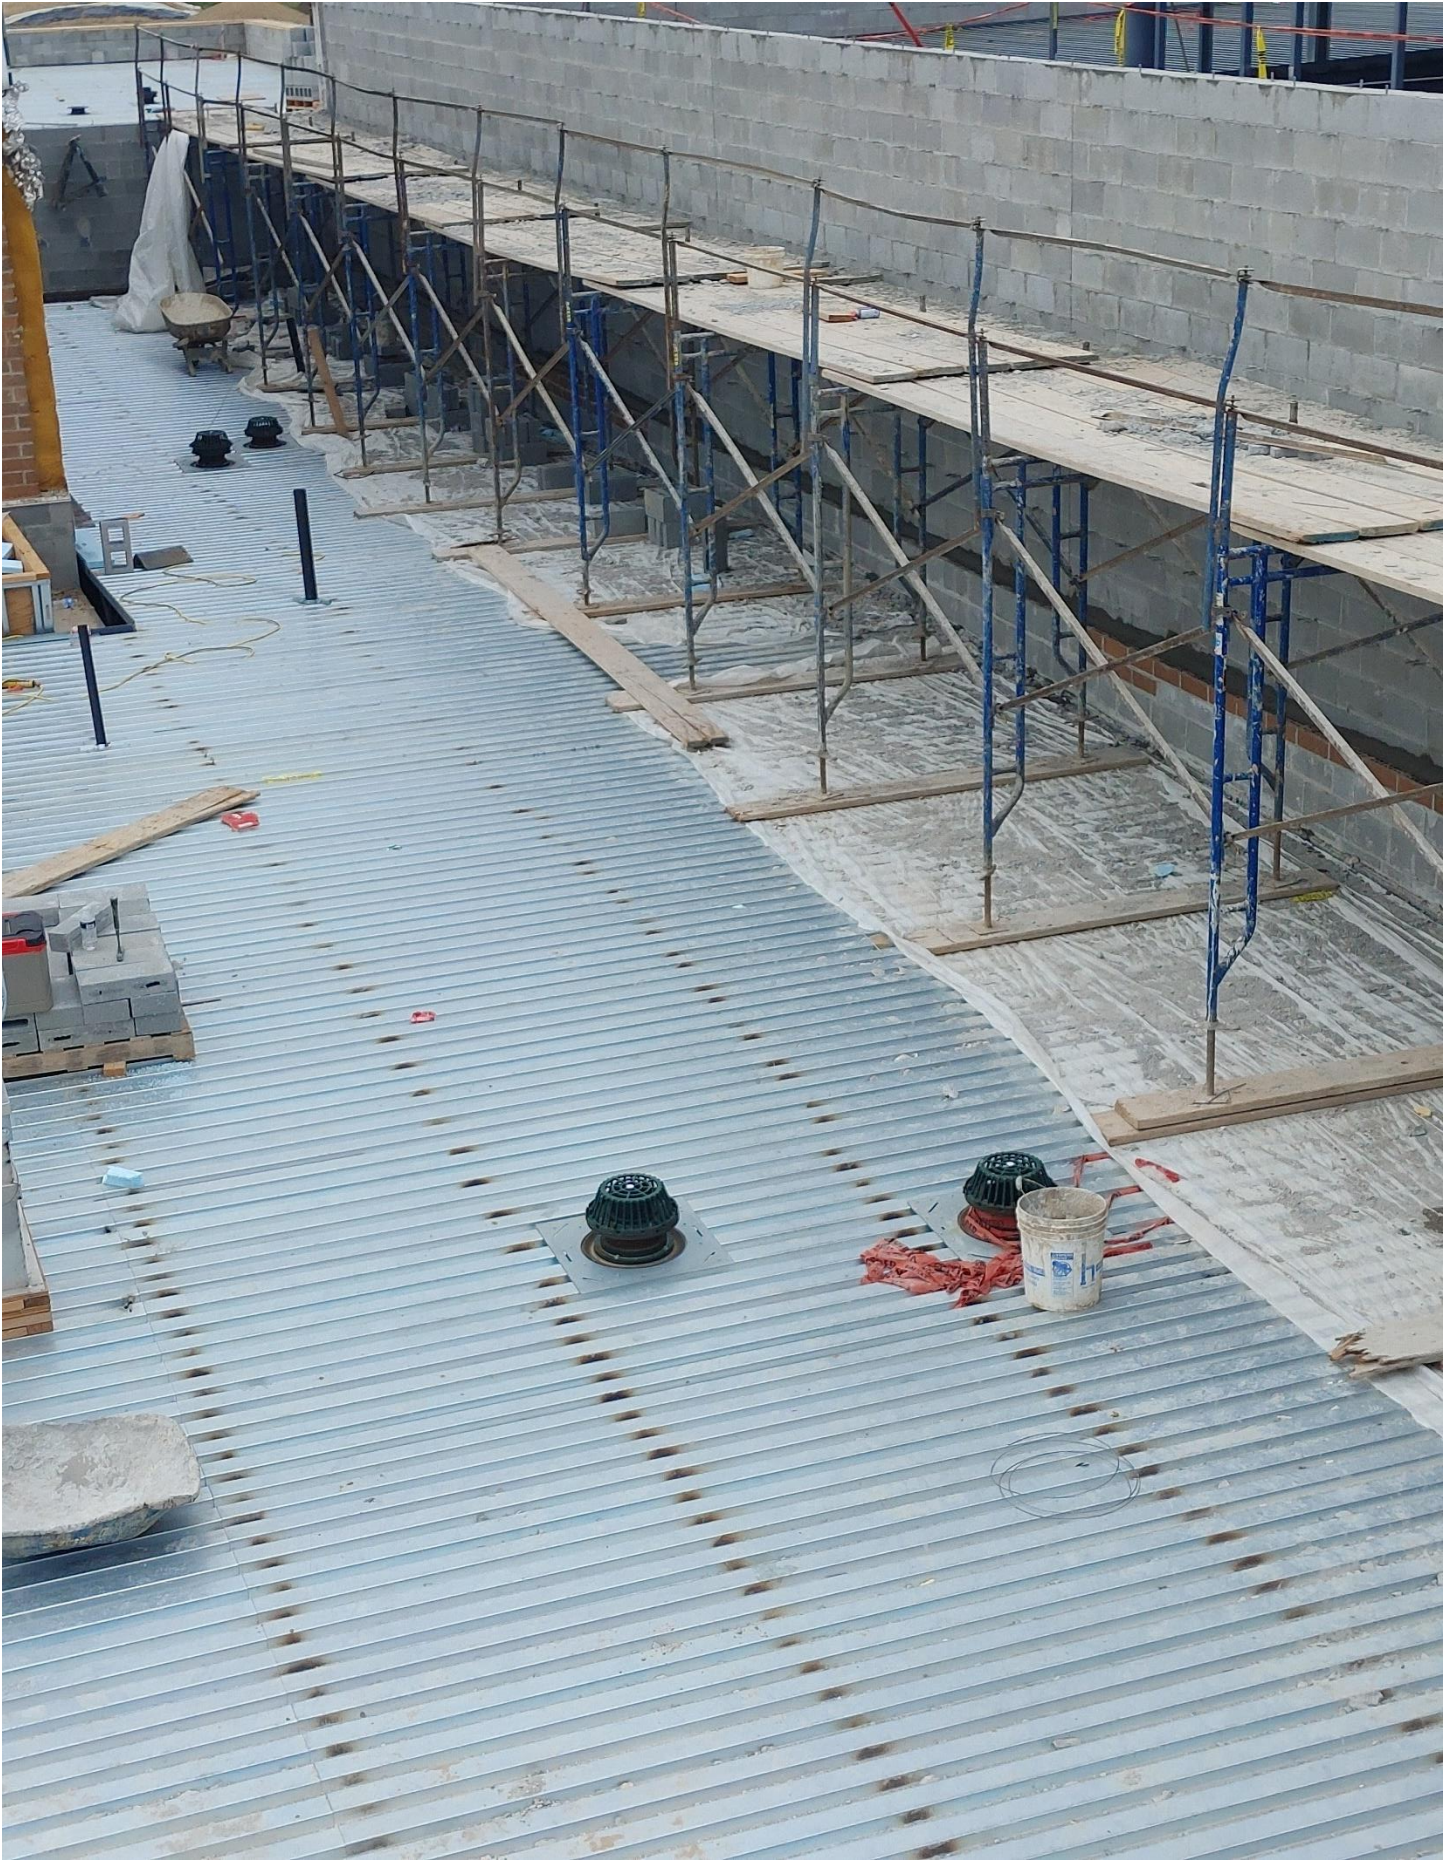


Photo 7 - Block/brick has been grouted so that flashing can be installed on the roof of Area D.
