



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 06/9/2022

Weather: 84 degrees - High of 92 degrees today. Partly Sunny

Hours Worked: 08:00 – 11:00hrs - High School Site Visit

11:00 – 12:30hrs – Progress Meeting Montross Middle School & Cople Elementary School.

12:30 – 13:30hrs – Report Preparation

My last visit to the site was on May 12, 2022. I walked the site to observe the work that had transpired since my last visit. I noted a crew on site installing the Auditorium seating. A few Electricians were on site pulling wire and setting receptacles and two men were trenching between the flag poles in front of the building for what I believe to be Flag Pole Lighting. I also observed a man replacing damaged ceiling tiles. Chandler and another man was installing wood trim around the side and back of the Grand Staircase. Two men were installing wood trim on the Bulk Head area leading into the Gymnasium Hallway.

I met with Chandler and asked if he had been able to set up a meeting with Mr. Chandler, the adjacent property owner to discuss the Farmer's Road. Chandler said he had not yet been able to set up the meeting. He said that he would not be on site next week but Lee would be and Lee would attend the meeting. I told Chandler that we need to set up this meeting.

At the request of Dr. Perry I attended the Progress Meeting for the Montross Middle School/Cople Elementary School. I advised everyone that a Proof Roll needed to be conducted of the Drive Lane Loop by Hillis-Carnes. I also advised everyone that the Owner's Third Party Inspector, Hillis-Carnes, did not need to test each six yard concrete pour of the sidewalk and curb. However, the Hillis- Carnes would need to test/inspect any concrete that was structural, such as the Canopy footing. A discussion also transpired related to the removal of Asbestos. I asked if the Owner would be receiving copies of all of the documentation related to identification and removal/disposal. The Contractor advised that he would see that the Owner received copies.

I met with Ralph Fallin and Chris Evans after the Progress meeting. We discussed the High School the Punch List that is being conducted by Branch Builds and Grimm & Parker.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports –**
- Hillis-Carnes Bio Retention Pond Reports –**
- Submittals -**
- RFIs –**
- Patrick Byrne –**
- Alexes Lee –**
- Tara Delaney –**
- Change Order/PCOs/Pay App –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



Photo 1 - Administrative Office Area



Photo 2 - Kitchen Serving Line



Photo 3 - Kitchen Prep Area



Photo 4 - Dishwasher Area



*Photo 5 - Auditorium Seats are being installed*



Photo 6 - Auditorium and Stage





*Photo 7 - Dressing Room #132 HVAC Unit is mounted approximately 14" above Door Frame as compared to the next picture in Room #132 where it is mounted literally on top of the Door Frame.*



Photo 8 - HVAC Unit in Room #132 mounted on Door Frame.



Photo 9 - Auditorium Stage

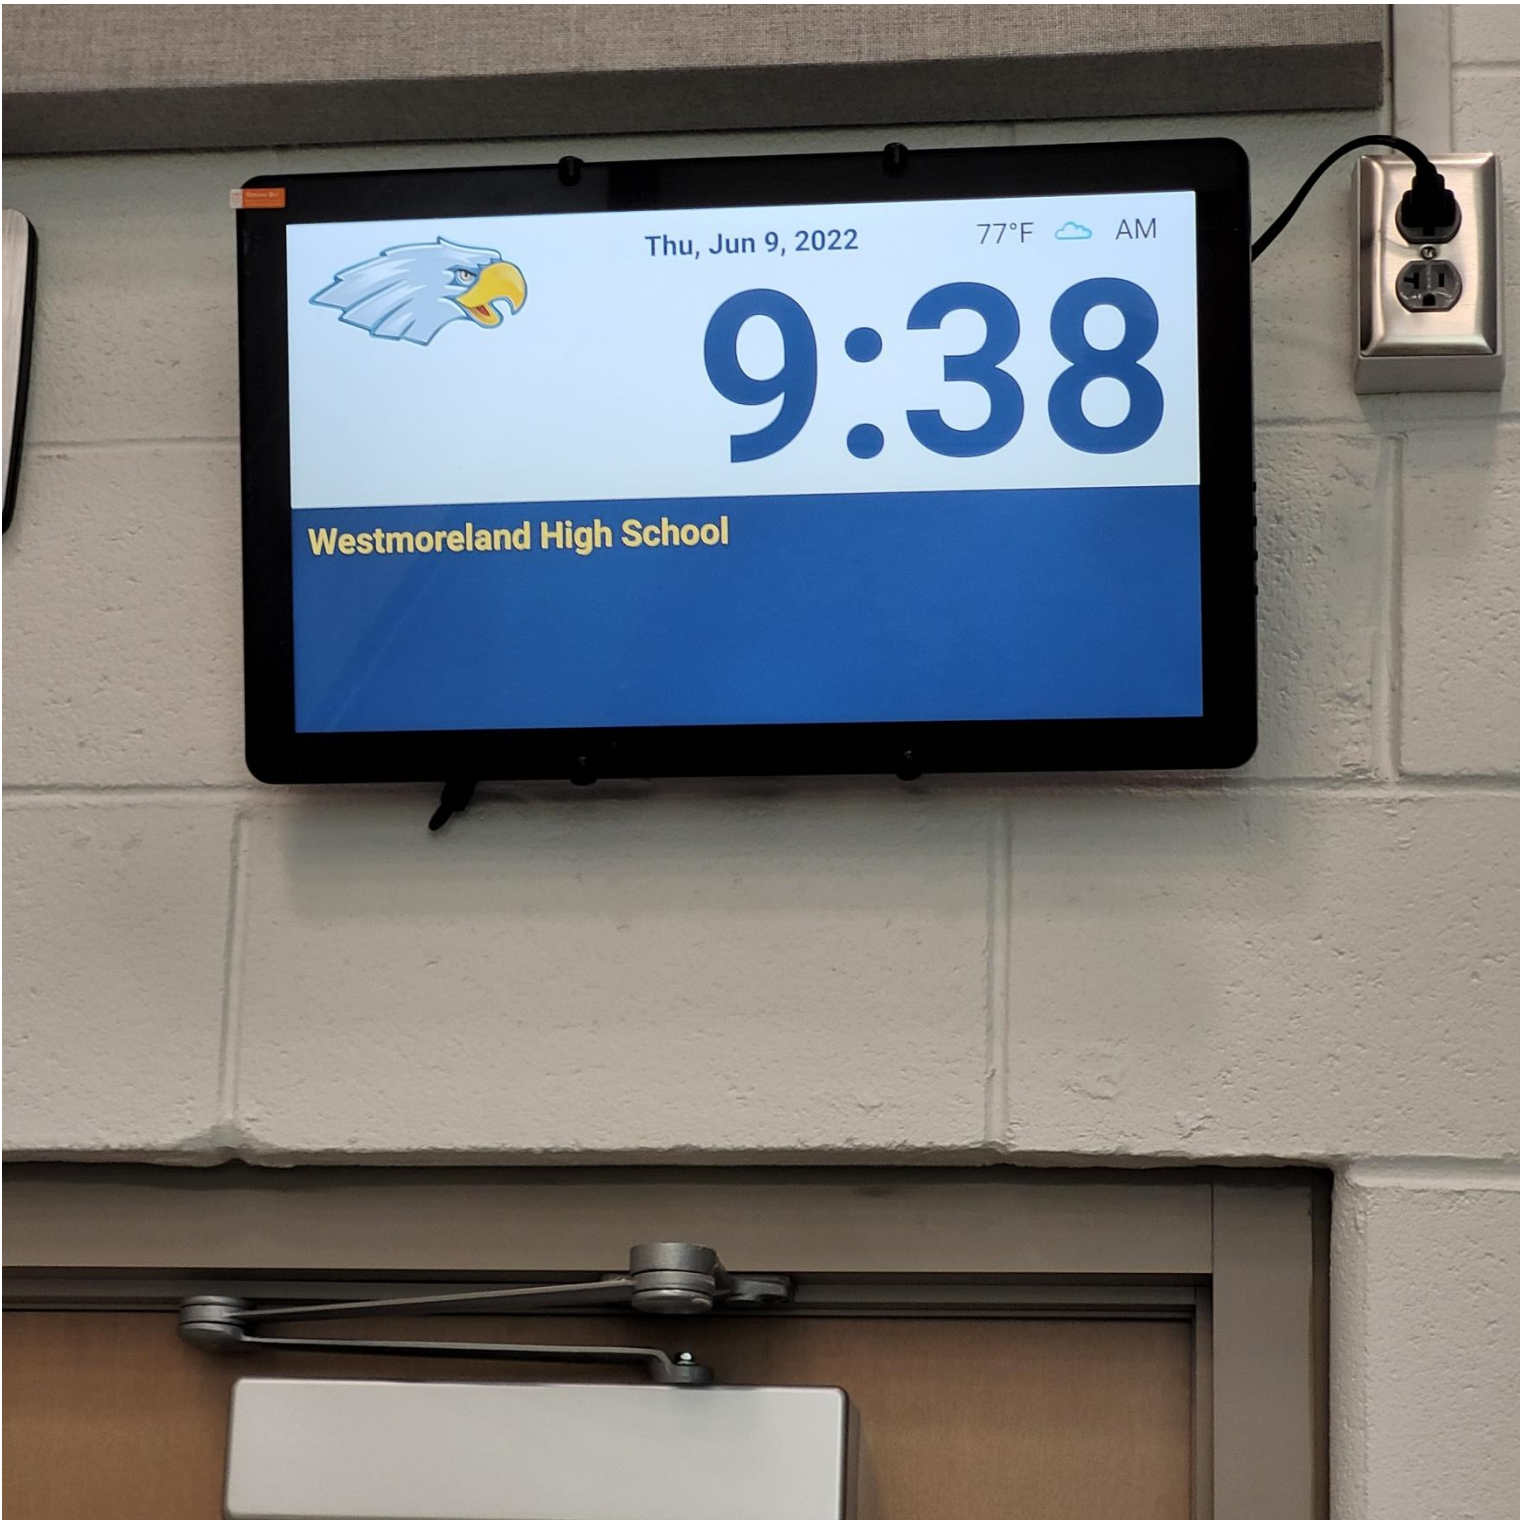


Photo 10 - Clocks installed in Learning Labs

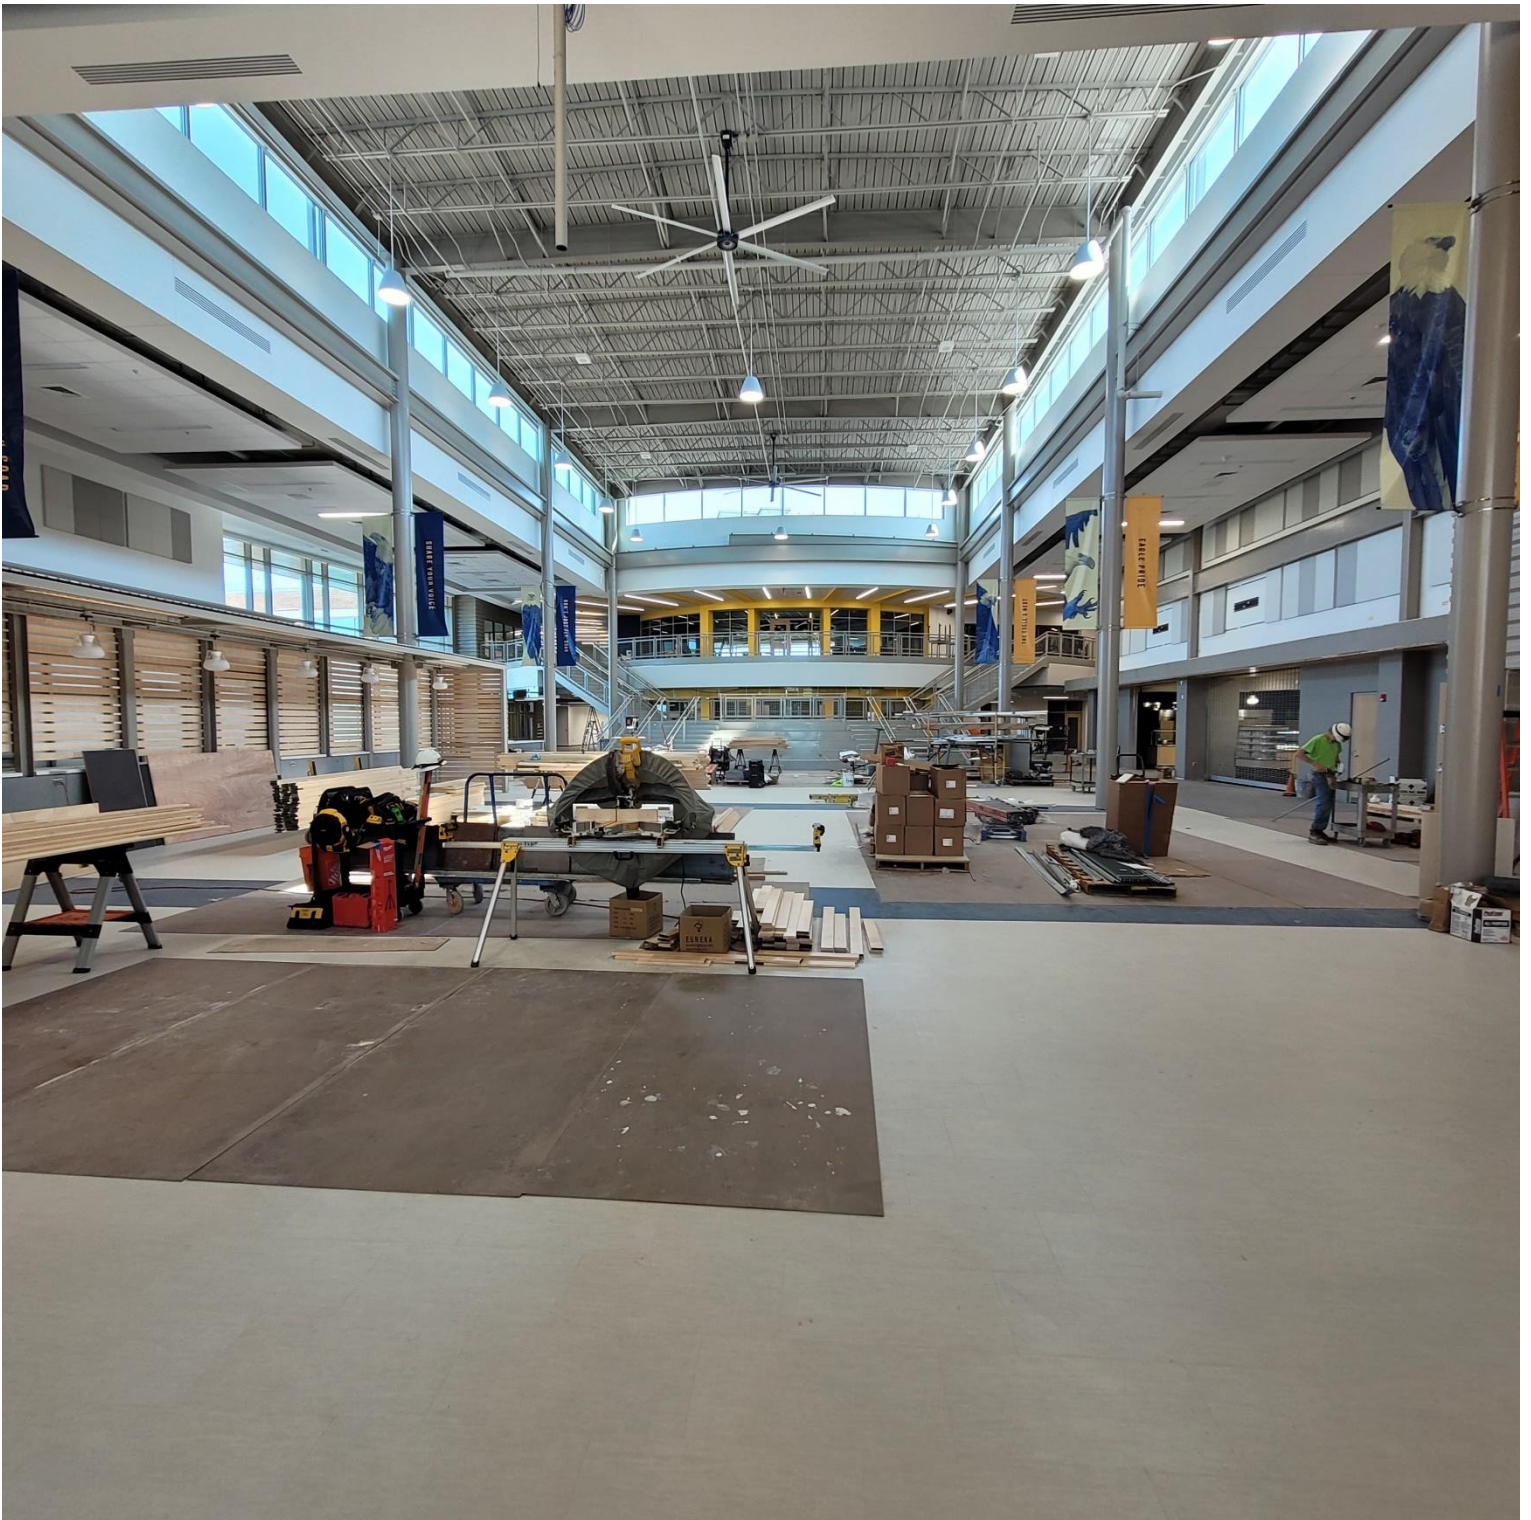


Photo 11 - Area C looking towards the Grand Staircase.



*Photo 12 - Courtyard between Areas D & E*



Photo 13 - Wall Tile in Boys Restroom E103



Photo 14 - Wall Tile in E103





Photo 15 - Gymnasium Hallway looking East



*Photo 16 - Metal Decking in Stairwell #1*



*Photo 17 - Area between Areas B & E*



Photo 18 - Southside of Area E



Photo 19 Southside of Area D



Photo 20 - Eastside of Area E



*Photo 21 - Front of High School*
