



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 07/08/2021

Weather: 84 degrees. Partly Sunny. High of 86 degrees today. Rain is in the forecast for this afternoon. A Tropical Storm Warning is in effect until 19:15hrs.

Hours Worked: 10:00hrs – 12:30hrs (2.5hrs)

I walked the site and observed the work being performed. Branch held their Sub-Contractor meeting at 11:00hrs this morning.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** They continue to lay block in Area C and Brick on the South side of Area A above the low roof in Area C.

**Hazzard Electric:** They continue to pull wire in Area A, B, C & D. They have also begun to install wall receptacles on the 1<sup>st</sup> floor of Area A.

**Colonial Webb:** They are currently working in Area D running HVAC Duct and in Area A insulating pipe, Duct and also running HVAC Duct.

**Weldon Steel:** They continue to cut & weld Steel in the Auditorium.

**JP Construction:** They are hanging sheetrock in the Administrative Office area and framing and sheathing Parapet walls on the roof of Area C.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is on site today.

**FG & M:** They continue to work on Curtain walls.

**United Sprinkler:** They continue to run Sprinkler pipe ion the 2<sup>nd</sup> floor of Area A.

**CTSI:** No one is on site today.

**M. L. Straight:** Two (2) men are on site today working in Area B.

**S&S Concrete Cutting Company:** I did not observe anyone on site today during my visit.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe a Tech on site today.

**Questions to or from Branch Builds:** Met briefly with Brian and Jake after the Sub-Contractor meeting. I expressed my concern about the incoming storm and the potential for the retention ponds to overflow their banks again causing damage to the Rec Park again.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) –**

**Submittals – #12 36 00-2.0, #32 33 00-5.0**

**RFIs –**

**Patrick Byrne –**

**Change Order/PCOs/Pay App –**

**Changes in Procore –**

**Weekly Submittal Status Report –**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**

**PCO Log –**



Photo 1 - Masons are laying brick above the low roof of Area C on the South side of Area A



Photo 2 - Weldon Steel is cutting and welding steel in the Auditorium

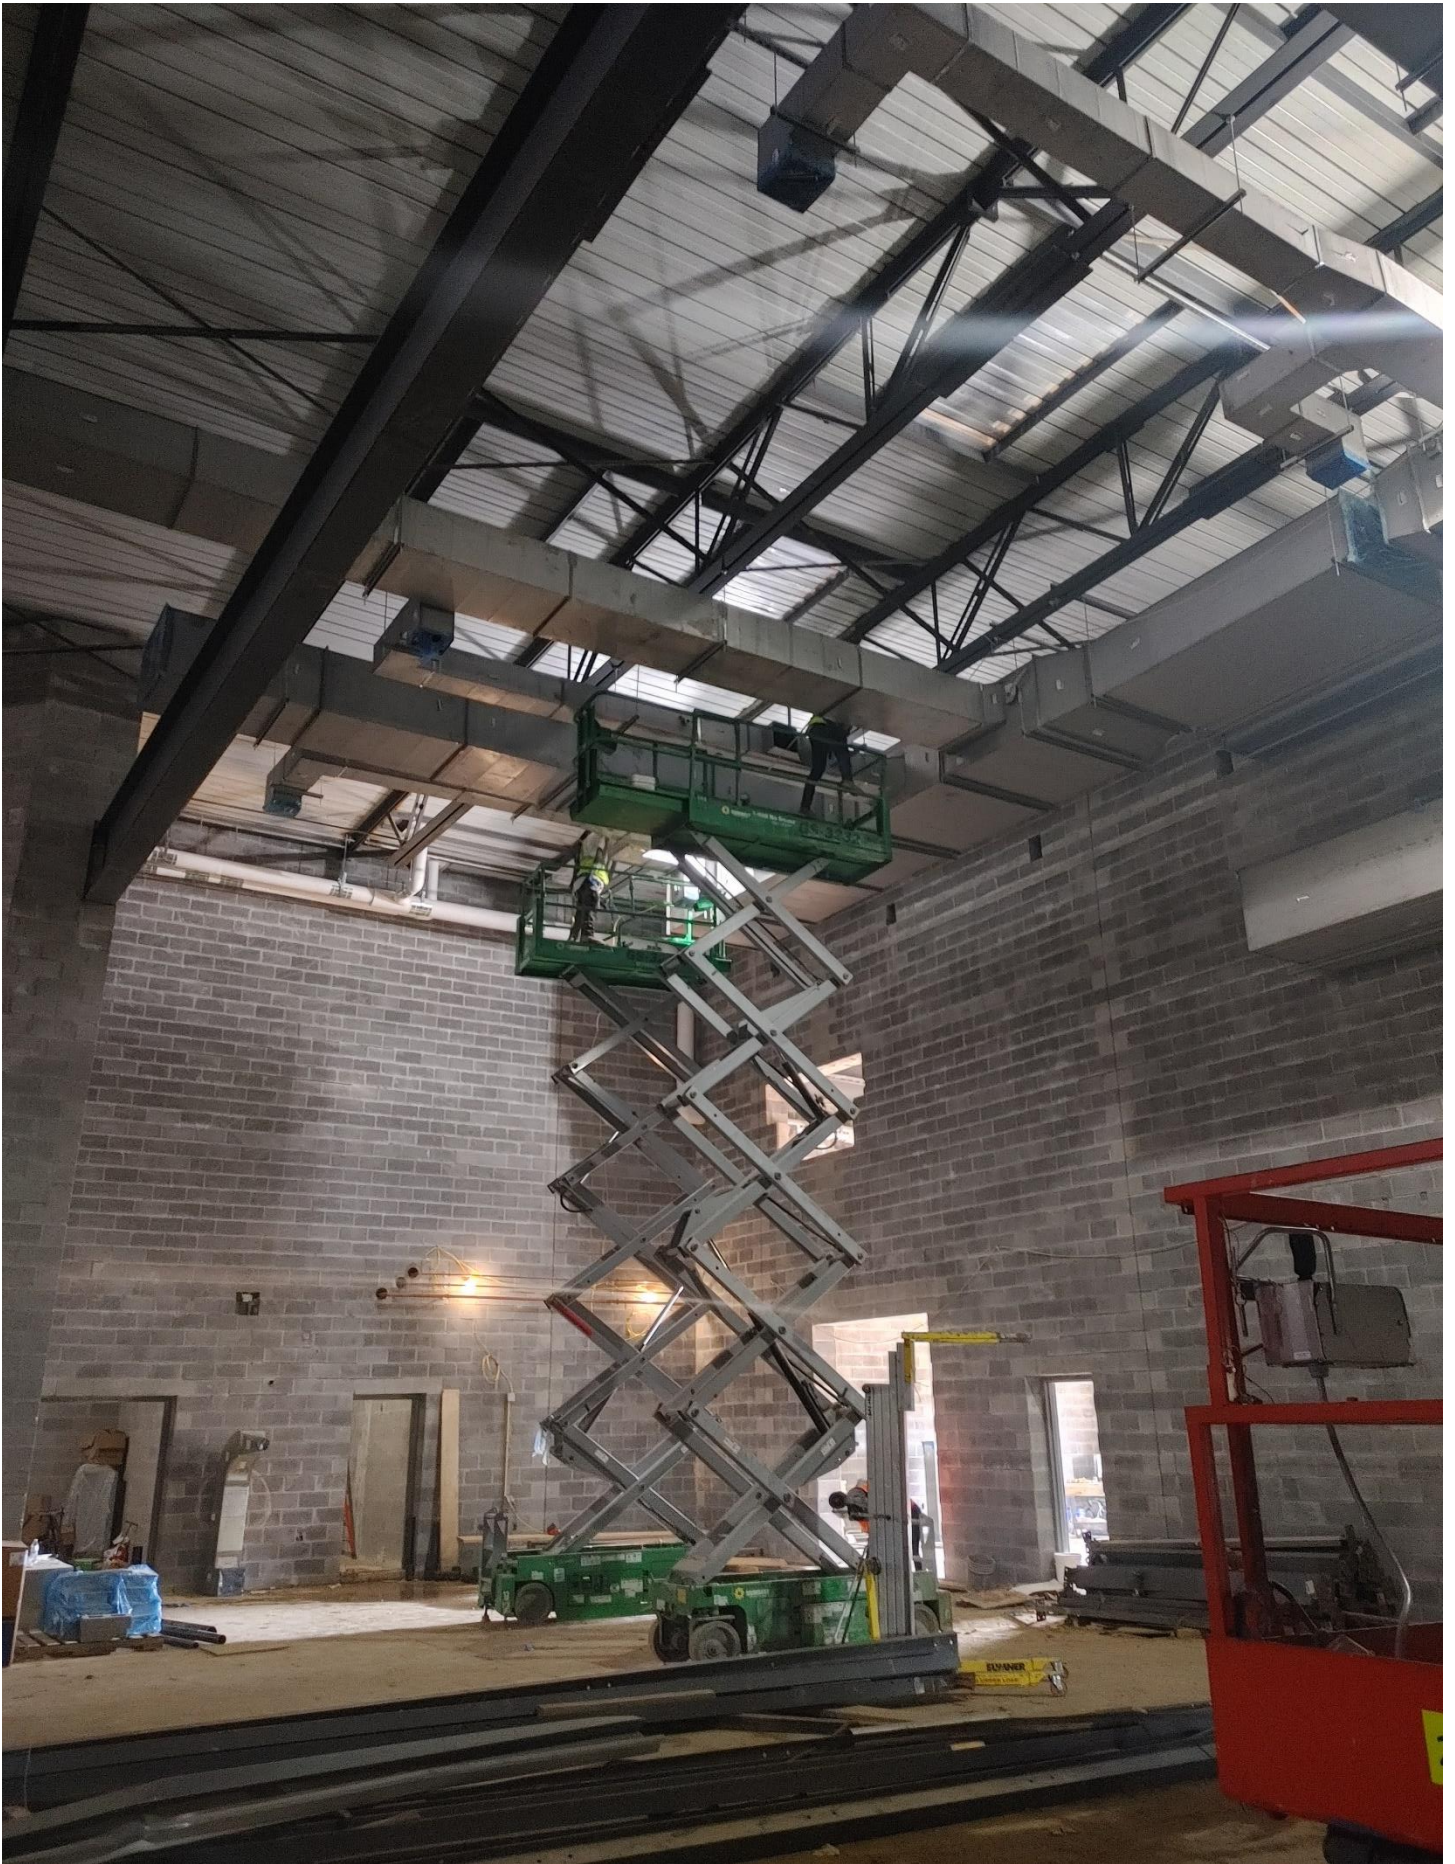
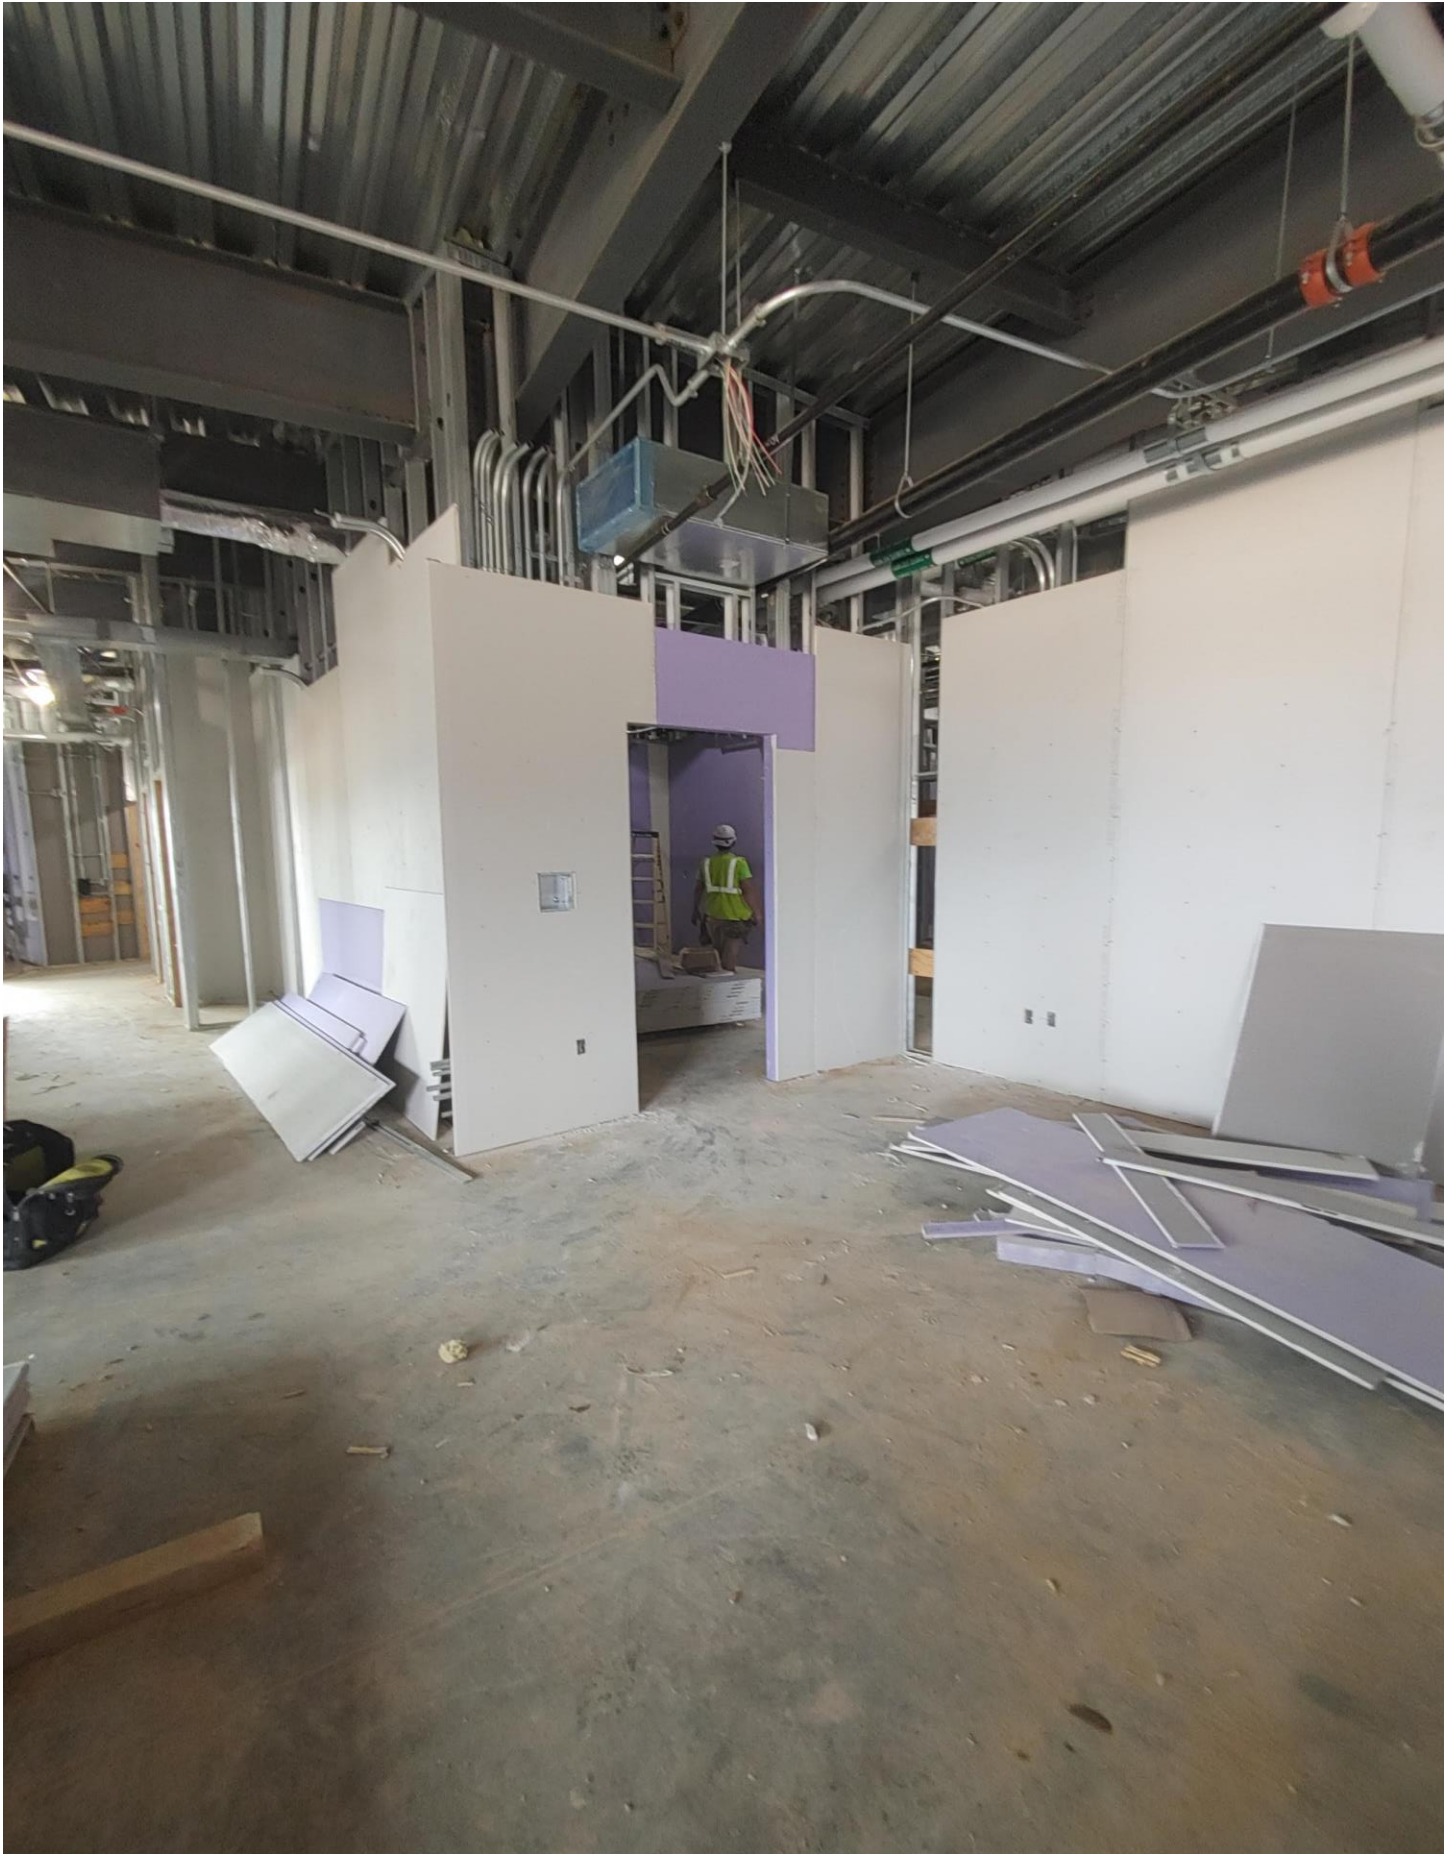


Photo 3 - Colonial Webb is running HVAC Duct in the Auditorium



*Photo 4 - Duct work is being run and pipe insulated on the 2nd floor of Area A.*



*Photo 5 - Sheetrock is being hung in the Administrative Office area.*

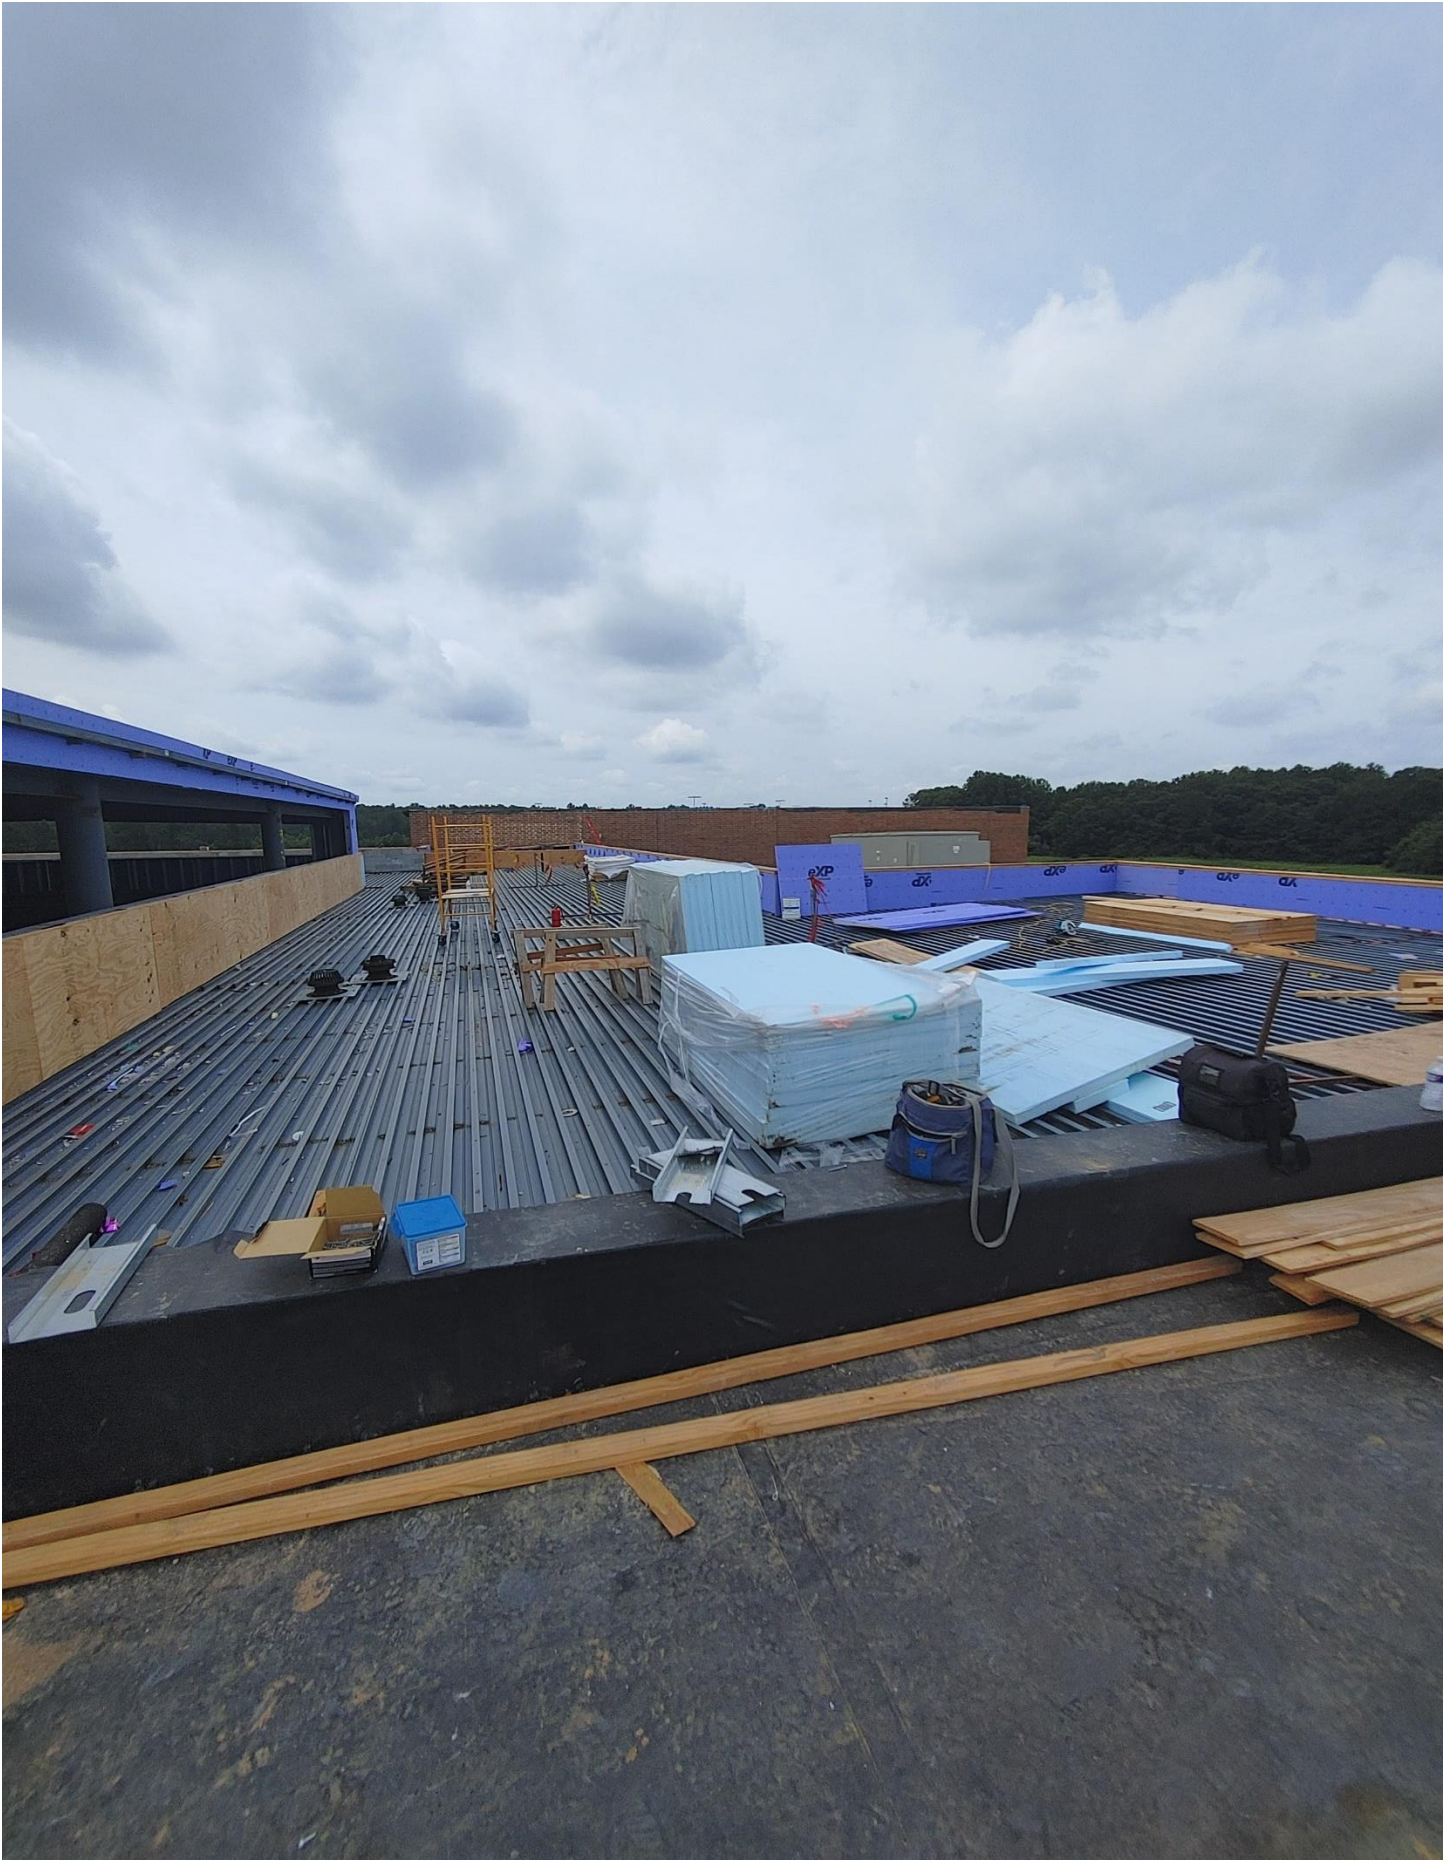


Photo 6 - Parapet walls are being framed and sheathed in Area C.





Photo 7 - Cement Board has been hung in the 1st floor bathrooms in Areas A & B.

