



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

DAILY REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 07/12/2021

Weather: 85 degrees. Sunny. High of 93 degrees today.

Hours Worked: 09:30hrs – 12:30hrs (3hrs)

I walked the site and observed the work being performed.

Beuchert Excavation: No one is on site today.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Fourteen (14) Men are on site today. They continue to lay block in Area C and Brick on the east side of Area C and on the South side of Area A. The Fraco Scaffolding has been disassembled on the South side of Area B.

Hazzard Electric: Fourteen (14) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: Eighteen (18) men are on site. They are running Duct in Area D and Area A. A crew is also insulating pipe & duct in Area A.

Weldon Steel: No one is on site today.

JP Construction: Nineteen (19) men are on site today. They are finishing sheetrock in Area B, Framing metal studs in Area A and constructing Parapet walls on the roof of Area C. A few men are also off loading Acoustical Ceiling tile from a truck and staging the tile on the 2nd floor of Area A.

AAR Roofing: No one is on site today.

Tailored Foam: No one is on site today.

FG & M: No one is on site today.

United Sprinkler: Two (2) men are on site today.

CTSI: Two men are on site today running low voltage wire.

M. L. Straight: A small crew is on site today painting and back rolling in Areas A & B.

S&S Concrete Cutting Company: I did not observe anyone on site today during my visit.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: Brian is off today and tomorrow. Cooper is on Vacation this week. I met with Jake out on site this morning. Jake advised that they held a Sub-Contractor meeting this morning. He also said that the Mobile A/C being used in Area A wasn't running this morning. He has contacted the rental company and they are dispatching someone today to trouble shoot the unit.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

- Hillis-Carnes Concrete Break Report -**
- Hillis-Carnes Grout Inspection/Compression Strength Test –**
- Hillis-Carnes Field Reports (Concrete and Steel) –**
- Submittals –**
- RFIs – #290**
- Patrick Byrne –**
- Change Order/PCOs/Pay App –**
- Changes in Procore –**
- Weekly Submittal Status Report –**
- Weekly RFI Status Update –**
- Weekly Daily Log Summary –**
- PCO Log –**



Photo 1 - A shipment of Acoustical Ceiling tile is being off loaded on to the 2nd floor of Area A

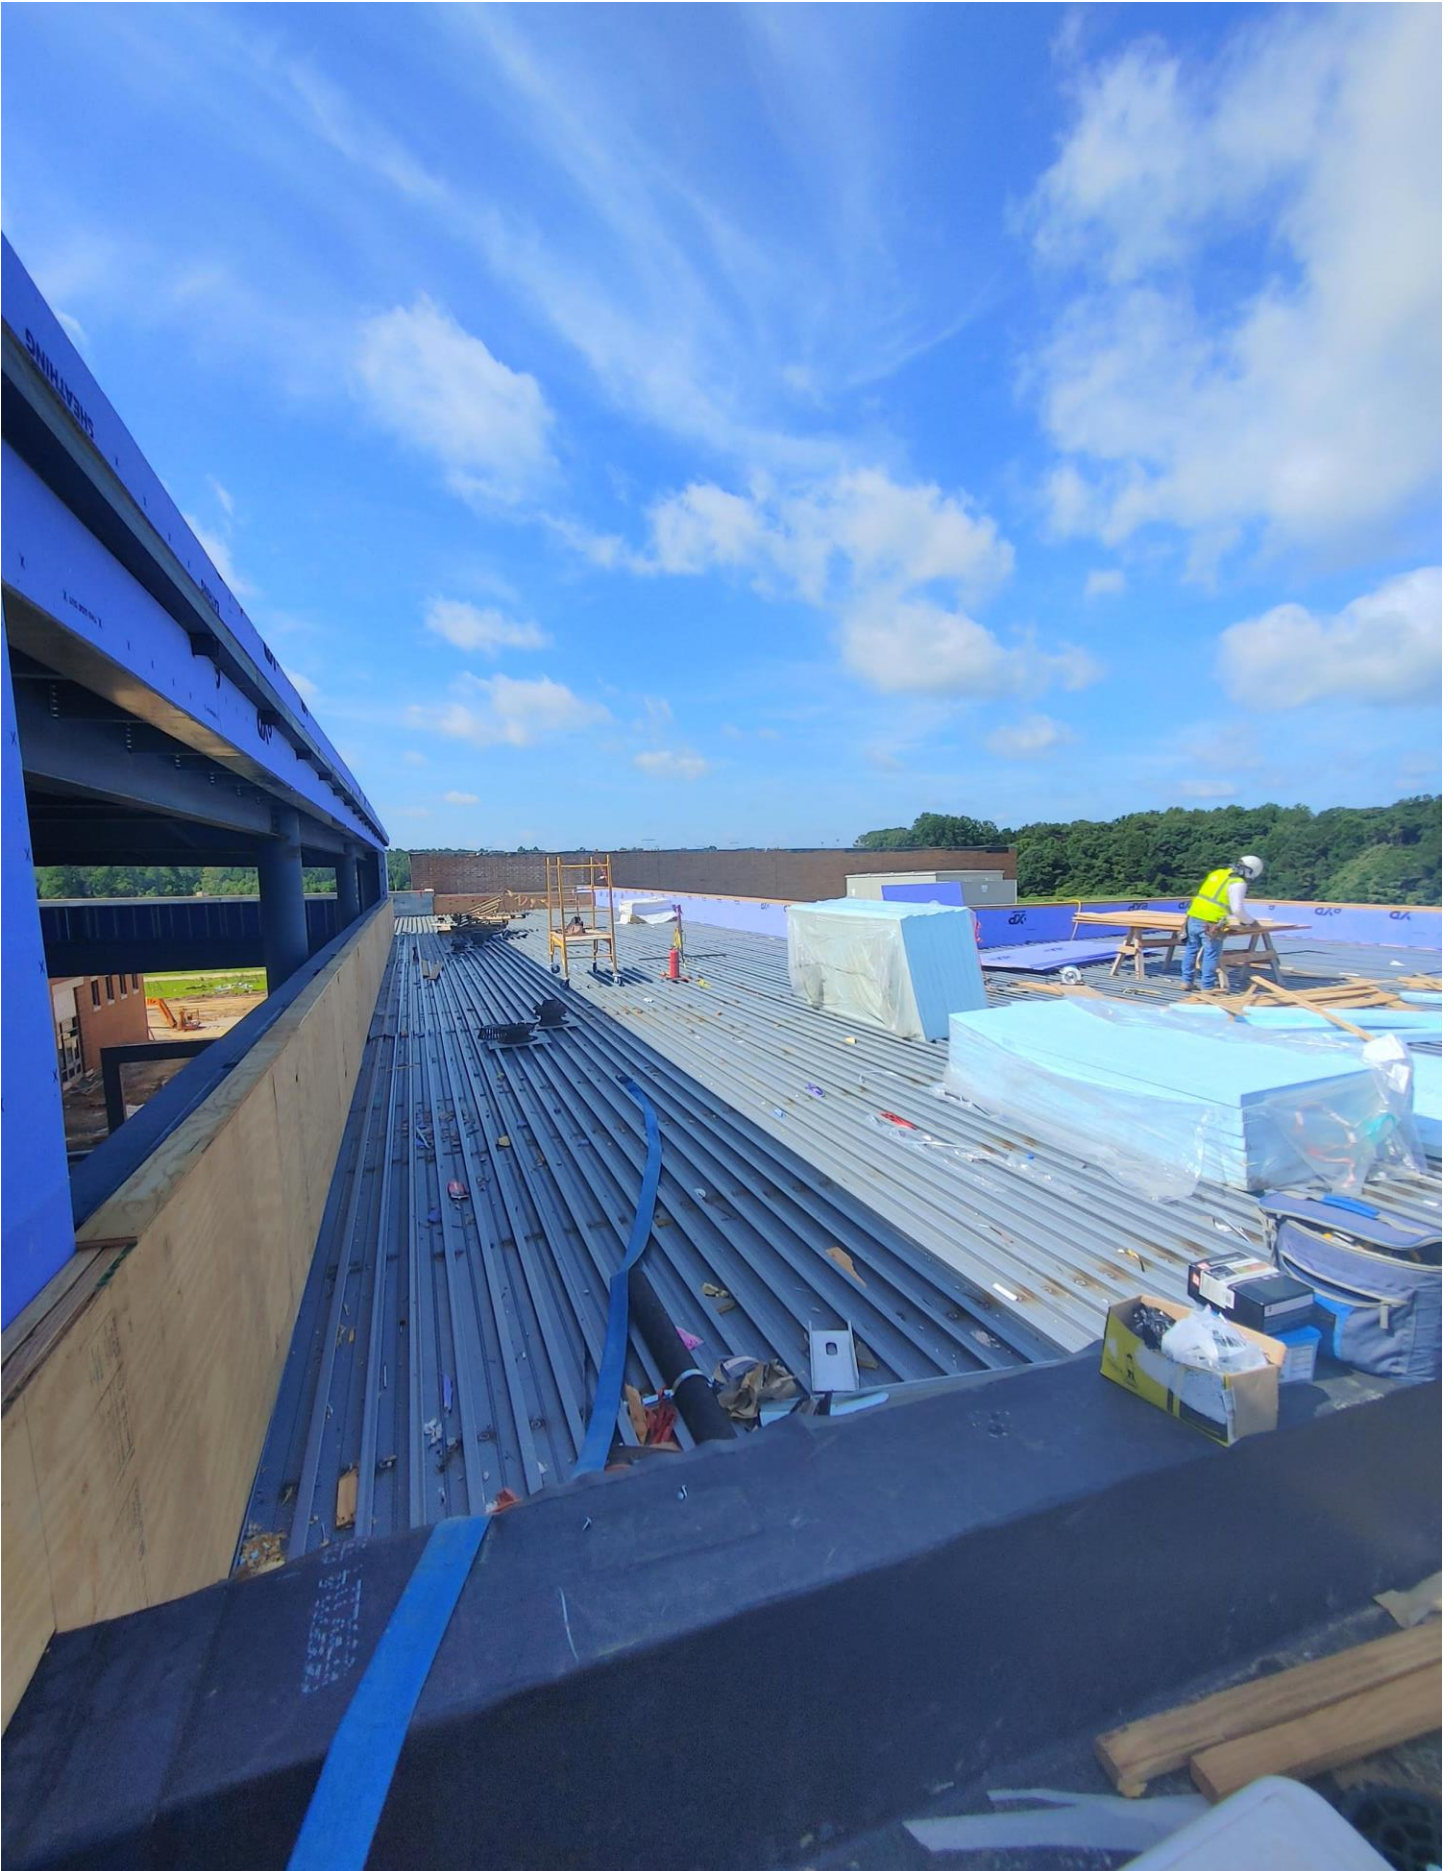


Photo 2 - Parapet walls being constructed in Area C



Photo 3 - Trash and debris on the metal pan in areas around parapet wall in Area C needs to be cleaned before roofing material is applied



Photo 4 - Pipe being insulated in Area A



Photo 5 - Fire caulking has been applied around pipe in Area A



Photo 6 - Masons continue to lay block in the Kitchen area



Photo 7 - Brick is being laid in the Loading Dock Area



Photo 8 - Metal framing is going up on the front entrance
