



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**DAILY REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 07/15/2021

Weather: 90 degrees. Sunny. High of 91 degrees today. Heat index of 99 degrees.

Hours Worked: 13:30hrs – 15:30hrs (2hrs)

I walked the site and observed the work being performed. A major cleanup of the entire site is occurring this afternoon. We received between 1.5 and 2 inches of rain last night. The site is wet and muddy today.

**Beuchert Excavation:** No one is on site today.

**Industrial Concrete:** No one is on site today.

**J.D. Long, Masons:** Twenty (20) men are on site today. They continue to lay block in Area C, chase walls in Area E and setting precast on the South side of area A.

**Hazzard Electric:** Seventeen (17) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D.

**Colonial Webb:** Nineteen (19) men are on site. They are running Duct in Area D and Area A. and a crew continues to insulate pipe & duct in Area A. Two men are working on rooftop HVAC units in Area A.

**Weldon Steel:** Three (3) men are here today working on Stairwell # 4.

**JP Construction:** Nineteen (19) men are on site today. They are finishing sheetrock in Area B, Framing metal studs in Area A and installing Acoustical Ceiling grid in Area B.

**AAR Roofing:** They are scheduled now to return on Monday, July 19, 2021.

**Tailored Foam:** Two (2) men are on site spraying foam on the front of Area A and on the South side of Area B.

**FG & M:** No one is on site today.

**United Sprinkler:** Two (2) men are on site today. They are setting Sprinkler heads in Area A.

**CTSI:** Two men are on site today running low voltage wire throughout the site.

**M. L. Straight:** Three (3) men are on site today painting and back rolling in Area A.

**K-Plus:** One (1) man is here today caulking various areas.

**S&S Concrete Cutting Company:** I did not observe anyone on site today during my visit.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe a Tech on site today.

**Questions to or from Branch Builds:** Met with Brian and Todd in the Trailer. Todd forwarded an email to me from United Sprinkler identifying the Node Points that they need identified by Resource International. Brian and I discussed the project.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report - 07/14/2021**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) –**

**Submittals – #11 66 23-4.0, #26 50 00-5.1**

**RFIs – #277, #283, #284, #290, #292,**

**Patrick Byrne – Westmoreland County HS BDA, 7/9/2021 Field Report**

**Change Order/PCOs/Pay App –**

**Changes in Procore –**

**Weekly Submittal Status Report –**

**Weekly RFI Status Update –**

**Weekly Daily Log Summary –**

**PCO Log –**



Photo 1 - Precast is being laid on the South side of Area A

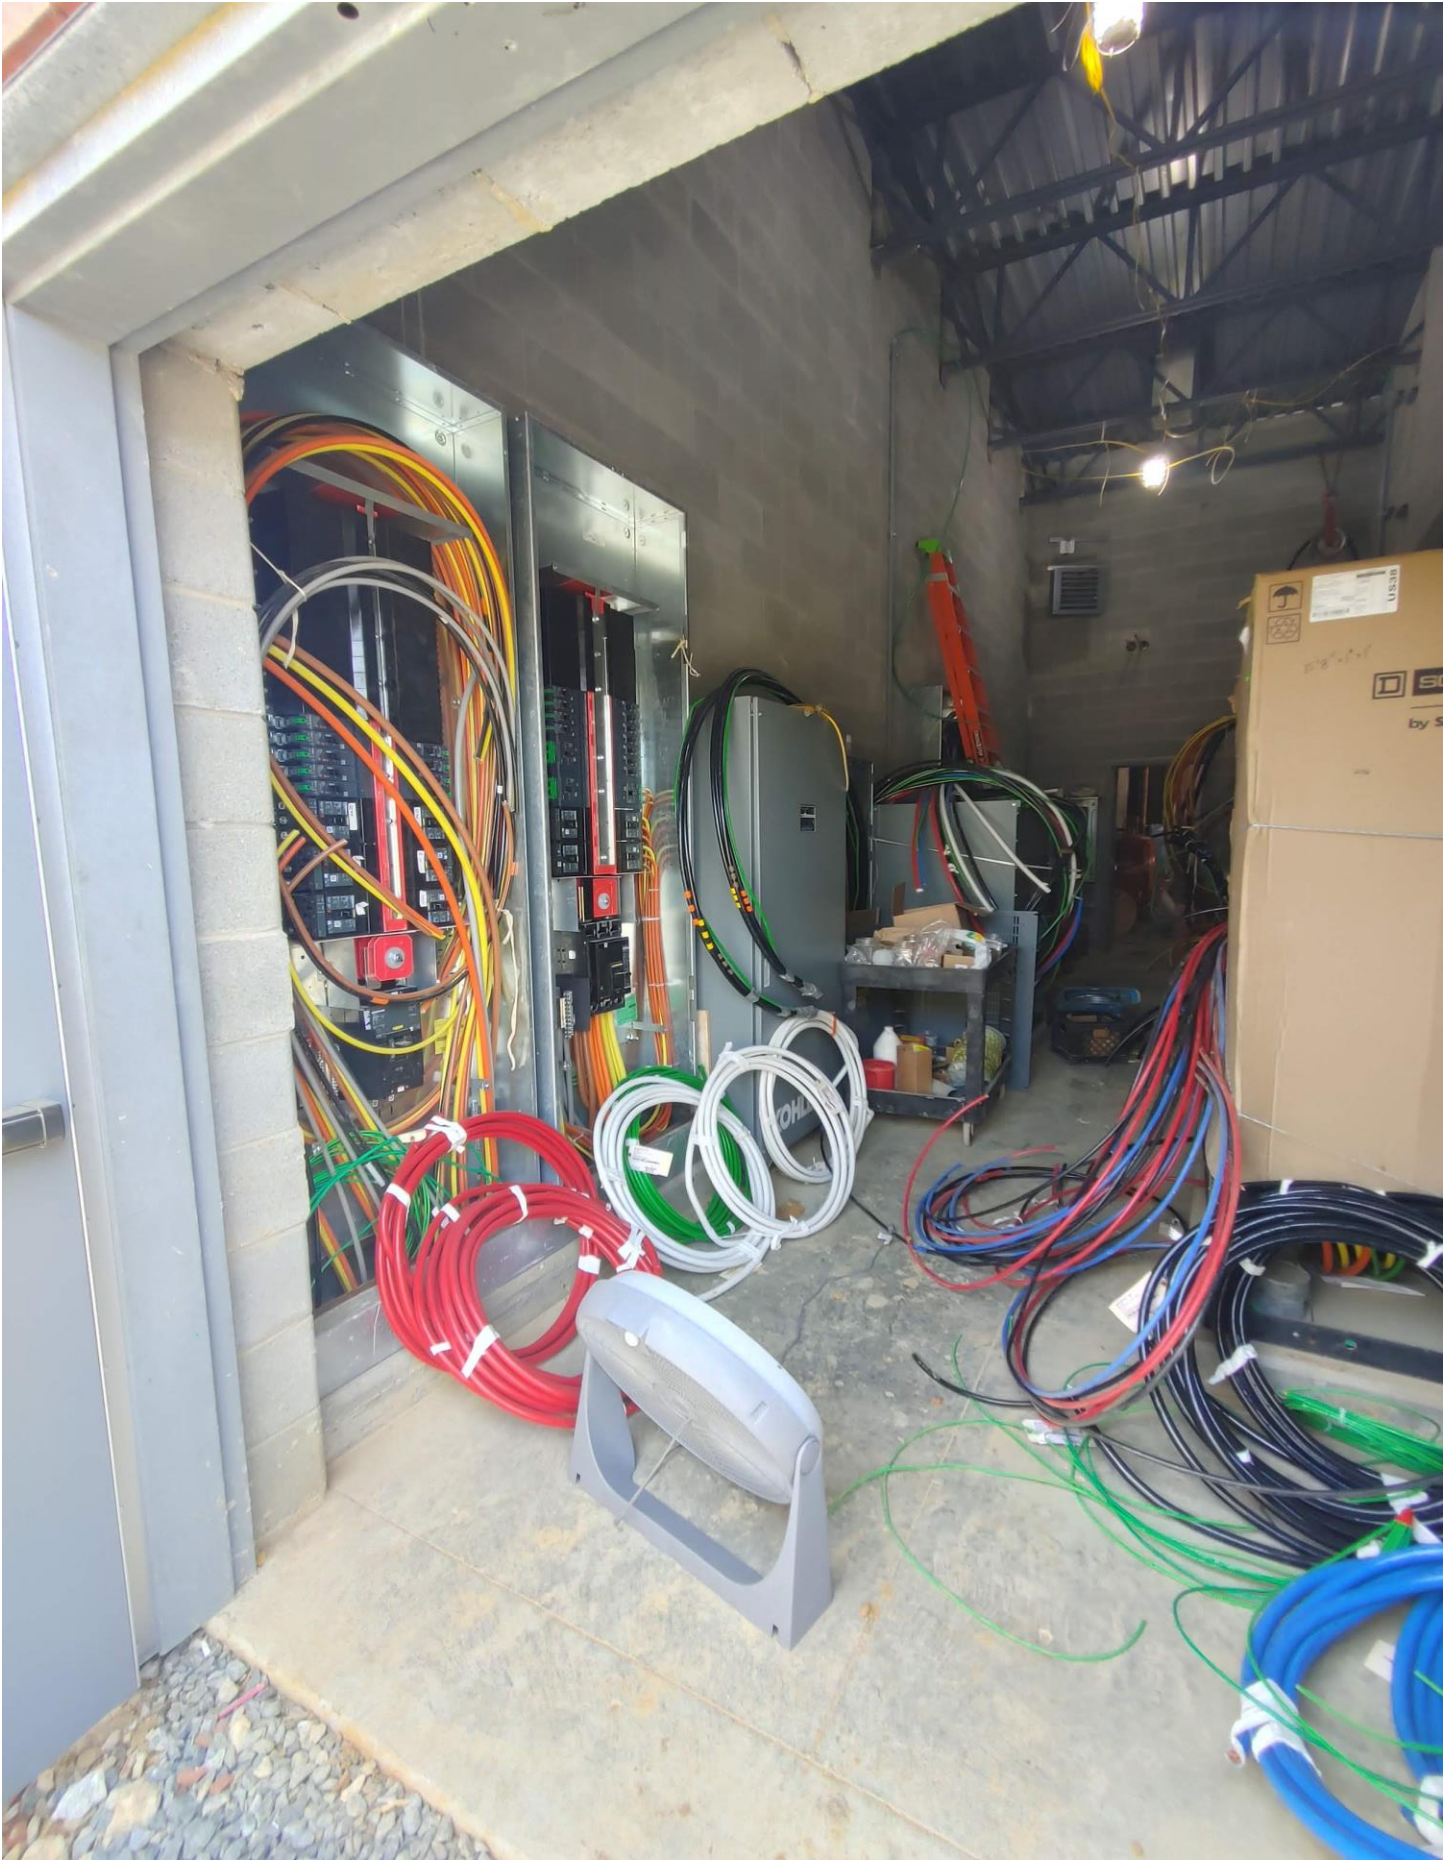


Photo 2 - Electricians continue to pull wire to the main electrical room



Photo 3 - Mason continue to lay block in the Kitchen area.



Photo 4 - The Masons are laying chase walls in Area e



Photo 5 - Acoustical Ceiling Grid is being installed in Area B



Photo 6 - Walls being framed on the 2nd floor of Area A





Photo 7 - Motion Light Sensors, Fire Alarms Horns and Strobes, Sound System Speakers and Sprinkler Heads are being installed in Area A



Photo 8 - Tailored Foam spray foamed the front of Area A. Green foam was sprayed today.
