



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 08/24/2021

Weather: 89 degrees. Sunny. High of 93 degrees today. Heat index of 100 today.

Hours Worked: 10:30hrs – 14:00hrs (3.5hrs)

Dominion Power is on site today making the final connections to energize the building.

I walked the site and observed the work being performed.

Beuchert Excavation: Four (4) men are on site today. They are working on the Bus Parking area.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Eight (8) They are laying block in Areas E & D, Chase Walls.

Hazzard Electric: Thirteen (13) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: Eleven (11) are on site today. They continue to are insulate pipe in Areas A & C. Crews are also running HVAC Duct in Area D.

Weldon Steel: No one is on site today.

JP Construction: Seventeen (17) men are on site today. They are pointing up sheetrock in Area A; framing walls, hanging sheet rock and installing ceiling grid in Area A and also framing walls in Area D. Two guys are also hanging sheetrock in Area C.

AAR Roofing: No one is on site today.

Tailored Foam: Two (2) are on site today. They are spraying foam on the West side of Area C.

FG & M: Seven (7) men are on site. They are installing the SF53B and various frames throughout the Administrative area of Area A.

United Sprinkler: Two (2) men are on site running pipe in Area D.

CTSI: Three (3) men are here today running low voltage wire in the Administrative area of Area A.

M. L. Straight: Four (4) men are here today painting in Area E.

K-Plus: No one is here today.

AAM: Four (4) men are on site today. They have begun to install metal panels on the North side of Area B.

Hodgemen: Seven (7) men are on site today laying tile on the 2nd floor of Area A. they have completed all of the Learning Studios on the first floor of Area A.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: In my last report I noted that condensation was building up on the first floor of Area A due to the temp wall removal for the installation of the A10 frame. I also noted that erosion had occurred around the retention pond and the drop inlet along County Park Drive. Brian immediately constructed a new temp wall with a tarp to rectify the situation and he also had Beuchert repair the erosion at the retention pond and drop inlet.

I met with Beuchert Superintendent and thanked him for repairing the retention pond. He advised me that they are nearing the completed elevation of the Bus Loop Parking Area. He said his plan is to move to the front of the building and continually work his way around the site. He said he also will be working in the Bio Ponds once they get the mixture right.

I met with Brian in the trailer and he updated me on what was going on today.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) – 08/18/2021, 08/19/2021

Submittals –

RFIs – #299

Patrick Byrne –

Change Order/PCOs/Pay App – PCO #56

Changes in Procore –

Weekly Submittal Status Report – 08/20/2021

Weekly RFI Status Update –08/20/2021

Weekly Daily Log Summary – 08/20/2021

PCO Log – 08/20/2021



Photo 1 - Conduit for lighting stubbed up in front of Area A



Photo 2 - Walls are being framed in Area D.



Photo 3 - Sheetrock is being hung in Area C.



Photo 4 - Sheetrock is being hung on the radius bulkhead.



Photo 5 - Raised slabs for locker have been poured in Rooms E135B & E136B



Photo 6 - Painters are working in Area E.



Photo 7 - Tile has been laid in all of the Learning Studios on the 1st floor of Area A.



Photo 8 - Sheetrock is being hung on the 2nd floor of Area A.



Photo 9 - Spray Foam being applied to the West side of Area C.



Photo 10 - Flashing being applied to the high roof of Area C.

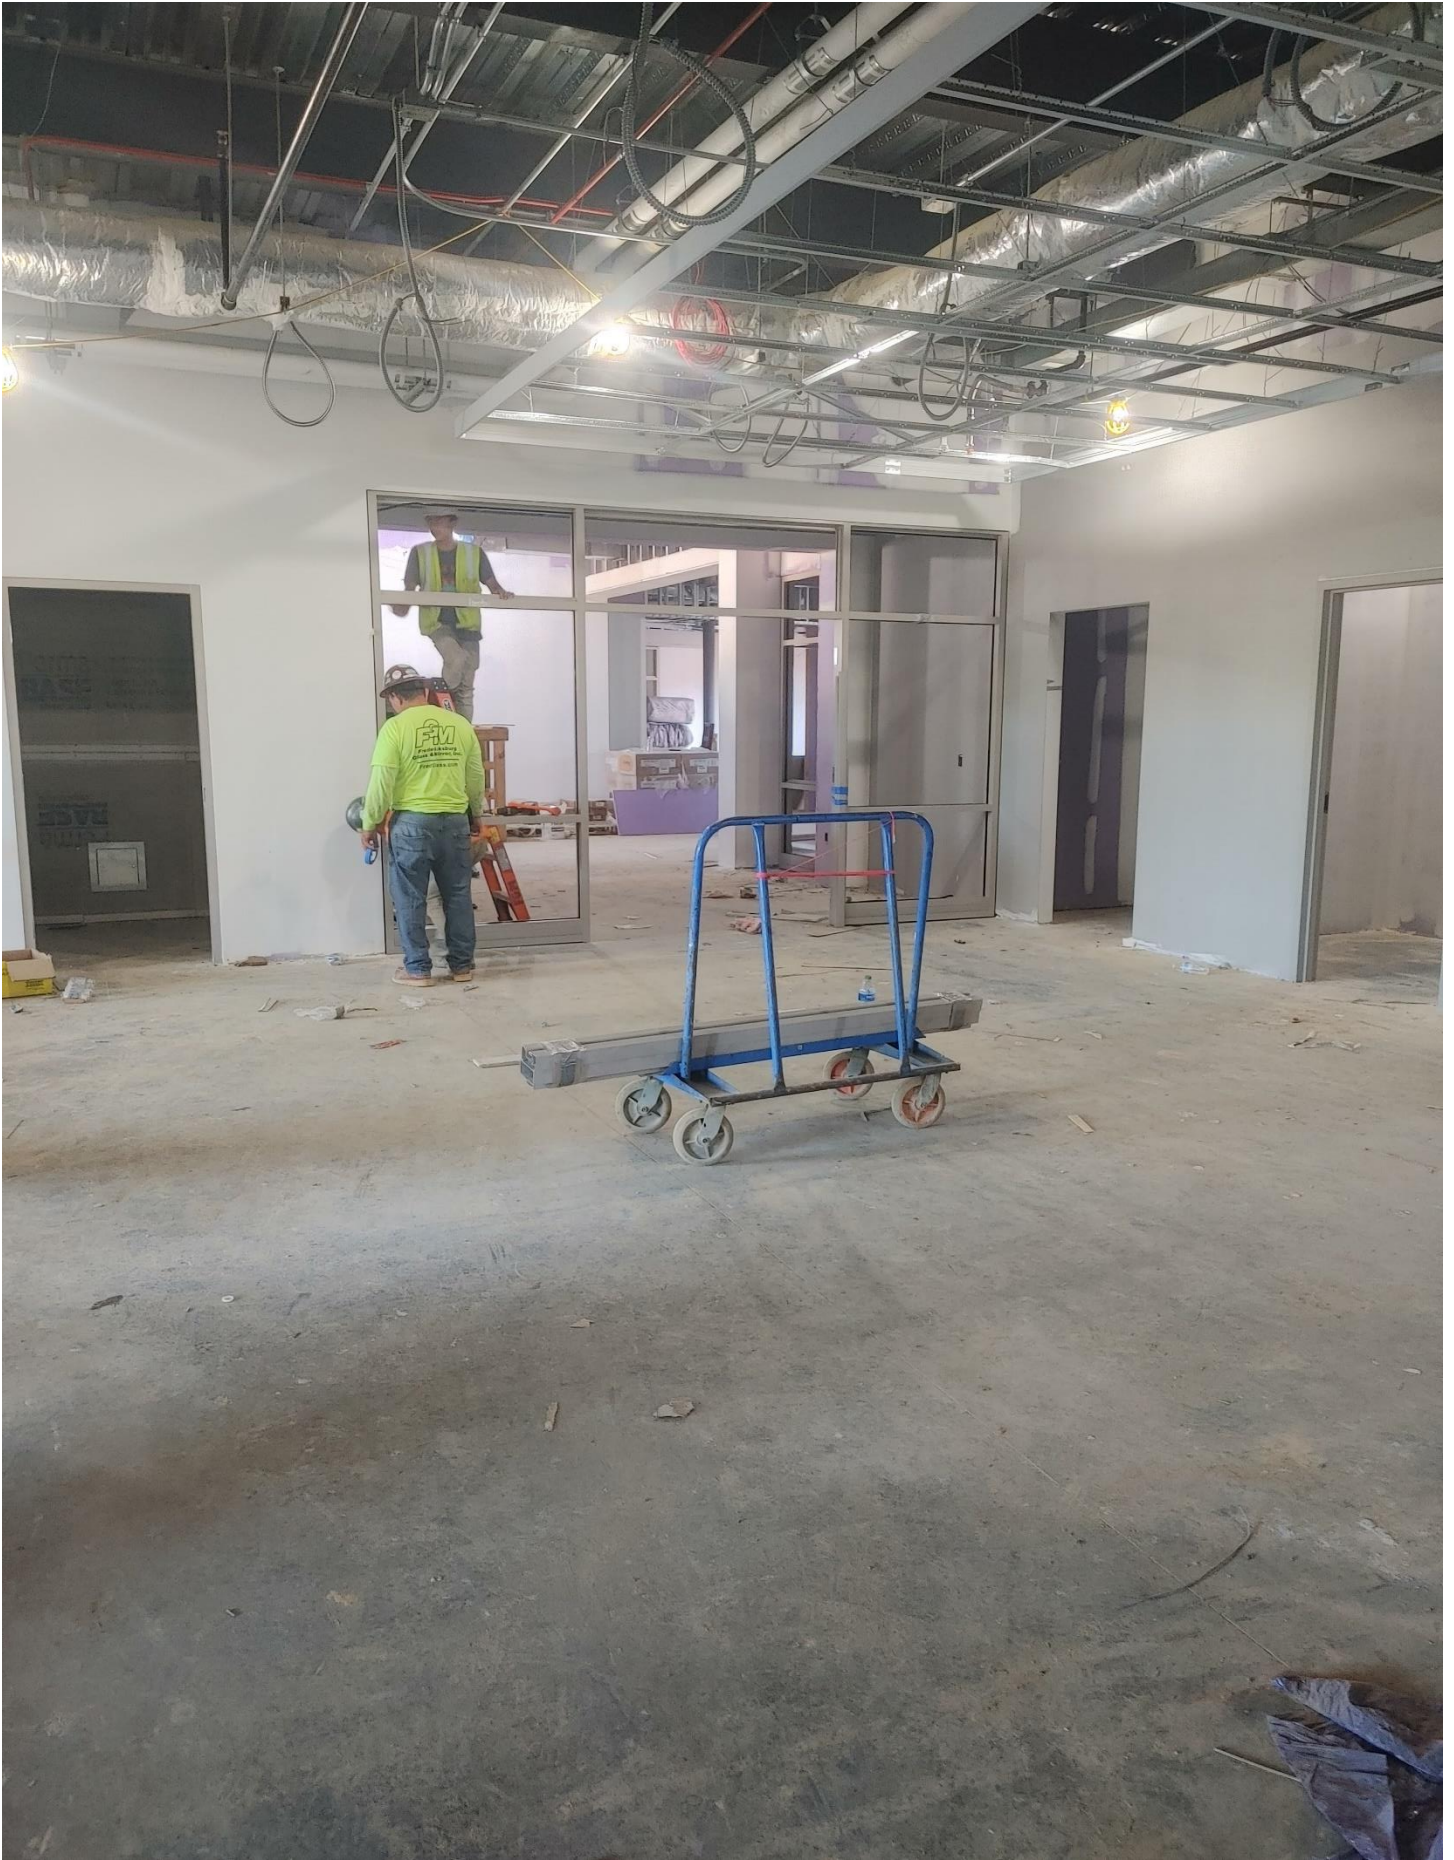


Photo 11 - Storefront 53B is being installed.



Photo 12 - Storefronts and door frames are being installed in the Administrative area.
