



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 08/30/2021

Weather: 89 degrees. Sunny. High of 91 degrees today. Heat index of 100 today.

Hours Worked: 10:00hrs – 11:00hrs & 13:30 – 15:00 (2.5hrs)

This morning I met with Norm Risavi to discuss Patrick Byrne's email pertaining to the Heavy Asphalt in the Parking lot area. I then met with John and Jake in the Branch Builds trailer to discuss the asphalt the time line for the removal of my office trailer.

Beuchert Excavation: Four (4) men are on site today. They continue to work on the Bus Parking area.

Industrial Concrete: No one is on site today.

J.D. Long, Masons: Two (2) They continue to clean up various areas and point up block.

Hazzard Electric: Ten (10) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D.

Colonial Webb: Twelve (12) men are on site today. Running duct and insulating pipe in Area C.

Weldon Steel: No one is on site today.

JP Construction: Seventeen men are on site today. They are hanging & finishing and framing in Area A.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: Six (6) men are on site. They are installing the glass in the Storefronts in Area A.

United Sprinkler: Two men are on site running pipe in Area D.

CTSI: Three (3) men are on site pulling wire in Area A.

M. L. Straight: Four (4) men are on site today painting in Area E.

K-Plus: Two (2) men are here caulking various areas.

AAM: Five (5) men are on site today. They are installing metal panels on the South side of Area B.

Hodgemen: No one is here.

S&S Concrete Cutting Company: No one is on site today.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe a Tech on site today.

Questions to or from Branch Builds: I met with Brian Topper this afternoon in the Trailer. We discussed the potential Change Order for the Parking lot and the impact it could have on the schedule as it relates to the removal of my Office and the overall schedule. We also discussed the progress of the project.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report - 08/24/2021, 08/26/2021, 08/27/2021

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports (Concrete and Steel) –

Submittals –

RFIs – #302

Patrick Byrne –

Change Order/PCOs/Pay App –

Changes in Procore –

Weekly Submittal Status Report:

Weekly RFI Status Update –

Weekly Daily Log Summary –

PCO Log –



Photo 1 - FG&M working on Frames on the North side of Area A.



Photo 2 - Storefronts continue to be set on Area A.



Photo 3 - HVAC Duct is being run in Area C and sheetrock is being finished.



Photo 4 - Metal Panels are being installed on the South side of Area B.

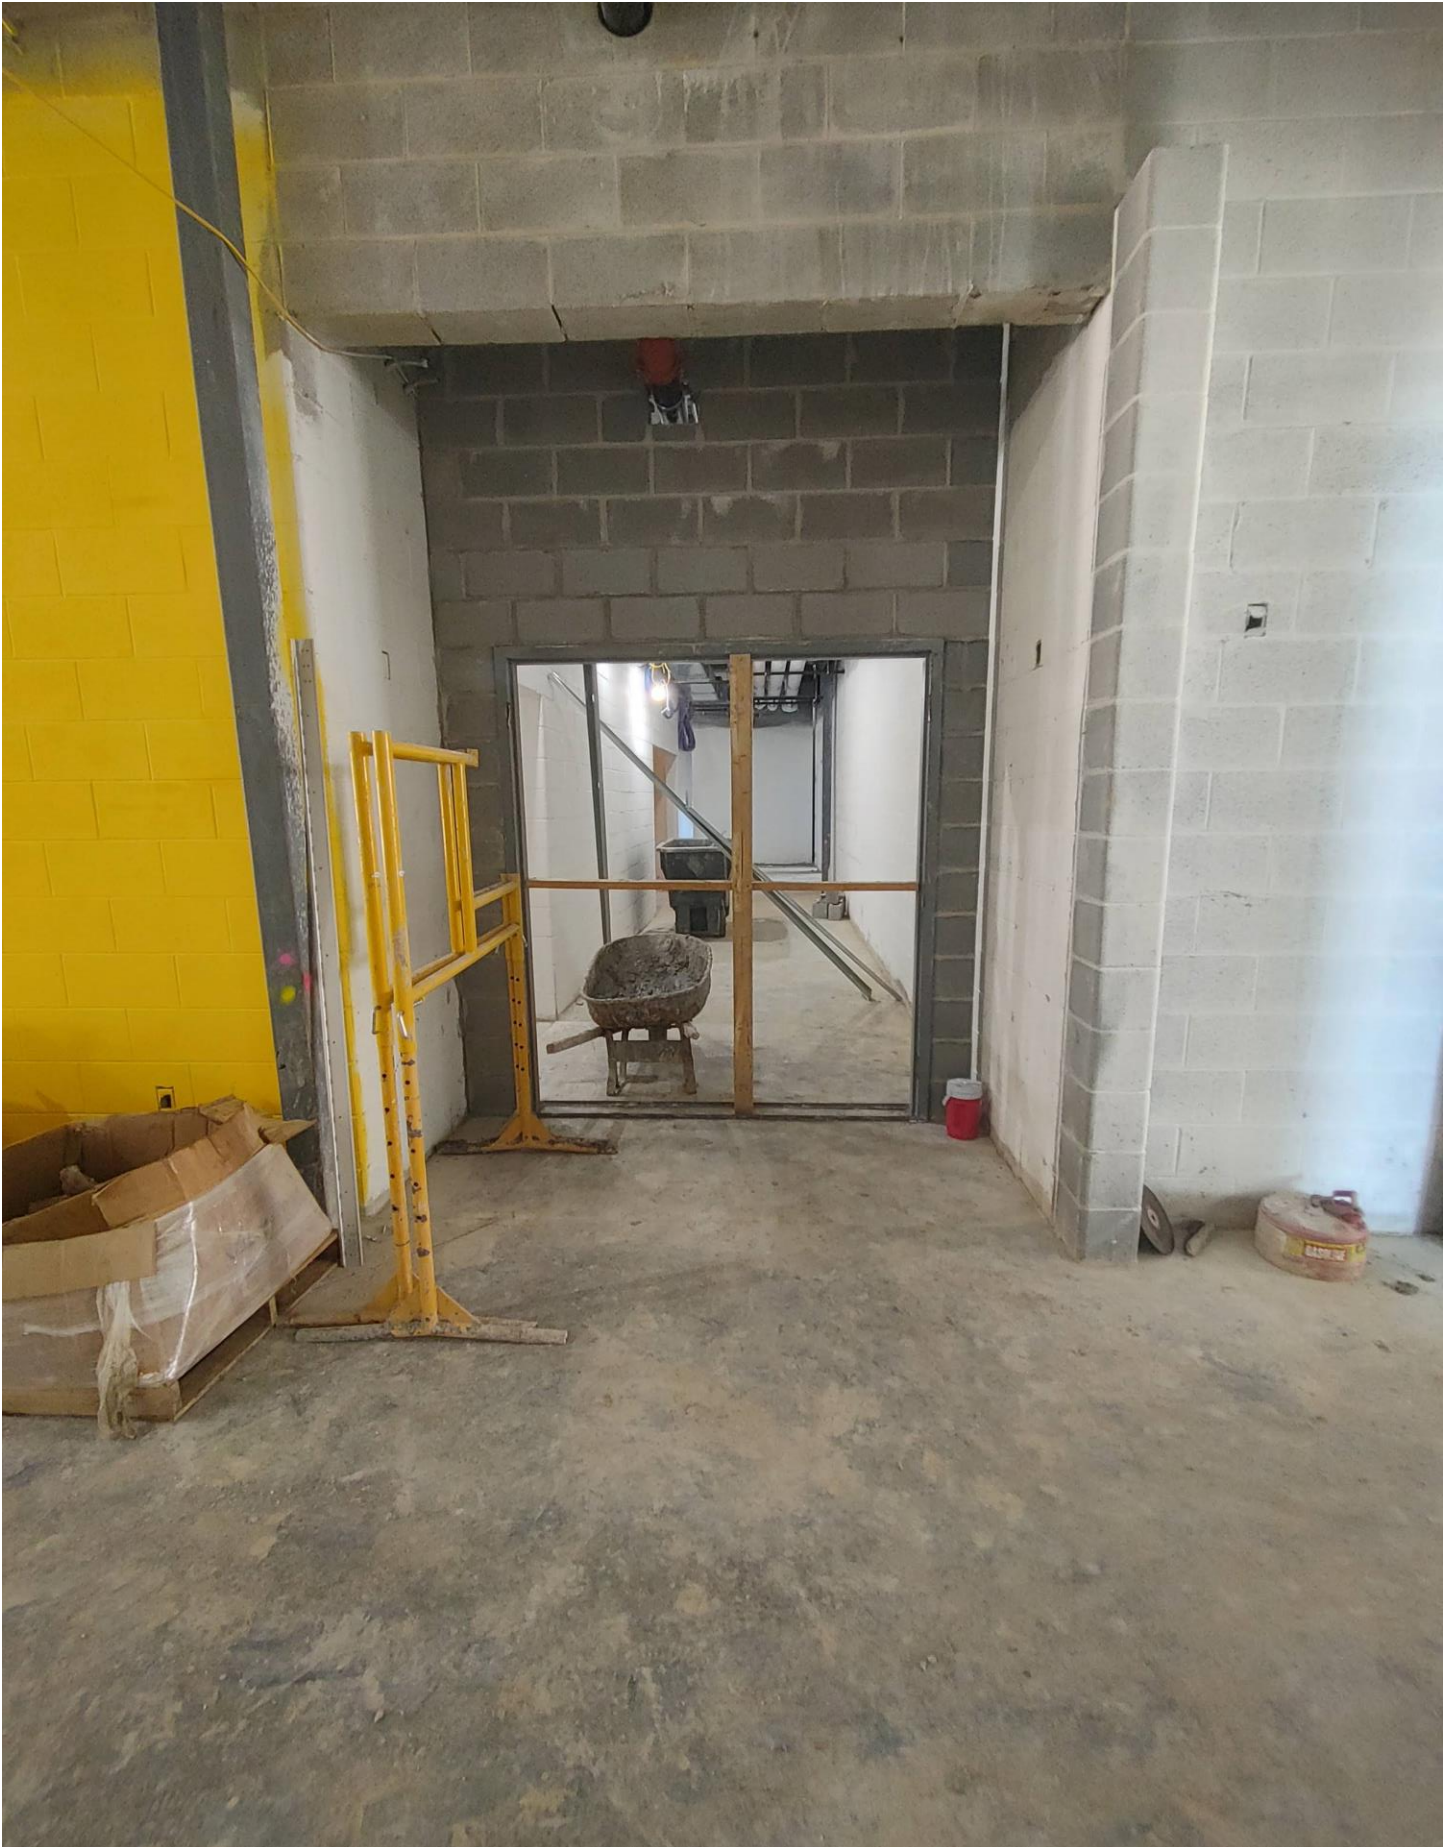


Photo 5 - E12 frame has been set and block laid.



Photo 6 - Storefronts are being et in Corridor D12



Photo 7 - Electrical Conduit is being run in Area D.



Photo 8 - Hat Channel is being installed in the Auditorium.



Photo 9 - Hat Channel has been installed on the rear wall of the Auditorium.
