



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 09/15/2021

Weather: 87 degrees. Sunny. High of 94 degrees today.

Hours Worked: 09:00hrs – 14:30hrs (5.5hrs)

I attended the Progress Meeting today from Norm Risavi's Conference room. Dominion Power began to run the Service to the Rec Park yesterday. The Sub-Contractor installing the 12" waterline made the tie-in to the 8" water line yesterday afternoon. Monday afternoon, with the help of Ronnie Saunders, I move the furniture, drawings, files etc. out of my office on the High School site. Then on Tuesday Morning I had the Office moved to the Monroe Hall Transfer Station. I have also been corresponding back and forth with Hillis-Carnes and Branch Builds since this past Friday on the Schedule, Scope of Work and project Cost for Hillis-Carnes Services for the BMPs.

**Beuchert Excavation:** Four (4) men are on site today. They have begun to work on the BMP on the West side of the Bus Parking Area and they are also working on the main travel lane in front of the school.

**Industrial Concrete:** No men are on site today.

**J.D. Long, Masons:** Seven (7) They are laying brick on the North side of Area A and on the East side of Area C.

**Hazzard Electric:** Thirteen (13) men are on site today. They continue to pull wire and run conduit in Area A, B, C & D. A couple of guys are also running conduit in front of the school for light poles.

**Colonial Webb:** Thirteen (13) men are on site today. Running duct and insulating pipe in Areas A, C and in Area E.

**Weldon Steel:** No one is on site today.

**JP Construction:** Seventeen (17) men are on site today. They are hanging & finishing sheetrock and framing walls in Area A.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is here today.

**FG & M:** Five (5) men are on site. They are working on CW #2.

**United Sprinkler:** One (1) man continues to run pipe in Area D.

**CTSI:** Five (5) men are on site pulling wire throughout the site.

**M. L. Straight:** Four (4) men are on site today painting in Area D.

**K-Plus:** One (1) man is on site caulking Control Joints on the exterior West side of Area B.

**AAM:** Five (5) men are on site today. They are installing metal panels on the East side of Area D.

**Hodgemen:** No one is here.

**S&S Concrete Cutting Company:** No one is on site today.

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** A Tech is on site today. He is observing the construction of the BMP on the West side of the School Bus Parking area.

**Questions to or from Branch Builds:** I arrived this morning and met with Brian Topper and Dean Bunn of Hillis-Carnes at the BMP on the West side of the School Bus Parking Area. Two sections of pipe were set in the BMP to conduct a Infiltration Test. Water was poured into the pipe and measured after one hour. Both tests passed the requirement of water drainage of a minimum of 1" per hour. After the Progress meeting I returned to the site and noted that Beuchert had almost completed the installation of 12" of 57 stone.

Todd Demetriou sent out an email on September 10, 2021 – August Schedule Update.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report -**

**Hillis-Carnes Grout Inspection/Compression Strength Test –**

**Hillis-Carnes Field Reports (Concrete and Steel) – 09/13/2021**

**Submittals – #07 42 13-6.0, #07 42 13-7.0, #09 64 66-1.2, #12 35 53-1.1, #12 35 53-3.11**

**RFIs – #306, #313, #314, #315**

**Patrick Byrne –**

**Change Order/PCOs/Pay App –**

**Changes in Procore –**

**Weekly Submittal Status Report: 09/10/2021**

**Weekly RFI Status Update – 09/10/2021**

**Weekly Daily Log Summary – 09/10/2021**

**PCO Log – 09/10/2021**



*Photo 1 - Infiltration Test being performed in the BMP on the West side of the School Bus Parking Area*



*Photo 2 - The BMP on the West side of the Site is being constructed*



*Photo 3 - 2nd Infiltration Test being conducted in the BMP on the West side of the site.*



*Photo 4 - Drive Lanes in front of the school have been laid out and are being graded*



Photo 5 - Drive lane



Photo 6 - Steps are being taken to protect the Curtain wall as the mason lays brick.





*Photo 7 - Poly is being hung over the storefront to protect it as the Mason lays brick.*



*Photo 8 - The masons are running conduit for Pole Lights*



Photo 9 - SF #32A & #33 have been installed



Photo 10 - Duct work is being installed in Area C.



Photo 11 - SF #35 has been installed



Photo 12 - CW#2 is being installed



*Photo 13 - Lighting has been installed in A118*

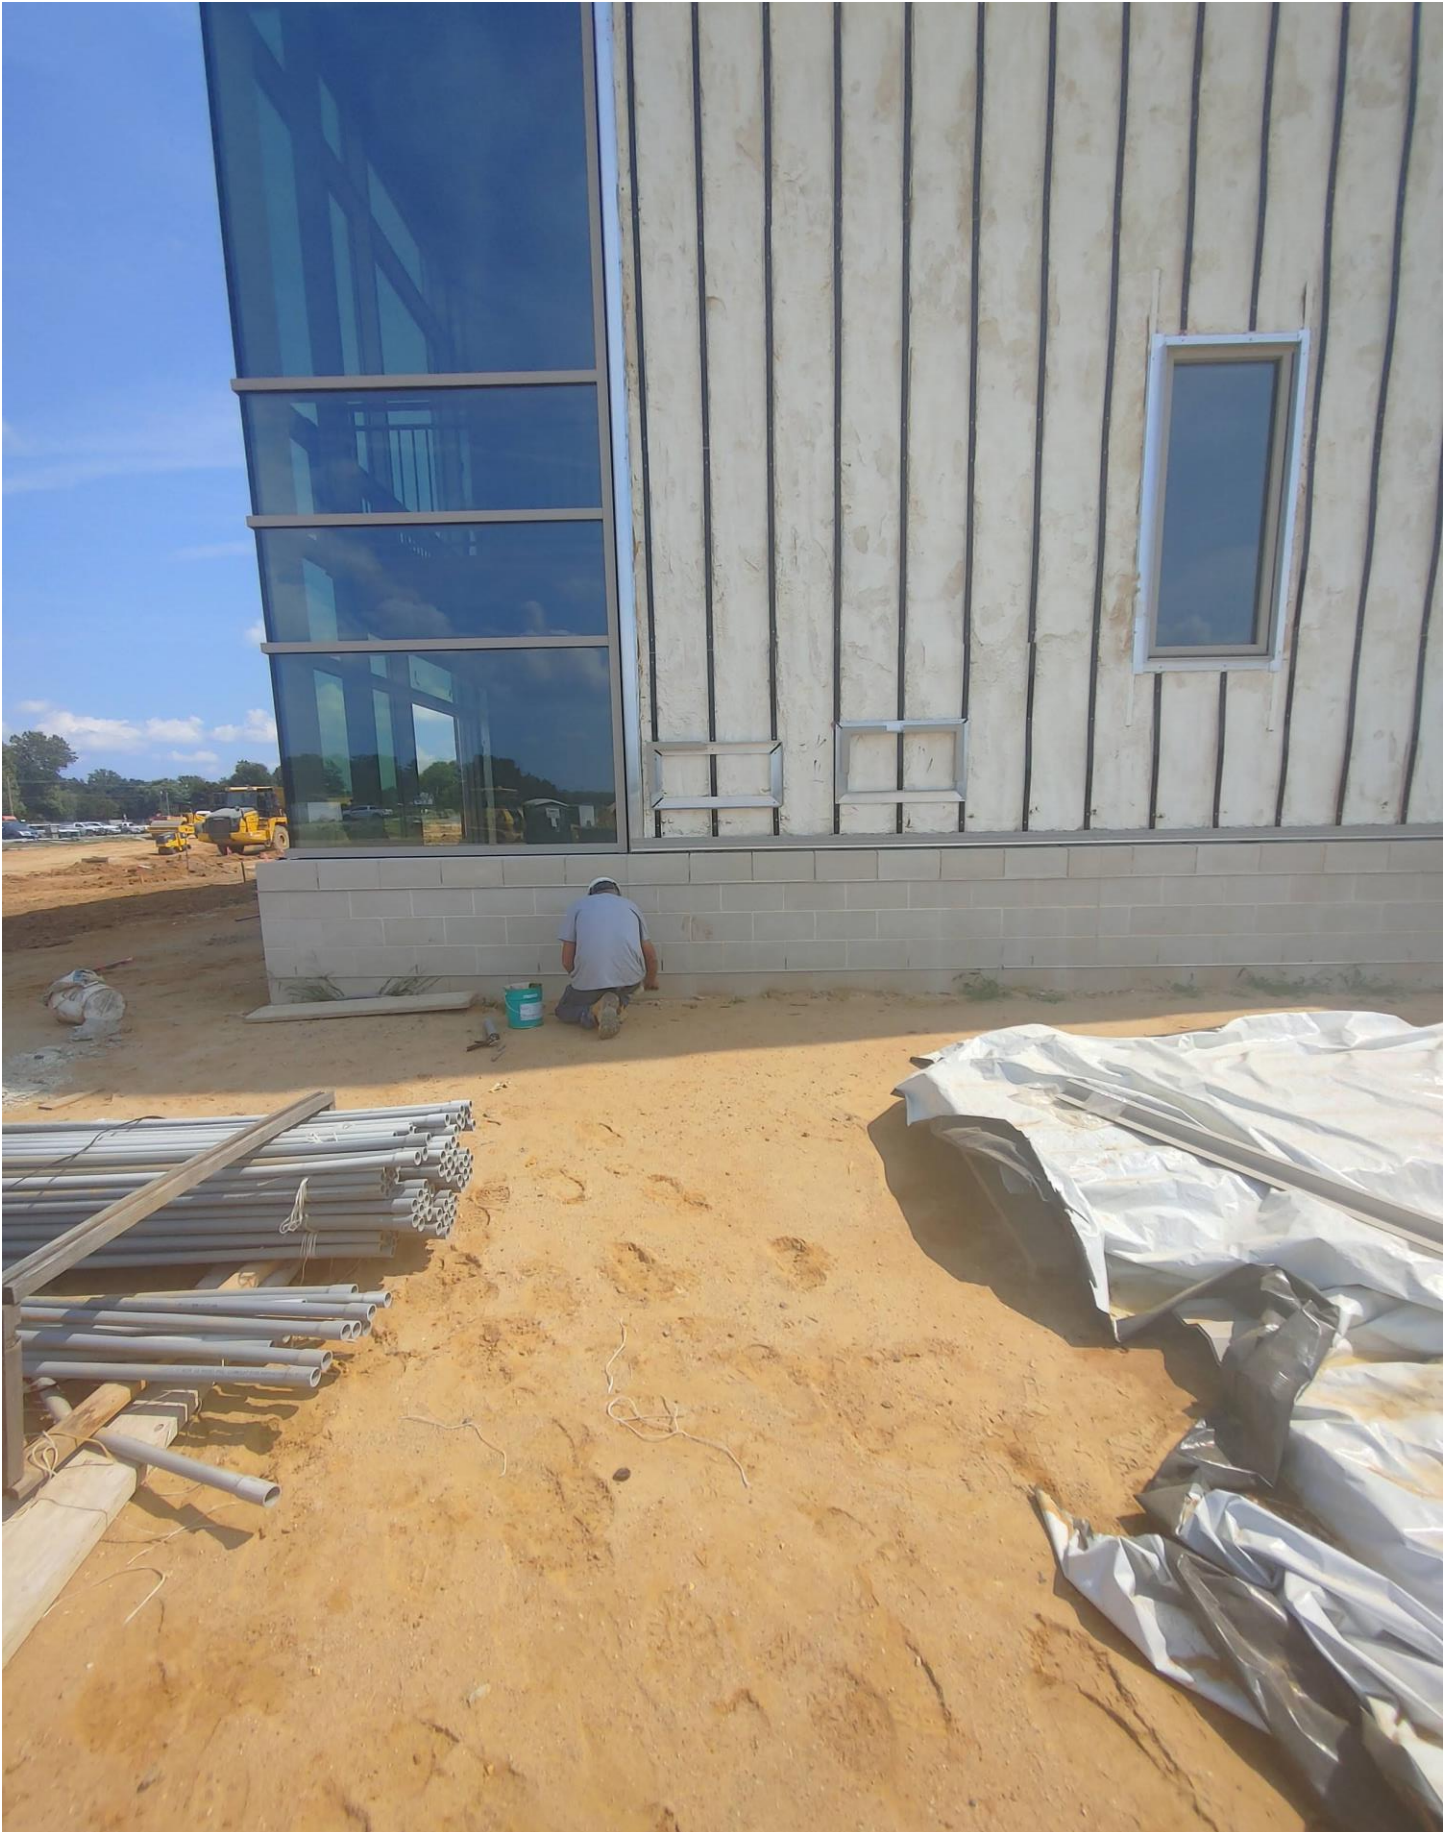


Photo 14 – Exterior Control Joints are being Caulked in Area B





Photo 15 - 12" of 57 Stone is being installed in the BMP on the West side of the School.



Photo 16 - SF #47 has been installed



Photo 17 - The Canopy is being Installed on the South side of Area C



Photo 18 – The Masons are laying Brick of the East side of Area C.
